



CalSAWS-CalWIN
Implementation Support
Weekly Status Report

Reporting Period: May 24, 2021 to May 30, 2021

Table of Contents

1.0 CalWIN Implementation Support Services.....2

1.1 Highlights of the Reporting Period.....2

1.2 Project Deliverable Summary4

1.3 Project Risks and Issues5

1.4 CRFI/CIT Communications Information5

1.5 Activities for the Next Reporting Period.....5

1.6 Deviations from Plan/Adjustments6

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, June 2, 2021

Reporting Period: May 24, 2021 to May 30, 2021

1.0 CalWIN Implementation Support Services

1.1 Highlights of the Reporting Period

Project Management

- ▶ Finalized the setup of the CalWIN ISS email account and confirmed that receipt and send functions work properly; worked out processes for assigning Questions to team members.
- ▶ Continued the monitoring of Action Items (AIs) and followed up with POCs to update the statuses.
- ▶ Worked with BPR on Final Work Product Sign-Off (FWP).

Business Process Re-Engineering (BPR)

- ▶ Obtained Sign-Off on the Final Work Product for Santa Cruz and Solano Counties.
- ▶ Completed Week-2 of Fresno and Alameda Counties As-Is BPR sessions, including a hybrid onsite/offsite delivery for Fresno County.
- ▶ Prepare base flows for San Francisco As-Is County Sessions.
- ▶ Continued with To-Be pre-work and data gathering.
- ▶ Continued definition of Global To-Be Process flows.
- ▶ Agreed on a plan to engage the CalSAWS BAs/SMEs throughout the To-Be Process Definition.

Figure 1 – As-Is Process Timetable by County

County	Session Start Date	Session End Date	First Review Start Date	First Review End Date	Incorporate Feedback	Start Final Review	County Sign-Off on FINAL As-Is Processes
Wave 1							
Contra Costa	02/22/21	03/25/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Placer	02/22/21	03/12/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Yolo	03/01/21	03/19/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Wave 2							
Tulare	03/01/21	03/19/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Santa Clara	03/22/21	04/02/21	04/05/21	04/16/21	04/23/21	04/26/21	04/30/21
Wave 3							
Santa Barbara	03/22/21	04/02/21	04/05/21	04/16/21	04/23/21	04/26/21	04/30/21
Orange	04/05/21	04/16/21	04/19/21	04/30/21	05/07/21	05/10/21	05/14/21
Ventura	04/05/21	04/16/21	04/19/21	04/30/21	05/07/21	05/10/21	05/14/21
Wave 4							
Solano	04/19/21	04/30/21	05/03/21	05/14/21	05/21/21	05/24/21	06/01/21
Santa Cruz	04/19/21	04/30/21	05/03/21	05/14/21	05/21/21	05/24/21	06/01/21
San Mateo	05/03/21	05/14/21	05/17/21	05/28/21	06/07/21	06/08/21	06/15/21
San Diego	05/03/21	05/14/21	05/17/21	05/28/21	06/07/21	06/08/21	06/15/21
Wave 5							
Alameda	05/17/21	05/28/21	06/01/21	06/15/21	06/22/21	06/23/21	06/30/21
Fresno	05/17/21	05/28/21	06/01/21	06/15/21	06/22/21	06/23/21	06/30/21
Sonoma	06/14/21	06/25/21	06/28/21	07/09/21	07/16/21	07/19/21	07/23/21
Wave 6							
San Francisco	06/07/21	06/18/21	06/21/21	07/02/21	07/09/21	07/12/21	07/16/21
Sacramento	06/14/21	06/25/21	06/28/21	07/09/21	07/16/21	07/19/21	07/23/21
San Luis Obispo	06/01/21	06/11/21	06/14/21	06/25/21	07/02/21	07/05/21	07/09/21

***As of 05/28/21**

Organizational Change Management (OCM)

- ▶ Reviewed draft materials for June OCM POC meeting on 06/09/21.
- ▶ Reviewed draft materials for the County impacted end-user register.
- ▶ Prepared for the June CalWIN Stand Up meeting on 06/14/21.

Training

- ▶ Prepared and participated in first walkthrough of the June JPA presentation.
- ▶ Presented a Training update for the OPAC meeting on 05/27/21.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, June 2, 2021

Reporting Period: May 24, 2021 to May 30, 2021


- ▶ Prepared for the June CalWIN Stand Up meeting on 06/14/21.
- ▶ Began to prepare for the June TAC meeting on 06/23/21.

Implementation Support Services

- ▶ Continued pre-work activities and developed agenda for county profile review meetings
- ▶ Continued developing Global to-be process maps for Ancillary systems
- ▶ Scheduled County profile review meetings with Wave 1 Counties to confirm baseline.
- ▶ Participated in ongoing meetings with DD&I and the Consortium for conversion, API User Groups, and DDID.
- ▶ Summarized Visioning Lab Survey results on 5/27/21.
- ▶ Scheduled Waves 4 through 6 ISS Timeline reviews with the Counties.

Project Timeline

Figure 2 – Project Gantt Chart

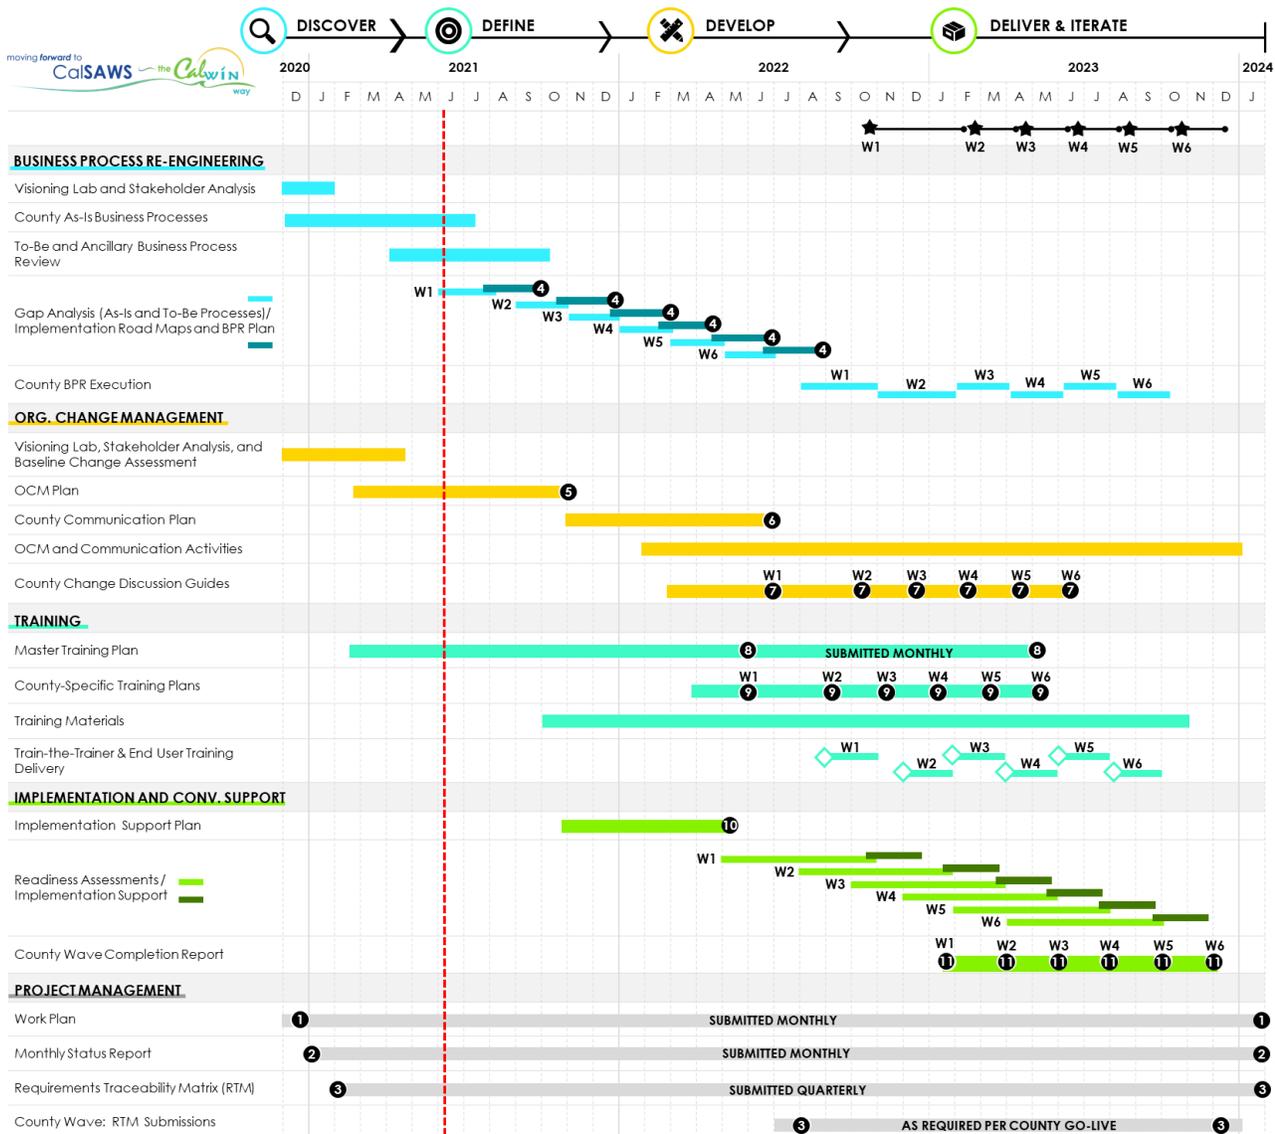

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, June 2, 2021

Reporting Period: May 24, 2021 to May 30, 2021

1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below.

Table 1 – Deliverable Status for Current Reporting Period

Completed
Coming Soon

DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final
01	Workplan – Initial	12/4/20	12/15/20	12/23/20	1/14/21	01/22/21
02	Monthly Status Report – Initial	12/4/20	12/18/20	01/05/21	01/12/21	01/27/21
03	Requirements Traceability Matrix Initial	12/22/20	01/07/21	02/01/21	02/16/21	02/23/21
04	Business Process Re-Engineering Plan – W1	06/18/21	06/30/21	10/11/21	11/01/21	11/08/21
05	Organizational Change Management Plan	06/11/21	06/23/21	10/04/21	10/26/21	11/02/21
06	County Communication Plan	08/16/21	08/26/21	01/03/22	01/25/22	02/01/22
07	County Change Guide	01/14/22	01/27/22	03/24/23	04/17/23	04/24/23
08	Master Training Plan	08/13/21	08/25/21	05/13/22	06/06/23	06/13/23
09	County Specific Training Plan	09/14/21	09/24/21	05/08/23	05/30/23	06/06/23
10	Implementation Support Plan	01/14/22	01/27/22	05/16/22	06/07/22	06/14/22
11	Wave Completion Report	09/15/22	09/27/22	01/11/24	01/24/24	01/31/24

Table 2 – Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
01	Workplan – Initial	Complete	
01.05	Work Plan – May 2021	On-Track	FDEL submission due 06/04/21 FDEL approval 06/11/21
02	Monthly Status Report – Initial	Complete	
02.05	Monthly Status Report – May 2021	On-Track	FDEL submission due 06/04/21 FDEL approval 06/11/21
03	Requirements Traceability Matrix Initial	Complete	
03.01	Requirement Traceability Matrix – Quarter 1	On-Track	FDEL submission due 06/04/21 FDEL approval 06/11/21
04	Business Process Re-engineering Plan	On-Track	DDED submission due 06/18/21
05	Organizational Change Management Plan	On-Track	DDED submission due 06/11/21
06	County Communication Plan	On-Track	DDED submission due 08/16/21
07	County Change Guide	On-Track	DDED submission due 01/14/22
08	Master Training Plan	On-Track	DDED submission due 08/13/21
09	County Specific Training Plan	On-Track	DDED submission due 09/14/21
10	Implementation Support Plan	On-Track	DDED submission due 01/14/22
11	Wave Completion Report	On-Track	DDED submission due 09/15/22

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, June 2, 2021

Reporting Period: May 24, 2021 to May 30, 2021

1.3 Project Risks and Issues

There were no CalSAWS Risks or Issues created and/or still open for the reporting period.

Table 3 – Risks & Issues

ID	Title	Details	Status	Impact	Severity	Date Logged

1.4 CRFI/CIT Communications Information

There were no CalSAWS Information Transmittals (CITs) sent and/or still open for the reporting period.

Table 4 – CITs

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact

There were no CalSAWS Requests for Information (CRFIs) sent and/or still open for the reporting period.

1.5 Activities for the Next Reporting Period

Project Management

- ▶ Continue planning for and on-boarding staff resources.
- ▶ Continue to collaborate with other teams to coordinate resources to meet dependencies, including the Training environments and DISCO tool access to the CalWIN system.
- ▶ Review the Q&A process and Q&A Log sample with the Consortium.
- ▶ Compile results of the Visioning Lab survey and determine agenda for July Lab.
- ▶ Prepare draft materials for WCDS meeting to be held 06/11/21.
- ▶ Prepare and submit Work Plan, Monthly Status Report, and Quarterly RTM on 06/04/21.

Business Process Re-Engineering (BPR)

- ▶ Review initial feedback on As-Is Draft Work Product from Alameda and Fresno Counties.
- ▶ Conduct Week-1 Sessions for San Luis Obispo County.
- ▶ Incorporate real-time feedback from the BPR sessions for continuous improvement.
- ▶ Continue with To-Be BPR pre-work.
- ▶ Continue working on definition of Global To-Be Process Flows.

Organizational Change Management (OCM)

- ▶ Onboard new team member on 06/01/21
- ▶ Prepare for June OCM POC meeting on 06/09/21
- ▶ Prepare for the June CalWIN Stand Up meeting on 06/14/21

Training

- ▶ Prepare steps for conducting Training audience analysis.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, June 2, 2021

Reporting Period: May 24, 2021 to May 30, 2021

- ▶ Coordinate with CalWIN ISS OCM Team's stakeholder analysis in preparation for the Training audience analysis.
- ▶ Prepare for the June CalWIN Stand Up meeting on 06/14/21.
- ▶ Prepare for the June TAC meeting on 06/23/21.
- ▶ Review and update training slides for WCDS meeting.
- ▶ Present Training timelines for Waves 4 and 5 Timelines reviews on 06/04/21.
- ▶ Participate in Wave 1 Check-in meeting on 06/03/21.

Implementation Support Services

- ▶ Finalize the slide deck for Wave 1 Pre-meet (Ancillary Systems)
- ▶ Continue to review the conversion activities that will impact conversion of CalWIN Counties.
- ▶ Continue drafting the global To-Be Process for ancillary systems.
- ▶ Participate in an ancillary/data meeting with DD&I and the Consortium.
- ▶ Participate in ongoing conversion meetings with DD&I and the Consortium.

1.6 Deviations from Plan/Adjustments

- ▶ None for the reporting period.
