



CalSAWS DD&I Weekly Status Report

Reporting Period: June 27, 2022 to July 3, 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

1.0	Project Management	3
1.1	Project Deliverables Summary	3
1.2	Highlights of the Reporting Period	3
1.2.1	Project Management	3
1.2.2	Communications Management	5
1.2.3	Cultural Transformation	7
1.2.4	Inclusion, Diversity and Equity Advancement (IDEA)	7
1.3	CRFI/CIT Communications Information	8
1.4	Activities for the Next Reporting Period	9
1.4.1	Project Management	9
1.4.2	Communications Management	9
1.4.3	Cultural Transformation	10
1.4.4	Inclusion, Diversity & Equity Advancement (IDEA)	10
1.5	Deviations from Plan/Adjustments	10
2.0	Imaging	11
2.1	Highlights of the Reporting Period	11
2.2	Activities for the Next Reporting Period	14
2.3	Deviations from Plan/Adjustments	14
3.0	Customer Service Center (CSC)	14
3.1	Highlights of the Reporting Period	14
3.2	Activities for the Next Reporting Period	16
3.3	Deviations from Plan/Adjustments	16
4.0	Application Development and Test	16
4.1	Highlights of the Reporting Period	16
4.1.1	Application Development Summary	17
4.1.2	Design Difference Identifiers (DDID) System Test Status	17
4.1.3	State and CalWIN Wave 1 County Interface Partner File Exchange Test (IPT)	20
4.1.4	Task Management	21
4.1.5	Application Programming Interface (API)	21
4.1.6	General Assistance/General Relief (GA/GR)	22
4.1.7	CalWIN Wave 1 Batch Performance	23
4.1.8	Case Purge	24

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

- 4.1.9 Deliverable Management..... 26
- 4.2 Activities for the Next Reporting Period..... 26
- 4.3 Deviations from Plan/Adjustments..... 26
- 5.0 Conversion26**
- 5.1 Highlights of the Reporting Period 26
- 5.1.1 CalWIN Conversion 27
- 5.1.2 CalWIN Conversion Defects Converted Data Test Defect 27
- 5.1.3 Gainwell Technologies 28
- 5.1.4 Ancillary Systems Conversion..... 28
- 5.1.5 Deliverable Management..... 30
- 5.2 Activities for the Next Reporting Period..... 30
- 5.2.1 CalWIN Conversion 30
- 5.2.2 Gainwell Technologies 30
- 5.2.3 Ancillary Systems Conversion..... 31
- 5.2.4 Deliverable Management..... 31
- 5.3 Deviations from Plan/Adjustments..... 31
- 6.0 CalWIN Functional Support31**
- 6.1 Highlights of the Reporting Period 31
- 6.2 Activities for the Next Reporting Period..... 32
- 6.3 Deviations from Plan/Adjustments..... 33
- 7.0 Technical Infrastructure.....33**
- 7.1 Highlights of the Reporting Period 33
- 7.2 Activities for the Next Reporting Period..... 35
- 7.3 Deviations from Plan/Adjustments..... 35
- 8.0 Appendices.....37**

1.0 Project Management

1.1 Project Deliverables Summary

Table 1.1-1 – Overall Summary of Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	TEAM	STATUS [1]	STATUS
	None for the reporting period			

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

1.2 Highlights of the Reporting Period

Table 1.2-1 – CalSAWS Project Management Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Project Management	<ul style="list-style-type: none"> Submitted contract Change Notice No. 19 to the Consortium for review on June 30, 2022. Change Notice No. 19 is planned to be submitted to the CalSAWS JPA Board of Directors for approval on July 22, 2022 and will include an extension of Functional Support through October 2023

1.2.1 Project Management

- ▶ Continued CalSAWS DD&I Facility Management activities, including:
 - Key initiatives related to facilities at the Rancho Cordova Project Office are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) below

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Table 1.2.1-1 – Key Facility Initiatives/Projects

ITEM #	INITIATIVES/ PROJECTS	LOCATION	TARGET DATE	NOTES/STATUS
1	Return to Office (RTO)	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> • Continued reviewing and processing Return to Office (RTO) Approval Request forms submitted by CalSAWS Project staff, which are required to access the CalSAWS Rancho Cordova or Norwalk Project offices • Continued to monitor and review requests from CalSAWS Project staff who are interested in returning to the CalSAWS Rancho Cordova and Norwalk Project offices on a hybrid schedule • Continued to assess updates to Federal, State, and local policies and ordinances for the CalSAWS Project's return to office processes
2	Large Meeting Requests	Rancho Cordova and Norwalk Project Offices	Summer 2022	<ul style="list-style-type: none"> • Continued planning facility capacity and equipment needs for requested on-site meetings <ul style="list-style-type: none"> ○ CalWIN ISS Train-the-Trainer sessions scheduled for June 13 – July 15, 2022 ○ CalSAWS Leadership Alignment meeting for July 20, 2022 ○ Imaging UAT sessions scheduled for July 11-15, 2022

- ▶ Facilitated the CalSAWS Weekly Status Meeting that was held on June 29, 2022
- ▶ Completed preparations and participated in the Section Directors Meeting that was held on June 28, 2022
- ▶ Continued CalSAWS Risk Management activities, including:
 - Continued to work with risk and issue owners to develop and update mitigation plans for the accepted CalSAWS DD&I Project risks and issues
 - Continued preparing for the next Risk Management Group (RMG) meeting scheduled for July 6, 2022
- ▶ Continued supporting engagement of project staff working remotely, including:
 - Continued development of the monthly CalSAWS Connect newsletter that will be submitted to the CalSAWS Project Team on July 14, 2022
 - Continued preparations and planning for the next monthly virtual CalSAWS Project All Staff Meeting that is scheduled for July 20, 2022
- ▶ Continued discussions with the Consortium regarding the development of high-level Gantt charts for the CalSAWS Project and continued reviewing potential tools that may be used to create the CalSAWS Integrated Gantt charts
- ▶ Continued performing Contract Management activities for the CalSAWS DD&I Project

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

- Submitted contract Change Notice No. 19 to the Consortium for review on June 30, 2022. Change Notice No. 19 is planned to be submitted to the CalSAWS JPA Board of Directors for approval on July 22, 2022 and may include use of the contract's R&A Change Budget Services allocation for:
 - An extension of CalWIN Functional Support through October 2023
- Continued planning the implementation of requirements from the DHCS and CDSS Privacy and Security Agreements (PSAs) that were approved by the JPA Board of Directors on April 16, 2021
- ▶ Began development of the monthly CalSAWS IT Project Status Report for June 2022 and preparations for the monthly CalSAWS IT Report Meeting with OSI (Office of Systems Integration), CMS (Centers for Medicare and Medicaid Services), and FNS (Food and Nutrition Service) that is scheduled for July 13, 2022
- ▶ Completed preparations to support the logistical planning of the virtual CalSAWS JPA Business Meeting that was held on June 30, 2022
- ▶ Continued performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.2.1-2 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

1.2.2 Communications Management

- ▶ CalSAWS Communications Management activities including
 - Continued to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy
 - Continued oversight and management of Power of 58 materials
- ▶ CalSAWS External Website (www.calsaws.org)
 - Continued the administration and support of the CalSAWS external website
 - See Table 1.2.2-1 for details on website support activities

Table 1.2.2-1 – Website Support Activities

TASK	DATE (S)	TASK TYPE
Uploaded June 2022 Change Control Board Meeting Materials	June 28, 2022	Website Content Update

CalSAWS – California Statewide Automated Welfare System


CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Table 1.2.2-2 – CalSAWS.org Usage Statistics

CATEGORY	DURING REPORTING PERIOD	SINCE LAUNCH
Total Number of Subscribers	33	2,228
Total Number of Unique Users	11,836	1,551,171
Total Number of New Users	9,358	1,551,171
Total Number of Sessions (Individual site visits)	15,971	2,188,658
Average Number of Sessions per User	1.35	1.42
Average Number of Page Views per Session	1.36	1.31
Average Session Duration	0:55	0:56
AskCalSAWS Inquiries – Received/Resolved	6/12	782/769

Figure 1.2.2-1 – Overall CalSAWS.org Usage Trend

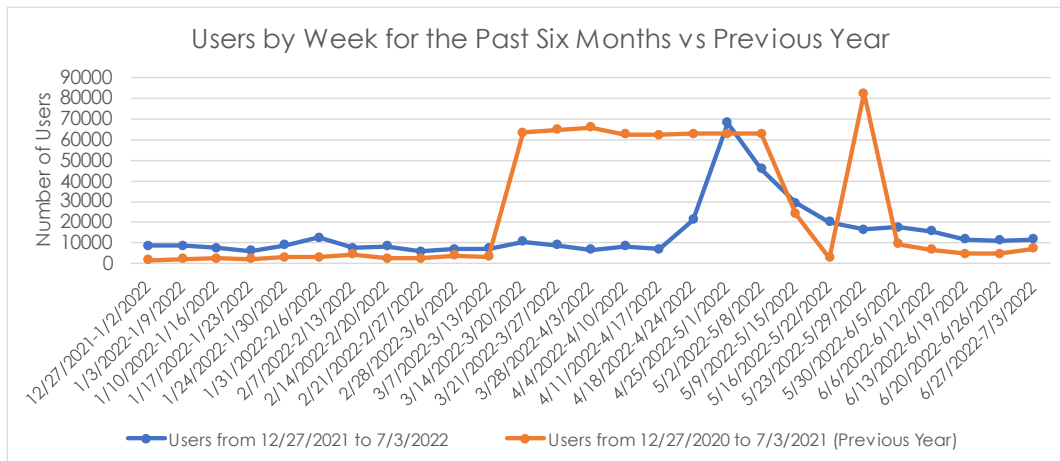

Note:

Increase in usage from the Previous Year (from March 14, 2021 to May 15, 2021) was investigated to be from cities in the United States

Table 1.2.2-3 – CalSAWS.org Subscription Service Statistics

WEBPAGE	PERCENT OF SUBSCRIBERS
Latest News – CalSAWS Buzz Newsletter	32%
Latest News – News	25%
Other Updates – System Updates	22%
Other Updates – Careers	21%
CalSAWS Committees – CalWORKs/CalFresh	21%

1.2.3 Cultural Transformation

- ▶ Re-scheduled next Cultural Ambassador status meeting for July 6, 2022

1.2.4 Inclusion, Diversity and Equity Advancement (IDEA)

- ▶ Co-Create Phase
 - Leadership
 - Continued to prepare for the session that we have with BOLD to plan for the July leadership coaching session
 - Sent out sign-up sheet to all Leads at CalSAWS
 - CalSAWS “We Are One” SharePoint Site
 - Continued to update the “We Are One” website tab
 - Pulse Survey
 - Updated the Organizational Change Management Update #9 Report Appendix with IDEA updates, including the pulse survey analysis
 - CalSAWS Table Talks
 - Discussing possible plans for August table talks session
 - Distributed additional resources to the CalSAWS Project from the May CalSAWS Table Talk speaker who presented on 19 Days in February: Fitz on Purpose, Life, Laughter, and Death
 - Buddy Program
 - Scheduled kick-off meeting for July 1, 2022, 11:00 a.m. – 11:30 a.m. to launch Round 3 of the Buddy Program
 - Continued matching buddy pairs
 - Received feedback from mentors and mentees on Round 2 buddy program
 - Small Team Building
 - Began preparing to promote Small Team Building initiative opportunities to teams at the virtual CalSAWS Project All Staff Meeting scheduled for July 20, 2022
 - Employee Resource Groups (ERGs)
 - Continued preparing output deck for the Juneteenth Celebration from the Employee Resource Group (BERG)
 - Continued discussing plans for a shared ERG session
- ▶ General
 - Continued to partner with the CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
 - Continued to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project
 - Began onboarding new team member

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

1.3 CRFI/CIT Communications Information

- ▶ The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period ending July 3, 2022

Table 1.3-1 – CITs

CIT ID	SUBJECT	CATEGORY	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
None					

- ▶ The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period ending July 3, 2022

Table 1.3-2 – CRFIs

CRFI ID	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	CalSAWS CONTACT
22-040	CalWIN readiness prerequisites for IPT and UAT	May 16, 2022	Closed	July 1, 2022	Melanie Gines, and Llyod Rankine
22-048	Change Network Champion (CNC) Identification for Wave 3 and 4 Counties	June 10, 2022	Open	July 8, 2022	Helen Cruz
22-049	Site Address Validation & Procurements	June 10, 2022	Open	July 1, 2022	Melanie Gines
22-050	Opt-In/Out of FFY Auto -Test Worker Reassignment for SCR CA-48513	June 20, 2022	Open	July 7, 2022	Nina Butler
22-052	CalSAWS Migration - Application Reference List Request	June 28, 2022	Open	July 15, 2022	Melanie Gines, and Lloyd Rankine
22-053	Change Readiness Survey Participant Demographic Data	June 28, 2022	Open	July 11, 2022	Helen Cruz
22-054	San Bernardino – ZScaler Discovery SCR	July 1, 2022	Open	July 15, 2022	Eric Prestwood

- ▶ The following table outlines overdue CalSAWS Requests for Information (CRFIs) for the reporting period ending July 3, 2022

Table 1.3-3 – Overdue CRFIs

CRFI ID	Subject	Region 1	Region 2	Region 3	Region 4	Region 5	Region 6
22-049	Site Address Validation & Procurements	Santa Clara County				Ventura County	

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

1.4 Activities for the Next Reporting Period

1.4.1 Project Management

- ▶ Continue CalSAWS DD&I Facility Management activities, including:
 - Continue key initiatives related to facilities at the Rancho Cordova and Norwalk Project Offices, which are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) above
- ▶ Continue CalSAWS Risk Management activities, including:
 - Continue to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
 - Facilitate the next Risk Management Group (RMG) meeting scheduled for July 6, 2022
- ▶ Facilitate the CalSAWS Weekly Status Meeting scheduled for July 6, 2022
- ▶ Participate in the Section Directors meeting that is scheduled for July 5, 2022
- ▶ Continue activities to support Project staff working remotely
 - Begin preparations and planning for the next monthly virtual CalSAWS Project All Staff Meeting that is scheduled for July 20, 2022
 - Continue developing the next monthly issue of the CalSAWS Connect newsletter that will be distributed to the CalSAWS Project Team on July 14, 2022
 - Continue developing Project communications, as needed
- ▶ Continue to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue process of reviewing tool capabilities for the high-level CalSAWS Integrated Gantt chart
- ▶ Continue performing Contract Management activities for the CalSAWS DD&I Project
- ▶ Finalize the monthly CalSAWS IT Project Status Report for June 2022 and participate in the monthly CalSAWS IT Report Meeting with OSI (Office of Systems Integration), CMS (Centers for Medicare and Medicaid Services), and FNS (Food and Nutrition Service) that is scheduled for July 13, 2022
- ▶ Continue performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.4.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
78	CalSAWS Migration Work Plan Update #39	<ul style="list-style-type: none">• Begin developing the Final Deliverable (FDEL)• Submission of the FDEL is due on July 13, 2022

1.4.2 Communications Management

- ▶ Continue to monitor usage and update materials as requested
 - See table 1.4.2-1 for planned website support activities
- ▶ CalSAWS Communications Management activities including:
 - Continue to gather key communication milestones from the Project teams

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

- ▶ CalSAWS Enhanced Communications Strategy:
 - Continue oversight and management of Power of 58 roll out

Table 1.4.2-1 – Website Support Activities

TASK	DATE(S)	TASK TYPE
None for the reporting period		

1.4.3 Cultural Transformation

- ▶ Continue to develop calendar of events for the ambassador initiatives through the end of the year
- ▶ Continue to provide project management support to Culture Ambassadors as they continue to develop the plans for the initiatives
- ▶ Continue to coordinate working sessions for each Ambassador group to progress their initiatives planning and discuss their individual contributions
- ▶ Continue to develop wellness initiative content to keep the project staff engaged
- ▶ Continue to update resources and a collaboration workspace (Teams Channel) with new relevant materials to support the implementation of the prioritized initiatives
- ▶ Continue to monitor Microsoft Teams channels for any help needed from Ambassadors

1.4.4 Inclusion, Diversity & Equity Advancement (IDEA)

- ▶ Finalize Round 3 matches of the Buddy Program
- ▶ Continue to prepare for the BOLD Culture Leading with Intention Workshop session
- ▶ Continue to partner with CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project

1.5 Deviations from Plan/Adjustments

- ▶ None for the reporting period

2.0 Imaging

2.1 Highlights of the Reporting Period

Table 2.1-1 – CalSAWS Imaging Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> None to note for reporting period

Table 2.1-2 – CalSAWS Imaging Project Milestones

MILESTONES	DUE DATE	STATUS
Migration Activities		In progress
Conduct Santa Barbara County Document Migration Discovery Session Check-in	June 28, 2022	Completed
Conduct San Diego County Document Migration Discovery Session Check-in	June 28, 2022	Completed
Conduct Placer County Document Migration Discovery Session Check-in	June 28, 2022	Completed
Conduct San Francisco County Document Migration Discovery Session Check-in	June 28, 2022	Completed
Conduct Yolo County Document Migration Discovery Session Check-in	June 28, 2022	Completed
Conduct Contra Costa County Document Migration Discovery Session Check-in	June 29, 2022	Completed
Conduct Orange County Document Migration Discovery Session Check-in	June 30, 2022	Completed
Conduct Ventura County Document Migration Discovery Session Check-in	June 23, 2022	Completed
Conduct Santa Barbara County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct Santa Barbara County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct Santa Barbara County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct San Diego County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct Santa Clara County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

MILESTONES	DUE DATE	STATUS
Conduct Placer County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct Santa Cruz County Document Migration Discovery Session Check-in	July 5, 2022	Scheduled
Conduct Contra Costa County Document Migration Discovery Session Check-in	July 6, 2022	Scheduled
Conduct Yolo County Document Migration Discovery Session Check-in	July 7, 2022	Scheduled
Conduct Orange County Document Migration Discovery Session Check-in	July 7, 2022	Scheduled
Conduct Ventura County Document Migration Discovery Session Check-in	July 7, 2022	Scheduled

Table 2.1-3 – CalWIN Counties’ Wave 1 Status Update

Wave 1	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Delta	Final Delta	Go Live
Placer County	Begin	7/29/20	10/1/20	8/6/20	8/31/20	4/1/21	2/17/22	4/15/22 5/27/22	9/22/22	6/29/22	10/22/22	Go Live 10/31/22 75% Progress
	Finish	7/29/20	10/1/20	10/6/20	3/26/21	2/11/22	5/26/22	6/10/22 6/1/22	10/6/22	10/21/22	10/27/22	
	Critical Path	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Begin 9/22/22	Begin 10/20/22	Begin 10/22/22	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	

Status: Gray: Completed; Green: On schedule, performing as planned; Amber: Potential delay/monitor with no material schedule impact; Red: Behind schedule and requires escalation

Green Status: Placer County is currently remediating files that failed to import due to map errors. The first remediation delta was submitted on 6/28/22. Hyland is running validations and results are scheduled to be completed by 07/05/22.

Wave 1	Target Dates	Project Charter Signoff	Mapping SS Completion	Req Document Completion	Document Keyword Mapping Sign Off	Solution/ Sample Build	Sample Testing	Bulk Export	Initial Import	Validate Images in Production	Delta	Final Batch	Go Live
Yolo County	Begin	12/3/22	1/6/22	1/24/22	1/6/22	2/1/22	3/21/22	4/11/22	5/14/22	9/22/22	10/11/22	10/28/22	Go Live 10/31/22 70% Progress
	Finish	12/7/22	1/20/22	1/31/22	1/31/22	3/17/22	4/8/22	5/12/22	5/16/22	10/6/22	10/21/22	10/29/22	
	Critical Path	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Begin 9/22/22	Begin 10/20/22	Begin 10/22/22	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	

Status: Gray: Completed; Green: On schedule, performing as planned; Amber: Potential delay/monitor with no material schedule impact; Red: Behind schedule and requires escalation

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Table 2.1-4 – CalWIN Counties’ Wave 2 Status Update

Wave 2	Target Dates	Project Charter Signoff	Mapping Completion	Document/ Keyword Mapping Sign Off	Sample Testing	Complete Change Order	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Batch	Go Live
Contra Costa County	Begin	11/5/21	12/21/21	12/22/21	2/22/22	2/8/22	4/4/22	6/6/22	1/30/23	1/6/23	2/1/23	Go Live 2/27/23 50% Progress
	Finish	11/11/21	1/5/22	12/31/21	3/18/22	4/1/22 4/15/22	5/21/22 6/3/22	7/8/22	02/03/23	1/23/23	2/23/23	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Green Status: Completed import for Contra Costa County. However, there is a small subset of images, 600,000, being corrected and plan to be re-imported by July 8, 2022

Wave 2	Target Dates	Conv Environment Setup	Vendor Kick Off	Document & Keyword Mapping	Document Mapping & Req Doc Signoff	Solution Sample Build	Sample Testing	Bulk Export	Bulk Import	Imaging UAT Refresh	Validate Images in Prod	Suppl Delta 1	Suppl Delta 2	Go-Live
Santa Clara	Start	01/17/22	5/11/22	05/11/22	6/21/22	7/5/22	08/08/22	09/12/22	11/07/22	05/23/22	01/19/23	01/30/23	02/23/23	Go Live 02/27/23
	Finish	04/29/22	5/11/22	06/17/22	6/28/22	8/1/22	09/09/22	11/04/22	11/30/22	06/03/22	02/02/23	02/23/23	02/26/23	20% Progress
	Status	Completed	Completed	Completed	Completed	Awaiting	Awaiting	Awaiting	Awaiting	Completed	Awaiting	Awaiting	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Wave 2	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Delta	Final Delta	Go Live
Tulare County	Begin	10/5/20	12/1/20	11/30/20	12/2/20	8/2/21	2/15/22	7/23/22	1/19/23	6/16/22	2/1/23	Go Live 2/27/23
	Finish	10/5/20	12/1/20	1/31/21	7/29/21	12/30/21	4/4/22	8/27/22	2/2/23	1/31/23	2/23/23	70% Progress
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	In progress	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Table 2.1-5 – CalWIN Counties’ Wave 3 Status Update

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Delta	Final Delta	Go Live
Orange County	Begin	1/7/21	3/1/21	3/1/21	2/2/21	4/30/21	4/1/22 4/8/22	8/5/22	3/24/23	9/1/22	4/1/23	Go Live 4/24/23
	Finish	1/7/21	3/1/21	4/30/21	4/22/21	12/30/21	8/1/22	1/31/23	4/6/23	3/31/23	4/20/23	60% Progress
	Status	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Delta	Final Delta	Go Live
Santa Barbara County	Begin	1/19/21	3/1/21	3/1/21	2/18/21	1/15/22	8/1/22	11/01/22	3/24/23	11/1/22	4/1/23	Go Live 4/24/23
	Finish	1/19/21	3/1/21	9/31/21	09/31/21	7/31/22	10/31/22	12/30/22	4/6/23	3/31/23	4/20/23	30% Progress
	Status	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Delta	Final Delta	Go Live
Ventura County	Begin	1/19/21	3/1/21	3/1/21	2/18/21	6/30/21	4/4/22	9/2/22	3/24/23	9/3/22	4/1/23	Go Live 4/24/23 35% Progress
	Finish	1/19/21	3/1/21	4/30/21	5/31/21	3/31/22	8/31/22	10/21/22	4/6/23	3/31/23	4/20/23	
	Status	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray:** Completed; **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

2.2 Activities for the Next Reporting Period

- ▶ Continue to manage the milestones for the Image Migrations in the tables above
- ▶ Continue to prepare for the User Acceptance Testing (UAT) Imaging Administration session scheduled to begin on July 11, 2022

2.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

3.0 Customer Service Center (CSC)

3.1 Highlights of the Reporting Period

Table 3.1-1 – CalSAWS Customer Service Center Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> Continued discussions with Los Angeles County, Wave 1, Wave 2, Wave 3, and Wave 4 CalWIN Counties about migration to CalSAWS Contact Center Solution
N/A	<ul style="list-style-type: none"> Continued Build of Administration Page (CA-226672), Post-Call Survey (CA-228023), and Scheduled Callback (CA-229573)

- ▶ Continued discussions with Los Angeles County, Wave 1, Wave 2, Wave 3, and Wave 4 CalWIN Counties about migration to CalSAWS Contact Center Solution
- ▶ Began scheduling meetings with Wave 5 CalWIN Counties about migration to the CalSAWS Customer Service Center Solution
- ▶ Continued Build of Administration Page (CA-226672), Post-Call Survey (CA-228023), and Scheduled Callback (CA-229573)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Table 3.1-2 – Customer Service Center Enhancement Milestones

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2292, 2697, 2698, 2723, 2724 WFM/QA/QM Reporting (CA-226209)	December 3, 2021	In Production	22.01
DDID 2718 Task for Cancelling an Appointment in Outbound IVR (CA-25604)	January 24, 2022	System Test	22.05 22.07.XX
DDID 2219, 2716, 2717, 2728 Outbound IVR - (CA-226207)	February 4, 2022	System Test	22.05 22.07.XX
DDID 2700 Enhanced CCP (CA-226844)	March 18, 2022	In Production	22.03 22.05.06
DDID 2727 Work-from-home Modifications (CA- 227064)	March 18, 2022	In Production	22.03 22.05.06
DDID 2216, 2725 External Party Access IVR (CA-226839)	March 25, 2022	In Production	22.05
DDID 2211, 2217, 2218, 2220, 2729, 2730, 2731, 2046, 2732 Telephonic Signature (CA-226838)	April 1, 2022	In Production	22.05
DDID 2687, 2688, 2689, 2690, 2691, 2692, 2693, 2694, 2695, 2696, 2222, 2702, 2721, 2169, 2284, 2722 Admin Page (CA-226672)	July 8, 2022	In Development	22.05 22.07.XX
DDID 2701, 2706 Voice Authentication Languages (CA-226843)	July 29, 2022	In Development	22.07 22.08.XX
DDID 2699, 2210, 2705, 2707, 2708, 2709, 2710, 2711, 2712, 2713, 2714, 2715, 2719, 2720, 2258 Inbound IVR (CA-226837)	July 8, 2022	In Development	22.05 22.07.XX
DDID 2704 Post-Call Survey (CA-228023)	July 8, 2022	Approved	22.05 22.07.XX
DDID 2284 Scheduled Callback (CA-229573)	July 8, 2022	Approved	22.05 22.07.XX
DDID 2268 Display the CalSAWS Contact Center IVR Caller ID for outbound calls	August 5, 2022	Design in progress	22.07 22.08.XX

Table 3.1-3 – Los Angeles County Milestones

MILESTONES		DUE DATE	OWNER
1	Design completion	March 11, 2022	CalSAWS Project Team
2	Initial performance/load testing	March 18, 2022	CalSAWS Project Team
3	Training development	May 16, 2022	CalSAWS Project Team
4	Build and unit test	May 20, 2022	CalSAWS Project Team
5	Training content review	May 20, 2022	Consortium
6	System Test	July 15, 2022	CalSAWS Project Team
7	Training execution	June 29, 2022	CalSAWS Project Team
8	Conduct model office	July 21, 2022	Los Angeles County
9	Go-live	August 26, 2022	CalSAWS Project Team
10	Post go-live support	August 29, 2022	CalSAWS Project Team

3.2 Activities for the Next Reporting Period

- ▶ Continue discussions with Contra Costa, Los Angeles, Santa Clara, Tulare, Orange, Santa Barbara, Ventura, Santa Cruz, Solano, San Mateo, and San Diego Counties for County-specific Interactive Voice Response (IVR) designs
- ▶ Continue build of System Change Requests (SCRs) CA-226672 Administrative Page, Post-Call Survey (CA-228023), and Scheduled Callback (CA-229573)
- ▶ Continue build of Los Angeles County Amazon Web Services (AWS) Accounts and Contact Center Infrastructure (CA-240156)

3.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

4.0 Application Development and Test

4.1 Highlights of the Reporting Period

Table 4.1-1 – CalSAWS Application Development and Test Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
4.1.2 Design Difference Identifiers (DDID) System Test Status	<ul style="list-style-type: none"> • 22.07 DD&I System Testing on schedule. Week 5 of 8 completed. 85% pass rate on a 63% target

4.1.1 Application Development Summary

Table 4.1.1-1 – CalSAWS Application Development Summary

	Status	22.07	22.09	22.11	23.01	23.02	23.05
Design	New	1	1	2	10	1	7
	Design in Progress	0	7	1	0	0	1
	Ready for Committee	0	1	0	0	0	0
	Committee Review	0	0	0	0	0	0
	Pending Approval	0	0	1	1	0	1
Build	Approved	0	2	1	1	1	2
	In Development	0	8	0	1	0	0
	Development Complete	0	1	0	0	0	0
	In Assembly Test	1	1	0	0	0	0
Test	System Test	7	3	0	0	0	0
	Test Complete	2	0	0	0	0	0
	In Production	0	0	0	0	0	0
	Grand Total	11	24	5	13	2	11


System Change Requests (SCRs) in Production	903
---	-----

Notes:

- This table includes Application Development System Change Requests (SCRs) with migration impact. SCRs in production represents a count of any SCR that have a project phase of migration and have been deployed to production. The "in Production" count is lower since we did a reconciliation and removed 17 that were implemented in C-IV prior to C-IV cutover
- Continued drafting designs and development activities. Status is provided in Table 4.1.1-1 (CalSAWS Application Development Summary), above

4.1.2 Design Difference Identifiers (DDID) System Test Status

Figure 4.1.2-1 – DDID System Test Status

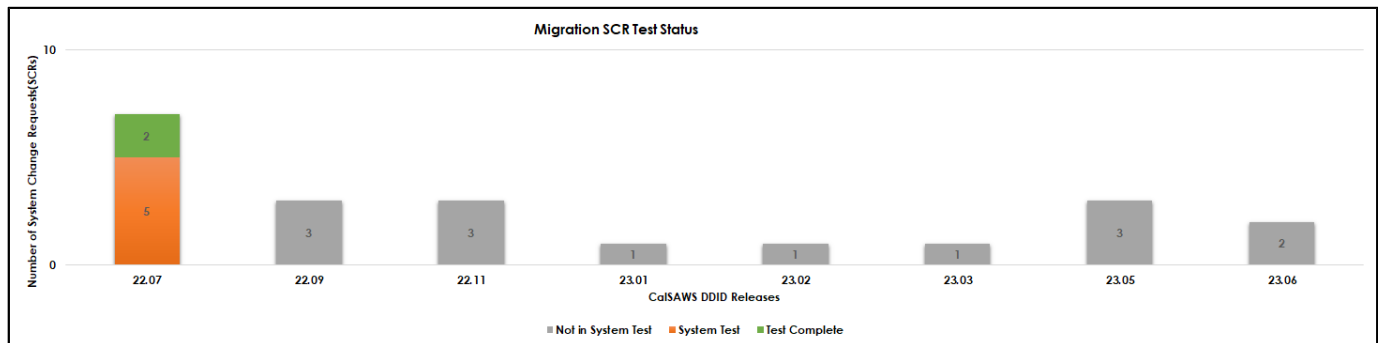

Notes:

- Includes all System Change Requests (SCRs) that have a funding source of CalSAWS DD&I that are not in "Rejected" or "Pending Rejection" status and are targeted for a baseline release. This includes SCRs associated to DDID 1967 for the unforeseen allowance and DDID 1631 for the reports allowance. In Production includes "In Production" status; Test Complete includes "Test Completed" status; System Test includes "System Test" status; Not in System Test includes all SCR statuses prior to System Test delivery
- Counts are higher in this chart (as compared with Design and Build Status) due to the inclusion of all CalSAWS DD&I System

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase


Weekly Status Report Period: June 27, 2022 to July 3, 2022

Change Requests (SCRs) targeted for the release, such as DD&I Training and Technical System Change Requests (SCRs)

Table 4.1.2-1 – DDID System Test Execution Status – 22.07

Pass rate target as of July 01, 2022	63%
Pass rate actual as of July 01, 2022	85%
System Test Completed date: July 20, 2022	

Figure 4.1.2-2 – DDID System Test Execution Status – 22.07

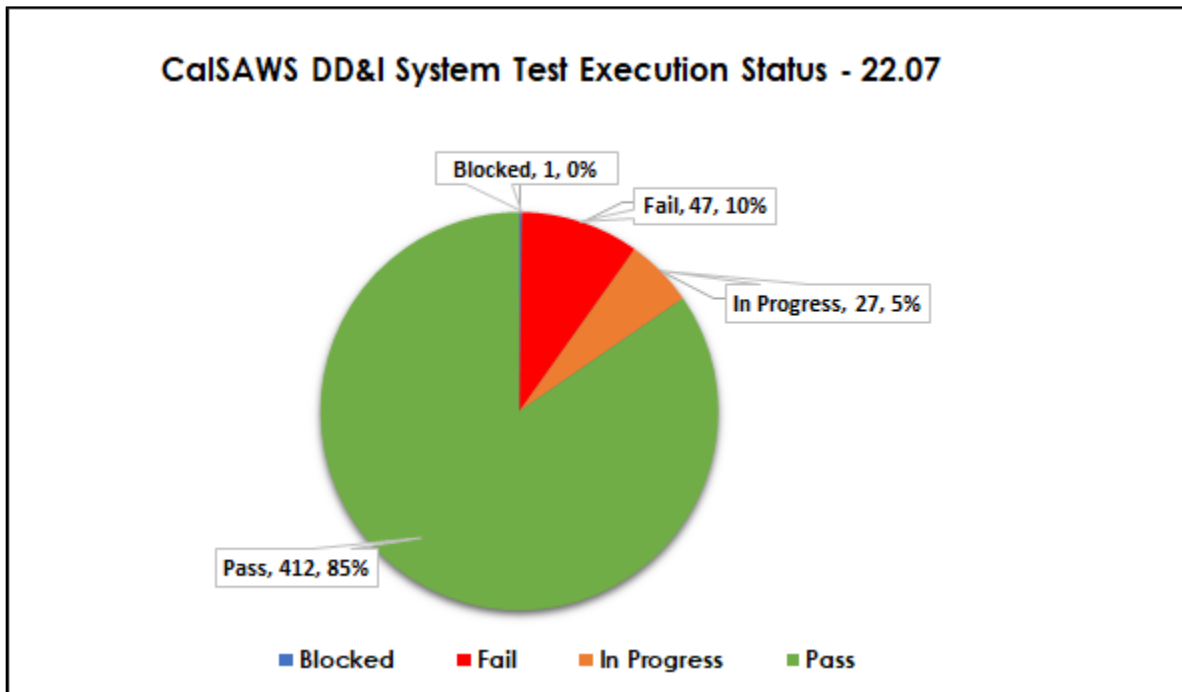

Note:

- Test Script counts are subject to change as test scripts are added or removed throughout the execution phase. Includes testing execution for all CalSAWS DD&I Test Scripts in the release

► Continued Test Execution for 22.07

Figure 4.1.2-3 – Overall GA/GR CalSAWS and Client Correspondence System Test Execution Status – 22.07



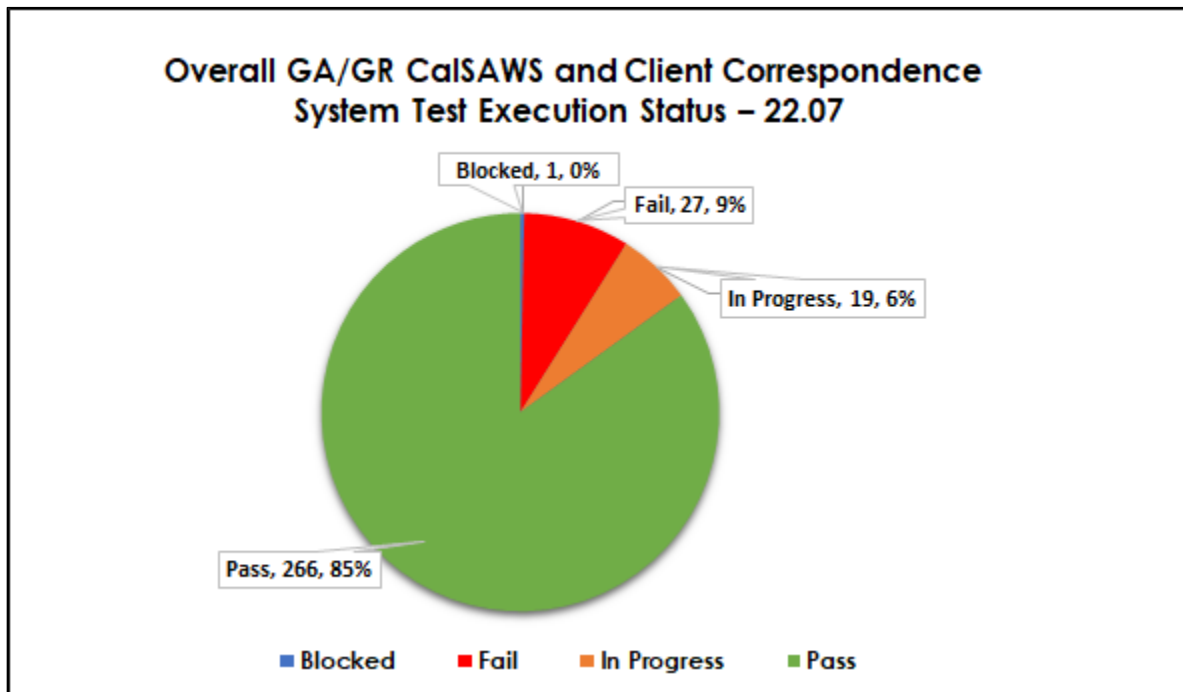


Table 4.1.2-2 - GA/GR System Test Execution Status by Area – 22.07

GA/GR CalSAWS	
Pass rate target as of July 01, 2022	63%
Pass rate actual as of July 01, 2022	81%
System Test completed date: July 20, 2022	

GA/GR Client Correspondence	
Pass rate target as of July 01, 2022	88%
Pass rate actual as of July 01, 2022	95%
System Test completed date: July 20, 2022	

Figure 4.1.2-4 – GA/GR System Test Execution Status by Area – 22.07

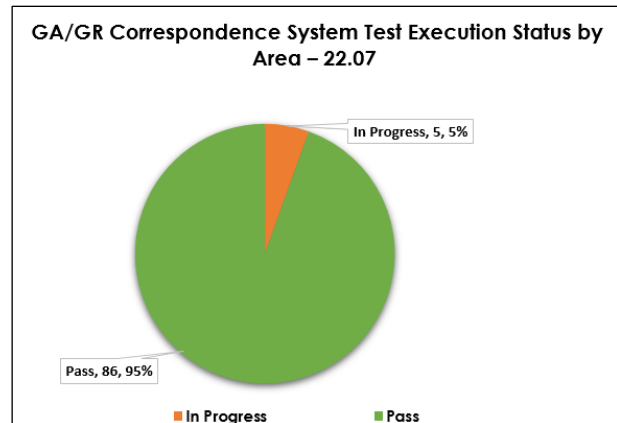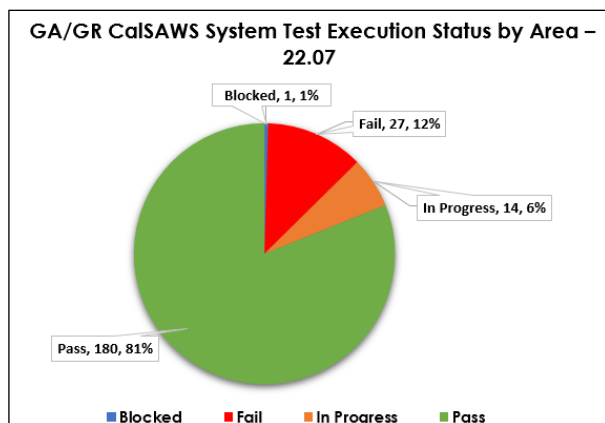

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

4.1.3 State and CalWIN Wave 1 County Interface Partner File Exchange Test (IPT)

Table 4.1.3-1 – Consortium Partners

INTERFACE TESTING		
CONSORTIUM PARTNER	STATUS	TARGET COMPLETION DATE
Electronic Inter County Transfer (EICT) - CalWIN	0/3	August 31, 2022
Online CalWORKS Appraisal Tool (OCAT)	2/2	June 28, 2022

Note:

- None as of July 1, 2022

Table 4.1.3-2 – State Partners

INTERFACE TESTING		
STATE PARTNER	STATUS	TARGET COMPLETION DATE
California Healthcare Eligibility, Enrollment, and Retention System (CalHEERS)	1/5	August 31, 2022
California Child Support Automation System (CCSAS) - DCSS	0/2	August 31, 2022
California Department of Social Services (CDSS) - DSS	1/2	August 31, 2022
Case Management Information and Payrolling System (CMIPS) - OSI	0/2	August 31, 2022
County Medical Services Program (CMSP)	1/1	June 30, 2022
Electronic Benefits Transfer (EBT) - FIS	0/2	August 31, 2022
Medi-Cal Eligibility Data System (MEDS) - DHCS	0/2	August 31, 2022
Welfare Data Tracking Implementation Project (WDTIP) - OSI	0/2	August 31, 2022
Welfare Intercept System (WIS) - DSS	1/2	August 31, 2022

Notes:

- CCSAS (DCSS):
 - Update: On June 30, 2022, CCSAS notified the project that their environment will be available to process records mid-July

Table 4.1.3-3 – CalWIN Wave 1 Counties

INTERFACE TESTING		
CalWIN Wave 1 COUNTY PARTNER	STATUS	TARGET COMPLETION DATE
Placer County	0/6	August 31, 2022
Yolo County	0/6	August 31, 2022

Notes:

- Placer County
 - Number of interfaces reduced to six with updated information from Placer regarding the opt-out of the Warrant Print Writer and School Lunch interfaces

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase


Weekly Status Report Period: June 27, 2022 to July 3, 2022

- End-to-end IPT pending county firewall configuration to be completed and ready by July 27, 2022. Refer to Risk 275. Interim testing will entail manual posting of interface files to secure web portal location
- Yolo County
 - Completed Blank File Exchange Test for Paid Warrant Reader and Direct Deposit Reader. Functional test file in progress. Destination for FTP confirmed with Yolo County and configuration in-progress

4.1.4 Task Management

- ▶ There are no Design Difference Identifiers (DDID) System Change Requests (SCRs) in the design/build phase


Figure 4.1.4-1 – Task Management Design Difference Identifiers (DDID) Status

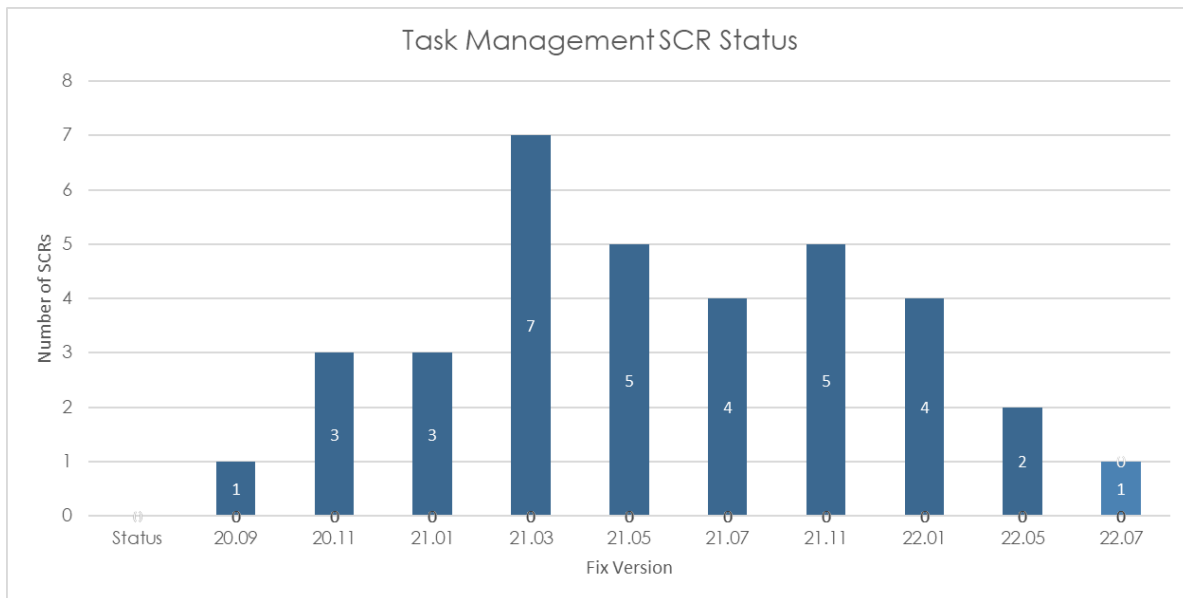

4.1.5 Application Programming Interface (API)

- ▶ There are no Design Difference Identifiers (DDID) System Change Requests (SCRs) in the design/build phase
- ▶ Completed MDM API test and scheduled for an upcoming priority release the week of July 5, 2022

Figure 4.1.5-1 – Application Programming Interface (API) DDID Status

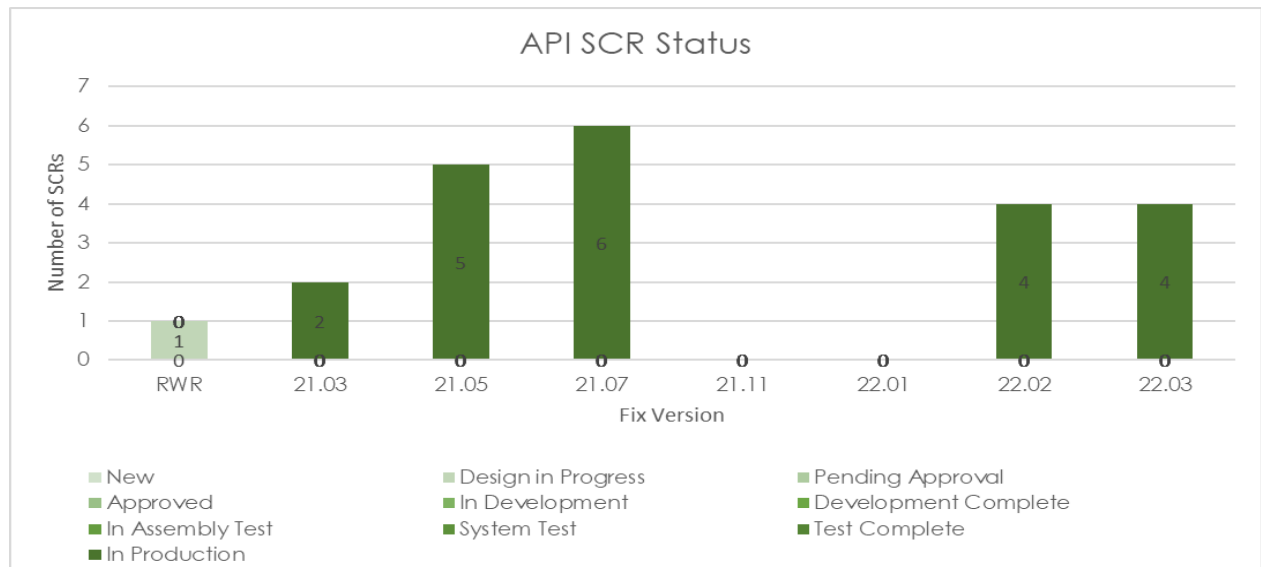


4.1.6 General Assistance/General Relief (GA/GR)

► General:

- Provided the weekly status update and General Assistance/General Relief (GA/GR) release plan changes to Consortium on June 30, 2022
- Discussed the General Assistance/General Relief (GA/GR) Correspondence web service design and web service clarifications on June 27, 2022, and June 29, 2022
- Discussed GA/GR CC Administrative process on June 30, 2022
- Discussed Gainwell System Test status on June 29, 2022
- Below GA/GR System Change Requests (SCRs) are in design
 - CA-242939: GA GR M&O Process for Correspondence Administration (documentation Only) (22.09)
 - CA-245148: GA GR Training Documentation (documentation Only) (22.09)
- Continued with Development for the below SCRs
 - CA-220016 GA GR Automated Solution Admin Changes - Wave 1 and Tier 3 Manual Correspondences
 - CA-240916 GA/GR Automated Solution - Imaging Updates
 - CA-244842 Set GA/GR Aid Code for CalFresh program on PACF cases (for GA/GR Automated solution)
- Continued with System Test support for the below 22.07 System Change Requests (SCRs)
 - CA-244108: GR Time on aid page changes
 - CA-245506: CA-226398 Batch Sync Recommendations
 - CA-245253: Implement Additional Miscellaneous Parameters for EDBC-triggered Reason Codes

Figure 4.1.6-1 – GA/GR Design Difference Identifiers (DDID) Status

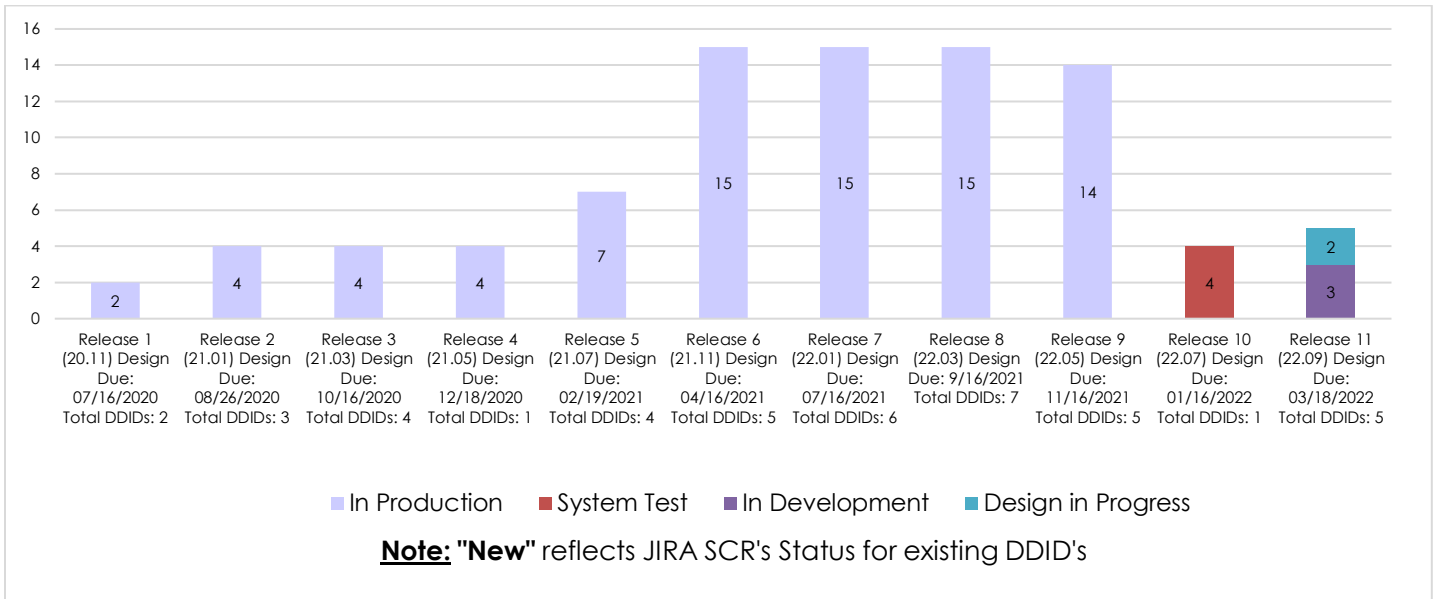

4.1.7 CalWIN Wave 1 Batch Performance

- ▶ The CalWIN Wave 1 Batch Performance effort (CA-217183) began on June 6, 2022
 - Golden Data Set (GDS) 7 loaded into the Batch Performance database
 - Automated test team ran scripts to create data for counties in the environment
 - Executed 43* County Batch
- ▶ The third execution of the "End of Month" batch cycle showed great performance of all main processes. The Analytics/Reports jobs were all completed before the 10-hour window for batch. The entire batch cycle competed in 9 hours, 24 minutes

*The Wave 1 Conversion will only include 42 Counties. However, GDS 7 still included Contra Costa County, so the first few performance tests will continue to include all 43 counties for testing purposes

Table 4.1.7-1- CalWIN Wave 1 Batch Performance Schedule and Results

Performance Cycle	Start Date	End Date	Run Time	Performance Defects
End of Month	June 6, 2022	June 19, 2022	(Run 1) 11 hours, 26 minutes	
			(Run 2) 10 hours, 39 minutes	
			(Run 3) 9 hours, 24 minutes	
First day of the Month	June 20, 2022	July 3, 2022	(Run 1) 10 hours, 3 minutes	
Main Payroll	July 5, 2022	July 17, 2022	(Run1) July 5, 2022 planned execution	
High volume forms process	July 18, 2022	July 31, 2022	TBD	
Interface Outbound files	July 18, 2022	July 31, 2022	TBD	
10-day cutoff	August 1, 2022	August 14, 2022	TBD	
Interface Inbound files	August 15, 2022	August 28, 2022	TBD	

4.1.8 Case Purge

In July 2020, a team was formed to design, build, test, and deploy a Case Purge solution for C-IV and CalSAWS. This Purge functionality is based on the records retention policy approved by the CalSAWS Project Steering Committee in September 2019. The Purge team is using the Agile methodology for this effort and is deploying functionality to Production at the conclusion of each Sprint. This team is operating independently of the existing Design, Application Development, Training, and Test teams

- ▶ Continued Design and Development for Sprint 9 features that will be included in the 22.07 baseline System Change Requests (SCRs). This release includes the following items and will be deployed to production with the 22.07 release on July 25, 2022:
 - Sprint 9 SCR CA-235667
 - Create Image Removal process for images associated with cases identified for Data Removal
 - Create Document Removal process for the CalSAWS Disaster Service Repository
 - Update Imaging Server with new deletion Image function to allow for the removal of an image record given a document identification
 - Update the Imaging Client Service Application Programming Interface (API) to allow for the new deletion Image function
 - Update API gateway with new URL to allow for the new deletion Image transaction

Figure 4.1.8-1 – Case Purge Burndown Chart



Table 4.1.8-1 – Planned Purge Sprints

SPRINT NUMBER	SPRINT DESCRIPTION
Sprint 1	Porting Case Summary page updates, Case Data Removal page updates
Sprint 2	Add Case Locking, Image View only
Sprint 3	Porting the Identification sweep logic, adding new Eligibility Determination Benefit Calculation/Recovery Account (EDBC/RA) Rules to Identification Sweeps, Porting Portable Document Format (PDF) Generation Process, Increasing Journal Portable Document Format (PDF) Character Limit
Sprint 4	Porting Case Deletion Logging process, adding new CalHEERS tables to Deletion Model, Remove Recovery Account Responsible Party tables from Deletion Model
Sprint 5	Porting Case Identification and Override Reports, Port Document Removal process to S3, Create Stored Procedure Database Change Requests (DBCRs), Schedule Batch for Journal Portable Document Format (PDF) Re-run
Sprint 6	Creating CalSAWS Re-Verification Batch, Updating Identification and Re-Verification logic to include new Recovery Account rules, Updating Document S3 storage service framework, Updating Identification Batch to exclude CS program
Sprint 7	Porting Time Limit Aid Summary page changes, Porting Case Completion Report, Updating Deletion Model to include Residential and Receipt tables, Updating CalSAWS page to validate and block CalHEERS referrals, Combining Document and Imaging removal process with Data Removal Batch, Updating Benefits Cal page to validate for removed cases during linkage
Sprint 8	OBIEE Cleanup for Delete Track, Updating Batch to Verify Lawful Presence (VLP)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

SPRINT NUMBER	SPRINT DESCRIPTION
Sprint 9	Image Deletion, Porting for Disaster Recovery Document Deletion
Sprint 10	Performance Environment Preparation and Execution
Sprint 11	Batch Scheduling, Case Purge Transition

4.1.9 Deliverable Management

Table 4.1.9-1 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

4.2 Activities for the Next Reporting Period

- ▶ Continue drafting designs for Migration Impact System Change Requests (SCRs)
- ▶ Continue test execution for CalSAWS 22.07 Release

Deliverable Management

Table 4.2-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

4.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

5.0 Conversion

5.1 Highlights of the Reporting Period

Table 5.1-1 – CalSAWS Conversion Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
5.1.1 CalWIN Conversion	<ul style="list-style-type: none"> • Evaluating Mock Cutover action items and results until July 1, 2022 • Supporting County Data Validation (CDV) until July 1, 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

5.1.1 CalWIN Conversion

- ▶ Continued to address open and unresolved Converted Data testing identified defects
- ▶ Continued Converted Data Validation (CDV) support activities
- ▶ Continued Golden Data Set (GDS) 9 Epic development and testing. This Epic is focused on:
 - 22.05 and 22.07 production data structure and code value changes which impact Conversion Transformation logic
 - Identified and unresolved Converted Data Test (CDT) defects
 - General Assistance/General Relief (GA/GR) data structure and code value enhancements where Conversion Transformation logic also need be enhanced to convert GA/GR
 - Planned to be delivered on August 31, 2022

Table 5.1.1-1 – CalWIN Conversion Statistics Golden Data Set (GDS) 9 (June 2022 – July 2022)


GDS#9												
Sprint	Total - Deferred Items	Sprint Duration		Item Status								
				0%	25%	30%	50%	75%	5%	100%	100%	0%
				Not Started	Analysis & Mapping in Progress	Ready for Consortium Review	Build In Progress	Ready for AT	On Hold	Completed [Tested]*	CNR	Deferred
Overall	153	6/6/2022	7/29/2022	60	25	0	7	15	0	53	0	0
GDS#9 Bugfix 1	56	6/6/2022	7/11/2022	0	10	0	5	12	0	29	0	0
GA/GR	63	6/6/2022	7/11/2022	35	5	0	0	0	0	23	0	0
GDS#9 Bugfix 2	TBD	7/5/2022	7/22/2022	0	4	0	0	2	0	1	0	0
22.5/22.07	34	7/5/2022	7/22/2022	25	6	0	2	1	0	0	0	0
Hardening	tbd	7/25/2022	7/29/2022	0	0	0	0	0	0	0	0	0

5.1.2 CalWIN Conversion Defects Converted Data Test Defect

Table 5.1.2-1 – Open Converted Data Test (CDT) Defects

Defect Delivery by Golden Data Set (GDS)	Priority 1	Priority 2	Priority 3/Priority 4	Total
GDS#9	0	66	7	73
Wave 1 Go-Live	TBD	TBD	TBD	TBD
GDS#10	0	0	76	76
GDS#11	0	0	19	19
Not Assigned	0	1	0	1
CDT Open Total	0	67	102	169

Figure 5.1.2-1– Open Converted Data Test (CDT) Defects by GDS

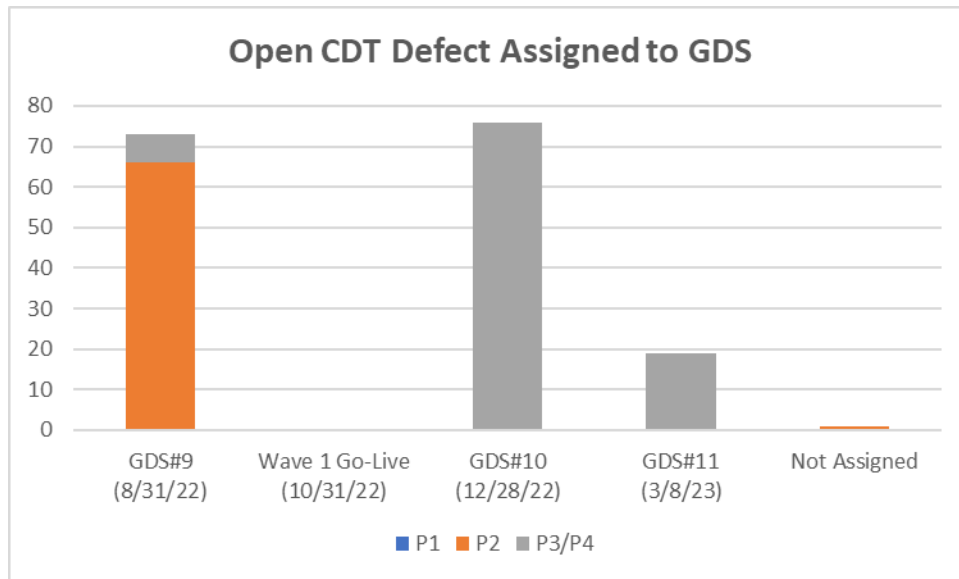

5.1.3 Gainwell Technologies

- ▶ CalWIN Document Migration
 - Continued planning for delivery of all Client Correspondence (CC)
 - Continued delivery of Client Correspondence (CC) from CalWIN

5.1.4 Ancillary Systems Conversion

- ▶ Continued to address issues found in production dataset size files. These files are necessary for CalWIN Core Conversion orchestration and integrations
- ▶ Facilitated exception reports review sessions with the Ancillary Counties to address questions and concerns
- ▶ Completed Wave 1 Mock Cutover Exception Reports Contra Costa, Placer, and Yolo Counties and confirmed they have been received

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

Figure 5.1.4-1– Ancillary Systems Conversion Gantt Chart

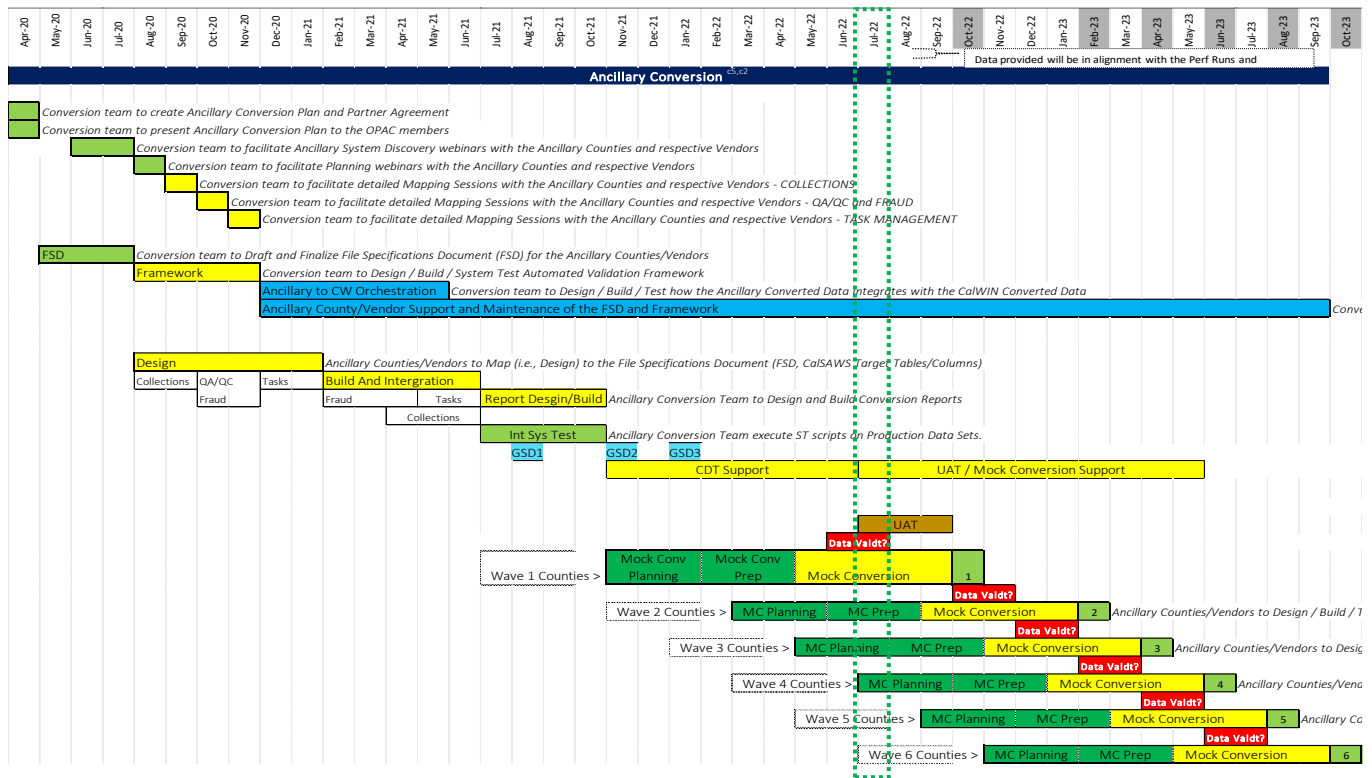


Table 5.1.4-2 – Ancillary Systems Conversion Milestones

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
July 2020	Project Kick-Off/Discovery Sessions	Team introductions and Project overview	Completed
August 2020	File Specification Document (FSD)	CalSAWS DB (structures) as Conversion Target	Completed
August 2020	Project Planning	Detailed walkthrough of the Project schedule and File Specification Document (FSD)	Completed
December 2020	Automation Framework Completed	Exception handling for Ancillary provided Data is ready for the Counties	Completed
February 2021	Design/Mapping	All CalSAWS DB Targets (defined in FSD) have Source Mappings from Ancillary	Completed
July 2021	Build	Development activities, dependent Design Mapping, are ready to Start (or are Completed)	Completed
January 2022	System Test	System Test execution, dependent on test scripts and Build Completed, are ready to Start (or are Completed)	Completed

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
June 2022	Integration Test	End-to-End Test execution, dependent on test scripts, System Test Completed and CDT completed, are ready to Start (or are Completed)	Completed
August 2023	Mock Conversion Ancillary System Data Delivered	Counties to delivery Ancillary System Data to the CalSAWS Conversion team as a Prerequisite to begin Mock Conversions	In progress
August 2023	Wave 1 – 6 Mock Conversions	Simulated Cutover Activities, dependent on Integration Test Completed, are ready to Start (or are Completed)	In progress
August 2023	Wave 1 – 6 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to Start (or are Completed)	In progress
October 2023	Wave 1 – 6 Conversion Cutovers	Execution of (live) Cutover Activities are ready to Start (or are Completed)	Not started

5.1.5 Deliverable Management

Table 5.1.5-1 – Conversion Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

5.2 Activities for the Next Reporting Period

5.2.1 CalWIN Conversion

- ▶ Continue to complete Jira epics and issue aligned with Golden Data Set (GDS) delivery schedule
- ▶ Continue development for the delivery of Golden Data Set (GDS) 9 Epic
- ▶ Continue activities for Mock Cutover

5.2.2 Gainwell Technologies

- ▶ CalWIN Data Migration
 - Continue planning for future CalWIN extractions
- ▶ CalWIN Data Retention M&O
 - Continue planning for future data retention runs

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

5.2.3 Ancillary Systems Conversion

- ▶ Continue ongoing support for mapping and data extract activities on Ancillary Collections, Fraud, and Task Management
- ▶ Continue to update the Ancillary Systems file specifications documents (as needed)
- ▶ Continue System Test scenario for automation development
- ▶ Review results for Wave 1 County Mock Cutover from June 11, 2022

5.2.4 Deliverable Management

Table 5.2.4-1 – Conversion Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

5.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

6.0 CalWIN Functional Support

6.1 Highlights of the Reporting Period

Table 6.1-1 – CalSAWS CalWIN Functional Support Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	• None for the reporting period

- ▶ Supported Wave 1 CalWIN County Configuration and Process Simulation by collaborating with the Implementation Support Services (ISS) team on June 27-30, 2022:
 - Placer County Configuration Development sessions on June 27-30, 2022
 - Placer County Configuration Meetings – Debrief and plan on June 27-30, 2022
 - Wave 1 Configuration – Next Steps on July 1, 2022
- ▶ Supported CalSAWS 3x Weekly Leadership Meetings on June 27, June 29, and July 1, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Supported Implementation Support Services (ISS) Team Leads Meetings on June 28, 2022 and June 30, 2022 to collaborate effectively
- ▶ Supported Post Deployment Support Model Working Session meetings on June 27 and June 29 to provide input to necessary post deployment support for CalWIN Counties
- ▶ Supported Sacramento County To-Be Business Process Reengineering (BPR) Sessions on June 27-July 1, 2022, upcoming sessions include:
 - Case Maintenance
 - General Assistance (GA)
 - Periodic Reporting (PR) / Re-Evaluation (RE)
 - Fiscal Processes and Benefits Recovery
 - Fiscal (continued)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

- ▶ Supported San Luis Obispo County To-Be Business Process Reengineering (BPR) Sessions on June 27-July 1, 2022, upcoming sessions include:
 - Case Maintenance
 - Case Maintenance (Continued) x2
 - Re-Evaluation (RE)
 - Fiscal
 - Fiscal and Benefits Recovery
 - CWS
 - CWS (Continued)
- ▶ Supported Sacramento and San Luis Obispo Counties (SLO) To-Be BPR – Tuesday/Wednesday/Thursday de-brief on June 28-30, 2022, to debrief the sessions that have occurred throughout the week to make any necessary changes to plan or support feedback
- ▶ Supported Process Simulation. Next steps on June 27, 2022 to coordinate data staging preparation and functional support coverage for process simulation

6.2 Activities for the Next Reporting Period

- ▶ Prepare for CalSAWS 3x Weekly Leadership Meetings on July 6 and July 8, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Prepare for Implementation Support Services (ISS) Team Leads Meetings on July 5, 2022 and July 7, 2022 to collaborate effectively
- ▶ Prepare for Post Deployment Support Model Working Session meetings on July 7, 2022 to provide input to necessary post deployment support for CalWIN Counties
- ▶ Prepare for Sacramento County To-Be Business Process Reengineering (BPR) Sessions on July 5-8, 2022, upcoming sessions include:
 - Children and Family Services
 - Veteran Services
 - Quality Control (QC)
 - Long Term Care
- ▶ Prepare for San Luis Obispo County To-Be Business Process Reengineering (BPR) Sessions on July 5-8, 2022, upcoming sessions include:
 - Help Desk, Appeals and Hearings
 - IEVS and Fraud
 - Quality Assurance (QA)
- ▶ Prepare for Sacramento and San Luis Obispo Counties (SLO) To-Be BPR – Tuesday/Wednesday/Thursday de-brief on July 5-8, 2022, to debrief the sessions that have occurred throughout the week to make any necessary changes to plan or support feedback
- ▶ Prepare for Santa Barbara County Process Change Inventory (PCI) Closeout Sessions on July 5-8, 2022, upcoming sessions include:
 - Application Registration, CBO, Case Maintenance
 - Employment Services and Child Care
- ▶ Prepare for Process Simulation during July 5-8, 2022 meet data requirements and functional support coverage for process simulation

6.3 Deviations from Plan/Adjustments

► None for the reporting period

7.0 Technical Infrastructure

7.1 Highlights of the Reporting Period

Table 7.1-1 – CalSAWS Technical Infrastructure Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
	<ul style="list-style-type: none"> None for the reporting period

Figure 7.1-1 – Wave 1 County Network Connectivity Readiness Burndown


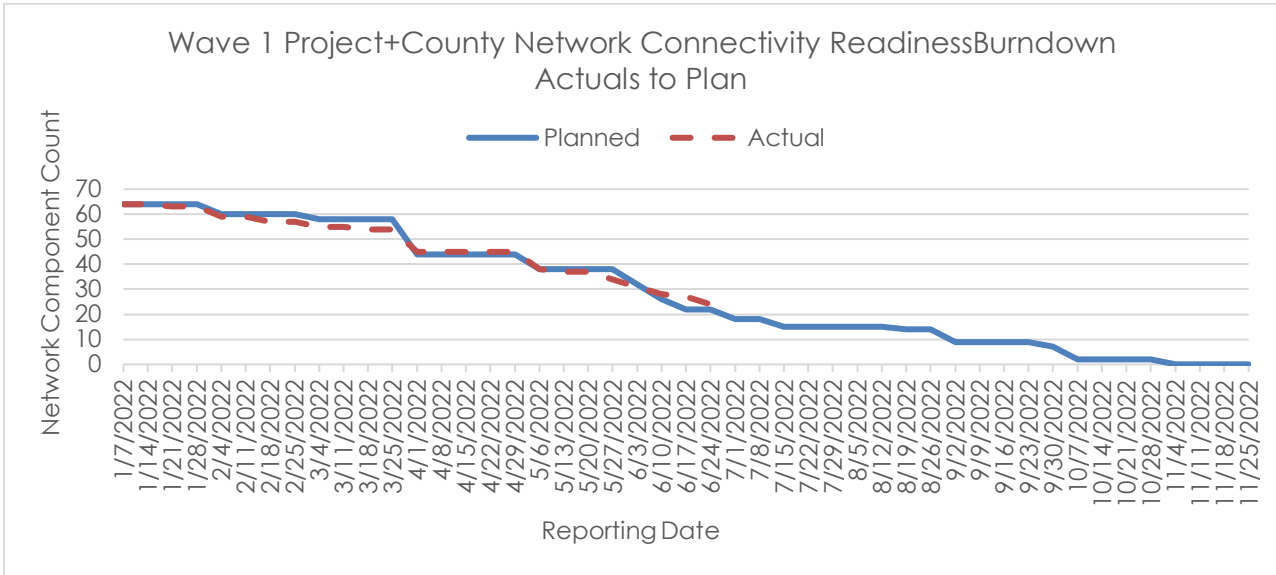


Figure 7.1-2 – Wave 2 County Network Connectivity Readiness Burndown

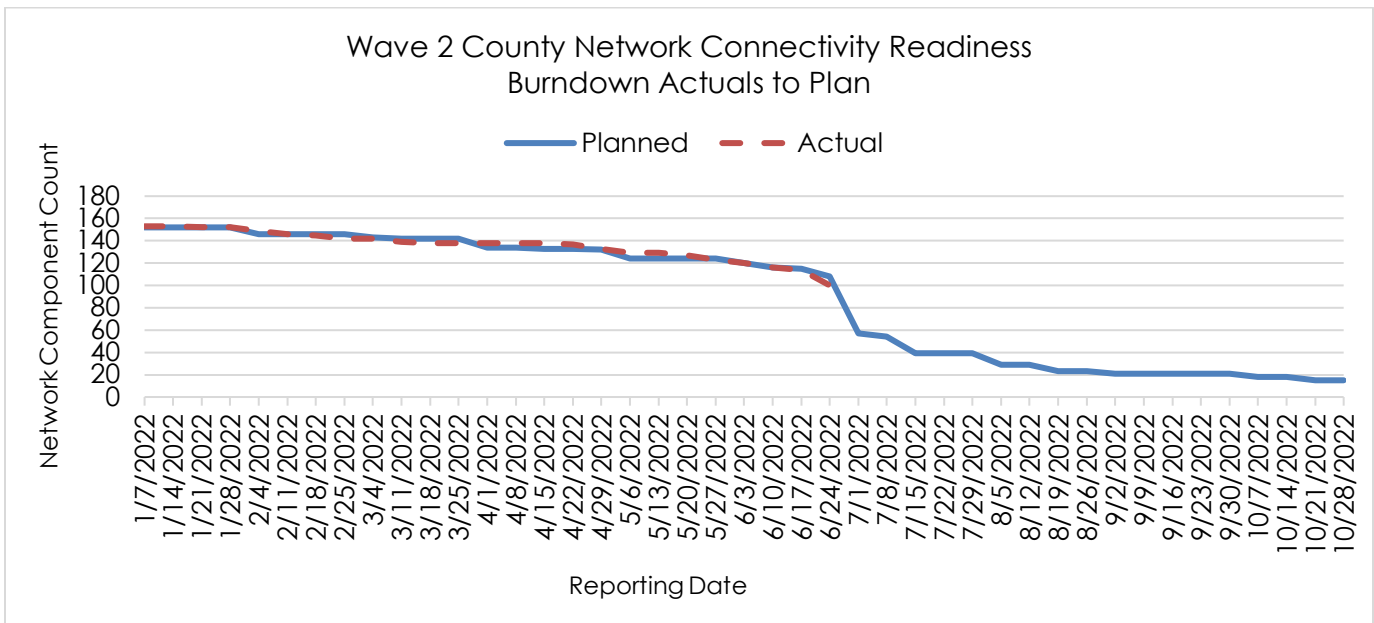

- ▶ Wave 1
 - Integration of Placer County network with CalSAWS behind schedule due to partial / incomplete responses to CalSAWS Requests for Information (CRFI) 22-040
 - Continue to support IPT test activities
 - Completed secondary router installation for Placer County on June 29, 2022
- ▶ Wave 2
 - Completed Santa Clara County SD-WAN and 4G circuit installs on June 29, 2022; continue with SD-WAN and circuit activation and testing activities
 - Completed SD-WAN infrastructure installation for Tulare County on June 27, 2022
- ▶ Wave 3
 - Continued to track circuit 1 activations for Orange and Ventura Counties
 - Distributed CRFI 22-052 to Wave 3 counties to seek and understand the Business-Critical Services and Applications which will be used by the Wave 3 CalWIN Counties; continued to track responses due on July 15, 2022
- ▶ Wave 4
 - Continued to plan for CalWIN Wave 4 County Kick off meeting scheduled for July 12, 2022
- ▶ CalWIN Counties
 - Continued assessment of CalWIN County capacity forecasts and bearing on procured bandwidth; identified proposed sites for bandwidth increases
 - Submitted CRFI 22-049 to Wave 2-6 Counties for reconfirming their Point of Presence (POP) site addresses in lieu of Risk 272 and to avoid any last-minute changes to the POP locations; responses from Counties due July 1, 2022

7.2 Activities for the Next Reporting Period

- ▶ CalSAWS Requests for Information (CRFI) for Security Assessment to be drafted and sent for review
- ▶ Continue to support Interface Partner Testing (IPT) for Wave 1 Counties
- ▶ Track responses to CRFI 22-049 for reconfirmation of Point of Presence (POP) site addresses
- ▶ Continue to implement remaining configuration changes for enabling Secure File Transfer Protocol (SFTP), Batch and Database access for Wave 1 and 2 Counties, where new CRFI responses are received
- ▶ Submit change requests for Cisco router and SD-WAN infrastructure installs at Wave 3 County Santa Barbara County
- ▶ Awaiting Wave 1 County response to Request for Information (CRFI) 22-040 due June 10, 2022 (Placer)
- ▶ Awaiting Wave 2 County response to Request for Information (CRFI) 22-040 due July 1, 2022

7.3 Deviations from Plan/Adjustments

- ▶ Santa Clara County has changed the designated Point of Presence (PoP) site location resulting in previously completed procurement and planning tasks having to be re-done. This will result in a 3-month impact to all downstream tasks and milestones for Santa Clara County unless mitigated
 - Mitigation:
 - Temporary installation (scheduled for June 29, 2022) of 4G connection (at additional cost) which will allow the County to complete pre-readiness and technical enablement tasks. This will isolate the County from being on-hold for 2 months. However, procured circuits will need to be delivered before beginning Interface Partner Testing (IPT) and User Acceptance Testing (UAT) testing
 - SD-WAN circuit in process of install (circuit 1) and once successfully enabled by July 15, 2022, alleviates risk with one end-state circuit being in place; will need to continue to monitor target delivery date for circuit 2
- ▶ Delivery date for Cisco routers required by CalWIN Wave 3-6 Counties has a lead time of greater than 90 days (ETA is September 2022). This poses an imminent risk for Wave 3 Counties. Anticipate a 2-month delay to overall timeline if not mitigated
 - Mitigation:
 - Wave 1 and 2 Counties have received the necessary equipment. If these 5 Counties are deployed with only 1 active Cisco router and retrofitted with second standby backup router when equipment becomes available or before go-live (earlier date), this would effectively mitigate the risk for Wave 3 Counties
 - CalSAWS will be recommending all Counties be aware of this risk associated with delivery timelines and to expedite any County Purchase orders that may have a bearing on the migration of the Counties to the CalSAWS System

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 27, 2022 to July 3, 2022

- Cisco has delivered remaining order of CalWIN County routers; CalSAWS distributed CIT 0163-22 as reminder for Counties to continue to expedite County purchase orders
- ▶ Placer County unable to complete tech readiness activities (CRFI 22-040) required for start of Interface Partner Testing (IPT) and Go-Live
 - Placer County has indicated that due to a conflicting firewall replacement project (County driven) that failed and being reattempted, the County would delay the configuration of technical changes requested by CalSAWS in CRFI 22-040 (Due on June 10, 2022)
 - Effort to re-deploy of the firewall and navigate through change process would be effort intensive causing the technical changes (CRFI 22-040) be postponed.
 - This would impact completion of technical readiness and start of Interface Partner Testing (IPT) by approximately 8 weeks (from June 27, 2022 until early August 2022)
 - Decision made to proceed with IPT with transferring the file outside of leveraging the end-state network
 - Working with County to do initial connectivity test (without end-state firewall) to identify any additional connectivity considerations once firewall project completes

8.0 Appendices

Appendix A – CalSAWS Deliverable Summary

Appendix B – CalSAWS Migration Work Plan Summary

Appendix C – CalSAWS DD&I Project Gantt Chart

Appendix D – CalSAWS Project Risks and Issues Report

