

CaISAWS – CalWIN
Implementation Support
Weekly Status Report

Reporting Period: June 28, 2021 to July 4, 2021

Table of Contents

1.0 CalWIN Implementation Support Services.....2

1.1 Highlights of the Reporting Period.....2

1.2 Project Deliverable Summary5

1.3 Project Risks and Issues 6

1.4 CRFI/CIT Communications Information 6

1.5 Activities for the Next Reporting Period 6

1.6 Deviations from Plan/Adjustments7

1.0 CalWIN Implementation Support Services

1.1 Highlights of the Reporting Period

Project Management

- ▶ Continued planning for on-boarding staff resources.
- ▶ Continued the monitoring of Action Items (AIs) and followed up with the POCs to update the statuses.
- ▶ Continued monitoring and updating the Questions and Answers (Q&A) Log.
- ▶ Worked with the team to close out any remaining Action Items due by 06/30/21.

Business Process Re-Engineering (BPR)

- ▶ As-Is sessions for ALL 18 CalWIN Counties are complete.
- ▶ Alameda, Fresno, and San Luis Obispo (SLO) Counties' As-Is Final Work Product (FWP) are pending sign-off.
- ▶ Draft Work Product (DWP) for San Francisco, Sacramento, and Sonoma under review.
- ▶ Conducted Week 2 of the To-Be BPR sessions with Placer and Contra Costa Counties
- ▶ Scheduled the Week-1 To-Be BPR sessions for Yolo County.

Figure 1 – As-Is Process Timetable by County

County	Session Start Date	Session End Date	First Review Start Date	First Review End Date	Incorporate Feedback	Start Final Review	County Sign-Off on FINAL As-Is Processes
Wave 1							
Contra Costa	02/22/21	03/25/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Placer	02/22/21	03/12/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Yolo	03/01/21	03/19/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Wave 2							
Tulare	03/01/21	03/19/21	03/29/21	04/09/21	04/16/21	04/19/21	04/23/21
Santa Clara	03/22/21	04/02/21	04/05/21	04/16/21	04/23/21	04/26/21	04/30/21
Wave 3							
Santa Barbara	03/22/21	04/02/21	04/05/21	04/16/21	04/23/21	04/26/21	04/30/21
Orange	04/05/21	04/16/21	04/19/21	04/30/21	05/07/21	05/10/21	05/14/21
Ventura	04/05/21	04/16/21	04/19/21	04/30/21	05/07/21	05/10/21	05/14/21
Wave 4							
Solano	04/19/21	04/30/21	05/03/21	05/14/21	05/21/21	05/24/21	06/01/21
Santa Cruz	04/19/21	04/30/21	05/03/21	05/14/21	05/21/21	05/24/21	06/01/21
San Mateo	05/03/21	05/14/21	05/17/21	05/28/21	06/06/21	06/08/21	06/15/21
San Diego	05/03/21	05/14/21	05/17/21	05/28/21	06/06/21	06/08/21	06/15/21
Wave 5							
Alameda	05/17/21	05/28/21	06/01/21	06/15/21	06/25/21	06/25/21	07/06/21
Fresno	05/17/21	05/28/21	06/01/21	06/15/21	06/25/21	06/28/21	07/09/21
Sonoma	06/14/21	06/25/21	06/28/21	07/12/21	07/19/21	07/20/21	07/26/21
Wave 6							
San Francisco	06/07/21	06/23/21	06/28/21	07/12/21	07/19/21	07/20/21	07/26/21
Sacramento	06/14/21	06/25/21	06/28/21	07/12/21	07/19/21	07/20/21	07/26/21
San Luis Obispo	06/01/21	06/11/21	06/14/21	06/25/21	06/29/21	06/30/21	07/09/21

*As of 07/02/21

Organizational Change Management (OCM)

- ▶ Held office hours sessions with the County OCM POCs for the County End User Register validation.
- ▶ Continued drafting the DDED for the Organizational Change Management (OCM) Plan.
- ▶ Reviewed the July OCM POC meeting presentation feedback and made updates.
- ▶ Continued collecting the Change Impacts from the BPR To-Be sessions.
- ▶ Continued ChangeScout dashboard set-up.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, July 7, 2021

Reporting Period: June 28, 2021 to July 4, 2021

Training

- ▶ Prepared to onboard the Training Development team on 07/06/21.
- ▶ Participated in an OCM Planning session on 06/29/21.
- ▶ Participated in the Placer and Contra Costa BPR Debrief sessions on 06/29/21, 06/30/21, and 07/01/21.

Implementation Support Services (ISS)

- ▶ Participated in the Wave-1 Counties To-Be sessions.
- ▶ Continued preparing for Visioning Lab II and distributed the calendar invitation.
- ▶ Continued to review the conversion activities that will impact conversion of the CalWIN Counties and discussed open questions with the Conversion team on 06/29/21.
- ▶ Continued to work with the CalSAWS subject matter experts (SMEs) to gather details around the questions raised during their County profile review meeting.
- ▶ Participated in ongoing meetings with DD&I and the Consortium for conversion, API user groups, and DDID.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)


CalWIN Implementation Support Phase

Weekly Status Report, July 7, 2021

Reporting Period: June 28, 2021 to July 4, 2021

Project Timeline

Figure 2 – Project Gantt Chart

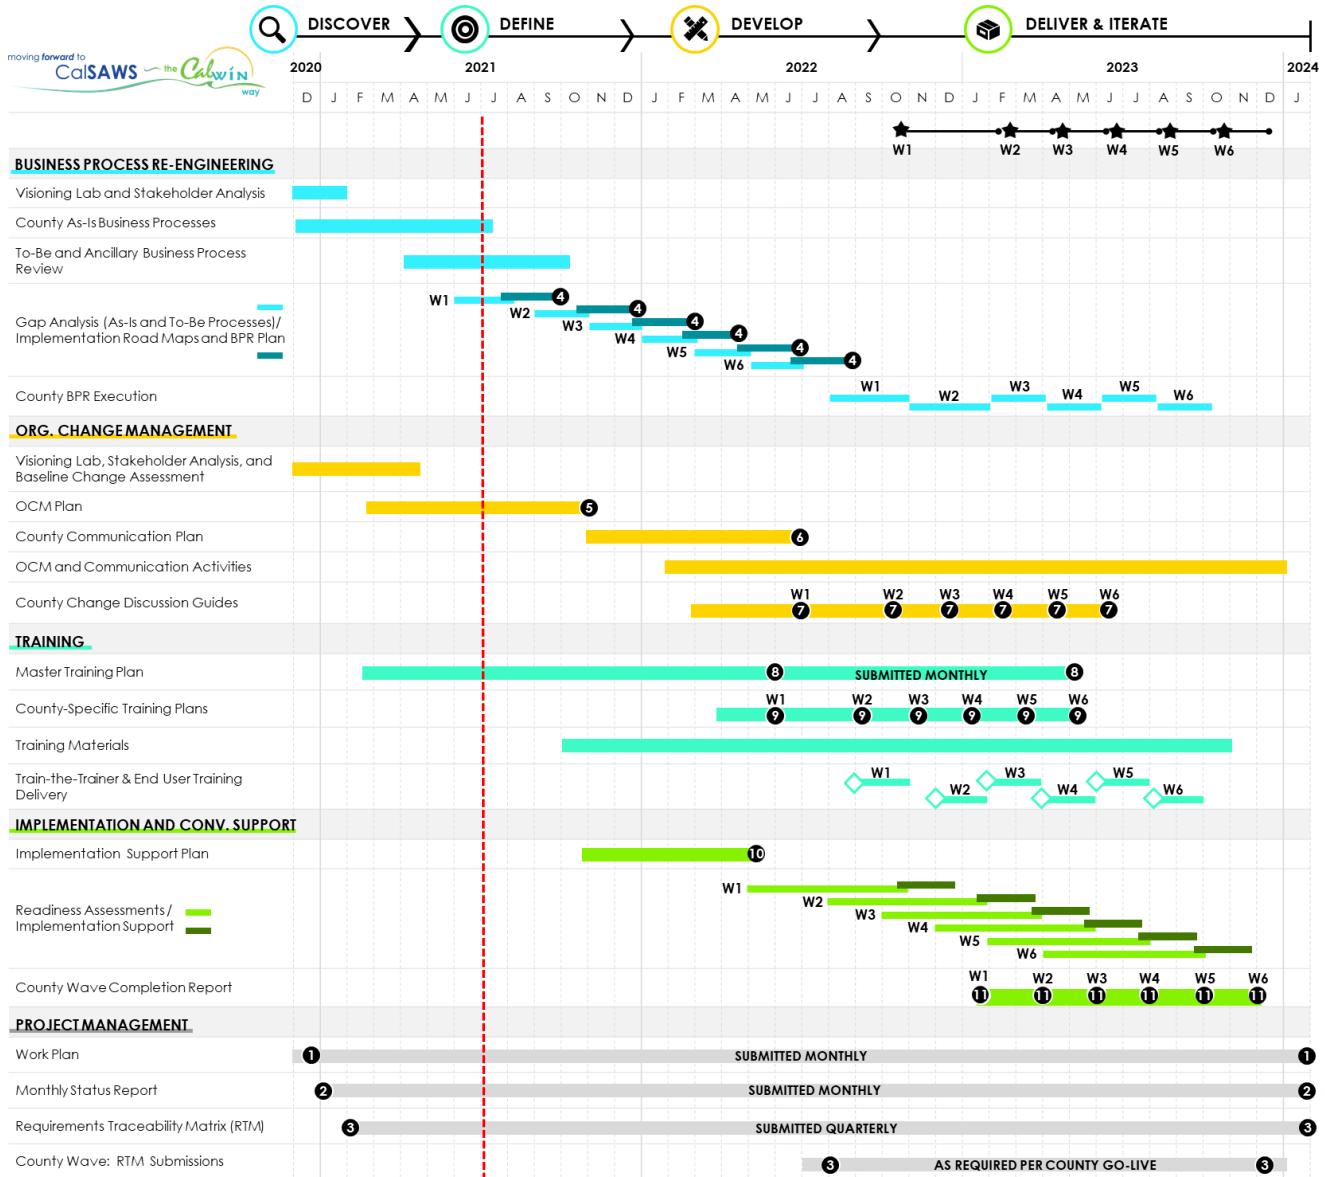

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, July 7, 2021

Reporting Period: June 28, 2021 to July 4, 2021

1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below.

Table 1 – Deliverable Status for Current Reporting Period

Completed
Coming Soon

DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final
01	Workplan – Initial	12/04/20	12/15/20	12/23/20	01/14/21	01/22/21
02	Monthly Status Report – Initial	12/04/20	12/18/20	01/05/21	01/12/21	01/27/21
03	Requirements Traceability Matrix Initial	12/22/20	01/07/21	02/01/21	02/16/21	02/23/21
04	Business Process Re-Engineering Plan – W1	07/14/21	07/26/21	10/11/21	11/01/21	11/08/21
05	Organizational Change Management Plan	07/14/21	07/26/21	10/04/21	10/26/21	11/02/21
06	County Communication Plan	08/16/21	08/26/21	01/03/22	01/25/22	02/01/22
07	County Change Guide	01/14/22	01/27/22	03/24/23	04/17/23	04/24/23
08	Master Training Plan	08/13/21	08/25/21	05/13/22	06/06/23	06/13/23
09	County Specific Training Plan	09/14/21	09/24/21	05/08/23	05/30/23	06/06/23
10	Implementation Support Plan	01/14/22	01/27/22	05/16/22	06/07/22	06/14/22
11	Wave Completion Report	09/15/22	09/27/22	01/11/24	01/24/24	01/31/24

Table 2 – Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
01	Workplan – Initial	Complete	
01.06	Work Plan – June 2021	On-Track	FDEL submission due 07/08/21 FDEL approval due 07/15/21
02	Monthly Status Report – Initial	Complete	
02.06	Monthly Status Report – June 2021	On-Track	FDEL submission due 07/08/21 FDEL approval due 07/15/21
03	Requirements Traceability Matrix Initial	Complete	
03.01	Requirement Traceability Matrix – Quarter 1	Complete	FDEL submitted on 06/04/21 FDEL approval due 06/11/21
04	Business Process Re-engineering Plan	On-Track	DDED submission due 07/14/21
05	Organizational Change Management Plan	On-Track	DDED submission due 07/14/21
06	County Communication Plan	On-Track	DDED submission due 08/16/21
07	County Change Guide	On-Track	DDED submission due 01/14/22
08	Master Training Plan	On-Track	DDED submission due 08/13/21
09	County Specific Training Plan	On-Track	DDED submission due 09/14/21
10	Implementation Support Plan	On-Track	DDED submission due 01/14/22
11	Wave Completion Report	On-Track	DDED submission due 09/15/22

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, July 7, 2021

Reporting Period: June 28, 2021 to July 4, 2021

1.3 Project Risks and Issues

There were no CalSAWS Risks or Issues created and/or still open for the reporting period.

Table 3 – Risks & Issues

ID	Title	Details	Status	Impact	Severity	Date Logged

1.4 CRFI/CIT Communications Information

There were no CalSAWS Information Transmittals (CITs) sent and/or still open for the reporting period.

Table 4 – CITs

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
XXX-21	CalWIN Counties	CalWIN Implementation Support Services – Publication of Q&A Log	CalSAWS DD&I	TBD	Greg Postulka	Richard Neumann

There were no CalSAWS Requests for Information (CRFIs) sent and/or still open for the reporting period.

1.5 Activities for the Next Reporting Period

Project Management

- ▶ Continue planning for and on-boarding staff resources.
- ▶ Continue to collaborate with other teams to coordinate information for the CalWIN Counties.
- ▶ Prepare and submit the Monthly Status Report– June 2021 on 07/08/21.
- ▶ Prepare and submit the Monthly Work Plan – June 2021 on 07/08/21.
- ▶ Publish the Q&A Log to the Web Portal.

Business Process Re-Engineering (BPR)

- ▶ Obtain sign-off for Alameda, Fresno, and San Luis Obispo (SLO) Counties.
- ▶ Conduct the Week-3 To-Be sessions for Placer and Contra Costa Counties.
- ▶ Distribute the Week-1 To-Be materials to Yolo County.
- ▶ Incorporate real-time feedback from the BPR sessions for continuous improvement.

Organizational Change Management (OCM)

- ▶ Continue building the CalWIN Monthly Stand-Up Meeting presentation.
- ▶ Continue drafting the DDED for the OCM Plan.
- ▶ Review the July OCM POC meeting presentation feedback and make updates.
- ▶ Continue collecting the Change Impacts from the BPR To-Be sessions.
- ▶ Continue ChangeScout tool set-up.

Training

- ▶ Start orientation and onboard the Training Development team on 07/06/21.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, July 7, 2021

Reporting Period: June 28, 2021 to July 4, 2021

- ▶ Participate in an OCM Planning session on 07/06/21.
- ▶ Participate in the Placer and Contra Costa BPR Debrief sessions on 07/06/21, 07/07/21, and 07/08/21.
- ▶ Participate in the Yolo County Leadership meeting for BPR/OCM on 07/07/21.
- ▶ Participate in the Wave-1 Check-in Meeting on 07/07/21.
- ▶ Participate in the Consortium Implementation and CalWIN ISS Team meeting on 07/08/21.
- ▶ Begin preparation for the 07/21/21 Training Advisory Council (TAC) Meeting.

Implementation Support Services

- ▶ Participate in To-Be sessions with Contra Costa County, Placer County.
- ▶ Continue preparing for Visioning Lab II (at the end of July).
- ▶ Continue to review the conversion activities that will impact conversion of the CalWIN Counties.
- ▶ Begin preparing the July OPAC meeting information.

1.6 Deviations from Plan/Adjustments

- ▶ None for the reporting period.
