



BenefitsCal UAT Weekly Status Report

**Reporting Period: October 4, 2021, to October 8,
2021**

Weekly Status Report, October 4, 2021

Table of Contents

1.0	Project Management.....	2
1.1	Highlights of the Reporting Period:.....	2
	UAT Planning:	2
1.2	Activities for the Next Reporting Period:.....	2
	Planning for Next Week:.....	2
1.3	Issues Observed: September 27 th thru October 1 st	2
	UAT Test Execution Status – Release 1.1	3
	UAT Test Execution Status – Release 1.2.....	4

Weekly Status Report, October 4, 2021

1.0 Project Management

1.1 Highlights of the Reporting Period:

October 4th thru October 8th, 2021

UAT Planning:

1. Participated in weekly Portal/Mobile Test Planning meeting to review the progress of Deloitte's test execution activities and defect status.
2. Led the team during BenefitsCal - UAT test stand-up meetings and during test execution for R1.2.
3. Started the conversation with Consortium and Vendor partners about R2.0 testing of BenefitsCal
4. Met with LA county to plan for BenefitsCal 2.0 UAT

1.2 Activities for the Next Reporting Period:

5. Start working with LA county on planning activities for R2.0 BenefitsCal release.
6. Start initial planning session on CalWIN UAT
7. Close out BenefitsCal R1.1 and R1.2 UAT activities

Planning for Next Week:

1. Continue to attend weekly Portal/Mobile Test Planning meetings to review the progress of Deloitte's test execution activities and defect status.
2. Continue with UAT Defect Triage Calls.
3. Continue to test defects deployed for Release 1.1.
4. Continue with test execution of Release 1.2 UAT test scripts.

1.3 Issues Observed: September 27th thru October 1st

- SAR7 Data is not transferred over to CalSAWS
- Renewal forms/SAR7 summary generated in BenefitsCal did not include all questions
- Duplicate individuals were showing up in the renewal flow
- Renewals were failing due to lack of primary applicant on the case in BenefitsCal


Weekly Status Report, October 4, 2021

UAT Test Execution Status – Release 1.1

Release 1.1 - BenefitsCal UAT Testing

Report Run Date: 10/11/2021

	Unique Scenarios (Component Testing + E2E)	Release 1.1					Grand Total
		Week 1 (09/07/21)	Week 2 (09/13/21)	Week 3 (09/20/21)	Week 3 (09/27/21)	Week 4 (10/04/21)	
Weekly Planned for Execution	112	50	34	28	0	0	112
Executed (Calculated - Pass + Failed)		30	56	50	7	8	112
Passed		18	44	35	7	8	112
Failed		12	12	15	0	0	0
Blocked		0	6	0	0	0	0
In Progress		20	9	0	0	0	0
Not Completed		72	12	0	0	0	0
Pass Percentage		60%	79%	70%	100%	100%	100%
Fail Percentage		40%	21%	30%	0%	0%	0%
Pass Percentage of Total		16%	39%	31%	6%	7%	100%
112 Total Scenarios							

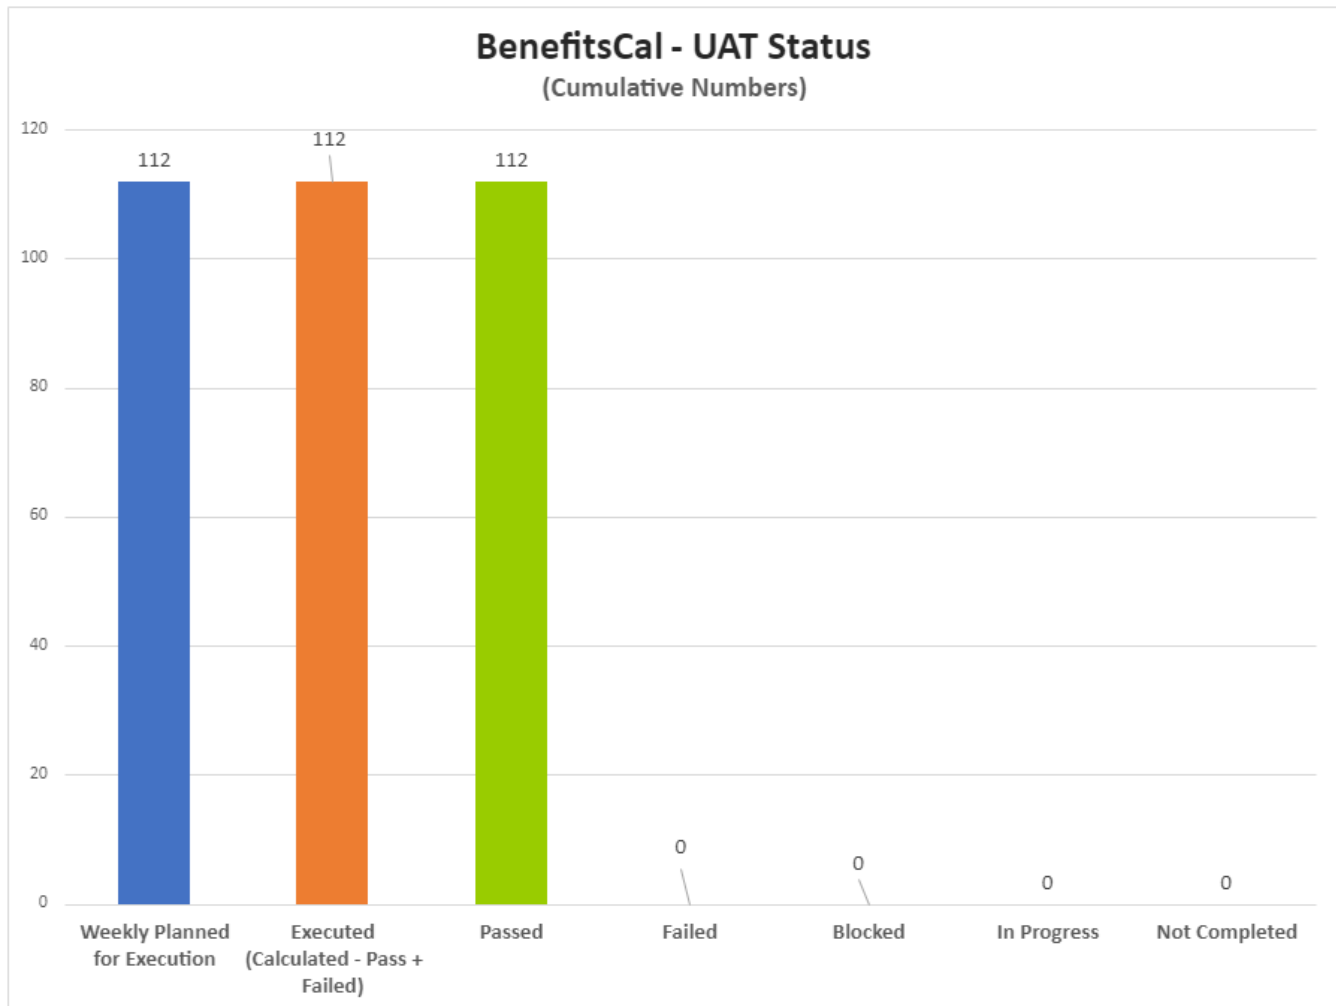

Weekly Status Report, October 4, 2021

UAT Test Execution Status – Release 1.2

Release 1.2 - Metrics:

Release 1.2 - BenefitsCal UAT Testing

Report Run Date: 10/01/2021					
	Unique Scenarios (Component Testing + E2E)	Release 1.2			Grand Total
		Week 1 (09/20/21)	Week 2 (09/27/21)	Week 3 (10/04/21)	
Weekly Planned for Execution	76	30	30	20	76
Executed (Calculated - Pass + Failed)		49	72	76	76
Passed		35	58	71	71
Failed		14	14	5	5
Blocked		0	4	0	0
In Progress		16	0		0
Not Completed		15	0		0
Pass Percentage		71%	81%	93%	93%
Fail Percentage		29%	19%	7%	7%
Pass Percentage of Total		46%	76%	93%	93%
Total Scenarios: 76					

Weekly Status Report, October 4, 2021

Release1.2 - Burndown Chart:

