

# CalSAWS Central Print Weekly Status Report

**Reporting Period: October 11, 2021 to October  
17, 2021**

**CalSAWS – Central Print Project**

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

---

**Table of Contents**

1.0 CalSAWS Central Print Project .....2

    1.1 Highlights of the Reporting Period .....2

    1.2 Project Deliverable Summary .....4

    1.3 Project Risks and Issues .....5

    1.4 CRFI/CIT Communications Information .....6

    1.5 Activities for the Next Reporting Period.....6

    1.6 Deviations from Plan/Adjustments .....7

# CalSAWS – Central Print Project

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021


## 1.0 CalSAWS Central Print Project

### 1.1 Highlights of the Reporting Period

#### Project Management

- ▶ Continued updates to project work plan.

#### Project Gantt

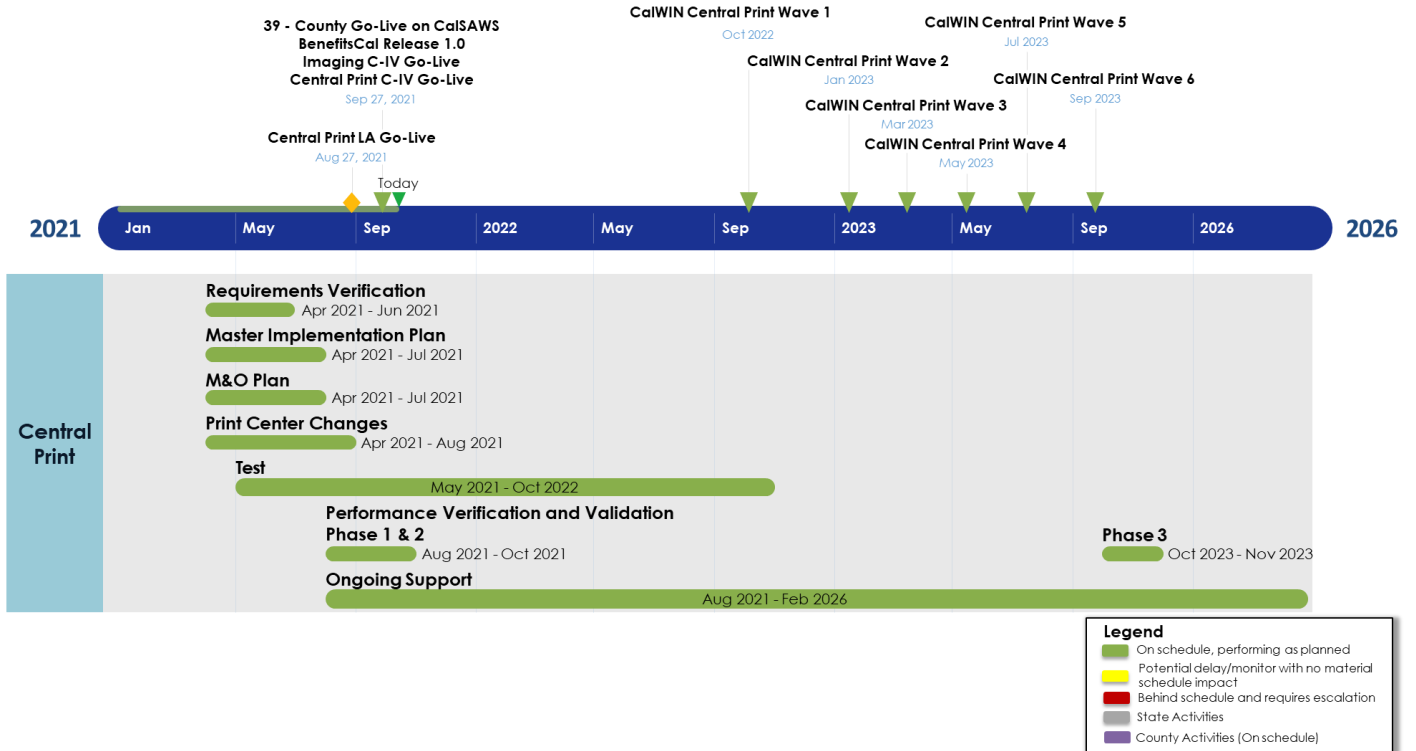


#### Requirements Verification

- ▶ N/A

## CalSAWS – Central Print Project

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

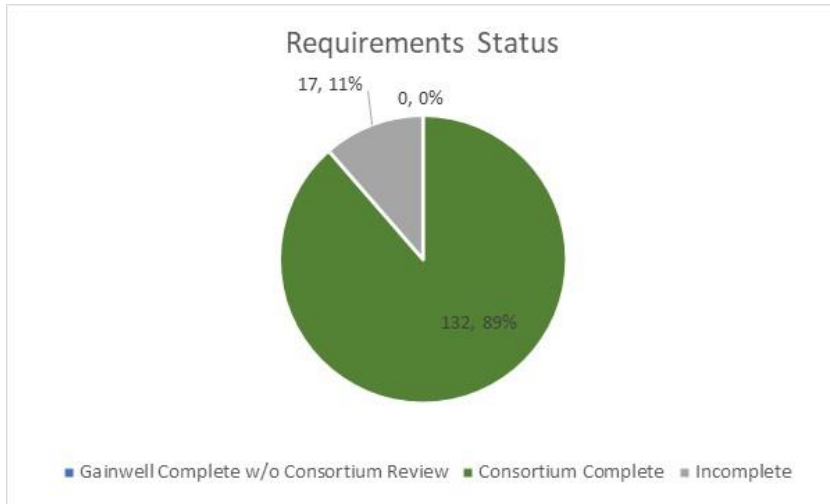

### Master Implementation Plan

- ▶ Continued work on materials inventory management.
- ▶ Began planning for CalWIN Wave 1 counties' kickoff meeting.

### Changes to Existing Print Centers

- ▶ N/A

### Establishment of the SoCal Print Center

- ▶ N/A

### Interface and File Considerations with CalSAWS

- ▶ N/A

### Fulfillment Platform Configuration

- ▶ Planning for next release of the Central Print Portal software.

### Maintenance and Operations Plan

- ▶ Continued ongoing operations for Phase 2 (40 County) Central Print.
- ▶ Continued monitoring of the Phase 2 PV&V results.

### Comprehensive Testing

- ▶ N/A

### Project Action Items – Overdue

- ▶ This table lists overdue action items, including the owner and due date.

ID	Description	Owner	Due Date
None	No overdue actions items		

Table 1.1-8 – Overdue Action Items

## CalSAWS – Central Print Project

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

### 1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below. Note that only the initial submission of the Monthly Status Report is listed in the table below. Each remaining Monthly Status Report will be submitted as an FDEL only per the date in the approved FDED and is not included in the list below.

#### Deliverable Status by Submission

DEL ID	Deliverable Name	DDED	FDED	Complete		Coming Soon
				DDEL	FDEL	Final
01	Monthly Status Report - March	4/29/21	5/24/21	5/28/21	6/7/21	6/8/21
02	Master Implementation Plan	4/29/21	5/24/21	5/28/21	6/11/21	6/28/21
03	Maintenance and Operations Plan	4/29/21	5/24/21	6/10/21	6/23/21	7/6/21
04	Final Acceptance Report	5/12/21	5/21/21	11/21/23	12/6/23	12/12/23

**Table 1.2-1 – Deliverable Status for Current Reporting Period**

#### Overall Deliverable Status

DEL #	DELIVERABLE NAME	STATUS	Next Deadline
01	Monthly Status Report – March 2021	Completed	Each remaining Monthly Status Report will be submitted as an FDEL only per the date in the approved FDED and are not listed here. Any exceptions will be noted.
02	Master Implementation Plan	Completed	Received WAC approvals on 7/9/21.
03	Maintenance and Operations Plan	Completed	Received WAC approvals on 7/9/2021.
04	Final Acceptance	On-track	DDEL submission due 11/21/23

**Table 1.2-2 – Upcoming Deliverable Deadlines**

## CalSAWS – Central Print Project


Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

### Project Risks and Issues

ID	Title	Details	Status	Impact	Severity	Date Logged
242	Central Print Insertion Barcode Placement & Margin Formatting Inconsistency	Recommended clearance for insertion bar codes is ¼ of white space around the bar code. The white space is designed to increase the accuracy of the bar code scan, reducing insertion errors or stoppages. The sample test file provided included pages with no clearance and on some forms, the bar code was overwritten by text or borders. Obtaining the recommended ¼ inch of white space would result in changes to the CalSAWS correspondence templates and would not be feasible prior to the planned go live for Los Angeles (August 2021) and C-IV (September 2021).	Closed	3	Medium	4/9/21

The following chart shows the number of risks currently open and previously closed, if applicable.

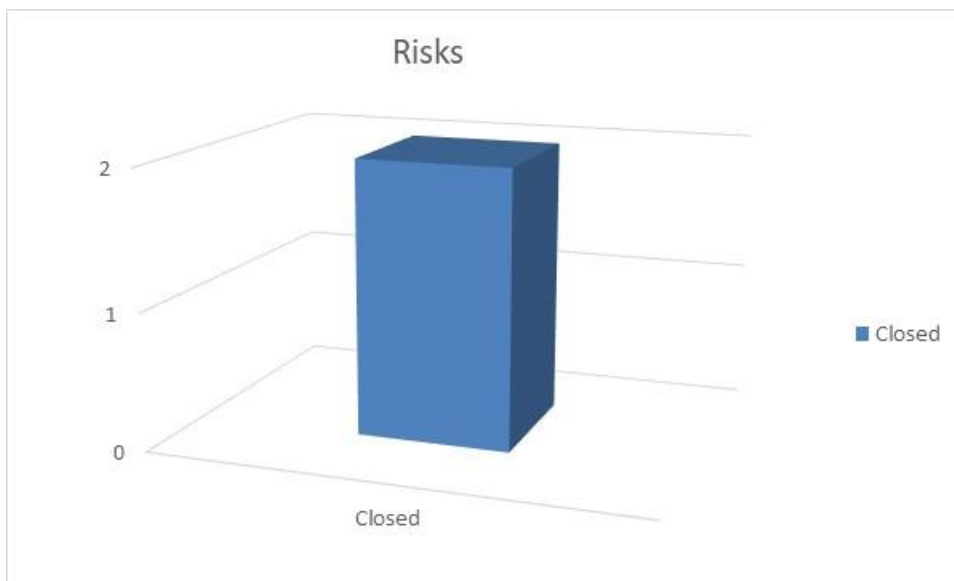

The following chart shows the number of issues currently open and previously closed, if applicable.

► Not applicable – No open or closed issues as of this status reporting period.

## CalSAWS – Central Print Project

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

### 1.3 CRFI/CIT Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

There was one CalSAWS Information Transmittals (CITs).

CIT ID	To	Subject	Category	Distribution Date
0181-21	LA/C-IV County	Central Print Postage Process	Correspondence	7/19/21

**Table 1.4-1 – CITs**

There was one CalSAWS Requests for Information (CRFIs).

CRFI ID	To	Subject	Distribution Date	Status	Response Due Date
21-041	LA/C-IV County	Central Print Correspondence	7/14/21	Open	7/23/21

**Table 1.4-2 – CRFIs**

### 1.4 Activities for the Next Reporting Period

#### Project Management

- ▶ Continue updates to project work plan.

#### Requirements Verification

- ▶ N/A

#### Master Implementation Plan

- ▶ Continue work on materials inventory management.
- ▶ Complete pickup of inventory from prior vendor.
- ▶ Provide submission for the initial updates to the SSP.
- ▶ Submit Phase 1 PV&V results.
- ▶ Schedule Contra Costa and Tulare checkpoint meeting.
- ▶ Schedule CalWIN Wave 1 counties' kickoff meeting.

#### Changes to Existing Print Centers

- ▶ N/A

#### Establishment of the SoCal Print Center

- ▶ N/A

#### Interface and File Considerations with CalSAWS

- ▶ N/A

#### Fulfillment Platform Configuration

- ▶ N/A

#### Maintenance and Operations Plan

- ▶ Continue ongoing operations for Phase 2 Central Print.
- ▶ Continue monitoring of the Phase 2 PV&V results.
- ▶ Submit potential risk for consideration related to the paper industry shortage.

## CalSAWS – Central Print Project

Weekly Status Report, October 18, 2021

Period: October 11, 2021 to October 17, 2021

---

### Comprehensive Testing

- ▶ N/A

### 1.5 Deviations from Plan/Adjustments

- ▶ No deviations from the plan are noted.
