



CalSAWS – CalWIN Implementation Support Weekly Status Report

**Reporting Period: December 13, 2021 to
December 19, 2021**

Table of Contents

1.0 CalWIN Implementation Support Services.....2

1.1 Highlights of the Reporting Period.....2

1.2 Project Deliverable Summary5

1.3 Project Risks and Issues7

1.4 CRFI/CIT Communications Information7

1.5 Activities for the Next Reporting Period.....7

1.6 Deviations from Plan/Adjustments8

1.0 CalWIN Implementation Support Services

1.1 Highlights of the Reporting Period

Project Management

- ▶ Continued planning for and onboarding staff resources.
- ▶ Continued monitoring Action Items (AIs) and following up with the points of contact (POCs) to update the statuses.
- ▶ Continued monitoring and updating the ISS Questions and Answers (Q&A) Log.
- ▶ Continued updating the County Work Plans for Wave 1.
- ▶ Continued gathering timelines for the Project teams for CalWIN County implementation activities.
- ▶ Submitted the following Work Products:
 - WP02 To-Be Processes – Orange County Draft Work Product (DWP) on 12/16/21.
 - WP02 To-Be Processes – Ventura County DWP on 12/18/21.

Business Process Reengineering (BPR)

- ▶ Completed To-Be BPR sessions with Orange and Ventura Counties.
- ▶ Submitted Orange and Ventura Counties' To-Be DWP for review.
- ▶ Continued planning for the To-Be BPR sessions for Santa Cruz and Solano Counties.
- ▶ Conducted Part 2 Pre-Meets for Santa Cruz and Solano Counties.
- ▶ Received sign-off on Santa Barbara To-Be Final Work Product (FWP).

Figure 1 – To-Be Process Timetable by County

	Session Start Date	Session End Date	First Review Start Date	First Review End Date	Start Final Review	County Sign-Off on Final To-Be Work Product
Wave 1						
Contra Costa	06/21/21	07/30/21	08/04/21	09/02/21	09/02/21	09/10/21
Placer	06/21/21	07/30/21	08/04/21	08/20/21	08/30/21	09/07/21
Yolo	07/12/21	08/11/21	08/11/21	08/27/21	09/08/21	09/17/21
Wave 2						
Tulare	09/13/21	10/08/21	10/11/21	10/22/21	11/01/21	11/08/21
Santa Clara	09/13/21	10/08/21	10/11/21	10/22/21	11/01/21	11/08/21
Wave 3						
Santa Barbara	10/18/21	11/12/21	11/15/21	11/30/21	12/08/21	12/14/21
Orange	11/15/21	12/14/21	12/20/21	01/07/21	01/18/22	01/24/22
Ventura	11/15/21	12/14/21	12/20/21	01/07/21	01/18/22	01/24/22
Wave 4						
Solano	01/10/22	02/04/22	02/07/22	02/18/22	02/28/22	03/04/22
Santa Cruz	01/10/22	02/04/22	02/07/22	02/18/22	02/28/22	03/04/22
San Mateo	02/07/22	03/04/22	03/07/22	03/18/22	03/28/22	04/01/22
San Diego	02/14/22	03/11/22	03/14/22	03/25/22	04/04/22	04/08/22
Wave 5						
Alameda	03/21/22	04/15/22	04/18/22	04/29/22	05/09/22	05/13/22
Fresno	03/21/22	04/15/22	04/18/22	04/29/22	05/09/22	05/13/22
Sonoma	04/25/22	05/20/22	05/23/22	06/06/22	06/14/22	06/20/22
Wave 6						
San Francisco	04/25/22	05/20/22	05/23/22	06/06/22	06/14/22	06/20/22
Sacramento	05/31/22	06/27/22	06/28/22	07/15/22	07/25/22	07/29/22
San Luis Obispo	05/31/22	06/27/22	06/28/22	07/15/22	07/25/22	07/29/22

*As of 12/19/21

Organizational Change Management (OCM)

- ▶ Socialized the T-Minus 12 Wave 1 Readiness Survey Response Report.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

- ▶ Shared the draft of the DEL 06: County Communication Plan Draft Deliverable (DDEL) with the OCM Leads and QA team.
- ▶ Refined the approach to the Change Discussion Guides with input from the OCM Leads, QA, and the BPR team.
- ▶ Reviewed the draft Change Network Champion (CNC) kickoff presentation with the OCM Leads and QA.

Training

- ▶ Continued developing the draft training schedules based on County Profile information (Wave 6).
- ▶ Discussed the Wave 1 training classroom needs analysis with the Consortium Project Manager on 12/16/21.
- ▶ Prepared for Waves 5 and 6 meetings with the Counties.
 - Met with Sonoma County on 12/16/21.
- ▶ Facilitated the Training Advisory Committee (TAC) meeting on 12/15/21.
- ▶ Participated in the CalWIN Stand Up meeting on 12/13/21.
- ▶ Participated in the Placer County Work Plan Update meeting on 12/13/21.
- ▶ Continued training development, creating instructional design documents for the CalSAWS Instructor-Led Training curriculum.
- ▶ Continued development of the Learning Journey Map.

Implementation Support Services (ISS)

- ▶ Continued to compile available cross-project schedules for impacts on Wave 1 CalWIN Counties and incorporate into county-specific timelines.
- ▶ Conducted follow-up Wave 1 County-specific Work Plan meetings with Placer County (12/13/21) and Yolo County (12/16/21) incorporating feedback.
- ▶ Continued drafting the DEL10: Implementation Support Plan Draft Deliverable Expectation Document (DDED).
- ▶ Participated in the CalWIN UAT meeting on 12/15/21.
- ▶ Participated in the Technical Point of Contact (TPOC) Kick-Off meeting on 12/16/21.
- ▶ Continued updating and incorporating feedback into the County-specific Work Plans for Wave 1 counties.
- ▶ Continued compiling the Wave 1 readiness checklist.
- ▶ Participated in ongoing meetings with DD&I and the Consortium for conversion, imaging, application programming interface (API) user groups, UAT, and DDID.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase


Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

Project Timeline

Figure 2 – Project Gantt Chart

Project Timeline

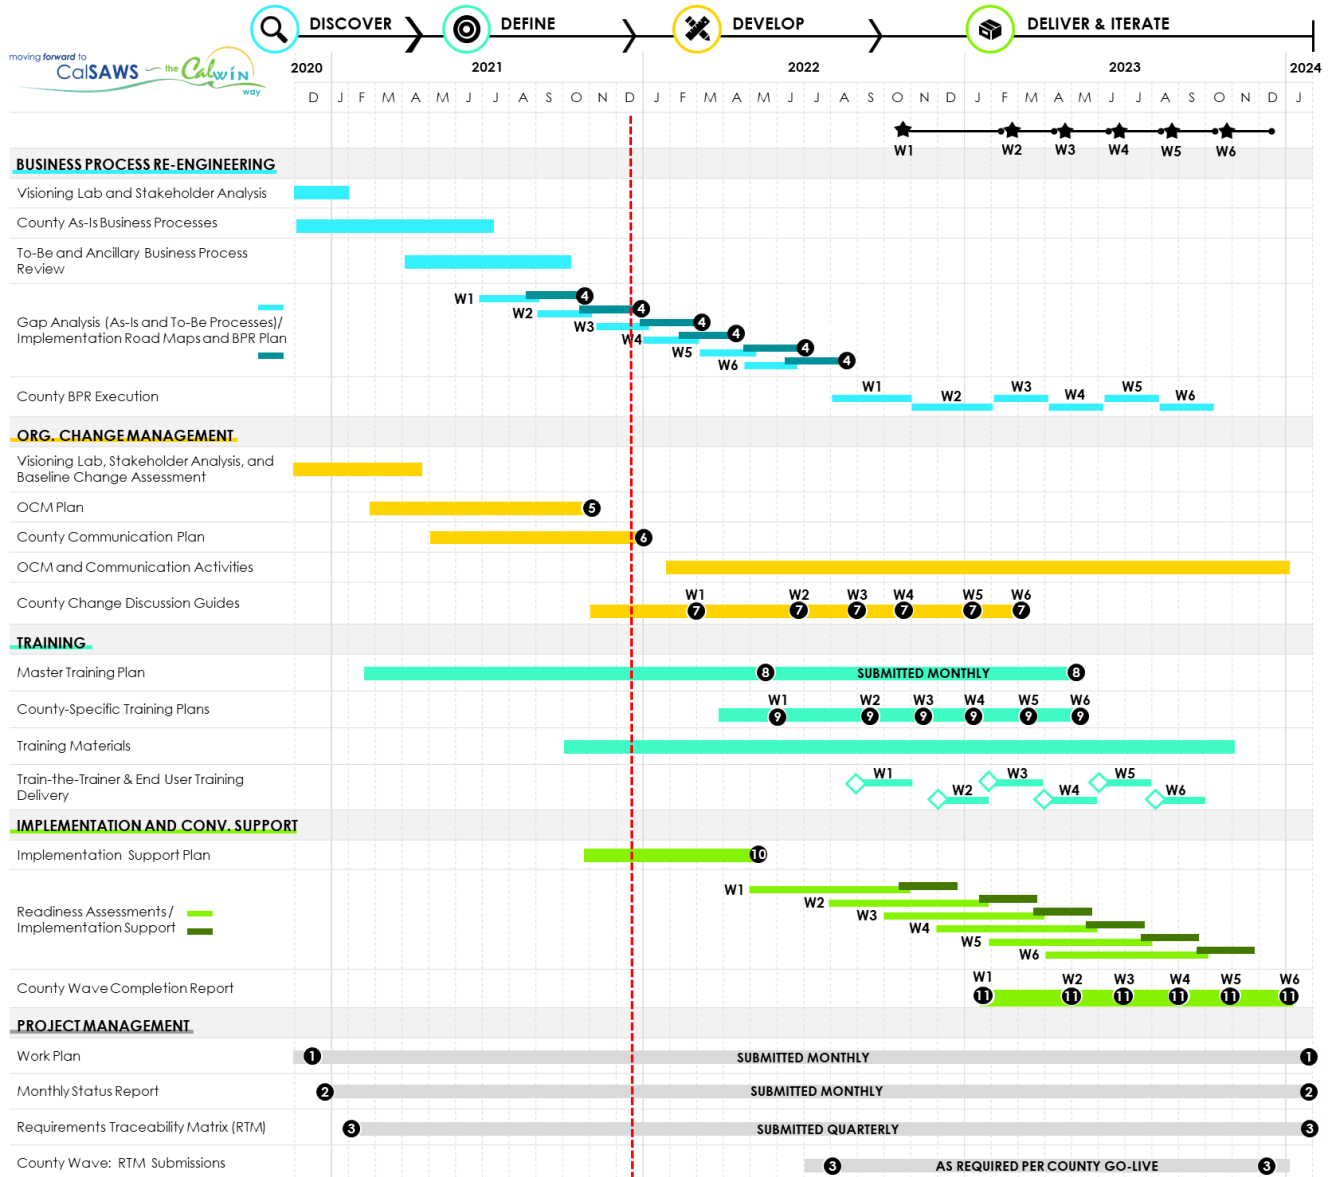

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below.

Table 1 – Deliverable Status for Current Reporting Period

Completed
Coming Soon

DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final
01	Workplan – Initial	12/04/20	12/15/20	12/23/20	01/14/21	01/22/21
02	Monthly Status Report – Initial	12/04/20	12/18/20	01/05/21	01/12/21	01/27/21
03	Requirements Traceability Matrix Initial	12/22/20	01/07/21	02/01/21	02/16/21	02/23/21
04	Business Process Reengineering Plan	07/14/21	07/26/21	10/01/21	10/22/21	10/27/21
05	Organizational Change Management Plan	07/14/21	07/26/21	10/04/21	10/26/21	11/02/21
06	County Communication Plan	08/16/21	08/26/21	01/03/22	01/25/22	02/01/22
07	County Change Guide	01/14/22	01/27/22	03/24/23	04/17/23	04/24/23
08	Master Training Plan	10/27/21	11/08/21	05/13/22	06/06/23	06/13/23
09	County Specific Training Plan (W1)	10/27/21	11/08/21	05/13/22	06/06/23	06/13/23
10	Implementation Support Plan	01/14/22	01/27/22	05/16/22	06/07/22	06/14/22
11	Wave Completion Report	09/15/22	09/27/22	01/11/24	01/24/24	01/31/24

Table 2 – Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
01	Workplan – Initial	Complete	
01.11	Work Plan – November 2021	Complete	FDEL submitted 12/03/21 FDEL approved 12/10/21
02	Monthly Status Report – Initial	Complete	
02.11	Monthly Status Report – November 2021	Complete	FDEL submitted 12/03/21 FDEL approved 12/10/21
03	Requirements Traceability Matrix Initial	Complete	

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

DEL #	Deliverable Name	Status	Next Deadline
03.03	Requirement Traceability Matrix – Quarter 3	Complete	FDEL submitted 12/01/21 FDEL approved 12/10/21
04	Business Process Reengineering Plan	Complete	
04.01	County BPR Plan – Contra Costa	On-Track	DDEL submitted 11/29/21 FDEL submission 12/20/21
04.02	County BPR Plan – Placer	On-Track	DDEL submitted 11/29/21 FDEL submission 12/20/21
04.03	County BPR Plan – Yolo	On-Track	DDEL submitted 11/29/21 FDEL submission 12/20/21
05	Organizational Change Management Plan	Complete	
06	County Communication Plan	On-Track	DDEL submission 01/03/22 FDEL submission 01/25/22
07	County Change Guide	On-Track	DDED submission 01/14/22 FDED submission 01/27/22
08	Master Training Plan	On-Track	DDEL submission 05/13/22 FDEL submission 06/06/22
09.01	County Specific Training Plan – Contra Costa	On-Track	DDEL submission 05/13/22 FDEL submission 06/06/22
09.02	County Specific Training Plan – Placer	On-Track	DDEL submission 05/13/22 FDEL submission 06/06/22
09.03	County Specific Training Plan – Yolo	On-Track	DDEL submission 05/13/22 FDEL submission 06/06/22
10	Implementation Support Plan	On-Track	DDED submission 01/14/22 FDED submission 01/27/22
11	Wave Completion Report	On-Track	DDED submission 09/15/22 FDED submission 09/27/22

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

1.3 Project Risks and Issues

There were no CalSAWS Risks or Issues created and/or still open for the reporting period.

Table 3 – Risks & Issues

ID	Title	Details	Status	Impact	Severity	Date Logged
N/A						

1.4 CRFI/CIT Communications Information

There are two (2) open CalSAWS Request for Information (CRFI) for the reporting period.

Table 4 – CRFIs

CRFI ID	To	Subject	Category	Distribution Date	Response Due Date
21-069	CalWIN Counties (PPOC, RM, Section Directors)	CalWIN Implementation Point of Contact (IPOC) Identification	Migration	12/03/21	12/13/21
21-070	Wave 1&2 Counties select their Change Network Champions	CalWIN Change Network Champion selection for Wave 1 and 2 counties	OCM	12/06/21	12/17/21

There are currently no new CalSAWS Information Transmittals (CITs) for the reporting period.

Table 5 – CITs

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
N/A						

1.5 Activities for the Next Reporting Period

Project Management

- ▶ Continue planning for and onboarding staff resources.
- ▶ Continue to collaborate with other teams to coordinate information for the CalWIN Counties.
- ▶ Continue updating the County Work Plans for Wave 1 and produce Gantt timelines for all Waves.
- ▶ Continued gathering timelines for the Project teams for CalWIN County implementation activities.
- ▶ Submit the following Deliverables:
 - DEL 04.01: Business Process Reengineering Plan – Wave 1 (Contra Costa) FDEL on 12/20/21.
 - DEL 04.02: Business Process Reengineering Plan – Wave 1 (Placer) FDEL on 12/20/21.
 - DEL 04.03: Business Process Reengineering Plan – Wave 1 (Yolo) FDEL on 12/20/21.

Business Process Reengineering (BPR)C

- ▶ Continue prep for the To-Be sessions for Santa Cruz and Solano Counties.

CalSAWS – California Statewide Automated Welfare System (CalSAWS)

CalWIN Implementation Support Phase

Weekly Status Report, December 15, 2021

Reporting Period: December 13, 2021 to December 19, 2021

- ▶ Submit Wave-1 County-Specific BPR Plan FDELS.
- ▶ Complete Leadership Visioning for Santa Cruz and Solano Counties.
- ▶ Begin planning for the To-Be BPR sessions for San Mateo and San Diego Counties.

Organizational Change Management (OCM)

- ▶ Incorporate feedback from the OCM Leads and QA team for the draft of the DEL 06: County Communication Plan Draft Deliverable (DDEL).
- ▶ Test and refine the approach to the Change Discussion Guides with input from the OCM Leads, QA, and the BPR team.
- ▶ Continue to refine the CNC kickoff presentation with the OCM Leads and QA.
- ▶ Prepare the DEL 07: Change Discussion Guide DDED.
- ▶ Schedule dry-run sessions for the CNC kickoff.

Training

- ▶ Participate in the UAT Planning and Approach meeting with the Customer Engagement Team on 12/21/21.
- ▶ Continue training development, creating instructional design documents for the CalSAWS Instructor-Led Training curriculum.
- ▶ Continue development of the Learning Journey Maps.

Implementation Support Services

- ▶ Continue to update the overall Implementation approach and Work Plan with the Customer Engagement Team.
- ▶ Conduct Wave 1 County-specific Implementation work plan meetings (Contra Costa rescheduled for 12/29/21).
- ▶ Update the County-specific Work Plans based on Wave-1 County-specific feedback and distribute to Placer County and Yolo County the week of 12/20/21.
- ▶ Follow up with the Conversion Team regarding planning the application security requirements and timeline (items specific to CalWIN emails).
- ▶ Develop Case Review Guides (CRGs) and update reporting requirements specific for CRG #3 Update Provider Name Information based on CalWIN screenshots received.
- ▶ Schedule and conduct ongoing cross-project meetings for the App Dev, Consortium, ISS, and Customer Engagement teams.
- ▶ Plan and create materials for the Wave 1 meeting on 01/05/21 and prepare for the Implementation Point of Contact (IPOC) Kick-Off meeting in January 2022.
- ▶ Participate in ongoing meetings with DD&I and the Consortium for conversion, imaging, API user groups, App Dev, and DDID.

1.6 Deviations from Plan/Adjustments

- ▶ None for the reporting period.
