



CalSAWS DD&I Weekly Status Report

Reporting Period: June 13, 2022 to June 19, 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

1.0	Project Management	3
1.1	Project Deliverables Summary	3
1.2	Highlights of the Reporting Period	3
1.2.1	Project Management	3
1.2.2	Communications Management	6
1.2.3	Cultural Transformation	7
1.2.4	Inclusion, Diversity and Equity Advancement (IDEA)	7
1.3	CRFI/CIT Communications Information	8
1.4	Activities for the Next Reporting Period	9
1.4.1	Project Management	9
1.4.2	Communications Management	10
1.4.3	Cultural Transformation	10
1.4.4	Inclusion, Diversity & Equity Advancement (IDEA)	10
1.5	Deviations from Plan/Adjustments	10
2.0	Imaging	11
2.1	Highlights of the Reporting Period	11
2.2	Activities for the Next Reporting Period	14
2.3	Deviations from Plan/Adjustments	14
3.0	Customer Service Center (CSC)	14
3.1	Highlights of the Reporting Period	14
3.2	Activities for the Next Reporting Period	16
3.3	Deviations from Plan/Adjustments	16
4.0	Application Development and Test	16
4.1	Highlights of the Reporting Period	16
4.1.1	Application Development Summary	17
4.1.2	Design Difference Identifiers (DDID) System Test Status	17
4.1.3	Task Management	20
4.1.4	Application Programming Interface (API)	20
4.1.5	General Assistance/General Relief (GA/GR)	21
4.1.6	CalWIN Wave 1 Batch Performance	21
4.1.7	Case Purge	22
4.1.8	Deliverable Management	24

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase



Weekly Status Report Period: June 13, 2022, to June 19, 2022

4.2	Activities for the Next Reporting Period	24
4.3	Deviations from Plan/Adjustments.....	24
5.0	Conversion	25
5.1	Highlights of the Reporting Period	25
5.1.1	CalWIN Conversion	25
5.1.2	CalWIN Conversion Defects Converted Data Test Defect	26
5.1.3	Gainwell Technologies	26
5.1.4	Ancillary Systems Conversion.....	26
5.1.5	Deliverable Management.....	30
5.2	Activities for the Next Reporting Period	30
5.2.1	CalWIN Conversion	30
5.2.2	Gainwell Technologies	30
5.2.3	Ancillary Systems Conversion.....	30
5.2.4	Deliverable Management.....	30
5.3	Deviations from Plan/Adjustments.....	30
6.0	CalWIN Functional Support	31
6.1	Highlights of the Reporting Period	31
6.2	Activities for the Next Reporting Period	32
6.3	Deviations from Plan/Adjustments.....	33
7.0	Technical Infrastructure.....	33
7.1	Highlights of the Reporting Period	33
7.2	Activities for the Next Reporting Period	34
7.3	Deviations from Plan/Adjustments.....	35
8.0	Appendices.....	36

1.0 Project Management

1.1 Project Deliverables Summary

Table 1.1-1 – Overall Summary of Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	TEAM	STATUS [1]	STATUS
71	CalACES Migration Final Acceptance Certification	PMO		<ul style="list-style-type: none"> Received approval of the Final Deliverable (FDEL) on June 13, 2022
76	CalSAWS Migration Work Plan Update #38	PMO		<ul style="list-style-type: none"> Submitted the FDEL on June 13, 2022 Received approval of the FDEL on June 17, 2022

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

1.2 Highlights of the Reporting Period

Table 1.2-1 – CalSAWS Project Management Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Project Management	<ul style="list-style-type: none"> Received approval for Deliverable #71, CalACES Migration Final Acceptance Certification, on June 13, 2022

1.2.1 Project Management

- ▶ Continued CalSAWS DD&I Facility Management activities, including:
 - Key initiatives related to facilities at the Rancho Cordova Project Office are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) below

Table 1.2.1-1 – Key Facility Initiatives/Projects

ITEM #	INITIATIVES/ PROJECTS	LOCATION	TARGET DATE	NOTES/STATUS
1	Return to Office (RTO)	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> Continued reviewing and processing Return to Office (RTO) Approval Request forms submitted by CalSAWS Project staff, which are required to access the CalSAWS Rancho Cordova or Norwalk Project offices Continued to monitor and review requests from CalSAWS Project staff who are interested in returning to the CalSAWS Rancho Cordova and Norwalk Project offices on a hybrid schedule Continued to assess updates to Federal, State, and local policies and ordinances for the CalSAWS Project's return to office processes
2	Large Meeting Requests	Rancho Cordova and Norwalk Project Offices	Summer 2022	<ul style="list-style-type: none"> Continued planning facility capacity and equipment needs for requested on-site meetings <ul style="list-style-type: none"> CalWIN ISS Train-the-Trainer sessions scheduled for June 13 – July 15, 2022 CalSAWS Leadership Alignment meetings for June 15, 2022 Imaging UAT sessions scheduled for July 11-15, 2022

- ▶ Completed preparations and participated in the Section Directors Meeting that was held on June 14, 2022
- ▶ Continued CalSAWS Risk Management activities, including:
 - Continued to work with risk and issue owners to develop and update mitigation plans for the accepted CalSAWS DD&I Project risks and issues
- ▶ Continued supporting engagement of project staff working remotely, including:
 - Continued development of the monthly CalSAWS Connect newsletter that will be submitted to the CalSAWS Project Team on July 14, 2022
 - Facilitated the CalSAWS All Staff Meeting that was held on June 15, 2022
- ▶ Continued discussions with the Consortium regarding the development of high-level Gantt charts for the CalSAWS Project and continued reviewing potential tools that may be used to create the CalSAWS Integrated Gantt charts
- ▶ Continued performing Contract Management activities for the CalSAWS DD&I Project
 - Continued development of contract Change Notice No. 19, which is planned to be submitted to the CalSAWS JPA Board of Directors for approval on July 22, 2022 and may include use of the contract's R&A Change Budget Services allocation for:

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

- An extension of CalWIN Functional Support through October 2023
- Additional CalSAWS enhancements during State Fiscal Year (SFY) 2022/23 related to CalFresh over-issuances, the Transitional Housing Supplement, removal of the Homeless Assistance asset limit, CalFresh Simplifications, and Medi-Cal redetermination forms
- Technical updates to shift funds from SFY 2021/22 to 2022/23 for enhancements related to the Elderly Simplified Application Project (ESAP), Stage One Continuous Eligibility, and the CalFresh Public Assistance Definition Alignment
 - o Continued planning the implementation of requirements from the DHCS and CDSS Privacy and Security Agreements (PSAs) that were approved by the JPA Board of Directors on April 16, 2021
- ▶ Continued to support the logistical planning of the virtual CalSAWS JPA Annual Conference/Member Representatives Meeting that is scheduled for June 23, 2022
- ▶ Continued to support the logistical planning of the virtual CalSAWS JPA Business Meeting that is scheduled for June 30, 2022
- ▶ Continued performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.2.1-2 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
71	CalACES Migration Final Acceptance Certification	<ul style="list-style-type: none">• Received approval of the FDEL on June 13, 2022
76	CalSAWS Migration Work Plan Update #38	<ul style="list-style-type: none">• Finalized and submitted the Final Deliverable (FDEL) to the Consortium for review and feedback on June 13, 2022• Facilitated a touchpoint meeting with Deliverable reviewers on June 17, 2022 to address questions and comments for the FDEL, as needed• Received approval of the FDEL on June 17, 2022

1.2.2 Communications Management

- ▶ CalSAWS Communications Management activities including
 - Continued to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy
 - Continued oversight and management of Power of 58 materials
- ▶ CalSAWS External Website (www.calsaws.org)
 - Continued the administration and support of the CalSAWS external website
 - See Table 1.2.2-1 for details on website support activities


Table 1.2.2-1 – Website Support Activities

TASK	DATE (S)	TASK TYPE
None for the reporting period		

Table 1.2.2-2 – CalSAWS.org Usage Statistics

CATEGORY	DURING REPORTING PERIOD	SINCE LAUNCH
Total Number of Subscribers	25	2,177
Total Number of Unique Users	11,845	1,533,253
Total Number of New Users	9,055	1,533,253
Total Number of Sessions (Individual site visits)	15,609	2,157,949
Average Number of Sessions per User	1.32	1.42
Average Number of Page Views per Session	1.36	1.31
Average Session Duration	0:51	0:56
AskCalSAWS Inquiries – Received/Resolved	10/14	763/749

Figure 1.2.2-1 – Overall CalSAWS.org Usage Trend

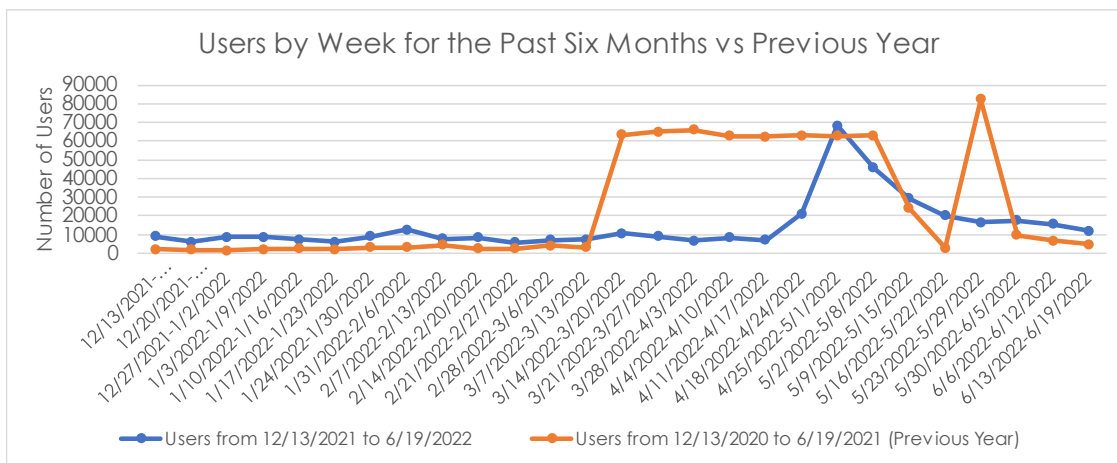

Note:

Increase in usage from the Previous Year (from March 14, 2021 to May 15, 2021) was investigated to be from cities in the United States

Table 1.2.2-3 – CalSAWS.org Subscription Service Statistics

WEBPAGE	PERCENT OF SUBSCRIBERS
Latest News – CalSAWS Buzz Newsletter	32%
Latest News – News	25%
Other Updates – System Updates	22%
Other Updates – Careers	21%
CalSAWS Committees – CalWORKs/CalFresh	21%

1.2.3 Cultural Transformation

- ▶ Shared the Cultural Transformation updates video at the June 18, 2022 CalSAWS Member Representatives meeting
- ▶ Continued planning the rescheduled first talk in the Growth and Mindset Conversation series: "Fueling Innovation in a Policy Driven Environment" currently scheduled on July 14, 2022
 - Scheduled a dry run for July 11, 2022
- ▶ Scheduled the next Cultural Ambassador meeting for June 30, 2022

1.2.4 Inclusion, Diversity and Equity Advancement (IDEA)

- ▶ Co-Create Phase
 - Leadership
 - Continued to prepare for the session that we have with BOLD to plan for the July leadership coaching session
 - Sent out sign-up sheet to all Leads at CalSAWS
 - CalSAWS "We Are One" SharePoint Site
 - Continued to update the "We Are One" website tab
 - Pulse Survey
 - Continued to prepare the video for the next JPA Board of Directors meeting, which includes the pulse survey analysis
 - CalSAWS Table Talks
 - Discussing possible plans for August table talks session
 - Buddy Program
 - Sent out sign-up sheet to the CalSAWS – closing sign-up sheet June 24, 2022
 - Preparing to schedule kick-off meeting
 - Small Team Building
 - Continued to add feedback and consensus from the small team building to include in the JPA Board of Directors video
 - Employee Resource Groups (ERGs)
 - Held final prepare call for Black Employee Resource Group (BERG) Juneteenth celebration
 - Began discussing plans for a shared ERG session

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

- ▶ General
 - Continued to partner with the CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
 - Continued to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project
 - Continue to connect with the CalSAWS Culture Transformation team on combining videos for the CalSAWS JPA Board of Directors

1.3 CRFI/CIT Communications Information

- ▶ The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period ending June 19, 2022

Table 1.3-1 – CITs

CIT ID	SUBJECT	CATEGORY	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
0162-22	Wave 1 and 2 CalSAWS Infographics #3	Informational	June 13, 2022	Helen Cruz	Araceli Gallardo
0163-22	CalWIN Network Specifications and Recommendations	Informational	June 14, 2022	Melanie Gines	Matt Zior, and Uzair Naveed
0165-22	CalSAWS Targeted Topic Session: Tax Intercept	Informational	June 14, 2022	Helen Cruz	Araceli Gallardo
0170-22	CalWIN Central Print Postage Process	Informational	June 17, 2022	Julie Holmes	Geoff Cosner

- ▶ The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period ending June 19, 2022

Table 1.3-2 – CRFIs

CRFI ID	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	CalSAWS CONTACT
22-040	CalWIN readiness prerequisites for IPT and UAT	May 16, 2022	Open	July 1, 2022	Melanie Gines, and Llyod Rankine
22-042	CalWIN Counties BenefitsCal Options	May 17, 2022	Closed	June 17, 2022	Joel Acevedo
22-048	Change Network Champion (CNC) Identification for Wave 3 and 4 Counties	June 10, 2022	Open	June 24, 2022	Helen Cruz
22-049	Site Address Validation & Procurements	June 10, 2022	Open	July 1, 2022	Melanie Gines

- ▶ The following table outlines overdue CalSAWS Requests for Information (CRFIs) for the reporting period ending June 19, 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

Table 1.3-3 – Overdue CRFIs

CRFI ID	Subject	Region 1	Region 2	Region 3	Region 4	Region 5	Region 6
None							

1.4 Activities for the Next Reporting Period

1.4.1 Project Management

- ▶ Continue CalSAWS DD&I Facility Management activities, including:
 - Continue key initiatives related to facilities at the Rancho Cordova and Norwalk Project Offices, which are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) above
- ▶ Continue CalSAWS Risk Management activities, including:
 - Continue to work with risk and owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
- ▶ Facilitate the CalSAWS Weekly Status Meeting scheduled for June 22, 2022
- ▶ Participate in the Section Directors meeting that is scheduled for June 21, 2022
- ▶ Continue activities to support Project staff working remotely
 - Begin preparations and planning for the next monthly virtual CalSAWS Project All Staff Meeting that is scheduled for July 20, 2022
 - Continue developing the next monthly issue of the CalSAWS Connect newsletter that will be distributed to the CalSAWS Project Team on July 14, 2022
 - Continue developing Project communications, as needed
- ▶ Continue to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue process of reviewing tool capabilities for the high-level CalSAWS Integrated Gantt chart
- ▶ Continue performing Contract Management activities for the CalSAWS DD&I Project
- ▶ Continue performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.4.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the next reporting period	

1.4.2 Communications Management

- ▶ Continue to monitor usage and update materials as requested
 - See table 1.4.2-1 for planned website support activities
- ▶ CalSAWS Communications Management activities including:
 - Continue to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy:
 - Continue oversight and management of Power of 58 roll out

Table 1.4.2-1 – Website Support Activities

TASK	DATE(S)	TASK TYPE
None for the reporting period		

1.4.3 Cultural Transformation

- ▶ Continue to develop calendar of events for the ambassador initiatives through the end of the year
- ▶ Continue to provide project management support to Culture Ambassadors as they continue to develop the plans for the initiatives
- ▶ Continue to coordinate working sessions for each Ambassador group to progress their initiatives planning and discuss their individual contributions
- ▶ Continue to develop wellness initiative content to keep the project staff engaged
- ▶ Continue to update resources and a collaboration workspace with new relevant materials to support the implementation of the prioritized initiatives
- ▶ Continue to monitor Microsoft Teams channels for any help needed from Ambassadors

1.4.4 Inclusion, Diversity & Equity Advancement (IDEA)

- ▶ Continue to prepare Inclusion, Diversity & Equity Advancement (IDEA) progress video for the June JPA General Membership Conference
- ▶ Continue to partner with CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
- ▶ Continue to partner with our Cultural Transformation team to update the conference video with culture content
- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project

1.5 Deviations from Plan/Adjustments

- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project

2.0 Imaging

2.1 Highlights of the Reporting Period

Table 2.1-1 – CalSAWS Imaging Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> None to note for reporting period

Table 2.1-2 – CalSAWS Imaging Project Milestones

MILESTONES	DUE DATE	STATUS
Migration Activities		In progress
Conduct Tulare County Document Migration Discovery Session Check-in	June 13, 2022	Completed
Conduct Placer County Document Migration Discovery Session Check-in	June 14, 2022	Completed
Conduct San Diego County Document Migration Discovery Session Check-in	June 14, 2022	Completed
Conduct Fresno County Document Migration Discovery Session Check-in	June 15, 2022	Completed
Conduct Contra Costa County Document Migration Discovery Session Check-in	June 15, 2022	Completed
Conduct Yolo County Document Migration Discovery Session Check-in	June 16, 2022	Completed
Conduct Orange County Document Migration Discovery Session Check-in	June 16, 2022	Completed
Conduct San Mateo County Document Migration Discovery Session Check-in	June 17, 2022	Completed
Conduct Santa Clara County Document Migration Discovery Session Check-in	June 20, 2022	Scheduled
Conduct Alameda County Document Migration Discovery Session Check-in	June 20, 2022	Scheduled
Conduct Solano County Document Migration Discovery Session Check-in	June 21, 2022	Scheduled
Conduct Santa Barbara County Document Migration Discovery Session Check-in	June 21, 2022	Scheduled
Conduct San Diego County Document Migration Discovery Session Check-in	June 21, 2022	Scheduled
Conduct Placer County Document Migration Discovery Session Check-in	June 21, 2022	Scheduled

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

MIILESTONES	DUE DATE	STATUS
Conduct Santa Cruz County Document Migration Discovery Session Check-in	June 21, 2022	Scheduled
Conduct Contra Costa County Document Migration Discovery Session Check-in	June 22, 2022	Scheduled
Conduct Yolo County Document Migration Discovery Session Check-in	June 23, 2022	Scheduled
Conduct Orange County Document Migration Discovery Session Check-in	June 23, 2022	Scheduled
Conduct Ventura County Document Migration Discovery Session Check-in	June 23, 2022	Scheduled

Table 2.1-3 – CalWIN Counties’ Wave 1 Status Update

Wave 1	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Placer County	Begin	7/29/20	10/1/20	8/6/20	8/31/20	4/1/21	2/17/22	4/15/22 5/27/22	9/22/22	6/27/22	10/22/22	Go Live 10/31/22 75% Progress
	Finish	7/29/20	10/1/20	10/6/20	3/26/21	2/11/22	5/26/22	6/10/22 6/11/22	10/6/22	10/21/22	10/27/22	
	Critical Path	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Begin 9/22/22	Begin 10/20/22	Begin 10/22/22	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Wave 1	Target Dates	Project Charter Signoff	Mapping SS Completion	Req Document Completion	Document Keyword Mapping Sign Off	Solution/ Sample Build	Sample Testing	Bulk Export	Initial Import	Validate Images in Production	Bulk Delta	Final Batch	Go Live
Yolo County	Begin	12/3/22	1/6/22	1/24/22	1/6/22	2/1/22	3/21/22	4/11/22	5/14/22	9/22/22	10/11/22	10/28/22	Go Live 10/31/22 70% Progress
	Finish	12/7/22	1/20/22	1/31/22	1/31/22	3/17/22	4/8/22	5/12/22	5/16/22	10/6/22	10/21/22	10/29/22	
	Critical Path	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Begin 9/22/22	Begin 10/20/22	Begin 10/22/22	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Table 2.1-4 – CalWIN Counties’ Wave 2 Status Update

Wave 2	Target Dates	Project Charter Signoff	Mapping Completion	Doc/ Keyword Mapping Sign Off	Sample Testing	Complete Change Order	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Batch	Go Live
Contra Costa County	Begin	11/5/21	12/21/21	12/22/21	2/22/22	2/8/22	4/4/22	6/6/22	1/30/23	1/6/23	2/1/23	Go Live 2/27/23
	Finish	11/11/21	1/5/22	12/31/21	3/18/22	4/1/22 4/15/22	5/21/22 6/3/22	7/1/22	02/3/23	1/23/23	2/23/23	65% Progress
	Status	Completed	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

Wave 2	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Santa Clara County	Begin	10/15/20	12/1/20	1/17/22	5/11/22	8/8/22	09/12/22	11/07/22	1/19/23	1/30/23	2/23/23	Go Live 2/27/23 20% Progress
	Finish	10/15/20	1/20/22	4/29/22	6/20/22	9/9/22	11/04/22	11/30/22	2/2/23	2/23/23	2/26/23	
	Status	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Wave 2	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Tulare County	Begin	10/5/20	12/1/20	11/30/20	12/2/20	8/2/21	2/15/22	7/23/22	1/19/23	6/16/22	2/1/23	Go Live 2/27/23 70% Progress
	Finish	10/5/20	12/1/20	1/31/21	7/29/21	12/30/21	4/4/22	8/27/22	2/2/23	1/31/23	2/23/23	
	Status	Completed	Completed	Completed	Completed	Completed	Completed	Awaiting	Awaiting	In progress	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Table 2.1-5 – CalWIN Counties' Wave 3 Status Update

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Orange County	Begin	1/7/21	3/1/21	3/1/21	2/2/21	4/30/21	4/1/22 4/8/22	8/5/22	3/24/23	9/1/22	4/1/23	Go Live 4/24/23 60% Progress
	Finish	1/7/21	3/1/21	4/30/21	4/22/21	12/30/21	8/1/22	1/31/23	4/6/23	3/31/23	4/20/23	
	Status	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Santa Barbara County	Begin	1/19/21	3/1/21	3/1/21	2/18/21	1/15/22	8/1/22	11/01/22	3/24/23	11/1/22	4/1/23	Go Live 4/24/23 30% Progress
	Finish	1/19/21	3/1/21	9/31/21	09/31/21	7/31/22	10/31/22	12/30/22	4/6/23	3/31/23	4/20/23	
	Status	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

Wave 3	Target Dates	Kick Off	Identify Migration Method/ Vendor	Test Network	Document Mapping	Testing	Initial Export	Initial Import	Validate Images in Production	Bulk Delta	Final Delta	Go Live
Ventura County	Begin	1/19/21	3/1/21	3/1/21	2/18/21	6/30/21	4/4/22	9/2/22	3/24/23	9/3/22	4/1/23	Go Live 4/24/23 35% Progress
	Finish	1/19/21	3/1/21	4/30/21	5/31/21	3/31/22	8/31/22	10/21/22	4/6/23	3/31/23	4/20/23	
	Status	Completed	Completed	Completed	Completed	Completed	In progress	Awaiting	Awaiting	Awaiting	Awaiting	

Status: **Gray**: Completed; **Green**: On schedule, performing as planned; **Amber**: Potential delay/monitor with no material schedule impact; **Red**: Behind schedule and requires escalation

2.2 Activities for the Next Reporting Period

- ▶ Continue to manage the milestones for the Image Migrations in the tables above
- ▶ Continue to prepare for the User Acceptance Testing (UAT) Imaging Administration session scheduled to begin on July 11, 2022

2.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

3.0 Customer Service Center (CSC)

3.1 Highlights of the Reporting Period

Table 3.1-1 – CalSAWS Customer Service Center Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none">• Continued to test Task for Cancelling an Appointment in Outbound IVR (CA-25604) Service Change Request (SCR)
N/A	<ul style="list-style-type: none">• Continued discussion with Los Angeles County, Wave 1, Wave 2, and Wave 3 CalWIN Counties about migration to CalSAWS Contact Center Solution
N/A	<ul style="list-style-type: none">• Continued Build of Administration Page (CA-226672)

- ▶ Continued to test Task for Cancelling an Appointment in Outbound IVR (CA-25604) Service Change Requests (SCR)
- ▶ Continued discussion with Los Angeles County, Wave 1, Wave 2, and Wave 3 CalWIN Counties about migration to CalSAWS Contact Center Solution
- ▶ Began meetings with Wave 4 CalWIN Counties about migration to the CalSAWS Customer Service Center Solution
- ▶ Continued Build of Administration Page (CA-226672)
- ▶ Began build of Scheduled Callback (CA-229573)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

Table 3.1-2 – Customer Service Center Enhancement Milestones

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2292, 2697, 2698, 2723, 2724 WFM/QA/QM Reporting (CA-226209)	December 3, 2021	In Production	22.01
DDID 2718 Task for Cancelling an Appointment in Outbound IVR (CA-25604)	January 24, 2022	System Test	22.05 22.06.XX
DDID 2219, 2716, 2717, 2728 Outbound IVR - (CA-226207)	February 4, 2022	System Test	22.05 22.06.XX
DDID 2700 Enhanced CCP (CA-226844)	March 18, 2022	In Production	22.03 22.05.06
DDID 2727 Work-from-home Modifications (CA-227064)	March 18, 2022	In Production	22.03 22.05.06
DDID 2216, 2725 External Party Access IVR (CA-226839)	March 25, 2022	In Production	22.05
DDID 2211, 2217, 2218, 2220, 2729, 2730, 2731, 2046, 2732 Telephonic Signature (CA-226838)	April 1, 2022	In Production	22.05
DDID 2687, 2688, 2689, 2690, 2691, 2692, 2693, 2694, 2695, 2696, 2222, 2702, 2721, 2169, 2284, 2722 Admin Page (CA-226672)	June 30, 2022	In Development	22.05 22.07.XX
DDID 2701, 2706 Voice Authentication Languages (CA-226843)	July 29, 2022	In Development	22.07 22.08.XX
DDID 2699, 2210, 2705, 2707, 2708, 2709, 2710, 2711, 2712, 2713, 2714, 2715, 2719, 2720, 2258 Inbound IVR (CA-226837)	July 8, 2022	In Development	22.05 22.07.XX
DDID 2704 Post-Call Survey (CA-228023)	July 8, 2022	Approved	22.05 22.07.XX
DDID 2284 Scheduled Callback (CA-229573)	July 8, 2022	Approved	22.05 22.07.XX
DDID 2268 Display the CalSAWS Contact Center IVR Caller ID for outbound calls	August 5, 2022	Design in progress	22.07 22.08.XX

Table 3.1-3 – Los Angeles County Milestones

MILESTONES		DUE DATE	OWNER
1	Design completion	March 11, 2022	CalSAWS Project Team
2	Initial performance/load testing	March 18, 2022	CalSAWS Project Team
3	Training development	May 16, 2022	CalSAWS Project Team
4	Build and unit test	May 20, 2022	CalSAWS Project Team
5	Training content review	May 20, 2022	Consortium
6	System Test	June 3, 2022	CalSAWS Project Team
7	Training execution	June 6, 2022	CalSAWS Project Team
8	Conduct model office	June 13, 2022	Los Angeles County
9	Go-live	August 19, 2022	CalSAWS Project Team
10	Post go-live support	August 22, 2022	CalSAWS Project Team

3.2 Activities for the Next Reporting Period

- ▶ Continue discussions with Contra Costa, Los Angeles, Santa Clara, Tulare, Orange, Santa Barbara, and Ventura Counties for County-specific Interactive Voice Response (IVR) designs
- ▶ Continue build of System Change Requests (SCRs) CA-226843 Voice Authentication Languages and CA-226672 Administrative Page
- ▶ Continued build of Los Angeles County Amazon Web Services (AWS) Accounts and Contact Center Infrastructure (CA-240156)

3.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

4.0 Application Development and Test

4.1 Highlights of the Reporting Period

Table 4.1-1 – CalSAWS Application Development and Test Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
4.1.2 Design Difference Identifiers (DDID) System Test Status	<ul style="list-style-type: none"> • 22.07 DD&I System Testing on schedule. Week 3 of 8 completed. 41% pass rate on a 38% target

4.1.1 Application Development Summary

Table 4.1.1-1 – CalSAWS Application Development Summary

	Status	22.05	22.07	22.09	22.11	23.01	23.02	23.05
Design	New	0	0	4	2	10	1	8
	Design in Progress	1	0	4	1	0	0	1
	Ready for Committee	1	0	1	0	0	0	0
	Committee Review	0	0	0	0	0	0	0
	Pending Approval	0	0	0	1	1	1	2
Build	Approved	1	0	5	1	1	0	1
	In Development	0	0	3	0	1	0	0
	Development Complete	0	0	2	0	0	0	0
	In Assembly Test	0	0	0	0	0	0	0
Test	System Test	0	8	2	0	0	0	0
	Test Complete	0	1	0	0	0	0	0
	In Production	24	0	0	0	0	0	0
	Grand Total	27	9	21	5	13	2	12

System Change Requests (SCRs) in Production


919

Notes:

- This table includes Application Development System Change Requests (SCRs) with migration impact. SCRs in production represents a count of any SCR that have a project phase of migration and have been deployed to production
- Continued drafting designs and development activities. Status is provided in Table 4.1.1-1 (CalSAWS Application Development Summary), above

4.1.2 Design Difference Identifiers (DDID) System Test Status

Figure 4.1.2-1 – DDID System Test Status

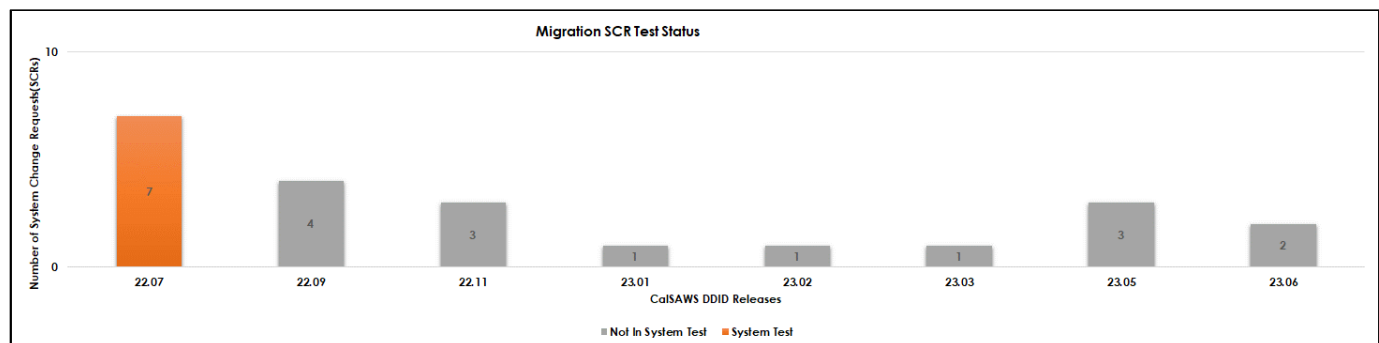

Notes:

- Includes all System Change Requests (SCRs) that have a funding source of CalSAWS DD&I that are not in "Rejected" or "Pending Rejection" status and are targeted for a baseline release. This includes SCRs associated to DDID 1967 for the unforeseen allowance and DDID 1631 for the reports allowance. In Production includes "In Production" status; Test

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022


Complete includes "Test Completed" status; System Test includes "System Test" status; Not in System Test includes all SCR statuses prior to System Test delivery

- Counts are higher in this chart (as compared with Design and Build Status) due to the inclusion of all CalSAWS DD&I System Change Requests (SCRs) targeted for the release, such as DD&I Training and Technical System Change Requests (SCRs)

Table 4.1.2-1 – DDID System Test Execution Status – 22.07

Pass rate target as of June 17, 2022	38%
Pass rate actual as of June 17, 2022	41%
System Test Completed date: July 20, 2022	

Figure 4.1.2-2 – DDID System Test Execution Status – 22.07

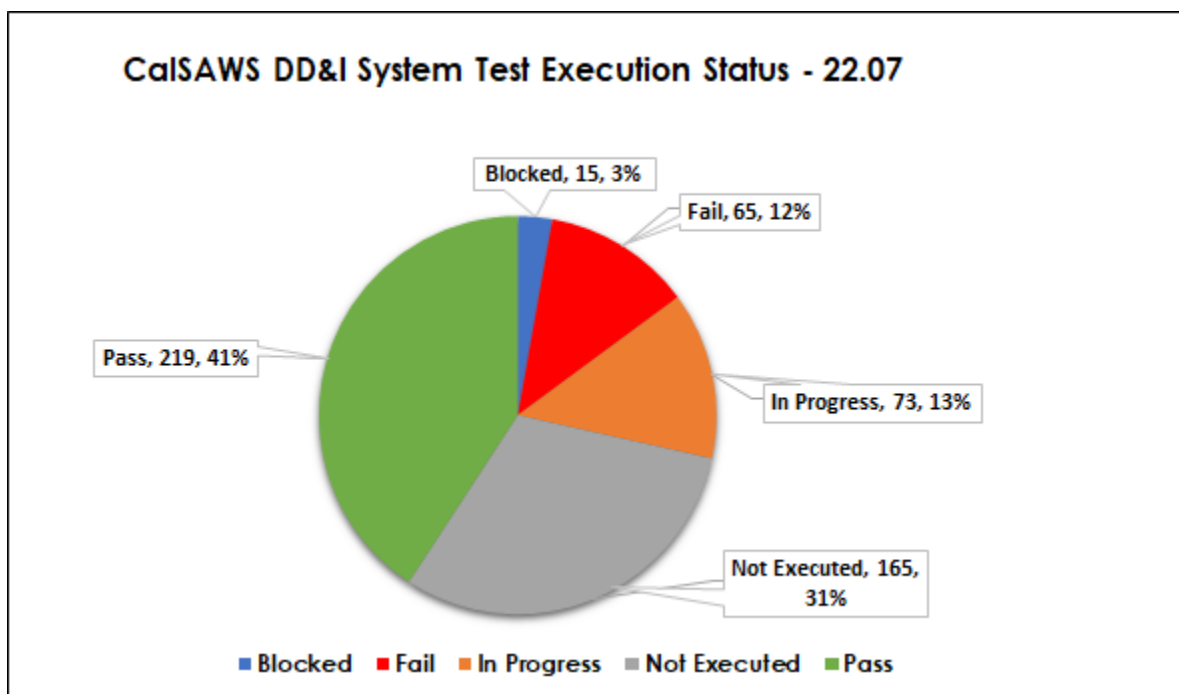

Note:

- Test Script counts are subject to change as test scripts are added or removed throughout the execution phase. Includes testing execution for all CalSAWS DD&I Test Scripts in the release

► Continued Test Execution for 22.07

Figure 4.1.2-3 – Overall GA/GR CalSAWS and Client Correspondence System Test Execution Status – 22.07



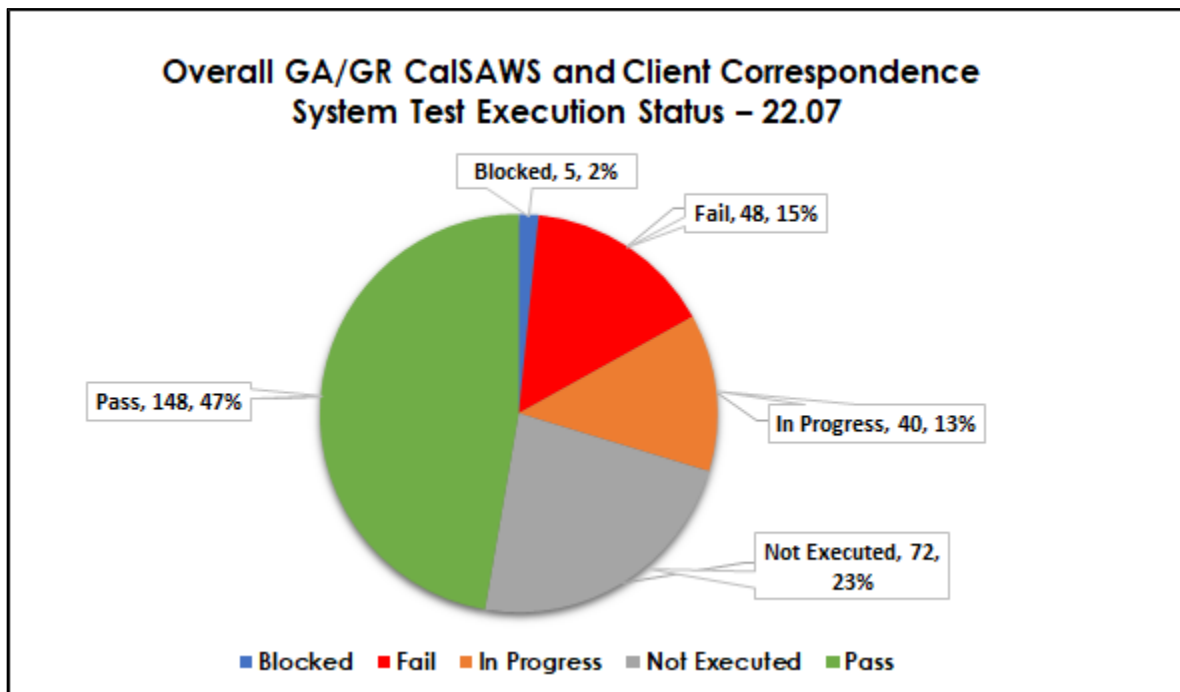


Table 4.1.2-2 - GA/GR System Test Execution Status by Area – 22.07

GA/GR CalSAWS	
Pass rate target as of June 17, 2022	38%
Pass rate actual as of June 17, 2022	43%
System Test completed date: July 20, 2022	

GA/GR Client Correspondence	
Pass rate target as of June 19, 2022	38%
Pass rate actual as of June 19, 2022	57%
System Test completed date: July 20, 2022	


Figure 4.1.2-4 – GA/GR System Test Execution Status by Area – 22.07

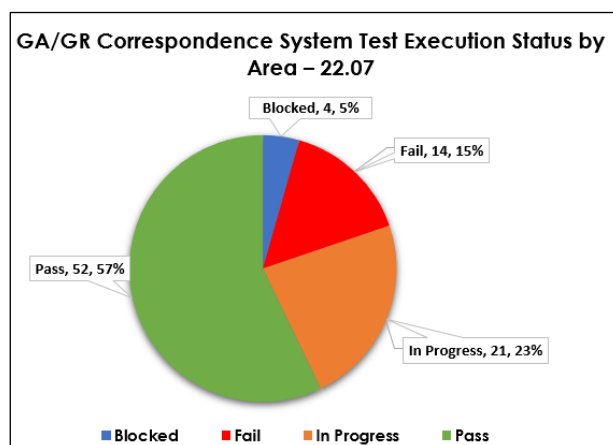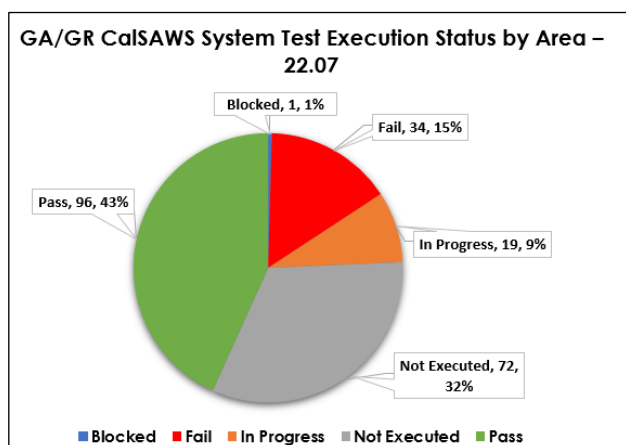

4.1.3 Task Management

- There are no Design Difference Identifiers (DDID) System Change Requests (SCRs) in the design/build phase


Figure 4.1.3-1 – Task Management Design Difference Identifiers (DDID) Status

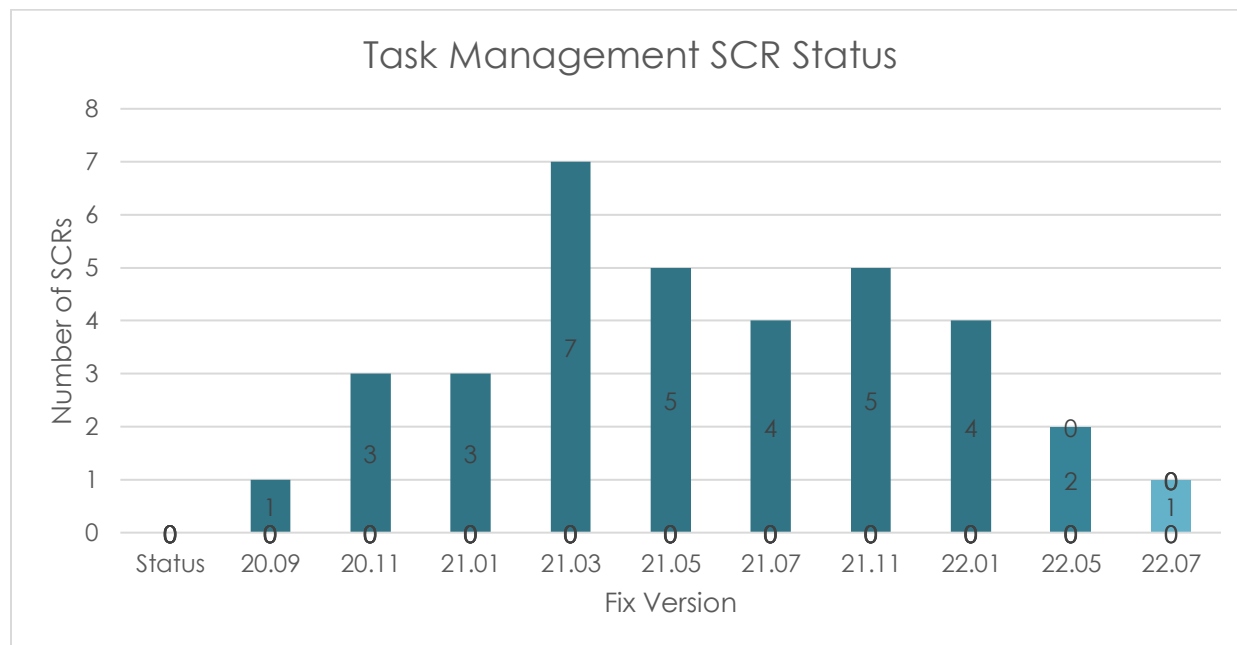

4.1.4 Application Programming Interface (API)

- Continued development on the following Application Programming Interfaces (APIs):
 - CA-214741 DDID 2298 – FDS: API - Person - MDM API


Figure 4.1.4-1 – Application Programming Interface (API) DDID Status

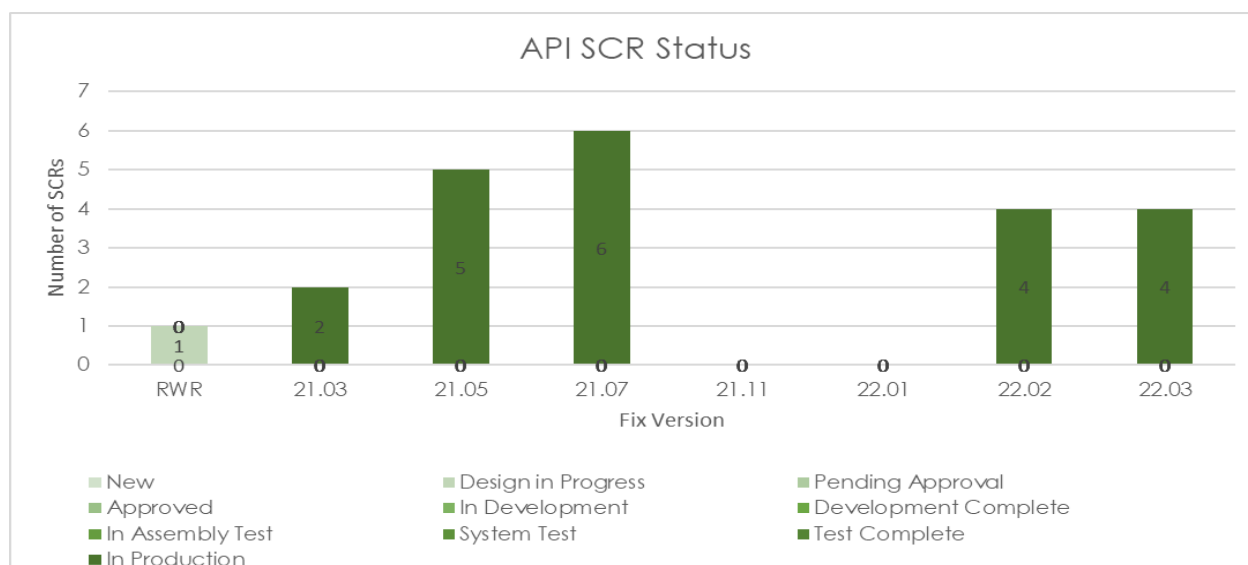

4.1.5 General Assistance/General Relief (GA/GR)

- General:
 - Provided the weekly status update and General Assistance/General Relief (GA/GR) release plan changes to Consortium on June 15, 2022
 - Discussed the General Assistance/General Relief (GA/GR) Correspondence web service design and web service clarifications on June 13, 2022, and June 15, 2022
 - Discussed Gainwell System Test status on June 15, 2022
 - Below GA/GR SCR's are in design
 - CA-242939: GA GR M&O Process for Correspondence Administration (documentation Only) (22.09)
 - CA-245148: GA GR Training Documentation (documentation Only) (22.09)
 - Continued with System Test support for the below SCR's
 - CA-244108: GR Time on aid page changes
 - CA-245506: CA-226398 Batch Sync Recommendations
 - CA-245253: Implement Additional Miscellaneous Parameters for EDBC-triggered Reason Codes

Figure 4.1.5-1 – GA/GR Design Difference Identifiers (DDID) Status

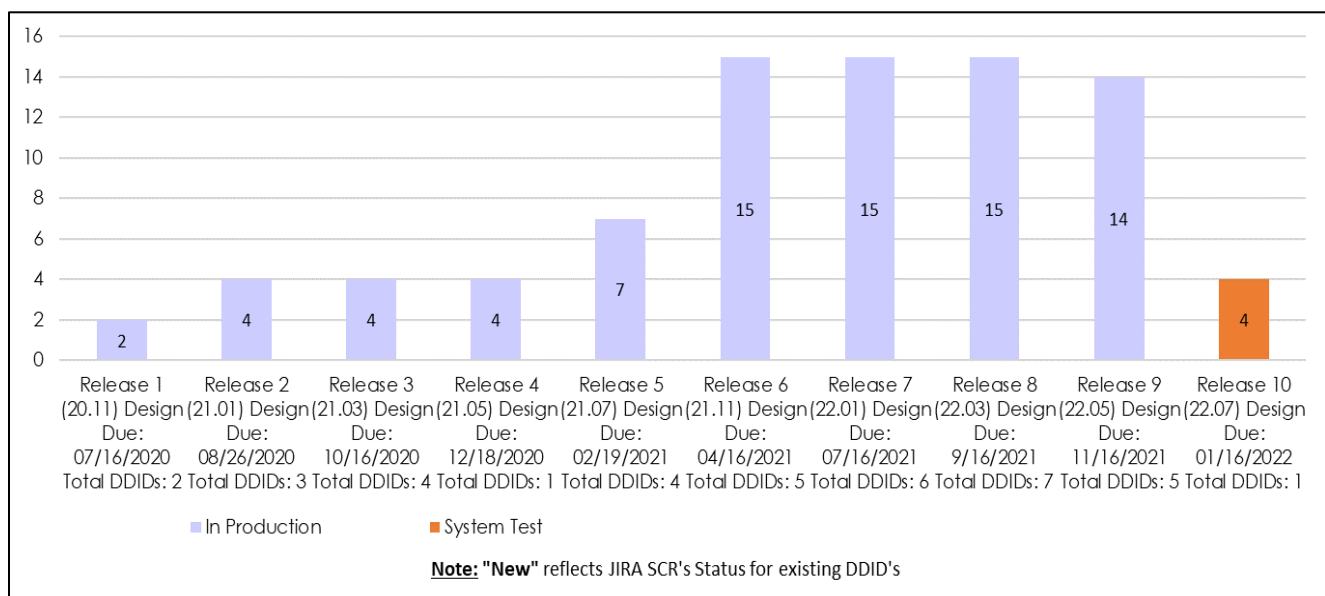

4.1.6 CalWIN Wave 1 Batch Performance

- The CalWIN Wave 1 Batch Performance effort (CA-217183) began on June 6, 2022
 - Golden Data Set (GDS) 7 loaded into the Batch Performance database
 - Automated test team ran scripts to create data for Counties in the environment
 - Executed 43* County Batch
- The second run of Batch Performance for Wave 1 showed great improvements for the issues identified during the first run. Even though the run exceeded the target 10-hour window, all jobs were complete by the 9-hour mark except for 10 jobs. The analytics set up issue was the cause of these jobs running beyond the batch window
 - Issuance Threads ran into an issue with query management due to an identified

Oracle bug. Configuration changes (CA-246501) were applied, and the issuance threads ran in 8 minutes

- o The analytics process ran into a configuration issue during set up which delayed the process from starting for approximately 1 hour. Steps have been taken to prevent this issue in future runs

*The Wave 1 Conversion will only include 42 Counties. However, GDS 7 still included Contra Costa County, so the first few performance tests will continue to include all 43 counties for testing purposes

Table 4.1.6-1- CalWIN Wave 1 Batch Performance Schedule and Results

Performance Cycle	Start Date	End Date	Run Time	Performance Defects
End of Month	June 6, 2022	June 19, 2022	(Run 1) 11 hours, 26 minutes	CA-243987 CA-246501 CA-235524
			(Run 2) 10 hours, 39 minutes	
First day of the Month	June 20, 2022	July 3, 2022	TBD	
Main Payroll	July 4, 2022	July 17, 2022	TBD	
High volume forms process	July 18, 2022	July 31, 2022	TBD	
Interface Outbound files	July 18, 2022	July 31, 2022	TBD	
10-day cutoff	August 1, 2022	August 14, 2022	TBD	
Interface Inbound files	August 15, 2022	August 28, 2022	TBD	

4.1.7 Case Purge

In July 2020, a team was formed to design, build, test, and deploy a Case Purge solution for C-IV and CalSAWS. This Purge functionality is based on the records retention policy approved by the CalSAWS Project Steering Committee in September 2019. The Purge team is using the Agile methodology for this effort and is deploying functionality to Production at the conclusion of each Sprint. This team is operating independently of the existing Design, Application Development, Training, and Test teams

- Continued Design and Development for Sprint 9 features that will be included in the 22.07 baseline System Change Requests (SCRs). This release includes the following items and will be deployed to production with the 22.07 release on July 25, 2022:
 - o Sprint 9 SCR CA-235667
 - Create Image Removal process for images associated with cases identified for Data Removal
 - Create Document Removal process for the CalSAWS Disaster Service Repository
 - Update Imaging Server with new deletion Image function to allow for the removal of an image record given a document identification
 - Update the Imaging Client Service Application Programming Interface (API) to allow for the new deletion Image function

- Update API gateway with new URL to allow for the new deletion Image transaction

Figure 4.1.7-1 – Case Purge Burndown Chart



Table 4.1.7-1 – Planned Purge Sprints

SPRINT NUMBER	SPRINT DESCRIPTION
Sprint 1	Porting Case Summary page updates, Case Data Removal page updates
Sprint 2	Add Case Locking, Image View only
Sprint 3	Porting the Identification sweep logic, adding new Eligibility Determination Benefit Calculation/Recovery Account (EDBC/RA) Rules to Identification Sweeps, Porting Portable Document Format (PDF) Generation Process, Increasing Journal Portable Document Format (PDF) Character Limit
Sprint 4	Porting Case Deletion Logging process, adding new CalHEERS tables to Deletion Model, Remove Recovery Account Responsible Party tables from Deletion Model
Sprint 5	Porting Case Identification and Override Reports, Port Document Removal process to S3, Create Stored Procedure Database Change Requests (DBCRs), Schedule Batch for Journal Portable Document Format (PDF) Re-run
Sprint 6	Creating CalSAWS Re-Verification Batch, Updating Identification and Re-Verification logic to include new Recovery Account rules, Updating Document S3 storage service framework, Updating Identification Batch to exclude CS program
Sprint 7	Porting Time Limit Aid Summary page changes, Porting Case Completion Report, Updating Deletion Model to include Residential and Receipt tables,

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

SPRINT NUMBER	SPRINT DESCRIPTION
	Updating CalSAWS page to validate and block CalHEERS referrals, Combining Document and Imaging removal process with Data Removal Batch, Updating Benefits Cal page to validate for removed cases during linkage
Sprint 8	OBIEE Cleanup for Delete Track, Updating Batch to Verify Lawful Presence (VLP)
Sprint 9	Image Deletion, Porting for Disaster Recovery Document Deletion
Sprint 10	Performance Environment Preparation and Execution
Sprint 11	Batch Scheduling, Case Purge Transition

4.1.8 Deliverable Management

Table 4.1.8-1 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

4.2 Activities for the Next Reporting Period

- ▶ Continue drafting designs for Migration Impact System Change Requests (SCRs)
- ▶ Continue test execution for CalSAWS 22.07 Release

Deliverable Management

Table 4.2-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

4.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

5.0 Conversion

5.1 Highlights of the Reporting Period

Table 5.1-1 – CalSAWS Conversion Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
5.1.1 CalWIN Conversion	<ul style="list-style-type: none"> Completed Wave 1 Mock Cutover 1A and 1B Evaluating Mock Cutover Action Items and Results until July 1, 2022 Delivered GDS 8 on June 20, 2022 for County Data Validation (CDV) per baseline schedule Currently supporting CDV until July 1, 2022

5.1.1 CalWIN Conversion

- ▶ Continued to address Open and Unresolved Converted Data Testing (CDT) identified defects
- ▶ Completed Wave 1B (Go-Live) Mock Cutover
- ▶ Wave 1 counties as well as Contra Costa successfully participated in uploading their Ancillary Systems data as part of the Mock Cutover 1B Ancillary Systems data with the CalWIN core conversion.
- ▶ Began Golden Data Set (GDS) 9 Epic development and testing. This Epic focused on:
 - 22.05 and 22.07 production data structure and code value changes which impact Conversion Transformation logic
 - Identified and unresolved Converted Data Test (CDT) defects
 - General Assistance/General Relief (GA/GR) data structure and code value enhancements where Conversion Transformation logic also need be enhanced to convert GA/GR
 - Planned to be delivered on August 31, 2021

Table 5.1.1-1 – CalWIN Conversion Statistics Golden Data Set (GDS) 9 (June 2022 – July 2022)


Sprint	Total - Deferred Items	Sprint Duration		GDS#9								
				Item Status								
				0%	25%	30%	50%	75%	5%	100%	100%	0%
				Not Started	Analysis & Mapping in Progress	Ready for Consortium Review	Build In Progress	Ready for AT	On Hold	Completed (Tested)*	CNR	Deferred
Overall	215	6/6/2022	7/29/2022	87	28	0	5	14	0	31	0	0
GDS#9 Bugfix 1	96	6/6/2022	7/1/2022	50	19	0	3	13	0	11	0	0
GA/GR	70	6/6/2022	7/1/2022	48	3	0	0	0	0	19	0	0
GDS#9 Bugfix 2	15	7/5/2022	7/22/2022	14	0	0	0	0	0	1	0	0
22.5/22.07	34	7/5/2022	7/22/2022	25	6	0	2	1	0	0	0	0
Hardening	tbd	7/25/2022	7/29/2022	0	0	0	0	0	0	0	0	0

5.1.2 CalWIN Conversion Defects Converted Data Test Defect

Table 5.1.2-1 – Open Converted Data Test (CDT) Defects

Defect Delivery by Golden Data Set (GDS)	Priority 1	Priority 2	Priority 3/Priority 4	Total
GDS#8	2	54	14	70
GDS#9	0	59	5	64
Not Assigned	0	0	99	99
CDT Open Total	2	113	118	233

Figure 5.1.2-1– Open Converted Data Test (CDT) Defects by GDS

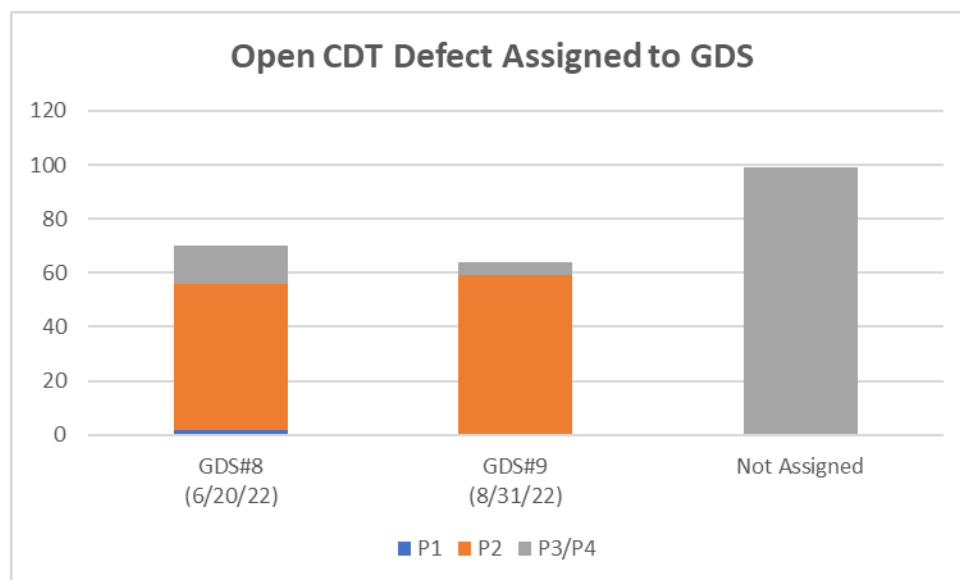

5.1.3 Gainwell Technologies

- ▶ CalWIN Document Migration
 - Continued planning for delivery of all Client Correspondence (CC)
 - Continued delivery of Client Correspondence (CC) from CalWIN

5.1.4 Ancillary Systems Conversion

- ▶ Continued to address issues found in production dataset size files. These files are necessary for CalWIN Core Conversion orchestration and integrations
- ▶ Facilitated exception reports review sessions with the Ancillary Counties to address questions and concerns
- ▶ Completed Wave 1 Mock Cutover with Contra Costa, Placer, and Yolo Counties. All data was received without any issues

Table 5.1.4-1 – County Status by Ancillary System

COUNTY	COLLECTIONS	FRAUD	TASK MANAGEMENT
Contra Costa	Design and build completed Received production sized files	N/A	N/A
Placer	Design and build completed Received production sized files	Design and build completed Received production sized files	Design and build completed Received production sized files
Yolo	Design and build completed Received production sized files	N/A	N/A
Santa Clara	N/A	N/A	Design and build completed Received production sized files
Tulare	Design and build completed Received production sized files	N/A	N/A
Orange	Design and build completed Received production sized files	Design and build completed Received production sized files	Design and build completed Received production sized files
Santa Barbara	N/A	N/A	Design and build completed Received production sized files
Ventura	Design and build completed Received production sized files	N/A	N/A
San Mateo	Design and build completed Received production sized files	N/A	Design and build completed Received production sized files
Santa Cruz	Design and build completed Received production sized files	N/A	Design and build in-progress Received production sized files
Solano	Design and build completed Received production sized files	N/A	N/A
Alameda	Design and build completed Received production sized files	Design and build completed Received production sized files	N/A
Fresno	Design and build completed	N/A	N/A


CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

COUNTY	COLLECTIONS	FRAUD	TASK MANAGEMENT
	Received production sized files		
Sonoma	Design and build completed Received production sized files	N/A	Design and build completed Received production sized files
Sacramento	N/A	Design and build completed Received production sized files	Design and build completed Received production sized files
San Francisco	Design and build completed Received production sized files	N/A	N/A
San Luis Obispo	Design and build completed Received production sized files	Design and build completed Received production sized files	N/A

Figure 5.1.4-1– Ancillary Systems Conversion Gantt Chart

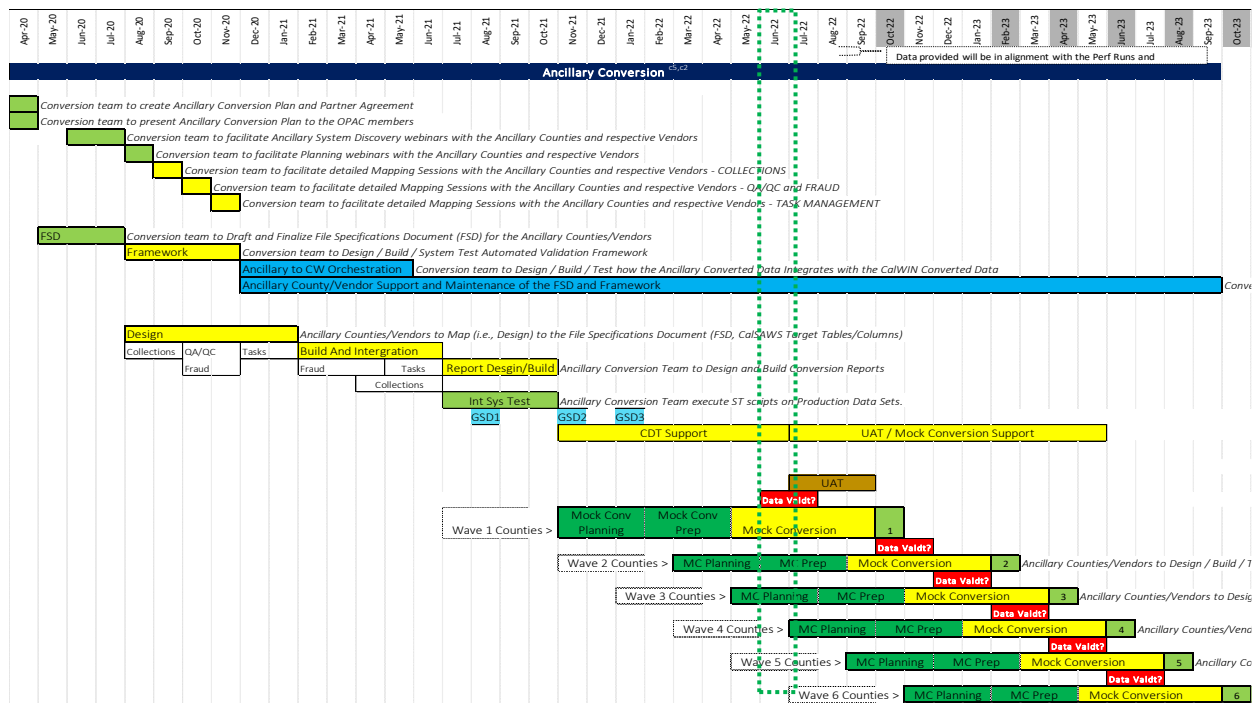

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: June 13, 2022, to June 19, 2022

Table 5.1.4-2 – Ancillary Systems Conversion Milestones

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
July 2020	Project Kick-Off/Discovery Sessions	Team introductions and Project overview	Completed
August 2020	File Specification Document (FSD)	CalSAWS DB (structures) as Conversion Target	Completed
August 2020	Project Planning	Detailed walkthrough of the Project schedule and File Specification Document (FSD)	Completed
December 2020	Automation Framework Complete	Exception handling for Ancillary provided Data is ready for the Counties	Completed
February 2021	Design/Mapping	All CalSAWS DB Targets (defined in FSD) have Source Mappings from Ancillary	Completed
July 2021	Build	Development activities, dependent Design Mapping, are ready to Start (or are Completed)	Completed
January 2022	System Test	System Test execution, dependent on test scripts and Build Completed, are ready to Start (or are Completed)	Completed
June 2022	Integration Test	End-to-End Test execution, dependent on test scripts, System Test Completed and CDT completed, are ready to Start (or are Completed)	Completed
August 2023	Mock Conversion Ancillary System Data Delivered	Counties to delivery Ancillary System Data to the CalSAWS Conversion team as a Prerequisite to begin Mock Conversions	In Progress
August 2023	Wave 1 – 6 Mock Conversions	Simulated Cutover Activities, dependent on Integration Test Completed, are ready to Start (or are Completed)	In Progress
August 2023	Wave 1 – 6 Mock Conversions Data Validation	Validation of Data, (from Mock Conversion), are ready to Start (or are Completed)	In Progress
October 2023	Wave 1 – 6 Conversion Cutovers	Execution of (live) Cutover Activities are ready to Start (or are Completed)	Not started

5.1.5 Deliverable Management

Table 5.1.5-1 – Conversion Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

5.2 Activities for the Next Reporting Period

5.2.1 CalWIN Conversion

- ▶ Continue to complete Jira epics and issue aligned with Golden Data Set (GDS) delivery schedule
- ▶ Continue development for the delivery of Golden Data Set (GDS) 9 Epic
- ▶ Continue activities for Mock Cutover

5.2.2 Gainwell Technologies

- ▶ CalWIN Data Migration
 - Continue planning for future CalWIN extractions
- ▶ CalWIN Data Retention M&O
 - Continue planning for future data retention runs

5.2.3 Ancillary Systems Conversion

- ▶ Continue ongoing support for mapping and data extract activities on Ancillary Collections, Fraud, and Task Management
- ▶ Continue to update the Ancillary Systems file specifications documents (as needed)
- ▶ Continue System Test scenario for automation development
- ▶ Review results for Wave 1 County Mock Cutover from June 11, 2022

5.2.4 Deliverable Management

Table 5.2.4-1 – Conversion Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

5.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

6.0 CalWIN Functional Support

6.1 Highlights of the Reporting Period

Table 6.1-1 – CalSAWS CalWIN Functional Support Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> None for the reporting period

- ▶ Supported Wave 1 CalWIN County Configuration and Process Simulation by collaborating with the Implementation Support Services (ISS) team on June 13-16, 2022 by:
 - Yolo County Configuration Verification on June 13 -14, 2022
 - Placer County Configuration Verification on June 15 -16, 2022
- ▶ Supported CalSAWS 3x Weekly Leadership meetings on June 13, June 15, and June 17, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Supported Implementation Support Services (ISS) Team Leads Meetings on June 14, 2022 to collaborate effectively
- ▶ Supported CalSAWS Leadership Alignment Working Sessions on June 15, 2022 to align with leadership on all open items for CalWIN
- ▶ Supported Post Deployment Support Model Planning meeting on June 13, 2022 to provide input to necessary post deployment support for CalWIN Counties
- ▶ Supported County Preparation Metrics on June 14, 2022 to stack hands on everything around metrics for County progress on County preparation phase activities
- ▶ Supported CalSAWS Project: Wave 2 Work Plan Update on June 14, 2022 to align all CalSAWS Project Readiness Tasks
- ▶ Supported CalWIN/CalSAWS Cutover Inter County Transfer (ICT) Plan Discussion on June 16, 2022 to finalize a plan for CalWIN to CalSAWS pre-cutover preparations as they relate to eICTs
- ▶ Supported Education Sessions for County Preparation on June 16, 2022 to plan County Education Sessions to prepare Counties for the upcoming County Preparation Phase activities
- ▶ Supported Sacramento County To-Be Business Process Reengineering (BPR) Sessions on June 13 -17, 2022, upcoming sessions include:
 - Kick-Off
 - Workload (Caseload) Management
 - Task Management and Imaging
 - Lobby Management
 - Application Registration / Intake
 - Appointment Scheduling / Management
 - Application Registration / Intake (Continued)
 - Hearings
 - Cash Assistance Program for Immigrants (CAPI)
 - Income Eligibility and Verification System (IEVS)

- ▶ Supported San Luis Obispo County To-Be Business Process Reengineering (BPR) Sessions on June 13 -17, 2022, upcoming sessions include:
 - Lobby Management
 - Imaging
 - Task Management / Workload Assignment
 - Application Registration and Intake
 - Application Registration and Intake (Continued)
 - Appointment Scheduling
 - Service Arrangements, Valuables, Resources

6.2 Activities for the Next Reporting Period

- ▶ Prepare for Wave 1 CalWIN County Configuration and Process Simulation by collaborating with the Implementation Support Services (ISS) team on June 20-24, 2022:
 - Placer County Process Simulation Working sessions on June 20, 2022
 - Yolo County Configuration Development sessions on June 20-24, 2022
 - Yolo County Configuration Meetings – Debrief and plan on June 20-23, 2022
- ▶ Prepare for CalSAWS 3x Weekly Leadership Meetings on June 20, June 22, and June 24, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Prepare for Implementation Support Services (ISS) Team Leads Meetings on June 21, 2022 to collaborate effectively
- ▶ Prepare for Training – Preparation Enablement Synchronization on June 22, 2022 to coordinate support for the ISS Training team's technology and laptop needs
- ▶ Prepare for Post Deployment Support Model Planning meetings on June 20, 2022 and June 24, 2022 to provide input to necessary post deployment support for CalWIN Counties
- ▶ Prepare for Sacramento County To-Be Business Process Reengineering (BPR) Sessions on June 20-24, 2022, upcoming sessions include:
 - Service Arrangements, Resource Databank (RDB), Valuables
 - Quality Assurance/ Quality Control (QA/QC)
 - Employment Services
 - Child Care
 - Help Desk
 - Fraud
 - Fiscal 101 Workshop
 - Homeless Assistance/Veterans Services
 - Inter County Transfer (ICT)
 - Employment Services (continued)
- ▶ Prepare for San Luis Obispo County To-Be Business Process Reengineering (BPR) Sessions on June 20-24, 2022, upcoming sessions include:
 - Inter County Transfer (ICT)
 - General Assistance (GA)
 - Employment Services
 - Employment Services (continued)
 - Fiscal 101 Workshop
 - General Overflow x2

- Prepare for Sacramento and San Luis Obispo Counties (SLO) To-Be BPR – Tuesday/Wednesday/Thursday de-brief on June 21-23, 2022, to debrief the sessions that have occurred throughout the week to make any necessary changes to plan or support feedback

6.3 Deviations from Plan/Adjustments

- None for the reporting period

7.0 Technical Infrastructure

7.1 Highlights of the Reporting Period

Table 7.1-1 – CalSAWS Technical Infrastructure Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
	<ul style="list-style-type: none"> • None for the reporting period

Figure 7.1-1 – Wave 1 County Network Connectivity Readiness Burndown


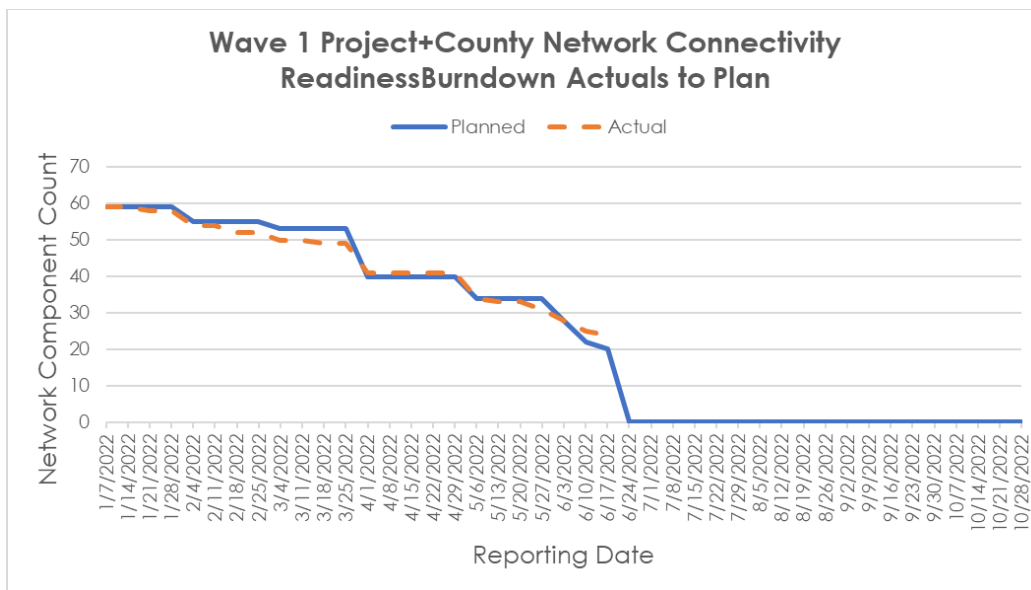


Figure 7.1-2 – Wave 2 County Network Connectivity Readiness Burndown

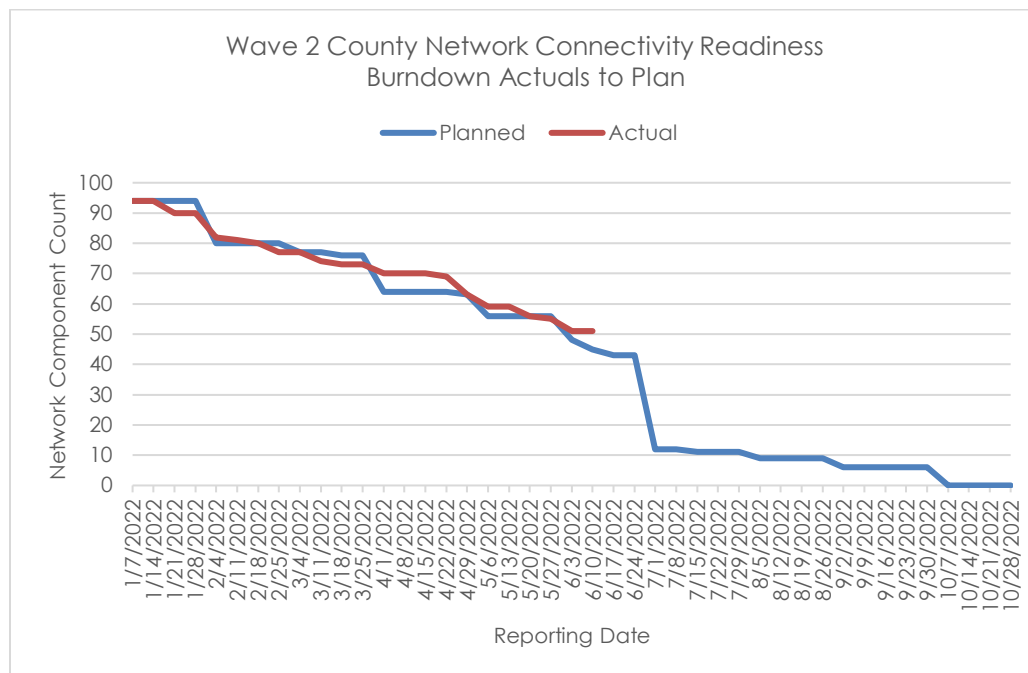

- ▶ Integration of Contra Costa and Placer County network with CalSAWS behind schedule due to partial / incomplete responses to CalSAWS Requests for Information (CRFI) 22-040
- ▶ Changes to deploy secondary routers to CalWIN Counties submitted for review
- ▶ CalWIN Wave 4 County Kick off meeting scheduled for Mid-July 2022
- ▶ Continued assessment of CalWIN County capacity forecasts and bearing on procured bandwidth
- ▶ CRFI 22-045 submitted to Wave 2-6 Counties for reconfirming their Point of Presence (POP) site addresses in lieu of Risk 272 and to avoid any last-minute changes to the POP locations
- ▶ CalSAWS Informational Transmittal (CIT) 0163-22 submitted for all CalWIN Counties to remind them of Risk 273 and ask to assess any local hardware procurement requirements and fast track them to avoid the supply chain issue

7.2 Activities for the Next Reporting Period

- ▶ CalSAWS Requests for Information (CRFI) for Security Assessment to be drafted
- ▶ Begin Interface Partner Testing (IPT)
- ▶ Implement configuration changes for enabling Secure File Transfer Protocol (SFTP), Batch and Database access for Wave 1 and 2 Counties
- ▶ Process Change orders to deploy redundant Cisco Routers for Wave 1 Counties
- ▶ Awaiting Wave 1 County response to Request for Information (CRFI) 22-040 by June 10, 2022
- ▶ Awaiting Wave 2 County response to Request for Information (CRFI) 22-040 by July 1, 2022

7.3 Deviations from Plan/Adjustments

- ▶ Santa Clara County has changed the designated Point of Presence (PoP) site location resulting in previously completed procurement and planning tasks having to be re-done. This will result in a 3-month impact to all downstream tasks and milestones for Santa Clara County unless mitigated
 - Mitigation:
 - Temporary installation of 4G connection (at additional cost) which will allow the County to complete pre-readiness and technical enablement tasks. This will isolate the County from being on-hold for 2 months. However, procured circuits will need to be delivered before beginning Interface Partner Testing (IPT) and User Acceptance Testing (UAT) testing
- ▶ Delivery date for Cisco routers required by CalWIN Wave 3-6 Counties has a lead time of greater than 90 days (ETA is September 2022). This poses an imminent risk for Wave 3 Counties. Anticipate a 2-month delay to overall timeline if not mitigated
 - Mitigation:
 - Wave 1 and 2 Counties have received the necessary equipment. If these 5 Counties are deployed with only 1 active Cisco router and retrofitted with second standby backup router when equipment becomes available or before go-live (earlier date), this would effectively mitigate the risk for Wave 3 Counties
 - CalSAWS will be recommending all Counties be aware of this risk associated with delivery timelines and to expedite any County Purchase orders that may have a bearing on the migration of the Counties to the CalSAWS System
- ▶ Placer County unable to complete tech readiness activities (CRFI 22-040) required for start of Interface Partner Testing (IPT) and Go-Live
 - Placer County has indicated that due to a conflicting firewall replacement project (County driven) that failed and being reattempted, the County would delay the configuration of technical changes requested by CalSAWS in CRFI 22-040 (Due on June 10, 2022)
 - Effort to re-deploy of the firewall and navigate through change process would be effort intensive causing the technical changes (CRFI 22-040) be postponed.
 - This would impact completion of technical readiness and start of Interface Partner Testing (IPT) by approximately 8 weeks (from June 27, 2022 until early August 2022)

8.0 Appendices

Appendix A – CalSAWS Deliverable Summary

Appendix B – CalSAWS Migration Work Plan Summary

Appendix C – CalSAWS DD&I Project Gantt Chart

Appendix D – CalSAWS Project Risks and Issues Report

