



CalSAWS Central Print Weekly Status Report

**Reporting Period: August 8, 2022, to August 14,
2022**

CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

Table of Contents

| | | |
|-----|---|---|
| 1.0 | CalSAWS Central Print Project | 2 |
| 1.1 | Highlights of the Reporting Period | 2 |
| 1.2 | Project Deliverable Summary | 4 |
| 1.3 | Project Risks and Issues | 6 |
| 1.4 | CRFI/CIT Communications Information | 6 |
| 1.5 | Activities for the Next Reporting Period..... | 7 |
| 1.6 | Deviations from Plan/Adjustments | 7 |

CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

1.0 CalSAWS Central Print Project

1.1 Highlights of the Reporting Period


Table 1.1-1 – CalSAWS Central Print Status Agenda Topics

| STATUS REPORT SUB-SECTION | STATUS AGENDA TOPIC |
|---------------------------|--|
| 1.1 | <ul style="list-style-type: none">Continued discussions with CalWIN Counties.Validation meeting with Orange County. |

Project Management

- Continued updates to project work plan.

Project Gantt

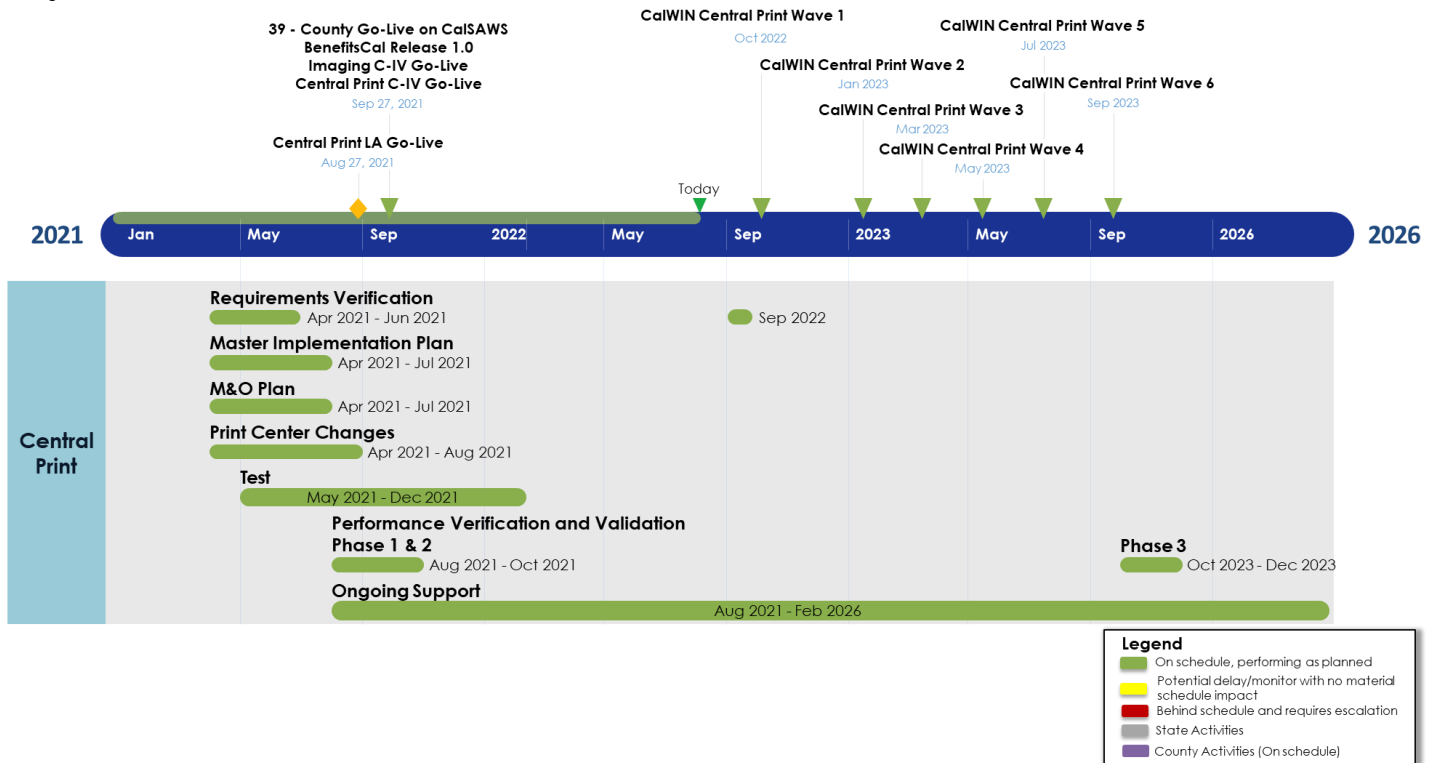


CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

Requirements Verification

- No Update

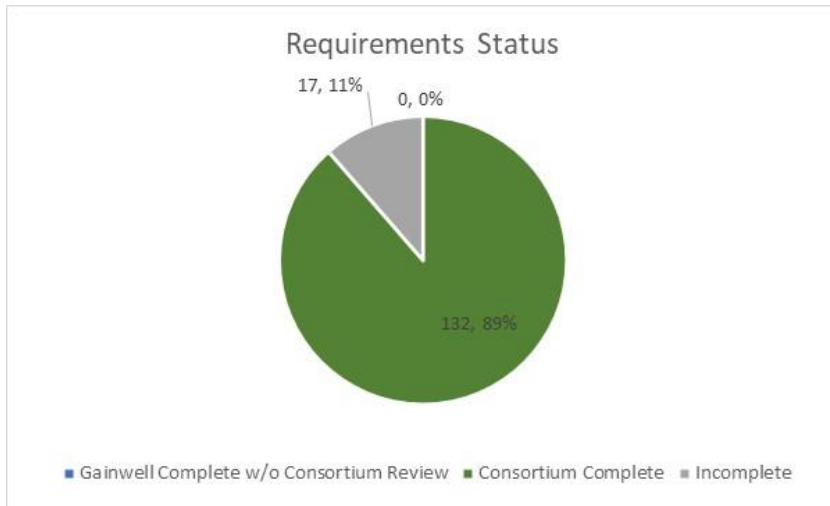

Master Implementation Plan

- Continued work on materials inventory management.
- Continued discussions regarding the metadata SCR.
- Continued discussions regarding the iText upgrade for CalSAWS.
- Continued discussions with Contra Costa County regarding Central Print configuration.
- Continued discussions with Santa Clara County regarding Central Print configuration.
- Continued discussions with Orange County regarding Central Print configuration.
- Continued discussions with Santa Barbara County regarding Central Print configuration.
- Continued discussions with Ventura County regarding Central Print configuration.
- Continued discussions with San Diego County regarding Central Print configuration.
- Continued discussions with San Mateo County regarding Central Print configuration.
- Continued discussions with Santa Cruz County regarding Central Print configuration.
- Continued discussions with Solano County regarding Central Print configuration.
- Conducted validation meeting with Orange County on 8/9/22.

Changes to Existing Print Centers

- No Update

Establishment of the SoCal Print Center

- No Update

Interface and File Considerations with CalSAWS

- No Update

Fulfillment Platform Configuration

- No Update


CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

Maintenance and Operations Plan

- ▶ Continued ongoing operations for Phase 2 (40 County) Central Print.
- ▶ Continued processing Los Angeles CW/CFR RD correspondences.
- ▶ Began processing MC RE correspondences.

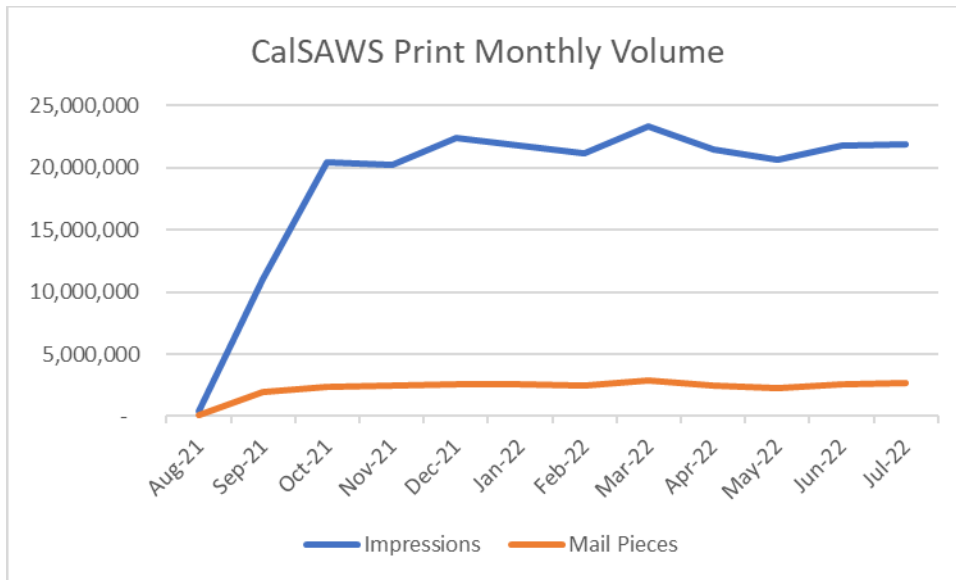

Comprehensive Testing

- ▶ No Update

Project Action Items – Overdue

- ▶ This table lists overdue action items, including the owner and due date.

| ID | Description | Owner | Due Date |
|------|--------------------------|-------|----------|
| None | No overdue actions items | | |

Table 1.1-8 – Overdue Action Items

1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below. Note that only the initial submission of the Monthly Status Report is listed in the table below. Each remaining Monthly Status Report will be submitted as an FDEL only per the date in the approved FDED and is not included in the list below.

Deliverable Status by Submission

| | | Complete | | Coming Soon | | |
|--------|-------------------------------|----------|---------|-------------|---------|---------|
| DEL ID | Deliverable Name | DDED | FDDED | DDEL | FDEL | Final |
| 01 | Monthly Status Report - March | 4/29/21 | 5/24/21 | 5/28/21 | 6/7/21 | 6/8/21 |
| 02 | Master Implementation Plan | 4/29/21 | 5/24/21 | 5/28/21 | 6/11/21 | 6/28/21 |

CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

| DEL ID | Deliverable Name | DDED | FDED | DDEL | FDEL | Final |
|--------|---------------------------------|---------|---------|----------|---------|----------|
| 03 | Maintenance and Operations Plan | 4/29/21 | 5/24/21 | 6/10/21 | 6/23/21 | 7/6/21 |
| 04 | Final Acceptance Report | 5/12/21 | 5/21/21 | 11/21/23 | 12/6/23 | 12/12/23 |

Table 1.2-1 – Deliverable Status for Current Reporting Period**Overall Deliverable Status**

| DEL # | DELIVERABLE NAME | STATUS | Next Deadline |
|-------|------------------------------------|-----------|---|
| 01 | Monthly Status Report – March 2021 | Completed | Each remaining Monthly Status Report will be submitted as an FDEL only per the date in the approved FDED and are not listed here. Any exceptions will be noted. |
| 02 | Master Implementation Plan | Completed | Received WAC approvals on 7/9/21. |
| 03 | Maintenance and Operations Plan | Completed | Received WAC approvals on 7/9/2021. |
| 04 | Final Acceptance | On-track | DDEL submission due 11/21/23 |

Table 1.2-2 – Upcoming Deliverable Deadlines

CalSAWS – Central Print Project


Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

Project Risks and Issues

| ID | Title | Details | Status | Impact | Severity | Date Logged |
|-----|---|---|--------|--------|----------|-------------|
| 255 | Global paper shortage may impact CalSAWS ability to print/mail correspondence | Due to the current global paper shortage, paper for envelopes and printing is in limited supply. This could result in delays in receiving shipments of envelopes and paper for printing affecting CalSAWS ability to produce timely correspondence. | Open | 4 | Medium | 11/2/2021 |

The following chart shows the number of risks currently open and previously closed, if applicable.

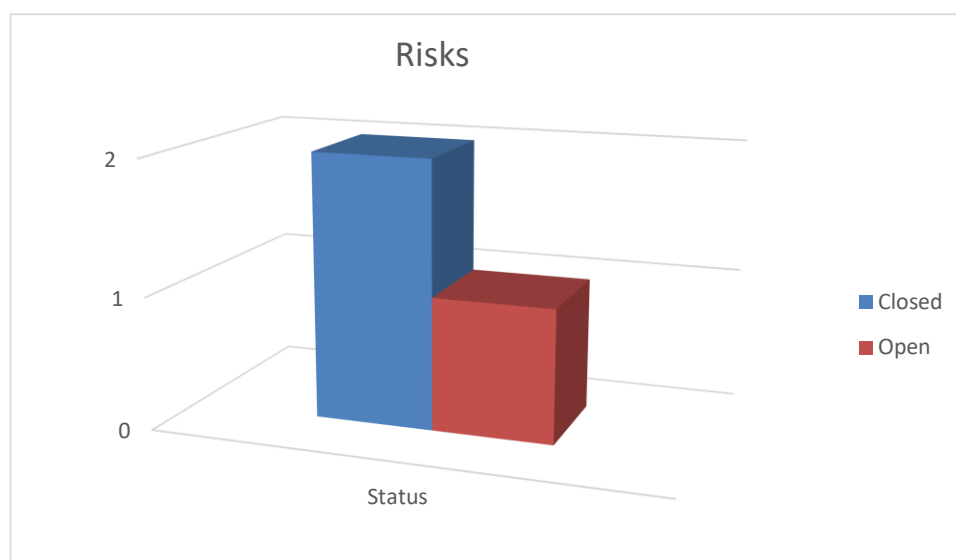

The following chart shows the number of issues currently open and previously closed, if applicable.

► Not applicable – No open or closed issues as of this status reporting period.

1.3 CRFI/CIT Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

There was no CalSAWS Information Transmittals (CITs).

| CIT ID | To | Subject | Category | Distribution Date |
|--------|----|---------|----------|-------------------|
| | | | | |

Table 1.4-1 – CITs

There was no CalSAWS Requests for Information (CRFIs).

CalSAWS – Central Print Project

Weekly Status Report, August 15, 2022

Period: August 8, 2022, to August 14, 2022

| CRFI ID | To | Subject | Distribution Date | Status | Response Due Date |
|---------|-----------------|---|-------------------|--------|-------------------|
| 22-065 | Wave 1 Counties | CalWIN Wave 1 Counties Central Print Portal Users | 8/4/22 | Open | 8/14/22 |

Table 1.4-2 – CRFIs

1.4 Activities for the Next Reporting Period

Project Management

- ▶ Continue updates to project work plan.

Requirements Verification

- ▶ No Update

Master Implementation Plan

- ▶ Continue work on materials inventory management.
- ▶ Continue discussions regarding the metadata SCR.
- ▶ Reschedule Configuration meeting with Santa Barbara County.
- ▶ Continue discussions with Contra Costa County regarding Central Print configuration.
- ▶ Continue discussions with Ventura County regarding Central Print configuration.
- ▶ Continue discussions with Orange County regarding Central Print configuration.
- ▶ Continue discussions with Santa Clara County regarding Central Print configuration.
- ▶ Schedule CalWIN Counties Wave 5 Kickoff meeting.

Changes to Existing Print Centers

- ▶ No Update

Establishment of the SoCal Print Center

- ▶ No Update

Interface and File Considerations with CalSAWS

- ▶ No Update

Fulfillment Platform Configuration

- ▶ No Update

Maintenance and Operations Plan

- ▶ Continue ongoing operations for Phase 2 Central Print.
- ▶ Continue processing of CW/CFR RDs for Los Angeles County.
- ▶ Begin processing of MC RE correspondence.

Comprehensive Testing

- ▶ No Update

1.5 Deviations from Plan/Adjustments

- ▶ No deviations from the plan are noted.
