



CalSAWS DD&I Weekly Status Report

**Reporting Period: October 3, 2022 to October 9,
2022**

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

1.0	Project Management	3
1.1	Project Deliverables Summary	3
1.2	Highlights of the Reporting Period	3
1.2.1	Project Management	3
1.2.2	Communications Management	5
1.2.3	Cultural Transformation	6
1.2.4	Inclusion, Diversity and Equity Advancement (IDEA)	7
1.3	CRFI/CIT Communications Information	7
1.4	Activities for the Next Reporting Period	9
1.4.1	Project Management	9
1.4.2	Communications Management	10
1.4.3	Cultural Transformation	10
1.4.4	Inclusion, Diversity & Equity Advancement (IDEA)	11
1.5	Deviations from Plan/Adjustments.....	11
2.0	Imaging	11
2.1	Highlights of the Reporting Period	11
2.2	Activities for the Next Reporting Period	13
2.3	Upcoming Performance Tests.....	13
2.4	Deviations from Plan/Adjustments.....	13
3.0	Customer Service Center (CSC).....	14
3.1	Highlights of the Reporting Period	14
3.2	Activities for the Next Reporting Period	15
3.3	Upcoming Performance Tests.....	15
3.4	Deviations from Plan/Adjustments.....	16
4.0	Application Development and Test	16
4.1	Highlights of the Reporting Period	16
4.1.1	Application Development Summary	16
4.1.2	Design Difference Identifiers (DDID) System Test Status	17
4.1.3	State and CalWIN Wave 2 County Interface Partner File Exchange Test (IPT)	17
4.1.4	Case Purge	18
4.1.5	Deliverable Management.....	20
4.2	Activities for the Next Reporting Period	20

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase



Weekly Status Report Period: October 3, 2022 to October 9, 2022

4.3	Upcoming Performance Tests.....	20
4.4	Deviations from Plan/Adjustments.....	21
5.0	Conversion	21
5.1	Highlights of the Reporting Period	21
5.1.1	CalWIN Conversion	21
5.1.2	CalWIN Conversion Defects (CDT, CDV, and UAT)	22
5.1.3	Gainwell Technologies	22
5.1.4	Ancillary Systems Conversion.....	23
5.1.5	Deliverable Management.....	25
5.2	Activities for the Next Reporting Period	25
5.2.1	CalWIN Conversion	25
5.2.2	Gainwell Technologies	25
5.2.3	Ancillary Systems Conversion.....	26
5.2.4	Deliverable Management.....	26
5.3	Deviations from Plan/Adjustments.....	26
6.0	CalWIN Functional Support	27
6.1	Highlights of the Reporting Period	27
6.2	Activities for the Next Reporting Period	28
6.3	Deviations from Plan/Adjustments.....	28
7.0	Technical Infrastructure.....	29
7.1	Highlights of the Reporting Period	29
7.2	Activities for the Next Reporting Period.....	31
7.3	Deviations from Plan/Adjustments.....	31
8.0	Appendices.....	33

1.0 Project Management

1.1 Project Deliverables Summary

Table 1.1-1 – Overall Summary of Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	TEAM	STATUS [1]	STATUS
72	CalSAWS Deployment Complete Milestone/Report – CalWIN Wave 1	Conversion		<ul style="list-style-type: none"> Draft Deliverable Expectation Document (DDED) is in progress Submission of the DDED is due on October 18, 2022
82	CalSAWS Migration Work Plan Update #42	PMO		<ul style="list-style-type: none"> Final Deliverable (FDEL) is in progress Submission of the FDEL is due on October 12, 2022

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

1.2 Highlights of the Reporting Period

Table 1.2-1 – CalSAWS Project Management Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Project Management	<ul style="list-style-type: none"> None to note for the reporting period

1.2.1 Project Management

- ▶ Continued CalSAWS DD&I Facility Management activities, including:
 - Key initiatives related to facilities at the Rancho Cordova Project Office are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) below

Table 1.2.1-1 – Key Facility Initiatives/Projects

ITEM #	INITIATIVES/ PROJECTS	LOCATION	TARGET DATE	NOTES/STATUS
1	Return to Office (RTO)	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> Continued reviewing and processing Return to Office (RTO) Approval Request forms submitted by CalSAWS Project staff, which are required to access the CalSAWS Rancho Cordova or Norwalk Project offices Continued to monitor and review requests from CalSAWS Project staff who are interested in returning to the CalSAWS Rancho Cordova and Norwalk Project offices on a hybrid schedule Continued to assess updates to Federal, State, and local policies and ordinances for the CalSAWS Project's return to office processes
2	Large Meeting Requests	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> Continued planning facility capacity and equipment needs for requested on-site meetings

- ▶ Completed preparations and participated in the Section Directors Meeting on October 4, 2022
- ▶ Continued CalSAWS Risk Management activities, including:
 - Continued to work with risk and issue owners to develop and update mitigation plans for the accepted CalSAWS DD&I Project risks and issues
 - Completed preparation and conducted Risk Management Group (RMG) meeting scheduled for October 5, 2022
- ▶ Continued supporting engagement of project staff working remotely, including:
 - Continued preparations and planning for next virtual CalSAWS Project All Staff Meeting on October 19, 2022
 - Began development the next monthly issue of the CalSAWS Connect newsletter that will be distributed to the CalSAWS Project Team on October 13, 2022
- ▶ Completed updates for the monthly CalSAWS IT Project Status Report for September 2022 and preparations for the monthly CalSAWS IT Report Meeting with OSI (Office of Systems Integration), CMS (Centers for Medicare and Medicaid Services), and FNS (Food and Nutrition Service) that will be held on October 12, 2022
- ▶ Began working on updates for the Project Steering Committee (PSC) Meeting on October 20, 2022
- ▶ Began working on updates and preparations for the Joint Powers Authority (JPA) Meeting that is scheduled on October 21, 2022
- ▶ Continued performing contract management activities:

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

- There are currently no Accenture Amendments or Change Notices planned for submission to the October Joint Powers Authority (JPA) Meeting that is scheduled on October 21, 2022
- Continued planning the implementation of requirements from the DHCS and CDSS Privacy and Security Agreements (PSAs) that were approved by the JPA Board of Directors on April 16, 2021
- ▶ Continued performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.2.1-2 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
82	CalSAWS Migration Work Plan Update #42	<ul style="list-style-type: none">• Began developing the FDEL• Submission of the FDEL is due on October 12, 2022

1.2.2 Communications Management

- ▶ CalSAWS Communications Management activities including
 - Continued to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy
 - Continued oversight and management of Power of 58 materials
- ▶ CalSAWS External Website (www.calsaws.org)
 - Continued the administration and support of the CalSAWS external website
 - See Table 1.2.2-1 for details on website support activities

Table 1.2.2-1 – Website Support Activities

TASK	DATE (S)	TASK TYPE
None for the reporting period	N/A	N/A

Table 1.2.2-2 – CalSAWS.org Usage Statistics


CATEGORY	DURING REPORTING PERIOD	SINCE LAUNCH
Total Number of Subscribers	144	2,948
Total Number of Unique Users	16,028	1,678,719
Total Number of New Users	11,780	1,684,099
Total Number of Sessions (Individual site visits)	22,951	2,415,060
Average Number of Sessions per User	1.43	1.44
Average Number of Page Views per Session	1.53	1.32
Average Session Duration	1:02	0:57
AskCalSAWS Inquiries – Received/Resolved	12/3	917/913

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

Figure 1.2.2-2 – Overall CalSAWS.org Usage Trend

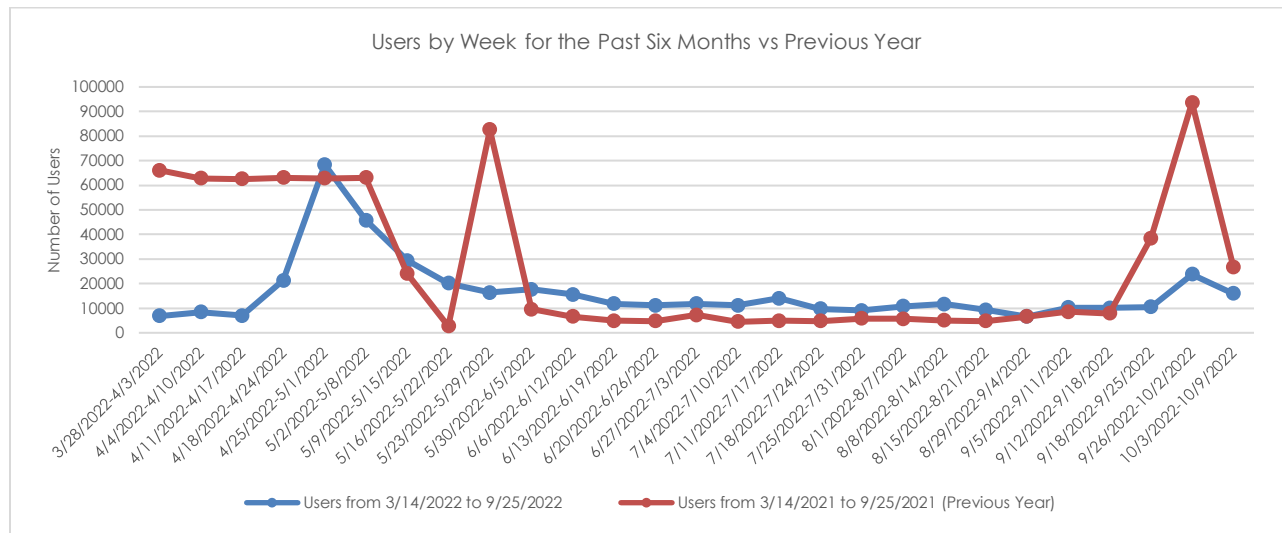

Note:

Increase in usage from the Previous Year (from March 14, 2021 to May 15, 2021) was investigated to be from cities in the United States

Table 1.2.2-3 – CalSAWS.org Subscription Service Statistics

WEBPAGE	PERCENT OF SUBSCRIBERS
Latest News – CalSAWS Buzz Newsletter	26%
Latest News – News	20%
Other Updates – System Updates	18%
Other Updates – Careers	17%
CalSAWS Committees – CalWORKs/CalFresh	17%

1.2.3 Cultural Transformation

- Culture Ambassadors Network (CAN)
 - Conducted CalSAWS System Overview on October 5, 2022
 - Approximately 200 in attendance
 - Future Conversation Series Topics
 - Amazon Web Services (AWS) Overview (TBD)
 - Navigating Security to Drive Innovation at CalSAWS (TBD January 2023)
- Wellness Wednesday
 - Created content by the IDEA Team "Re-igniting Our Flame" will be the featured series for October 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

1.2.4 Inclusion, Diversity and Equity Advancement (IDEA)

- ▶ Co-Create Phase
 - CalSAWS “We Are One” SharePoint Site
 - Continued to update the “We Are One” website tab
 - Pulse Survey
 - Continued to integrate pulse survey analysis into IDEA initiative planning
 - CalSAWS Table Talks
 - Buddy Program
 - Continued supporting mentors and mentees
 - Distributed Buddy Program check-in communications on October 10, 2022
 - Small Team Building
 - Continued to promote Small Team Building initiative opportunities for all CalSAWS teams
 - Employee Resource Groups (ERGs)
 - Continued to manage and support ERG Council
- ▶ General
 - Continued to partner with the CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
 - Continued to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project
 - Distributed Week 1 content for October 2022 Wellness Wednesday’s burnout theme

1.3 CRFI/CIT Communications Information

- ▶ The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period ending October 9, 2022

Table 1.3-1 – CITs

CIT ID	SUBJECT	CATEGORY	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
0284-22	CalSAWS LMS Guide for General Training – CalWIN Wave 2	Informational	October 3, 2022	Ashley Arnold	Renee Carter
0285-22	Wave 4 Counties T-9 Months Change Readiness Survey	Informational	October 3, 2022	Helen Cruz	Araceli Gallardo
0286-22	Monthly CalSAWS De-Duplication Report Posted	Informational	October 4, 2022	Cristy Sharma	Paul Trisler
0287-22	Wave 1: Yellow Banner Case Review Process	Informational	October 4, 2022	Rail Gonzalez	Rojana Turner
0288-22	CalWIN Wave 1 October Readiness Dashboard and Packet 1st Weekly	Informational	October 5, 2022	Jennifer Carpenter	Mara Jennings
0290-22	Wave 1 CalWIN County Go-Live Packet	Informational	October 7, 2022	Sumit Mukherjee	Rachel Frey, and Duncan Gilliam

- ▶ The following table outlines CalSAWS Requests for Information (CRFIs) sent for the

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

reporting period ending October 9, 2022

Table 1.3-2 – CRFIs

CRFI ID	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	CalSAWS CONTACT
22-078	CalSAWS Migration - Application Reference List Request	September 6, 2022	Open	October 12, 2022	Melanie Gines
22-083	Application Security; Training Roles; Recruitment for CDV and Process Simulation – Wave 3	September 16, 2022	Open	November 4, 2022	Mike Tombakian
22-084	CalWIN Readiness Prerequisites for IPT	September 16, 2022	Open	October 14, 2022	Melanie Gines, and Lloyd Rankine
22-085	Wave 3 County Site Plans	September 19, 2022	Open	October 5, 2022	Pete Quijada
22-086	CalWIN Wave 1 Counties - Request to identify Participants for CalWIN Go-Live Cutover County Click-Through	September 19, 2022	Closed	October 4, 2022	Paul Trisler
22-088	CalWIN Wave 1 Counties - Request to Identify Participants for CalHEERs/OCAT Interface Validation at Go-Live	September 20, 2022	Closed	October 4, 2022	Paul Trisler
22-089	Wave 3 CalWIN Counties CalSAWS Delegated Administrators	September 26, 2022	Open	October 7, 2022	Grady Howe
22-090	Change Network Champion (CNC) Identification for Wave 5 and 6 Counties	September 26, 2022	Open	October 10, 2022	Helen Cruz
22-091	CalWIN Wave 1 Counties – Verify Number of Imaging Office Queues	September 30, 2022	Open	October 21, 2022	Rhiannon Chin
22-092	CA-250173: Update Discontinued Case Worker Assignment Logic	September 30, 2022	Open	October 14, 2022	Ignacio Lázaro
22-093	CalSAWS and CalWIN Counties: Request for Source Internet IP Address for JIRA and Sandbox Access	October 3, 2022	Open	October 14, 2022	Melanie Gines
22-094	CalWIN Wave 1 Counties - Request to Identify Participants for GA/GR Correspondence Connectivity Test at Go-Live	October 4, 2022	Open	October 14, 2022	Paul Trisler
22-095	Batch CW/CF RE Appointment Scheduling Job for Migration Counties	October 6, 2022	Open	October 13, 2022	Caroline Bui

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

- ▶ The following table outlines overdue CalSAWS Requests for Information (CRFIs) for the reporting period ending October 9, 2022

Table 1.3-3 – Overdue CRFIs

CRFI ID	Subject	Region 1	Region 2	Region 3	Region 4	Region 5	Region 6
22-085	Wave 3 County Site Plans					Ventura County	
22-089	Wave 3 CalWIN Counties CalSAWS Delegated Administrators					Ventura County	

1.4 Activities for the Next Reporting Period

1.4.1 Project Management

- ▶ Continue CalSAWS DD&I Facility Management activities, including:
 - Continue key initiatives related to facilities at the Rancho Cordova and Norwalk Project Offices, which are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) above
- ▶ Complete updates for the Project Steering Committee (PSC) Meeting on October 20, 2022
- ▶ Complete updates and preparations for the Joint Powers Authority (JPA) Meeting that is scheduled on October 21, 2022
- ▶ Continue CalSAWS Risk Management activities, including:
 - Continue to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
- ▶ Participate in the Section Directors meeting that is scheduled for October 11, 2022
- ▶ Continue activities to support Project staff working remotely
 - Continue developing Project communications, as needed
 - Continue preparations and planning for next virtual CalSAWS Project All Staff Meeting on October 19, 2022
 - Complete development the next monthly issue of the CalSAWS Connect newsletter that will be distributed to the CalSAWS Project Team on October 13, 2022
- ▶ Continue to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue performing Contract Management activities for the CalSAWS DD&I Project
- ▶ Continue performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.4.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
82	CalSAWS Migration Work Plan Update #42	<ul style="list-style-type: none"> Finalize and submit the FDEL to the Consortium for review and feedback on October 12, 2022 Approval of the FDEL is due on October 19, 2022
72	CalSAWS Deployment Complete Milestone/Report - CalWIN Wave 1	<ul style="list-style-type: none"> Finalize and submit the DDED to the Consortium for review and feedback on October 18, 2022 Approval of the FDED is due on November 3, 2022

1.4.2 Communications Management

- ▶ Continue to monitor usage and update materials as requested
 - See table 1.4.2-1 for planned website support activities
- ▶ CalSAWS Communications Management activities including:
 - Continue to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy:
 - Continue oversight and management of Power of 58 roll out

Table 1.4.2-1 – Website Support Activities

TASK	DATE(S)	TASK TYPE
Update Plugins for CalSAWS.org	October 12, 2022	Plugin Management

1.4.3 Cultural Transformation

- ▶ Continue to develop calendar of events for the ambassador initiatives through the end of the year
- ▶ Continue to provide Project management support to Cultural Ambassadors as they continue to develop the plans for the initiatives
- ▶ Continue to coordinate working sessions for each Ambassador group to further their initiatives planning and discuss their individual contributions
- ▶ Continue to develop wellness initiative content to keep the project staff engaged
- ▶ Continue to update resources and a collaboration workspace (Teams Channel) with new relevant materials to support the implementation of the prioritized initiatives
- ▶ Continue to monitor Microsoft Teams channels for any help needed from Ambassadors

1.4.4 Inclusion, Diversity & Equity Advancement (IDEA)

- ▶ Determine CalSAWS members to be featured during All-Staff for Inspiration Station share-out
- ▶ Distribute Week 2 Wellness Wednesdays content for October 2022 burnout theme
- ▶ Continue to manage Buddy Program Round 3 and support buddy pairs
- ▶ Continue to partner with CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the project
- ▶ Continue to promote small team building activities

1.5 Deviations from Plan/Adjustments

- ▶ None for the reporting period

2.0 Imaging



















2.1 Highlights of the Reporting Period

Table 2.1-1 – CalSAWS Imaging Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Appendix E	<ul style="list-style-type: none">• San Diego County is identifying the documents they plan to purge and decrypt; the current timeline goes past their Go Live. Project has requested that the County executes the remediation plan

- ▶ Continued to monitor Imaging migration status by County
 - For future details of status' by County, they are now available in Appendix E - CalSAWS Imaging Document Migration

Table 2.1-2 – CalSAWS Imaging County Migration Risk Status

WAVE	COUNTY	STATUS [1]
1	• Placer County	
	• Yolo County	
2	• Contra Costa County	
	• Tulare County	
	• Santa Clara County	
3	• Ventura County	
	• Orange County	
	• Santa Barbara County	
4	• San Diego County	
	• Santa Cruz County	
	• Solano County	
	• San Mateo County	
5	• Alameda County	
	• Fresno County	
	• Sonoma County	
6	• San Francisco County	
	• San Luis Obispo County	
	• Sacramento County	

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Note:

- Detailed metrics of each County by wave has been included in the Appendix E - CalSAWS Imaging Document Migration

Table 2.1-3 – CalSAWS Imaging Project Milestones for Current Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 1	Conduct Placer County Document Migration Discovery Session Check-in	October 4, 2022	Completed
WAVE 2	Conduct Santa Clara County Document Migration Discovery Session Check-in	October 3, 2022	Completed
WAVE 3	Conduct Santa Barbara County Document Migration Discovery Session Check-in	October 4, 2022	Canceled
	Conduct Orange County Document Migration Discovery Session Check-in	October 6, 2022	Completed
WAVE 4	Conduct San Mateo County Document Migration Discovery Session Check-in	October 4, 2022	Completed
	Conduct San Diego County Document Migration Discovery Session Check-in	October 4, 2022	Completed

Table 2.1-4 – CalSAWS Imaging Project Milestones for Next Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 1	Conduct Placer County Document Migration Discovery Session Check-in	October 11, 2022	Scheduled
WAVE 2	Conduct Santa Clara County Document Migration Discovery Session Check-in	October 10, 2022	Scheduled
	Conduct Tulare County Document Migration Discovery Session Check-in	October 10, 2022	Scheduled
WAVE 3	Conduct Santa Barbara County Document Migration Discovery Session Check-in	October 11, 2022	Scheduled
	Conduct Orange County Document Migration Discovery Session Check-in	October 13, 2022	Scheduled
WAVE 4	Conduct San Mateo County Document Migration Discovery Session Check-in	October 11, 2022	Scheduled
	Conduct San Diego County Document Migration Discovery Session Check-in	October 11, 2022	Scheduled

2.2 Activities for the Next Reporting Period

- ▶ Continue to manage the milestones for the Image Migrations in the tables in Appendix E

2.3 Upcoming Performance Tests

- ▶ Prepare and organize the Performance testing plan for the first week of April 2023

2.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

3.0 Customer Service Center (CSC)

3.1 Highlights of the Reporting Period

Table 3.1-1 – CalSAWS Customer Service Center Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> Partnered with Los Angeles County to identify and prioritized the items complete prior to go live Placer County and Yolo County Model Office begins October 11, 2022

- ▶ Continued discussions with Los Angeles County, Wave 4, Wave 5, and Wave 6 CalWIN Counties about migration to CalSAWS Contact Center Solution
- ▶ Continued Build of Administration Page (CA-226672), and Scheduled Callback (CA-229573)
- ▶ Continued build of Yolo and Placer County Amazon Web Service (AWS) accounts and Contact Center infrastructure

Table 3.1-2 – Customer Service Center Enhancement Milestones

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2292, 2697, 2698, 2723, 2724 WFM/QA/QM Reporting (CA-226209)	December 3, 2021	In Production	22.01
DDID 2718 Task for Cancelling an Appointment in Outbound IVR (CA-25604)	January 24, 2022	System Test	22.09 22.10.XX
DDID 2219, 2716, 2717, 2728 Outbound IVR - (CA-226207)	February 4, 2022	System Test	22.09 22.10.XX
DDID 2700 Enhanced CCP (CA-226844)	March 18, 2022	In Production	22.03 22.05.06
DDID 2727 Work-from-home Modifications (CA- 227064)	March 18, 2022	In Production	22.03 22.05.06
DDID 2216, 2725 External Party Access IVR (CA-226839)	March 25, 2022	In Production	22.05
DDID 2211, 2217, 2218, 2220, 2729, 2730, 2731, 2046, 2732 Telephonic Signature (CA-226838)	April 1, 2022	In Production	22.05
DDID 2687, 2688, 2689, 2690, 2691, 2692, 2693, 2694, 2695, 2696, 2222, 2702, 2721, 2169, 2284, 2722 Admin Page (CA-226672)	October 7, 2022	In Development	22.09 22.10.XX
DDID 2699, 2210, 2705, 2707, 2708, 2709, 2710, 2711, 2712, 2713, 2714, 2715, 2719, 2720, 2258	November 10, 2022	In Development	22.09 22.11.XX

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
Inbound IVR (CA-226837)			
DDID 2704 Post-Call Survey (CA-228023)	July 8, 2022	In Production	22.07 22.09.16
DDID 2284 Scheduled Callback (CA-229573)	July 8, 2022	In Development	22.09 22.10.XX
DDID 2701, 2706 Voice Authentication Languages (CA-226843)	October 7, 2022	In Development	22.09 22.10.XX
DDID 2268 Display the CalSAWS Contact Center IVR Caller ID for outbound calls	TBD	Design In progress	22.09 22.11.XX

Table 3.1-3 – Los Angeles County Milestones

MILESTONES		DUE DATE	OWNER
1	Design completion	March 11, 2022	CalSAWS Project Team
2	Initial performance/load testing	March 18, 2022	CalSAWS Project Team
3	Training development	May 16, 2022	CalSAWS Project Team
4	Build and unit test	May 20, 2022	CalSAWS Project Team
5	Training content review	May 20, 2022	Consortium
6	Training execution	June 29, 2022	CalSAWS Project Team
7	System Test	July 15, 2022	CalSAWS Project Team
8	Conduct model office	July 21, 2022	Los Angeles County
9	Go-live	TBD	CalSAWS Project Team
10	Post go-live support	TBD	CalSAWS Project Team

3.2 Activities for the Next Reporting Period

- ▶ Continue discussions with Los Angeles, Santa Clara, Tulare, Orange, Santa Barbara, Ventura, Santa Cruz, Solano, San Mateo, and San Diego Counties for County-specific Interactive Voice Response (IVR) designs
- ▶ Continue build of System Change Requests (SCRs) CA-226672 Administrative Page, and Scheduled Callback (CA-229573)
- ▶ Continue build of Los Angeles, Yolo, and Placer Counties Amazon Web Services (AWS) accounts and Contact Center Infrastructure (CA-235356, CA-240152, and CA-240156)

3.3 Upcoming Performance Tests

- ▶ Schedule smoke testing to begin November 17, 2022
- ▶ Schedule performance testing to begin week of November 28, 2022

3.4 Deviations from Plan/Adjustments

- None for the reporting period

4.0 Application Development and Test

4.1 Highlights of the Reporting Period

Table 4.1-1 – CalSAWS Application Development and Test Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
4.1.3 State and CalWIN Wave 1 County Interface Partner File Exchange Test (IPT)	<ul style="list-style-type: none"> Continue preparation activities for Wave 2 IPT execution starting on October 17, 2022. 36 Consortium, State, and County interfaces in scope

4.1.1 Application Development Summary

Table 4.1.1-1 – CalSAWS Application Development Summary

	Status	22.09	22.11	23.01	23.02	23.03	23.05
Design	New	0	0	4	2	6	10
	Design in Progress	1	1	5	0	2	1
	Ready for Committee	0	0	0	0	0	0
	Committee Review	0	0	0	0	0	0
	Pending Approval	0	1	0	0	1	1
Build	Approved	1	1	5	1	3	2
	In Development	1	0	1	0	0	0
	Development Complete	0	0	0	0	0	0
	In Assembly Test	0	0	0	0	0	0
Test	System Test	5	1	0	0	0	0
	Test Complete	4	0	0	0	0	0
	In Production	14	0	0	0	0	0
	Grand Total	26	4	15	3	12	14

System Change Requests (SCRs) in Production


933

Notes:

- This table includes Application Development System Change Requests (SCRs) with migration impact. SCRs in production represents a count of any SCR that have a project phase of migration and have been deployed to production
- Continued drafting designs and development activities. Status is provided in Table 4.1.1-1 (CalSAWS Application Development Summary) above

4.1.2 Design Difference Identifiers (DDID) System Test Status

Figure 4.1.2-1 – DDID System Test Status

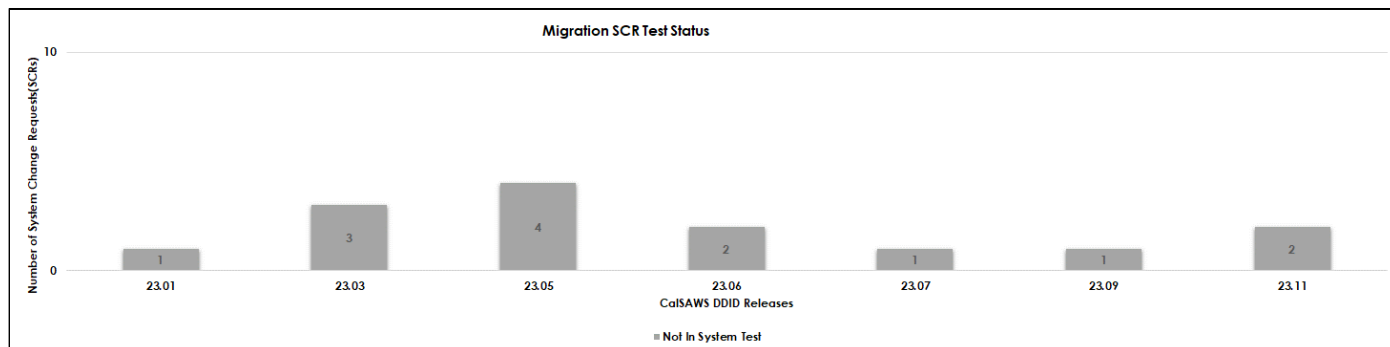

Notes:

- Includes all System Change Requests (SCRs) that have a funding source of CalSAWS DD&I that are not in "Rejected" or "Pending Rejection" status and are targeted for a baseline release. This includes SCRs associated to DDID 1967 for the unforeseen allowance and DDID 1631 for the reports allowance. In Production includes "In Production" status; Test Complete includes "Test Completed" status; System Test includes "System Test" status; Not in System Test includes all SCR statuses prior to System Test delivery
- Counts are higher in this chart (as compared with Design and Build Status) due to the inclusion of all CalSAWS DD&I System Change Requests (SCRs) targeted for the release, such as DD&I Training and Technical System Change Requests (SCRs).
- There is no DD&I system change request in the 22.11 release

4.1.3 State and CalWIN Wave 2 County Interface Partner File Exchange Test (IPT)

Table 4.1.3-1 – Consortium Partners

INTERFACE TESTING		
CONSORTIUM PARTNER	STATUS	TARGET COMPLETION DATE
Electronic Inter County Transfer (EICT) - CalWIN	0/3	December 31, 2022

Note:

- Testing begins October 17, 2022

Table 4.1.3-2 – State Partners

INTERFACE TESTING		
STATE PARTNER	STATUS	TARGET COMPLETION DATE
Case Management Information and Payrolling System (CMIPS) - OSI	0/2	December 31, 2022
Electronic Benefits Transfer (EBT) - FIS	0/2	December 31, 2022
Medi-Cal Eligibility Data System (MEDS) - DHCS	0/2	December 31, 2022
Welfare Data Tracking Implementation Project (WDTIP) - OSI	0/2	December 31, 2022

Note:

- Testing begins October 17, 2022

Table 4.1.3-3 – CalWIN Wave 2 Counties

INTERFACE TESTING		
CalWIN Wave 1 COUNTY PARTNER	STATUS	TARGET COMPLETION DATE
Contra Costa County	0/7	December 31, 2022
Santa Clara County	0/10	December 31, 2022
Tulare County	0/8	December 31, 2022

Notes:

- Testing begins October 17, 2022

4.1.4 Case Purge

In July 2020, a team was formed to design, build, test, and deploy a Case Purge solution for C-IV and CalSAWS. This Purge functionality is based on the records retention policy approved by the CalSAWS Project Steering Committee in September 2019. The Purge team is using the Agile methodology for this effort and is deploying functionality to Production at the conclusion of each Sprint. This team is operating independently of the existing Design, Application Development, Training, and Test teams

- ▶ Continued to monitor performance, storage, and batch log file impacts with the 60,000-case rate increase
- ▶ Completed the eighth and final week of Case Purge processing in CalSAWS with the following statistics
 - All identified cases have completed through the data removal process
- ▶ Began designing the Los Angeles County update to remove Time Limit records for GA/GR cases based on the data removal status of completed

Table 4.1.4-1 – Case Purge Completed Cases

CASES	NUMBER OF CASES
Completed	1,657,318
Remaining to process	0

Figure 4.1.4-1 – Case Burndown Chart

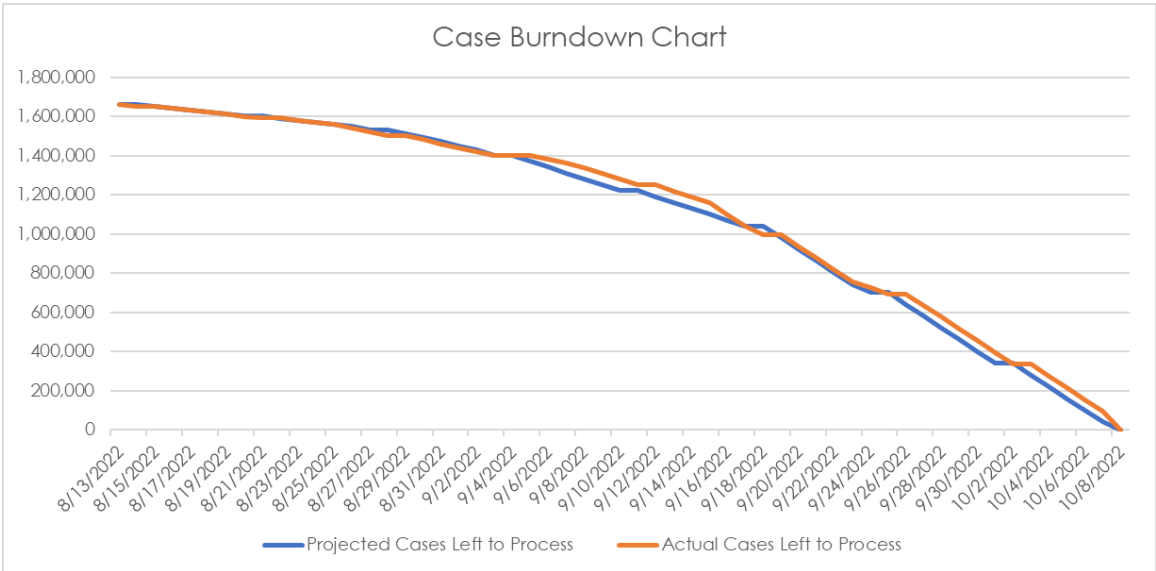


Figure 4.1.4-2 – Case Purge Sprint Burndown Chart

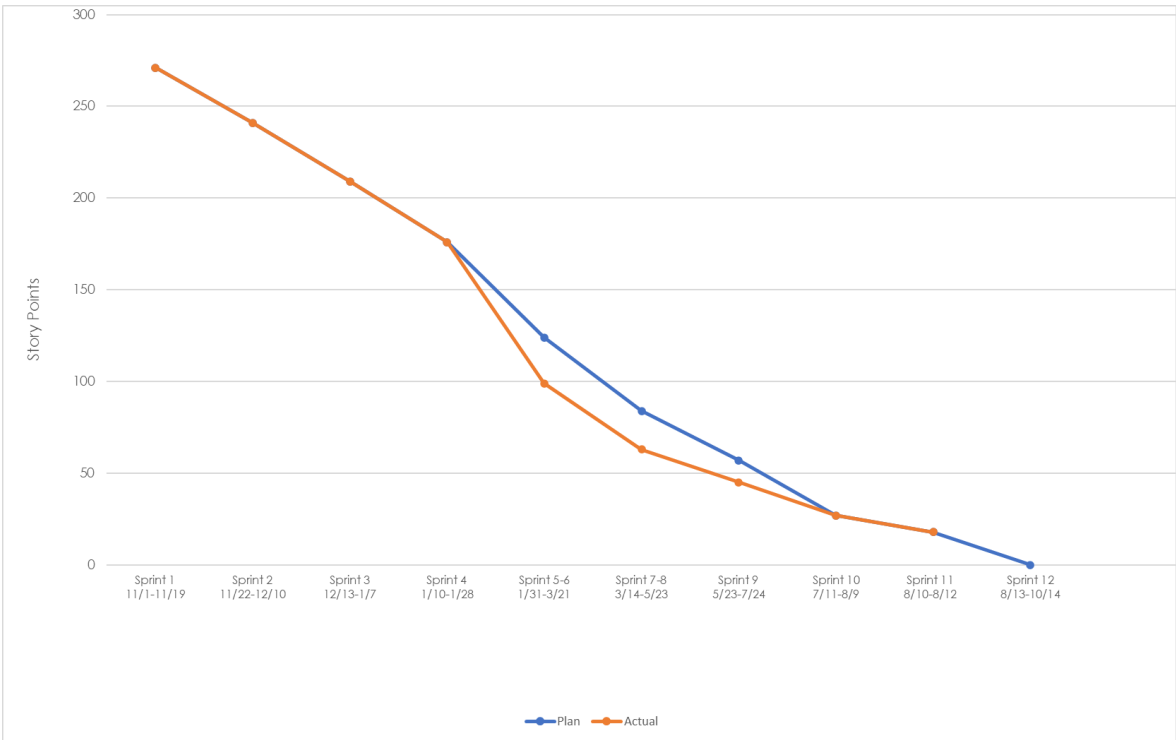


Table 4.1.4-2 – Planned Purge Sprints

SPRINT NUMBER	SPRINT DESCRIPTION
Sprint 1 - 11	Completed
Sprint 12	Execution, Post Data Removal updates for Los Angeles County Time Limit Records

4.1.5 Deliverable Management

Table 4.1.5-1 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

4.2 Activities for the Next Reporting Period

- ▶ Continue drafting designs for Migration Impact System Change Requests (SCRs)
- ▶ Continue test execution for CalSAWS 22.11 Release
- ▶ Continue processing cases through the data removal batch jobs

Deliverable Management

Table 4.2-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

4.3 Upcoming Performance Tests

- ▶ Upcoming Performance tests planned for Batch, CalSAWS Core Batch, and Core Online
 - Batch/Core Batch
 - Batch Performance testing for SCR CA-246043 – Table Partitioning
 - Partition testing showed improvement over the majority of batch
 - CalWIN Wave 2 Performance – Performing environment smoke test
 - Coordinating Correspondence event stream testing with Online
 - Core Online

Table 4.3-1 – Core Online Upcoming Performance Cycle

Performance Cycle	Start Date	End Date	Status
22.09 Release	September 1, 2022	September 16, 2022	Completed
CalWIN Wave 1 Final Workload Mix	September 19, 2022	October 14, 2022	In progress
Contact Center eCCP	October 10, 2022	October 28, 2022	In Progress
22.11 Release	October 31, 2022	November 18, 2022	Not started
CalWIN Wave 2	November 21, 2022	February 10, 2023	Not started

4.4 Deviations from Plan/Adjustments

- None for the reporting period

5.0 Conversion

5.1 Highlights of the Reporting Period

Table 5.1-1 – CalSAWS Conversion Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
5.1.1 CalWIN Conversion	<ul style="list-style-type: none"> Continued to communicate business mitigation options to address the Risk 258 Waves 2 through 6 regarding the Cutover Window Continued Golden Data Set 10 Wave 1 Go-Live Epic Continued to support Wave 1 County preparation Continued to prepare for Wave 1 Go-Live Cutover plans

5.1.1 CalWIN Conversion

- Continued to address open and unresolved Converted Data testing identified defects
- Continued Golden Data 10 Wave 1 go-live Epic. This Epic consists of the items to be completed and delivered with GDS #10 that will be included with Wave 1 go-live

Table 5.1.1-1 – CalWIN Conversion Statistics Golden Data Set (GDS) 10 Wave 1 go-live (August – October 2022)

Sprint	Total - Deferred Items	Sprint Duration		GDS#10 W1 go-live								
				Item Status								
				0%	25%	30%	50%	75%	5%	100%	100%	0%
				Not Started	Analysis & Mapping in Progress	Ready for Consortium Review	Build In Progress	Ready for AT	On Hold	Completed (Tested) *	CNR	Deferred
Overall	161	8/22/2022	10/14/2022	2	7	0	21	38	0	93	0	0
GDS#10 Sprint 1	38	8/22/2022	9/2/2022	0	0	0	0	1	0	37	0	0
GDS#10 Sprint 2	39	9/5/2022	9/16/2022	0	0	0	0	2	0	37	0	0
GDS#10 Sprint 3	39	9/19/2022	9/30/2022	0	0	0	2	20	0	17	0	0
Hardening	45	10/3/2022	10/14/2022	2	7	0	19	15	0	2	0	0


5.1.2 CalWIN Conversion Defects (CDT, CDV, and UAT)

Table 5.1.2-1 – Open Converted Data Test (CDT), County Data Validation (CDV), and User Acceptance Test (UAT) Defects

Open Defects by Phase	Priority 1	Priority 2	Priority 3/Priority 4	Total
CDT	0	28	82	110
CDV	0	0	12	12
UAT	0	4	3	7
Total Open Defects	0	32	97	129

Defect Delivery by Golden Data Set (GDS)	Priority 1	Priority 2	Priority 3/Priority 4	Total
Wave 1 Go-Live	0	28	19	47
GDS#10	0	3	47	50
GDS#11	0	0	17	17
In Triage	0	1	14	15
Total Open Defects	0	32	97	129
Conversion Resolved	0	-18	-15	-33
Total Open Unresolved Defects	0	14	82	96

Figure 5.1.2-1– Open Converted Data Test (CDT) Defects by GDS

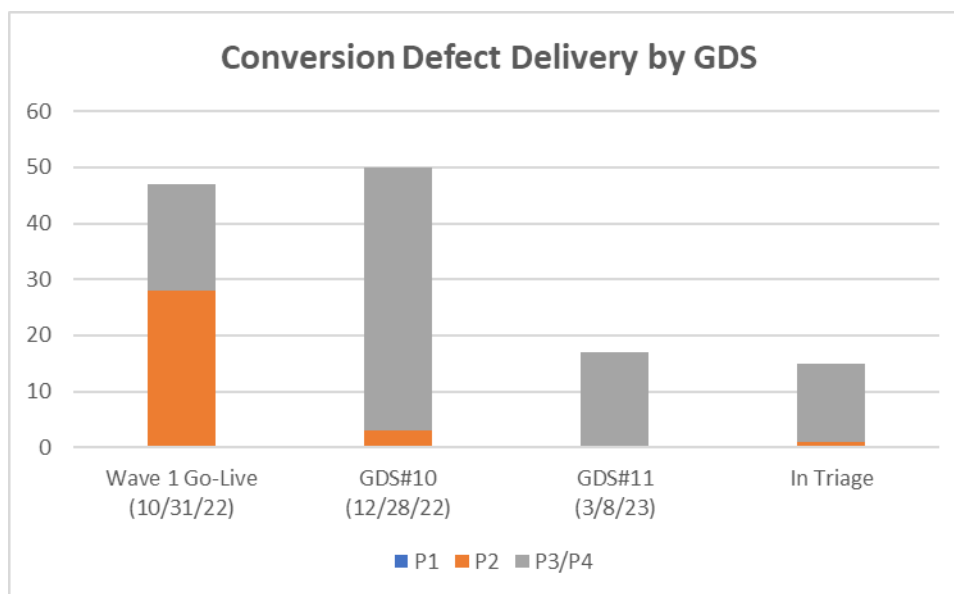

5.1.3 Gainwell Technologies

- CalWIN Document Migration
 - Continued delivery of Client Correspondence (CC) from CalWIN

5.1.4 Ancillary Systems Conversion

- ▶ Continued to address issues found in production dataset size files. These files are necessary for CalWIN Core Conversion orchestration and integrations
- ▶ Facilitated exception reports review sessions with the Ancillary Counties to address questions and concerns
- ▶ Delivered Wave 2 Ancillary Data Exceptions

Figure 5.1.4-1– Ancillary Systems Conversion Gantt Chart

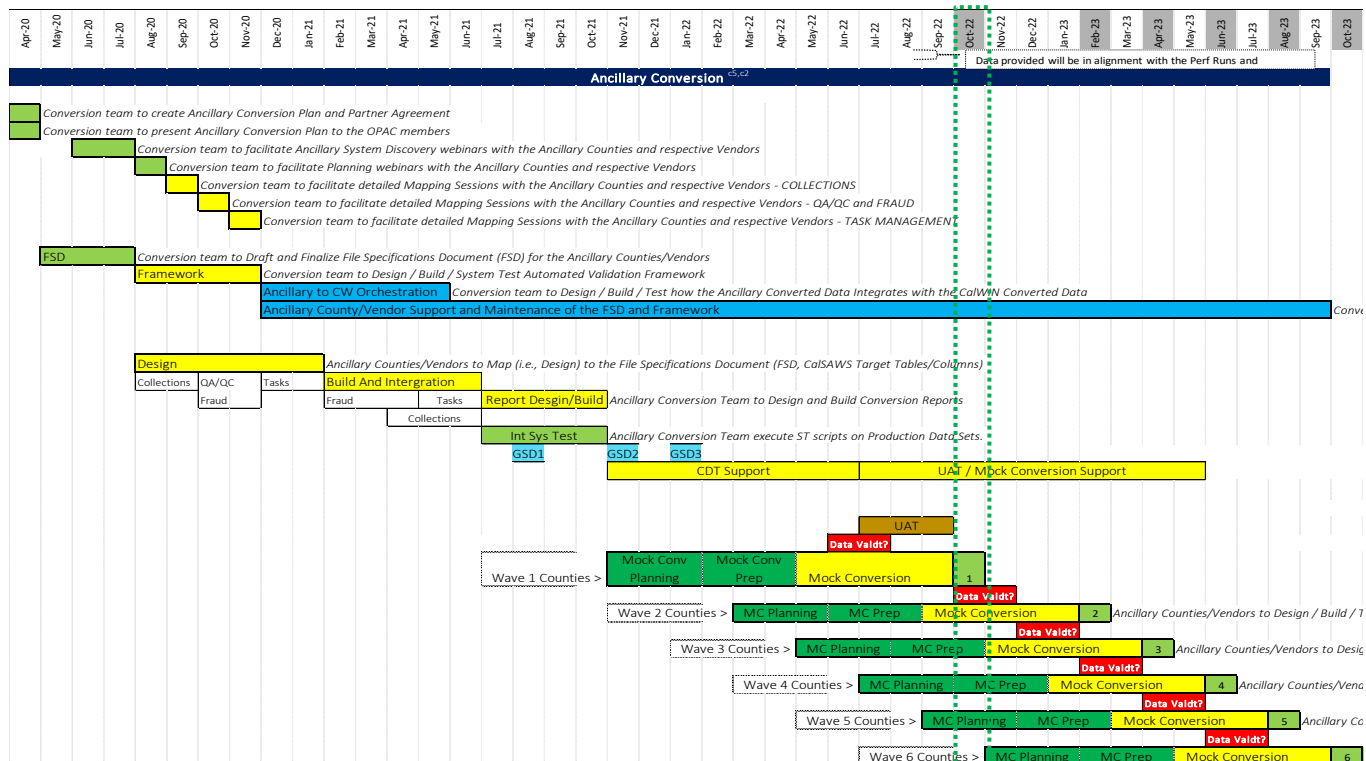


Table 5.1.4-2 – Ancillary Systems Conversion Milestones

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
July 2020	Project Kick-Off/Discovery Sessions	Team introductions and Project overview	Completed
August 2020	File Specification Document (FSD)	CalSAWS DB (structures) as Conversion target	Completed
August 2020	Project Planning	Detailed walkthrough of the Project schedule and File Specification Document (FSD)	Completed
December 2020	Automation Framework Completed	Exception handling for Ancillary provided data is ready for the Counties	Completed

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
February 2021	Design/Mapping	All CalSAWS DB targets (defined in FSD) have source mappings from Ancillary	Completed
July 2021	Build	Development activities, dependent design mapping, are ready to begin (or are completed)	Completed
January 2022	System Test	System Test execution, dependent on test scripts and build completed, are ready to begin (or are completed)	Completed
June 2022	Integration Test	End-to-End Test execution, dependent on test scripts, System Test completed, and CDT completed, are ready to begin (or are completed)	Completed
August 2022	Wave 1 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
October 2022	Wave 2 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	In progress
February 2022	Wave 3 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Not started
April 2023	Wave 4 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Not started
June 2023	Wave 5 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Not started
August 2023	Wave 6 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Not started

Table 5.1.4-3 – Conversion Milestones

WAVE	MOCK PREPARATION	MOCK CUTOVER	COUNTY PREPARATION	CUTOVER
Wave 1	July 30, 2022	August 6, 2022	September 19, 2022	October 27, 2022
	Completed	Completed	Completed	Not started
Wave 2	November 26, 2022	December 3, 2022	January 14, 2023	February 23, 2022
	Not started	Not started	Not started	Not started
Wave 3	January 28, 2023	February 4, 2023	March 25, 2023	April 20, 2023
	Not started	Not started	Not started	Not started
Wave 4	April 1, 2023	April 8, 2023	May 13, 2023	June 29, 2023
	Not started	Not started	Not started	Not started
Wave 5	June 3, 2023	June 10, 2023	July 15, 2023	August 31, 2023
	Not started	Not started	Not started	Not started
Wave 6	July 29, 2023	August 5, 2023	September 16, 2023	October 26, 2023
	Not started	Not started	Not started	Not started

Note: All Dates are the start of the Conversion window

5.1.5 Deliverable Management

Table 5.1.5-1 – Conversion Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
72	CalSAWS Deployment Complete Milestone/Report – CalWIN Wave 1	<ul style="list-style-type: none"> Continued developing the DDED Submission of the DDED is due on October 18, 2022

5.2 Activities for the Next Reporting Period

5.2.1 CalWIN Conversion

- ▶ Continue to complete Jira epics and issue aligned with Golden Data Set (GDS) delivery schedule
- ▶ Support Wave 1 Counties during the 6-week County Preparation timeframe
- ▶ Support Wave 2 County Data Validation (CDV)
- ▶ Finalize Wave 1 Go-Live Cutover plan

5.2.2 Gainwell Technologies

- ▶ CalWIN Data Migration
 - Continue planning for future CalWIN extractions
- ▶ CalWIN Data Retention M&O
 - Continue planning for future data retention runs

5.2.3 Ancillary Systems Conversion

- ▶ Continue ongoing support for mapping and data extract activities on Ancillary Collections, Fraud, and Task Management
- ▶ Continue to update the Ancillary Systems file specifications documents (as needed)
- ▶ Meet with Wave 1 Counties to address any cutover questions

5.2.4 Deliverable Management

Table 5.2.4-1 – Conversion Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
72	CalSAWS Deployment Complete Milestone/Report – CalWIN Wave 1	<ul style="list-style-type: none">• Continue developing the DDED• Submission of the DDED is due on October 18, 2022

5.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

6.0 CalWIN Functional Support

6.1 Highlights of the Reporting Period

Table 6.1-1 – CalSAWS CalWIN Functional Support Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> None to note for reporting period

- ▶ Supported CalSAWS 3x Weekly Leadership Meetings on October 5, 2022, and October 7, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Supported Implementation Support Services (ISS) Team Leads Meetings on October 4, 2022, and October 6, 2022 to collaborate effectively
- ▶ Supported San Luis Obispo County To-Be Business Process Reengineering (BPR) Closeout Sessions during October 3 – 7, 2022, upcoming sessions include:
 - Imaging
 - Workload Management, Service Arrangements, Resource Databank (RDB)
 - Appointments and General Assistance (GA)
 - E2Lite and Employment Services
 - Hearings, Quality Assurance (QA), Automated Actions/Pending Decisions
- ▶ Supported San Francisco County To-Be Business Process Reengineering (BPR) Closeout Sessions during October 3 – 7, 2022, upcoming sessions include:
 - Benefit Recover and Collections
- ▶ Supported Wave 1 County Preparation Phase during October 3 – 7, 2022, upcoming by:
 - Wave 1 County Preparation Phase Office Hours x5
 - Daily Debrief: Wave 1 County Preparation Phase x5
 - Run and Share County Preparation Metrics
- ▶ Supported Wave 2 Configuration during October 3 – 7, 2022, upcoming by:
 - Contra Costa BPR Flow Review for Configuration
 - Contra Costa – CalSAWS Configuration Verification Session x2
- ▶ Supported Wave 2 Process Simulation during October 3 – 7, 2022, upcoming by:
 - Wave 2 Process simulation data staging iteration
 - Wave 2 Batch Requirements and Schedule
- ▶ Supported Wave 1 Open Defect Strike Team – Meeting 3 on October 4, 2022, to align on an approach to Open Defects for the Wave 1 go live
- ▶ Supported Sonoma County Meeting functionality on October 5, 2022, to align on an approach for NSDI functionality at Sonoma County

6.2 Activities for the Next Reporting Period

- ▶ Prepare for CalSAWS 2x Weekly Leadership Meetings on October 12, 2022 to collaborate on leadership items for the CalWIN release
- ▶ Prepare for Implementation Support Services (ISS) Team Leads Meetings on October 11, 2022, and October 13, 2022 to collaborate effectively
- ▶ Prepare for Wave 1 County Preparation Phase during October 10 – 14, 2022, upcoming by:
 - Wave 1 County Preparation Phase Office Hours x5
 - Daily Debrief: Wave 1 County Preparation Phase x5
 - Run and Share County Preparation Metrics
- ▶ Prepare for Wave 2 Configuration during October 10 – 14, 2022, upcoming by:
 - Santa Clara County Configuration Set Up for Process Simulation
- ▶ Prepare for Wave 2 Process Simulation during October 10 – 14, 2022, upcoming by:
 - Wave 2 Process simulation data staging iteration
 - Wave 2 Batch Requirements and Schedule
- ▶ Prepare for Wave 1 Open Defect Strike Team Meetings during October 10 – 14, 2022, to align on an approach to Open Defects for the Wave 1 go live
- ▶ Prepare for CalWIN Reporting for Wave 1 Migrating Counties on October 10, 2022 to align on producing the month end reports for the month of October
- ▶ Prepare for Dry Run for Pre-Green Light: Wave 1 Go Live on October 11, 2022 to provide feedback on the dry run for the upcoming green light meeting
- ▶ Prepare for Wave 1: Business Metrics Touchpoint on October 11, 2022 to review and finalize post-go live business metrics
- ▶ Prepare for CalSAWS WTW opt in and out decisions for Sonoma County on October 11, 2022 to support Sonoma County decision making for their functionality opt-in/opt-out
- ▶ Prepare for UAT2 Communication, Refresh Schedule and Stakeholder Discussion on October 12, 2022 to plan out UAT2 environment support for all CalWIN implementation activities
- ▶ Prepare for Batch Ops Communication Meeting – Yolo County on October 12, 2022 to share information related to production batch operations communications

6.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

7.0 Technical Infrastructure

7.1 Highlights of the Reporting Period

Table 7.1-1 – CalSAWS Technical Infrastructure Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
N/A	<ul style="list-style-type: none"> None to note for reporting period

Table 7.1-2 – County Network Connectivity Readiness Status

CalWIN WAVE 1 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	Completed	100.0%	98.6%
Critical Path	Completed	100.0%	100.0%

CalWIN WAVE 2 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	On track	90.0%	73.2%
Critical Path	Completed	100.0%	80.0%

CalWIN WAVE 3 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	On track	85.1%	61.7%
Critical Path	On track	83.7%	68.4%

CalWIN WAVE 4 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Project Networking Connectivity	On track	31.0%	18.4%
County Networking Connectivity	On track	15.8%	15.8%

- Wave 1
 - Completed all technical enablement and connectivity for Placer and Yolo Counties
 - Continued circuit bandwidth upgrades for Placer and Yolo Counties to support Enhanced Data Reporting (EDR)
 - CalSAWS Requests for Information (CRFI) sent to Wave 1 Counties to perform regression testing prior to migration
 - Handover of Wave 1 sites to Operations underway
 - Response to CalSAWS Requests for Information (CRFI) 22-093 – Request for Source Internet IP Address for JIRA and Sandbox Access is due by October 14, 2022

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

► Wave 2

- Continued to monitor risks for Santa Clara County
 - Deployed and activated AT&T circuit on August 23, 2022. Risk rating lowered
 - Level 3 circuit delivery date pending from TPX
 - Comcast circuit scheduled for delivery on October 29, 2022
- Completed integration with CalSAWS
 - Santa Clara County configuration changes completed
 - Tulare and Contra Costa County testing completed
- Completed Interface Partner File Exchange Test (IPT) pre-readiness for Santa Clara, Tulare, and Contra Costa County
 - Santa Clara County IPT pre readiness to be re-worked due to county changing their IP Address requirements
- Completed database connectivity tests (EDR, JDBC, Apex) for Tulare, and Contra Costa Counties
- Response to CalSAWS Requests for Information (CRFI) 22-093 – Request for Source Internet IP Address for JIRA and Sandbox Access is due by October 14, 2022

► Wave 3

- Continued to track secondary circuit activation for Orange and Ventura Counties
 - Crown Castle circuit delivery date October 19, 2022 from TPX
- Response to CalSAWS Requests for Information (CRFI) 22-062 from Orange and Ventura Counties received. Response from Santa Barbara pending
- Completed integration with CalSAWS
 - Orange, Santa Barbara, Ventura County configuration changes completed
 - Orange, Santa Barbara, Ventura County testing completed
- Completed Interface Partner File Exchange Test (IPT) inbound and outbound connectivity for Orange, and Ventura Counties.
 - Santa Barbara Outbound test pending; Inbound test to CalSAWS successful.
- Completed database connectivity tests (EDR, JDBC, Apex) for Orange, Santa Barbara, Ventura Counties
- Response to CalSAWS Requests for Information (CRFI) 22-093 – Request for Source Internet IP Address for JIRA and Sandbox Access is due by October 14, 2022

○

► Wave 4

- Response to CalSAWS Requests for Information (CRFI) 22-078 – Application requirement list received
- Response to CalSAWS Requests for Information (CRFI) 22-084 – Routing and firewall changes required for CalSAWS integration received
- Response to CalSAWS Requests for Information (CRFI) 22-093 – Request for Source Internet IP Address for JIRA and Sandbox Access is due by October 14, 2022
- Ongoing San Diego County Circuit delivery
 - AT&T circuit delivery cancelled by County (Previously scheduled for August 30, 2022)
 - Level 3 circuit delivery date pending from TPX
- Ongoing San Mateo County Circuit delivery
 - Both circuits (AT&T and Level 3) delivery date pending from TPX
- Ongoing Santa Cruz County Circuit delivery
 - Century link circuit delivered and activated

- AT&T circuit undeliverable; Alternate carrier Comcast identified.
 - County requesting for additional bandwidth; will submit a SCR to formally request upgrade
- Ongoing Solano County Circuit delivery
 - Comcast circuit delivered and activated
 - AT&T circuit undeliverable; Alternate carrier Comcast identified.
 - County requesting for additional bandwidth; will submit a SCR to formally request upgrade
- ▶ CalWIN Counties
 - Ongoing requirement gathering sessions around EDR in progress
 - Enhanced Data Reporting (EDR) approved
 - New circuit orders submitted for Wave 2 – 6 Counties in anticipation of opting in for EDR and where additional bandwidth was required based on the completed assessment

7.2 Activities for the Next Reporting Period

- ▶ Submit Change requests for CalWIN Wave 4 Counties for approval
- ▶ Santa Clara SFTP access permissions to be reconfigured due to change in County IP Addresses (CalSAWS Requests for Information (CRFI) 22-040 Response revised by county)
- ▶ CalWIN Wave 5 Circuit Technical Point of Contact (TPOC) Meeting to be scheduled for mid-October 2022
- ▶ CalWIN Wave 5 Circuit orders to be placed
- ▶ Continue to work with Wave 3 Counties for CalSAWS integration, where new CalSAWS Requests for Information (CRFI) responses are received
- ▶ Schedule one-on-one low level design review sessions with the Wave 4 Counties for CalSAWS integration
- ▶ Continue to track circuit upgrades for Waves 1, and 2 for EDR enablement
- ▶ Continue to track circuit deliveries for Waves 2, 3, and 4

7.3 Deviations from Plan/Adjustments

- ▶ Santa Cruz County requesting for additional bandwidth to be procured; County will submit a SCR to formally request upgrade.
- ▶ Santa Clara County has changed the designated Point of Presence (PoP) site location resulting in previously completed procurement and planning tasks having to be re-done. This will result in a 3-month impact to all downstream tasks and milestones for Santa Clara County unless mitigated
 - Mitigation:
 - Temporary installation (deployed on June 29, 2022) of 4G connection (at additional cost) which will allow the County to complete pre-readiness and technical enablement tasks. This will isolate the County from being on-hold for 2 months. However, procured circuits will need to be delivered before beginning Interface Partner Testing (IPT) and User Acceptance Testing (UAT) testing
 - 4G connectivity for Santa Clara unusable due to poor 4G signal resulting in instability and unusable as a workaround

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 3, 2022 to October 9, 2022

- Comcast 600x35Mbps - Construction delays (ISP) could result in an additional 2 months to deliver (Target: November 2022)
- AT&T 100Mbps – Delivered on August 23, 2022
- Level 3 100Mbps Circuit order placed as contingency while dependencies with Comcast and AT&T are resolved
- Risk rating lowered with the delivery of the AT&T Circuit allowing county to proceed with testing and training requirements
- Santa Clara County has identified a 2 new public IP addresses which will be used for Outbound SFTP connectivity. This will result in reconfiguration and will require retesting of partner connectivity

8.0 Appendices

Appendix A – CalSAWS Deliverable Summary

Appendix B – CalSAWS Migration Work Plan Summary

Appendix C – CalSAWS DD&I Project Gantt Chart

Appendix D – CalSAWS Project Risks and Issues Report

Appendix E – CalSAWS Imaging Document Migration

