

CalSAWS BenefitsCal (Portal/Mobile) Weekly Status Report

**Reporting Period: February 27, 2023 to
March 5, 2023**

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

Table of Contents

1.0	Project Management	4
1.1	Executive Summary.....	4
1.2	PMO	5
1.2.1	Highlights of the Reporting Period	5
1.2.2	Activities for the Next Reporting Period	5
1.3	BenefitsCal Collaboration Model (CM)	5
1.3.1	Highlights of the Reporting Period	5
1.3.2	Activities for the Next Reporting Period	6
2.0	Application Development and Test	7
2.1	Requirements and Design	7
2.1.1	Highlights of the Reporting Period – Requirements and Design	7
2.1.2	Activities for the Next Reporting Period – Requirements and Design	7
2.1.3	Highlights of the Reporting Period – User Centered Design (UCD).....	7
2.1.4	Activities for the Next Reporting Period – UCD.....	8
2.2	Development	9
2.2.1	Highlights of the Reporting Period – Development	9
2.2.2	Activities for the Next Reporting Period – Development.....	9
2.2.3	Burndown.....	10
2.3	System Test Execution.....	11
2.3.1	Highlights of the Reporting Period – System Test Execution	11
2.3.2	Activities for the Next Reporting Period – System Test Execution.....	12
2.3.3	User Acceptance Test (UAT) Planning	12
2.3.4	Highlights of the Reporting Period – User Acceptance Test Planning	12
2.3.5	Activities for the Next Reporting Period – User Acceptance Test Planning.....	12
3.0	Performance Test.....	13

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

3.1	Highlights of the Reporting Period – Performance Test.....	13
3.2	Activities for the Next Reporting Period – Performance Test	13
4.0	Security	15
4.1	User Conversion	15
4.1.1	Highlights of the Reporting Period – User Conversion Testing.....	15
4.1.2	Activities for the Next Reporting Period – User Conversion Testing	15
4.2	Security	15
4.2.1	Highlights of the Reporting Period – Security	15
4.2.2	Activities for the Next Reporting Period – Security.....	15
5.0	Communications	16
5.1	Highlights of the Reporting Period.....	16
5.2	Activities for the Next Reporting Period	16
6.0	Appendices.....	16
6.1	Appendix A – Deliverable Summary.....	16
6.2	Appendix B – Risks and Issues Summary.....	17
6.3	Appendix C – Project Work Plan Reports.....	20

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

1.0 Project Management

1.1 Executive Summary

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
Release of Information (ROI) Enhancement	<ul style="list-style-type: none"> ➤ Development continued and on-schedule based on the current State policy and design ➤ Met with County Validation team on the timeline and RACI planning ➤ Shared draft ROI usability report for State Partner and CWDA review during the week of 02/27/23. ➤ Target Production implementation date is 05/26/23.
CalWIN ISS Support	<p>Wave 3</p> <ul style="list-style-type: none"> ➤ Wave 3 training prep in-progress. ➤ Training sessions scheduled.
CW Timeclocks Design	<ul style="list-style-type: none"> ➤ Conducted a Requirement Discovery Activity with Advocates and CBOs to collect their feedback for timeclock requirements (FN-135 and FN-105.1) during the UCD Monthly Meeting on 02/16/23. ➤ Conducted a Requirement Discovery Activity with the Time Limit Committee on 02/21/23. ➤ Met with CalSAWS to discuss revised the Time Clocks Requirements scope and assumptions on 03/02/23.
Continuous Coverage Unwind (CCU) Enhancements	<ul style="list-style-type: none"> ➤ Continued working on the Continuous Coverage Unwind (CCU) enhancements targeted for the March 2023 and April 2023 releases.
GetCalFresh (GCF) Parity List Items	<ul style="list-style-type: none"> ➤ Provided responses to the California Department of Social Services (CDSS) SAWS Cost Estimation Request For Research & Analysis (SCERFRA) with estimates for GCF parity list items. The CDSS to review and provide confirmation on the SCERFRA and priorities to establish a roadmap. ➤ The CDSS to provide SCERFRA for the Social Security Administration (SSA) flow. ➤ Pending direction from CDSS on the SCERFRA response provided with estimates for GCF parity list items

Table 1.1-1 – CalSAWS Executive Summary Agenda Topics

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

1.2 PMO

1.2.1 Highlights of the Reporting Period

- **Deliverables and Work Products submitted:**
 - None for the reporting period.

1.2.2 Activities for the Next Reporting Period

- **Deliverable and Work Product submissions for next week:**
 - FWP 28.11: BenefitsCal Work Plan Monthly Updates – February 2023 on 03/07/23.
 - FWP 29.11: BenefitsCal Monthly Status Report – February 2023 on 03/07/23.
 - DWP 25.13: Monthly M&O Report – February 2023 on 03/09/23.

1.3 BenefitsCal Collaboration Model (CM)

1.3.1 Highlights of the Reporting Period

- Continued to work on preparing a roadmap for CM model prioritized items.
- Identified Collaboration Model priorities as enhancements vs. Action items to perform additional research.

The table below contains all enhancements prioritized by Collaboration Model and their updates from this week:

ID	Summary	Status	Update this Week
CSPM-64317	Modify YouTube videos to address modified or new changes to BenefitsCal.	Prioritization Needed	Effort estimation was conducted
CSPM-41363	Provide a nudge for customers to verify their mailing address.	Analysis In Progress	Got approval on the Effort estimation; Updated BenefitsCal Designs
CSPM-64319	Add direct links to alternate options to apply for assistance on the outage page in BenefitsCal.	Prioritization Needed	N/A
CSPM-64320	Website Functionality: Move the search bar to the main page of the BenefitsCal website.	Prioritization Needed	N/A
CSPM-64321	Report a Change: address the problem of people not being able to upload a verification for a new HH member.	Prioritization Needed	N/A

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

ID	Summary	Status	Update this Week
CSPM-41222	Several enhancements logged where the word “application” in the document upload just needs to be changed to “renewal.”	Prioritization Needed	Sent to Consortium for Approval

Table 1.3-1 – Enhancements Updates, Prioritized by CM

1.3.2 Activities for the Next Reporting Period

- Perform design analysis on enhancements and research on action items identified in the Collaboration Model.

The table below contains all enhancements prioritized by CM (not yet delivered to production) and planned activities for next week.

ID	Summary	Activity for Next Week	Target Delivery Date
CSPM-64317	Modify YouTube videos to address modified or new changes to BenefitsCal.	Complete the effort estimation and send to Consortium for approval	April 2023
CSPM-41363	Provide a nudge for customers to verify their mailing address	Start Implementation	March 2023
CSPM-64319	Add direct links to alternate options to apply for assistance on the outage page in BenefitsCal.	N/A	N/A
CSPM-64320	Website Functionality: Move the search bar to the main page of the BenefitsCal website.	N/A	N/A
CSPM-64321	Report a Change: address the problem of people not being able to upload a verification for a new HH member.	N/A	N/A
CSPM-41222	Several enhancements logged where the word “application” in the document upload just needs to be changed to “renewal.”	Begin Design	April 2023

Table 1.3-2 – Planned Activities for Next Reporting Period for Enhancements, Prioritized by CM

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

2.0 Application Development and Test

2.1 Requirements and Design

2.1.1 Highlights of the Reporting Period – Requirements and Design

➤ **Designs**

- Continued providing functional and design support for ROI and enhancements development.
- Met with CalSAWS to discuss revised the Time Clocks Requirements scope and assumptions on 03/02/23.
- Worked on the enhancements for the March release.
- Worked on the Continuous Coverage Unwind enhancements targeted for the March 2023 and April 2023 releases.
- Met with CalSAWS and Consortium to review SCERFRA 23-515 CAPI Applications on 03/03/23.

2.1.2 Activities for the Next Reporting Period – Requirements and Design

➤ **Designs**

- Continue providing functional and design support for ROI and enhancements development.
- Continue working on the enhancements for March and April releases.
- Continue working on the Continuous Coverage Unwind enhancements targeted for the March 2023 and April 2023 releases.

2.1.3 Highlights of the Reporting Period – User Centered Design (UCD)

➤ **Customer Experience (CX) Measurements Data**

- Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues during the week of 02/27/23.

➤ **Advocate Engagement**

- Prepared materials the UCD process discussion with Advocates for Consortium review during the week of 03/06/23.
- Drafted materials for March UCD Monthly Meeting on 03/16/23.

➤ **Usability Testing**

- Shared draft ROI usability report for State Partner and CWDA review during the week of 02/27/23.

➤ **Enhancements**

- Collaborated with the Design/Functional on Continuous Coverage Unwind (CCU) enhancements for March and April 2023.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

2.1.4 Activities for the Next Reporting Period – UCD

- **CX Measurements Data**
 - Monitor the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues during the week of 03/06/23.
- **Usability Testing**
 - Share ROI usability report with Advocates during the week of 03/06/23.
- **Advocate Engagement**
 - Review materials for UCD process discussion with Advocates with Consortium on 03/07/23.
 - Finalize materials for March UCD Monthly Meeting on 03/16/23.
- **Enhancements**
 - Collaborate with the Design/Functional on Continuous Coverage Unwind (CCU) enhancements for April 2023.

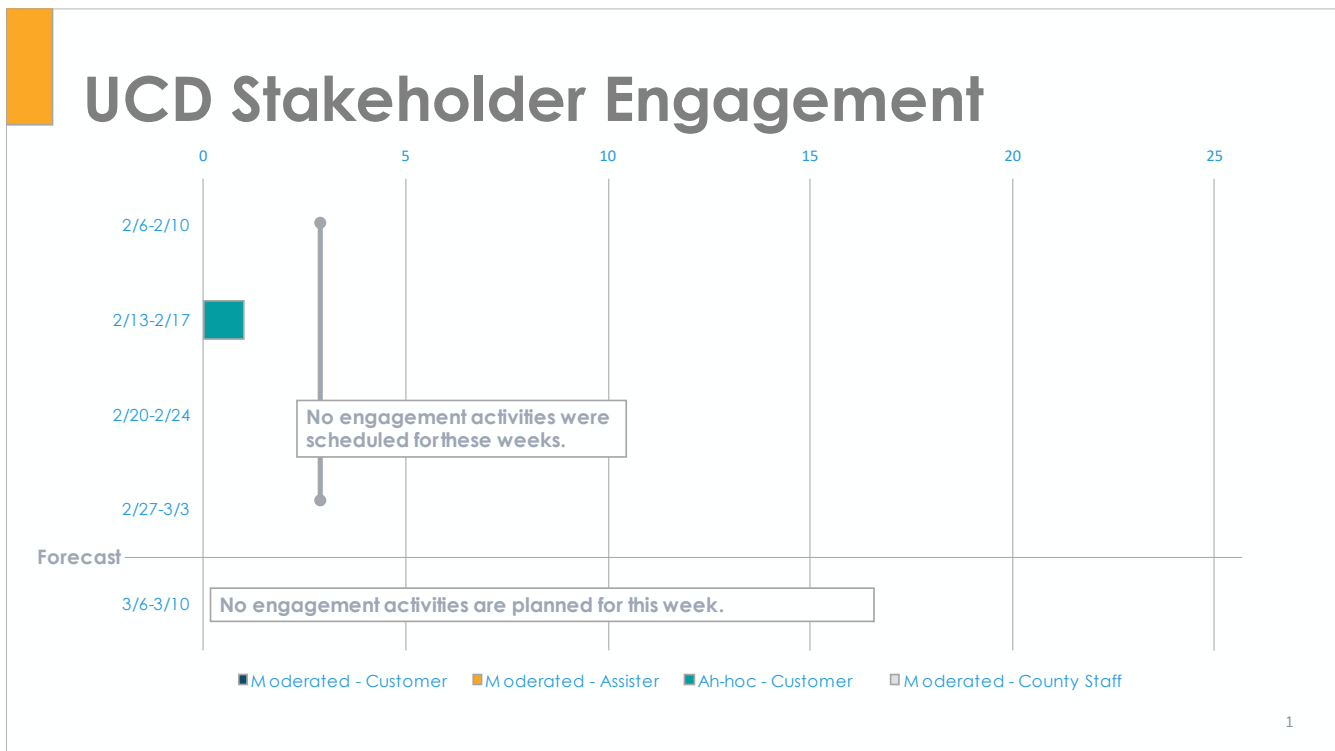


Figure 2.1-1 – UCD Stakeholder Engagement

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

2.2 Development

2.2.1 Highlights of the Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 02/24/23	Actual for Week Ending 02/24/23	Total Planned for the Release	Comments
23.03.30	3	3	14	Finalization of enhancements is in progress. CSPM-62201 is swapped with CSPM-41363.

Table 2.2-1– Enhancement Actuals for Reporting Period

- **Release of Information [DDI]**
 - Development started on 01/02/23.
 - Out of 16 widgets to be completed eight (8) widgets were on hold for DEV Integration testing because APIs were not available and the other eight (8) widgets are development complete.

2.2.2 Activities for the Next Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 03/03/23	Total Planned for the Release	Total Completed for the Release	Comments
23.02.27	1	1	1	CSPM-63274 – CALWIN Wave 2 roll out
23.03.30	0	14	0	Enhancements CSPM-50139 and CSPM-61718 will be spanning across two (2) weeks and are estimated to be completed in the next week.

Table 2.2-2 – Planned Enhancement Work

- **Release of Information [DDI]**
 - Develop eleven (11) widgets.
 - Eight (8) widgets are a DEV Integration testing task which will start once APIs are available.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

Unscheduled Release Updates

➤ **Chatbot**

- For the 25 issues that we have reported earlier related to Currency Slot and Custom Slot for Chinese, Japanese, and Korean languages, the AWS team is updating the Language model at their end and the provided ETA for those fixes is February/March 2023.
- The AWS team stated they have rolled out the fix for the mute detection issue in the Spanish, Korean, and Japanese languages, but during validation, we found the issue was still reproduceable in the Spanish and Korean languages. The AWS team is yet to provide an ETA for the resolution and fix. This is being tracked by CSPM-56537 and a follow up call with AWS team is being schedule for the week starting 01/23/23.

2.2.3 Burndown

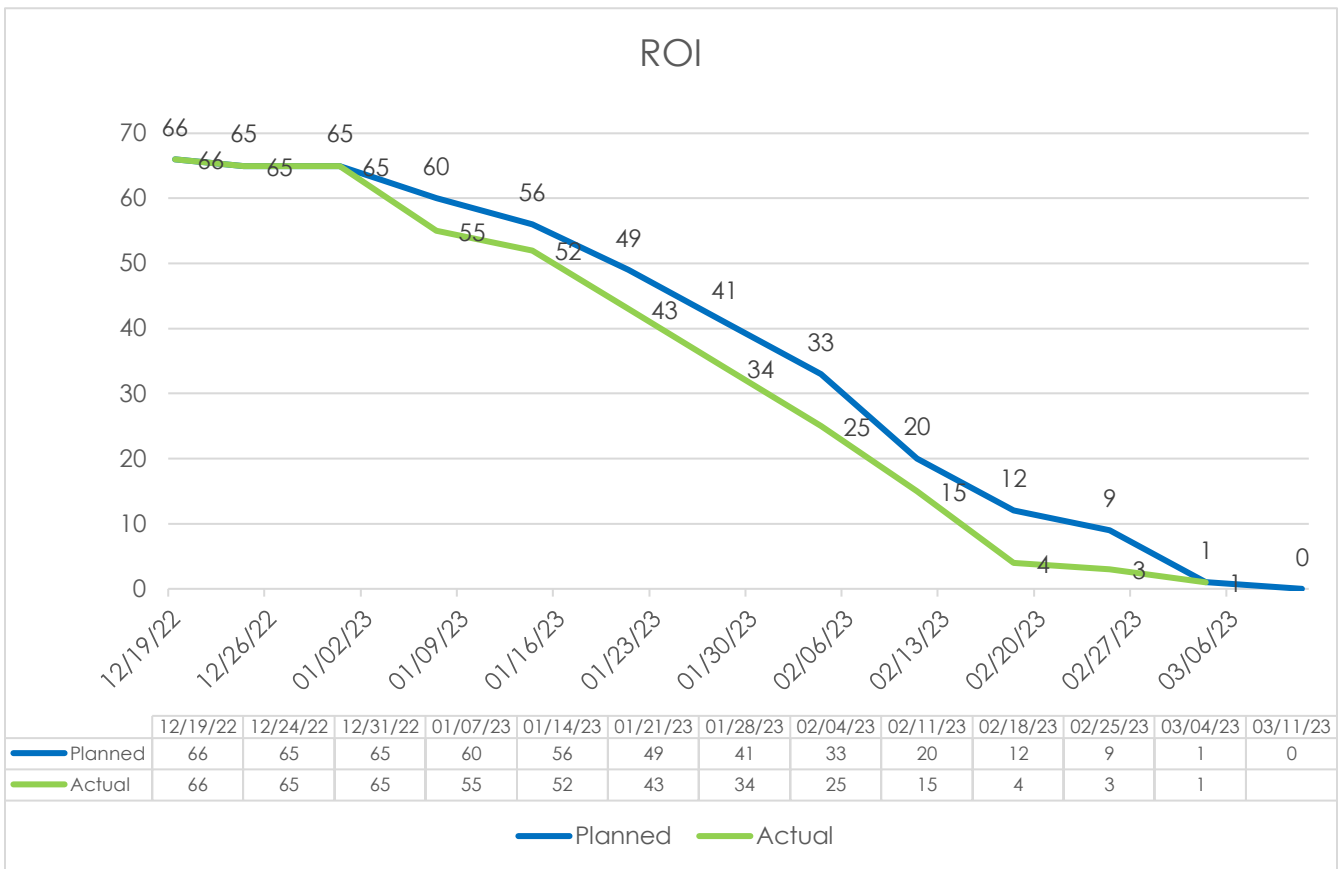


Figure 2.2-1 – Development: ROI

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

2.3 System Test Execution

2.3.1 Highlights of the Reporting Period – System Test Execution

- **Release 23.02.26**
 - Deployed the CalWIN Wave 2 – 23.02.26 into PRD.
- **Release 23.03.30 - March Enhancements**
 - Started validating Enhancements for March Release and conducted Partner Integration calls for any tickets that require E2E validation.
 - One build has been deployed to UAT2 on 03/10/23.
- **Release ROI – 23.05.25**
 - Started functional and non-functional execution.
 - Below are the burndown charts used to track the progress for the Functional and Non-Functional execution.

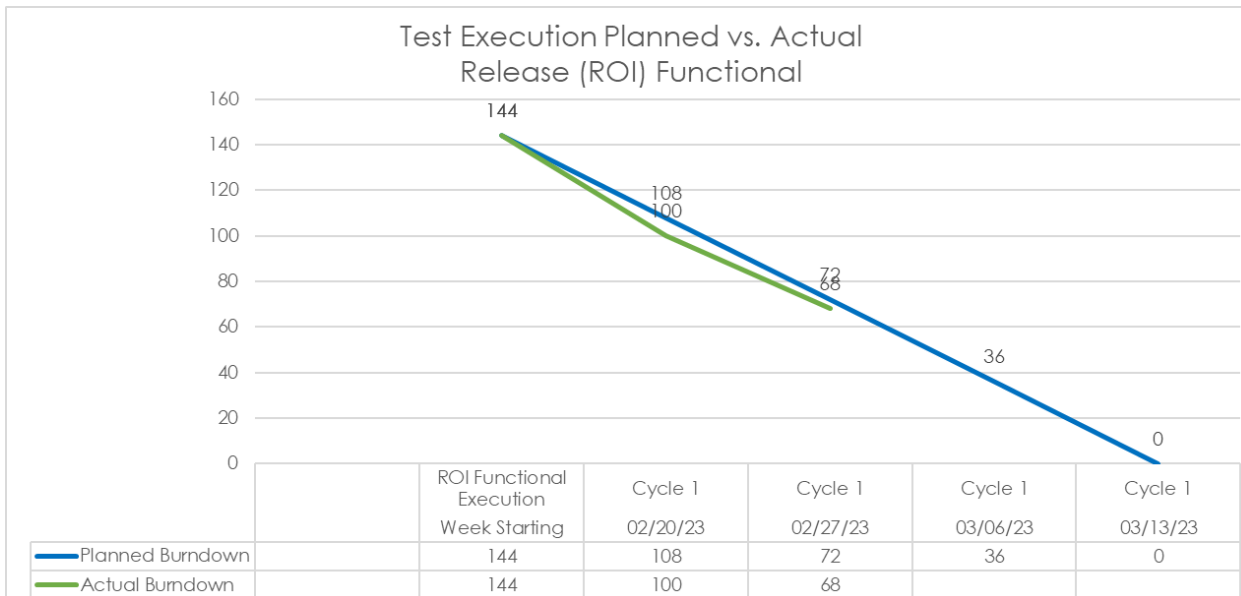


Figure 2.3-1 – ROI Functional Test Execution Burndown

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

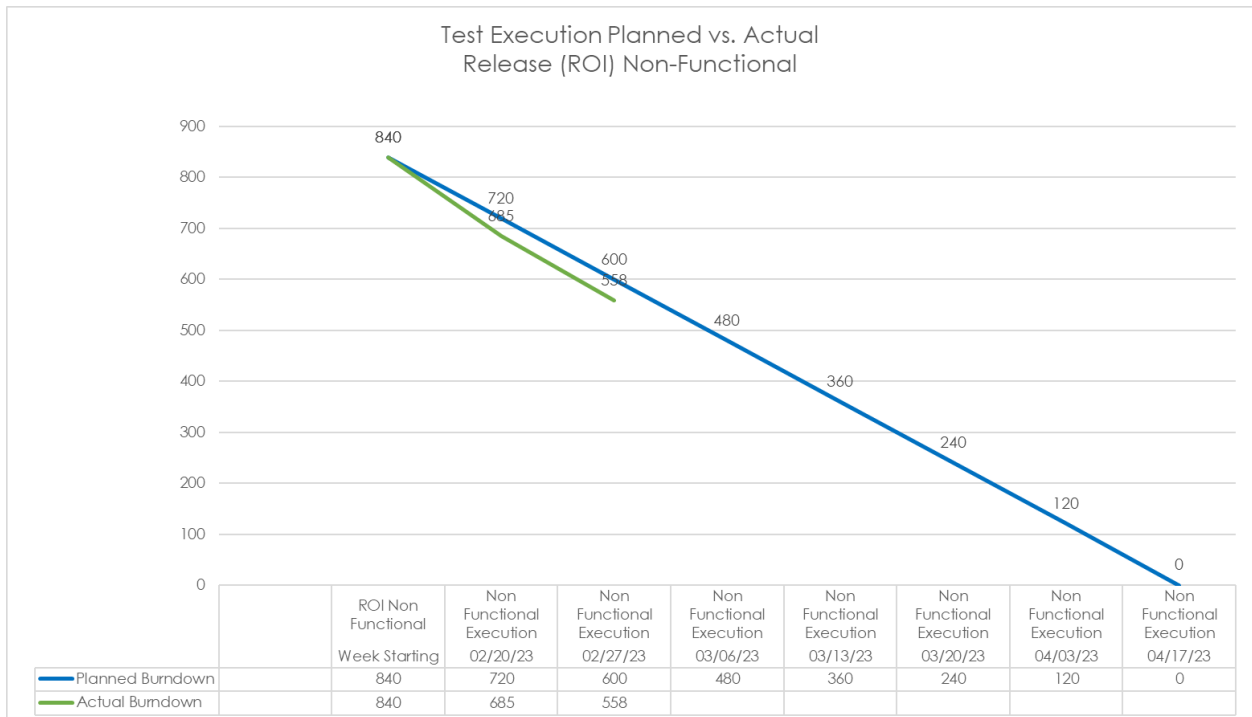


Figure 2.3-2 – ROI Non-Functional Test Execution Burndown

2.4 Activities for the Next Reporting Period – System Test Execution

- **Release ROI – 23.05.25**
 - Continue executing the Test Cases as per the SIT Schedule.
- **Release 23.03.30**
 - Continue validating Enhancements for March Release and conduct Partner Integration calls for any tickets that require E2E validation.

2.5 User Acceptance Test (UAT) Planning

2.5.1 Highlights of the Reporting Period – User Acceptance Test Planning

- **UAT Test Execution**
 - None for the period.

2.5.2 Activities for the Next Reporting Period – User Acceptance Test Planning

- **Test Support**
 - None for the period.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

3.0 Performance Test

3.1 Highlights of the Reporting Period – Performance Test

- The BenefitsCal team is preparing and planning for the March maintenance release performance testing activities. March release build are planned to be migrated to Performance environment in the week of March 12th and performance tests are planned in the week of March 20th.
- Release 5.0 onwards Performance Testing Activities
 - The discussion for the next round of Integration testing with CalSAWS and Hyland team in the month of April is progressing well; team has finalized the scope and volume for the integration tests. Team is planning to meet with partners in early March to discuss and confirm the preparation.

3.2 Activities for the Next Reporting Period – Performance Test

- None for the period.

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
12	03/13/23	03/24/23	March Maintenance Release	Scope: Isolated BenefitsCal performance test with 18 scripts for the March maintenance release Execution: Wednesday, 03/22/23 – Isolated Performance Test Thursday, 03/23/23 – Isolated Performance Test Friday, 03/24/23 – Isolated Performance Test	0%
13	04/03/23	04/14/23	Release 5.0 onward	Scope: The BenefitsCal team has identified 32 scripts leveraging and calling Hyland Imaging APIs for the next round of Integrated testing with CalSAWS and Hyland teams. Executions: Monday, 04/03/23 – Smoke Test Tuesday, 04/04/23 – Integration Performance Test	0%

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
				Thursday, 04/05/23 – Integration Performance Test Monday, 04/10/23 – Endurance Test Tuesday, 04/11/23 – Stress Test Wednesday, 04/12/23 – Optional Day	

Table 3.2-1 – Performance Test Cycles and Test Case Status

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

4.0 Security

4.1 User Conversion

4.1.1 Highlights of the Reporting Period – User Conversion Testing

- **CalWIN Conversion**
 - Reviewed the exception report from the Wave 2 PROD CBO User load which will be used to improve the accuracy of future user loads.

4.1.2 Activities for the Next Reporting Period – User Conversion Testing

- **Perform CBO User Data Validation**
 - Identify Primary Points of Contact (PPOCs) for the rest of the CalWIN Counties to perform Community Based Organization (CBO) user data validation.

4.2 Security

4.2.1 Highlights of the Reporting Period – Security

- **SAST**
 - Executed the weekly Static Application Security Testing (SAST) of the application source code and shared the analysis of the security scan reports with the BenefitsCal Development Team for remediation on 03/02/23.

4.2.2 Activities for the Next Reporting Period – Security

- **Identified Vulnerabilities**
 - After the validation of the identified vulnerabilities, advise on the remediation activities to be performed by the BenefitsCal Development Team. Log defects in Jira for tracking purposes (Weekly recurring activity).
- **AWS SSO for BenefitsCal**
 - Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

5.0 Communications

5.1 Highlights of the Reporting Period

- No activities planned for the reporting period.

5.2 Activities for the Next Reporting Period

- No activities planned for the next reporting period.

6.0 Appendices

6.1 Appendix A – Deliverable Summary

Deliverable Status by Submission

		Complete	Coming Soon	WAC Approval Pending		
DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final Approval
04.11	Requirements Traceability Matrix (BenefitsCal ROI 23.05.25)	N/A	N/A	12/21/22	01/13/23	01/23/23
05.09	General Systems Design (BenefitsCal ROI 23.05.25)	N/A	N/A	12/21/22	01/13/23	01/23/23
08.01	Implement. Complete Report & Final Acceptance – L.A. County	N/A	N/A	05/27/22	06/20/22	TBD
09.01	Maintenance & Operations (M&O) Plan – L.A. County	N/A	N/A	N/A	06/20/22	TBD
11.01	Mobile App Implementation Complete Report – L.A. County	N/A	N/A	05/27/22	06/20/22	TBD

Table 6.1-1 – Deliverable Status for Current Reporting Period

Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
	None for the reporting period.		

Table 6.1-2 – Upcoming Deliverable Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

Work Product Status by Submission

					Complete	Coming Soon	WAC Approval Pending
ID	Work Product Name	DWP	FWP	Final Approval			
17.01	System Security Plan (SSP) – Annual Update	12/07/22	01/11/23	01/19/23			
24.15	CX Monthly Report – December 2022	01/09/23	01/20/23	01/27/23			
24.16	CX Monthly Report – January 2023	02/09/23	02/21/23	02/28/23			
25.12	Monthly M&O Report – January 2023	02/09/23	02/21/23	02/28/23			
25.13	Monthly M&O Report – February 2023	03/09/23	03/20/23	03/28/23			
26.03	BOM Review and License Renewal	01/06/23	01/23/23	02/01/23			
27.03	Certificate Review	01/06/23	01/23/23	02/01/23			
28.09	BenefitsCal Work Plan Monthly Updates – December 2022	N/A	01/06/23	01/16/23			
28.10	BenefitsCal Work Plan Monthly Updates – January 2023	N/A	02/07/23	02/15/23			
28.11	BenefitsCal Work Plan Monthly Updates – February 2023	N/A	03/07/23	03/15/23			
29.09	BenefitsCal Monthly Status Report – December 2022	N/A	01/06/23	01/16/23			
29.10	BenefitsCal Monthly Status Report – January 2023	N/A	02/07/23	02/15/23			
29.11	BenefitsCal Monthly Status Report – February 2023	N/A	03/07/23	03/15/23			

Table 6.1-3 – Upcoming Work Product Deadlines

Upcoming Work Product Deadlines

WP #	Work Product Name	Status	Next Deadline
25.13	Monthly M&O Report – February 2023	On-Track	DWP submission 03/09/23 FWP submission 03/20/23 FWP approval 02/28/23
28.11	BenefitsCal Work Plan Monthly Updates – February 2023	On-Track	FWP submission 03/07/23 FWP approval 03/15/23
29.11	BenefitsCal Monthly Status Report – February 2023	On-Track	FWP submission 03/07/23 FWP approval 03/15/23

Table 6.1-4 – Upcoming Work Product Deadlines

6.2 Appendix B – Risks and Issues Summary

Project Risks and Issues

ID	Title	Details	Status	Impact	Probability	Date Logged
246	Perceived Gap in Functionality	A perceived gap in functionality between GetCalFresh and BenefitsCal was identified. Select features identified within	Open	2	Medium	05/10/21

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

ID	Title	Details	Status	Impact	Probability	Date Logged
		<p>GetCalFresh are not present within BenefitsCal as they are not part of the project requirements, and change requests were logged to address. Impacts BenefitsCal adoption by Community Partners may be lower as they rely on features (like the referral code) to complete their work. The future migration from GCF to BenefitsCal in 2022 is at risk until features are added to BenefitsCal.</p> <p>Status Updates:</p> <p>September 2, 2022:</p> <ul style="list-style-type: none"> ▶ Had multiple meetings with CDSS to discuss the GetCalFresh Gap List with Consortium and CWDA, latest on 08/29/22. There is a bi-weekly meeting cadence. Currently there are few enhancement suggestions from CDSS on partial gaps. <p>October 3, 2022:</p> <ul style="list-style-type: none"> ▶ Continued working sessions with CDSS, CWDA, Consortium and CalSAWS. With the CDSS's analysis, there is total of 41 gaps. 32 of are logged as enhancements for prioritization and the remaining 9 will be discussed at upcoming working sessions. There is also a plan to identify/classify must have vs nice to have items. Next working session is scheduled for 10/05/22. <p>November 11, 2022</p> <ul style="list-style-type: none"> ▶ CDSS is currently reviewing the final list to confirm 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

ID	Title	Details	Status	Impact	Probability	Date Logged
		<p>dispositions and next steps for prioritization. Any items that are identified as “must have” will be taken to collaboration model meeting. CDSS is targeting the end of the calendar year to complete the review.</p> <p>January 08, 2023</p> <ul style="list-style-type: none"> ▶ BenefitsCal team has started working on the effort estimations for the gaps list (31 gaps/52 enhancements). CWDA and Consortium will provide direction on the implementation schedule 				

Table 6.2-1 – Project Risks and Issues

CRFI/CIT/CalSAWS CR Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
None.						

Table 6.2-2 – CITs

The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period.

CRFI ID	To	Subject	Distribution Date	Status	Response Due Date	Primary BenefitsCal Contact	Backup BenefitsCal Contact
None.							

Table 6.2-3 – CRFIs


CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, March 8, 2023

Period: February 27, 2023 to March 5, 2023

6.3 Appendix C – Project Work Plan Reports

Project Timeline

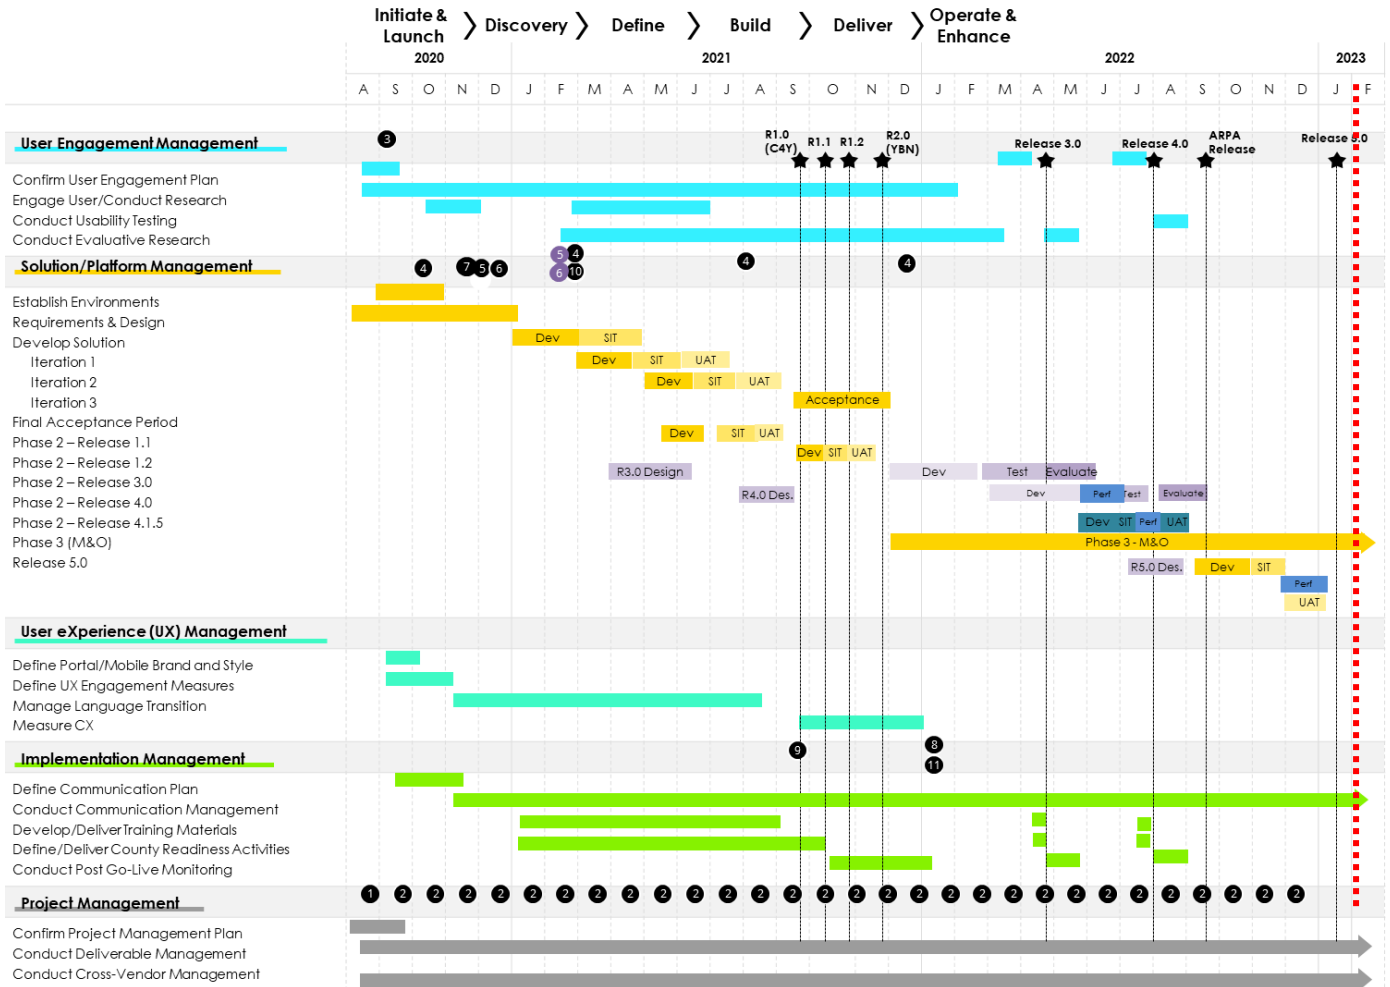

Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

ID	Description	Owner	Due Date
None			

Table 6.3-1 – Overdue Action Items
