

CalSAWS BenefitsCal
(Portal/Mobile) Weekly
Status Report

Reporting Period: April 24, 2023 to April 30, 2023

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

Table of Contents

1.0	Project Management	4
1.1	Executive Summary.....	4
1.2	PMO	5
1.2.1	Highlights of the Reporting Period	5
1.2.2	Activities for the Next Reporting Period	5
1.3	BenefitsCal Collaboration Model (CM)	5
1.3.1	Highlights of the Reporting Period	5
1.3.2	Activities for the Next Reporting Period	5
2.0	Application Development and Test	6
2.1	Requirements and Design	6
2.1.1	Highlights of the Reporting Period – Requirements and Design	6
2.1.2	Activities for the Next Reporting Period – Requirements and Design	6
2.1.3	Highlights of the Reporting Period – User Centered Design (UCD).....	6
2.1.4	Activities for the Next Reporting Period – UCD.....	7
2.2	Development	8
2.2.1	Highlights of the Reporting Period – Development	8
2.2.2	Activities for the Next Reporting Period – Development.....	9
2.2.3	Burndown.....	10
2.3	System Test Execution.....	10
2.3.1	Highlights of the Reporting Period – System Test Execution	10
2.4	Activities for the Next Reporting Period – System Test Execution.....	13
2.5	User Acceptance Test (UAT) Planning.....	13
2.5.1	Highlights of the Reporting Period – User Acceptance Test Planning	13
2.5.2	Activities for the Next Reporting Period – User Acceptance Test Planning.....	14

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

3.0	Performance Test.....	14
3.1	Highlights of the Reporting Period – Performance Test.....	14
3.2	Activities for the Next Reporting Period – Performance Test	14
4.0	Security	15
4.1	User Conversion	15
4.1.1	Highlights of the Reporting Period – User Conversion Testing.....	15
4.1.2	Activities for the Next Reporting Period – User Conversion Testing	15
4.2	Security	16
4.2.1	Highlights of the Reporting Period – Security	16
4.2.2	Activities for the Next Reporting Period – Security.....	16
5.0	Communications	16
5.1	Highlights of the Reporting Period.....	16
5.2	Activities for the Next Reporting Period	16
6.0	Appendices	16
6.1	Appendix A – Deliverable Summary.....	16
6.2	Appendix B – Risks and Issues Summary.....	18
6.3	CRFI/CIT/CalSAWS CR Communications Information	19
6.4	Appendix C – Project Work Plan Reports.....	20

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

1.0 Project Management

1.1 Executive Summary

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
Release of Information (ROI) Enhancement	<ul style="list-style-type: none"> ➤ Continued supporting County Validation testing for the ROI functionality. ➤ County Validation period 04/10/23–04/21/23. ➤ Continued providing support to independent testing which started during the week of 03/20/23. ➤ Target Production release 23.05 (based on draft ACL, and design). Will review the final ACL for potential downstream design implications.
CalWIN ISS Support	<p>Wave 3</p> <ul style="list-style-type: none"> ➤ Health metrics generation and M&O service management support are in-progress. ➤ Provided site visits to Santa Barbara, Venture and Orange County <p>Wave 4</p> <ul style="list-style-type: none"> ➤ Monitor and validate any new CBOs added post the mock conversion run. ➤ Customer communication campaign plan review with the consortium, and the Gainwell team is complete. ➤ BenefitsCal Tier-1 training preparations are in progress.
Collaboration Model	<ul style="list-style-type: none"> ➤ Started working on next collaboration meeting agenda prep, which is scheduled for June 2023.
Monthly UCD Meeting	<ul style="list-style-type: none"> ➤ Conducted Monthly UCD meeting on 04/26/23 and provided a ROI demo to stakeholders based on the current design
Training Environment	<ul style="list-style-type: none"> ➤ End-to-end Functional testing continued during the week of 04/24/23. ➤ Will participate in next Training committee meeting for the communication logistics for the counties.
GetCalFresh (GCF) Parity List Items	<ul style="list-style-type: none"> ➤ Next b-weekly meeting is scheduled on 05/03/23. ➤ CDSS will confirm the mapping of the components planned for decommissioning to parity list items, feedback on SCERFRA 23-512 and confirm the funding to establish a roadmap.

Table 1.1-1 – CalSAWS Executive Summary Agenda Topics

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

1.2 PMO

1.2.1 Highlights of the Reporting Period

- **Deliverables and Work Products submitted:**
 - None for the reporting period.

1.2.2 Activities for the Next Reporting Period

- **Deliverable and Work Product submissions for next week:**
 - WP 28.13: BenefitsCal Work Plan Monthly Updates – April 2023 on 05/05/23.
 - WP 29.13: BenefitsCal Monthly Status Report – April 2023 on 05/05/23.

1.3 BenefitsCal Collaboration Model (CM)

1.3.1 Highlights of the Reporting Period

- Continued to prepare a roadmap for the CM model prioritized items.
- Identified Collaboration Model priorities as enhancements versus action items to perform additional research.

The table below contains all enhancements prioritized by Collaboration Model and their updates from this week:

ID	Summary	Status	Update this Week
CSPM-64320	Website Functionality: Move the search bar to the main page of the BenefitsCal website.	Design Update Needed	Continued Design Research

Table 1.3-1 – Enhancements Updates, Prioritized by CM

1.3.2 Activities for the Next Reporting Period

- Perform design, development, and implementation analysis for enhancements and research action items identified in the Collaboration Model.

The table below contains all enhancements prioritized by CM (not yet delivered to production) and planned activities for the next week.

ID	Summary	Activity for Next Week	Target Delivery Date
CSPM-64320	Website Functionality: Move the search bar to the main page of the BenefitsCal website.	Continue with Research & Design Updates	June 2023

Table 1.3-2 – Planned Activities for Next Reporting Period for Enhancements, Prioritized by CM

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

2.0 Application Development and Test

2.1 Requirements and Design

2.1.1 Highlights of the Reporting Period – Requirements and Design

➤ Designs

- Continued providing functional and design support for ROI and enhancements development.
- Continued working on the May 2023 release enhancements.
- Continued working on the June 2023 enhancements.
- Met with CDSS to discuss enhancement CSPM-57458: Language Updates for RCA and TCVAP on 04/27/23.
- Presented Release of Information (ROI) Demo to Advocate and CBO Community during the UCD Monthly Meeting on 04/26/23.
- Started pre-design work on CalWORKs Time Clocks for requirements FN-105.1 and FN-135.
- Supported preparation for the Release of Information (ROI) County Demo hosted by the CalSAWS BAs on 05/04/23.

2.1.2 Activities for the Next Reporting Period – Requirements and Design

➤ Designs

- Continue providing functional and design support for ROI and enhancements development.
- Continue working on the May 2023 release enhancements.
- Continue working on the June 2023 enhancements.
- Attend and support the Release of Information (ROI) County Demo hosted by the CalSAWS BAs on 05/04/23.
- Continue pre-design work on CalWORKs Time Clocks for requirements FN-105.1 and FN-135.

2.1.3 Highlights of the Reporting Period – User Centered Design (UCD)

➤ Customer Experience (CX) Measurements Data

- Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues during the week of 04/24/23.
- Finalized the FWP 24.17: CX Report – Feb/March 2023.

➤ Enhancements

- Continued planning and scheduling for Collaboration Model enhancements that require additional clarification to define requirements and make estimations.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

- **Advocate Engagement**
 - Shared materials with the Advocate and CBO community to try our ROI functionality and share their comments by 05/05/23.
 - Facilitated the UCD Monthly Meeting on 04/26/23.
- **Customer Engagement**
 - Conducted one (1) focus group with customers to inform the design of enhancements on 04/24/23.

2.1.4 Activities for the Next Reporting Period – UCD

- **CX Measurements Data**
 - Monitor the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues during the week of 05/01/23.
- **Advocate Engagement**
 - Collect and start review of Advocate & CBO comments on ROI functionality on 05/05/23.
- **Enhancements**
 - Continue to draft materials and prepare for Collaboration Model enhancements that require additional clarification to define requirements and make estimations.
 - Facilitate a session with Collaboration Model participants to clarify enhancement requests during the week of 05/01/23.
- **Customer Engagement**
 - Conduct one (1) focus group with customers to inform the design of enhancements by 04/26/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

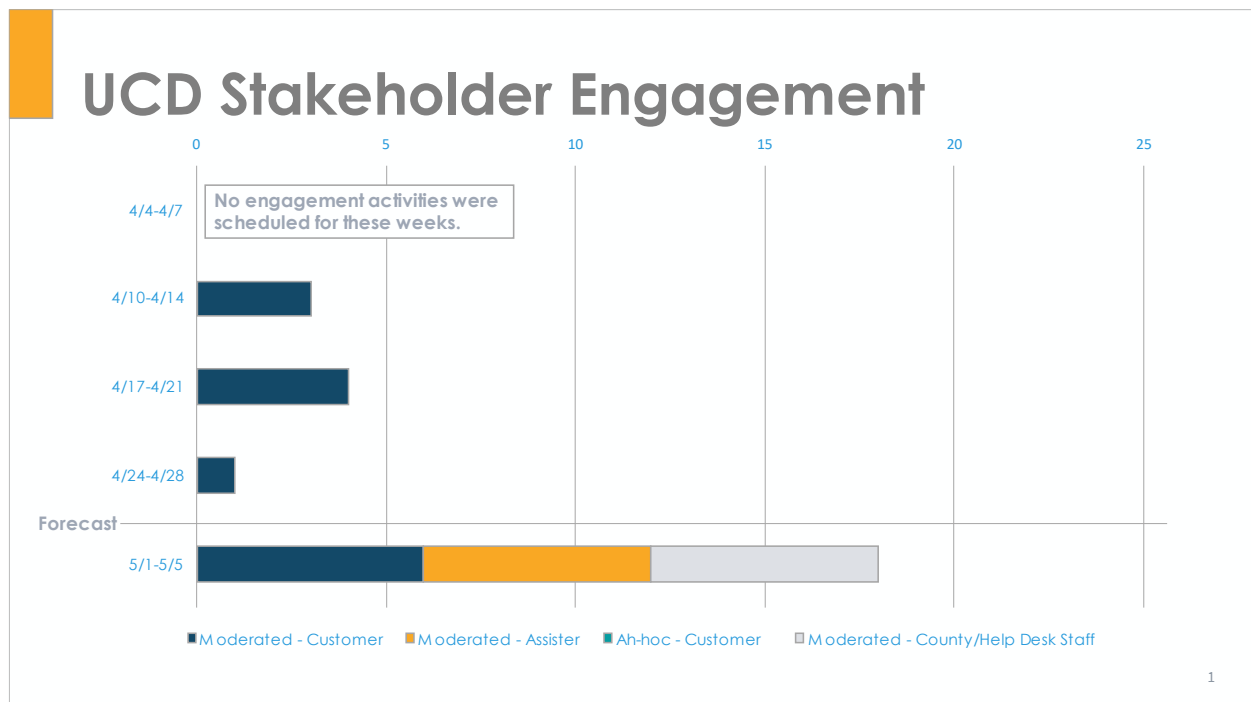


Figure 2.1-1 – UCD Stakeholder Engagement

2.2 Development

2.2.1 Highlights of the Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 04/28/23	Actual for Week Ending 04/21/23	Total Planned for the Release	Comments
23.04.24	1	1	1	Release 23.04.24 was deployed to production (CALWIN Wave 3)
23.05.09	2	2	2	CSPM-65179 & CSPM-65624 are planned for Priority release
23.05.25	6	5	18	CSPM-63247 moved out since that is internal enhancement for performance testing and is not supposed to be deployed on PROD, hence total count updated to 19

Table 2.2-1– Enhancement Actuals for Reporting Period

- **Release of Information [DDI]**
 - Completed three (3) widgets.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

- Support for UAT testing is in progress.

2.2.2 Activities for the Next Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 02/05/23	Total Planned for the Release	Total Completed for the Release	Comments
23.05.09	2	2	2	CSPM-65179 & CSPM-65624 are planned for priority release
23.05.25	6	18	10	CSPM-63247 moved out since that is internal enhancement for performance testing and is not supposed to be deployed on PROD, hence total count updated to 19

Table 2.2-2 – Planned Enhancement Work

- **Release of Information [DDI]**
 - Support for UAT testing is in progress.

Unscheduled Release Updates

- **Chatbot**
 - For the 25 issues that we have reported earlier related to Currency Slot and Custom Slot for Chinese, Japanese, and Korean languages, the AWS team is updating the Language model at their end and the provided ETA for those fixes is May 2023.
 - The AWS team stated they have rolled out the fix for the mute detection issue in the Spanish, Korean, and Japanese languages, but during validation, we found the issue was still reproduceable in the Spanish and Korean languages. The AWS team is yet to provide an ETA for the resolution and fix. This is being tracked by CSPM-56537.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

2.2.3 Burndown

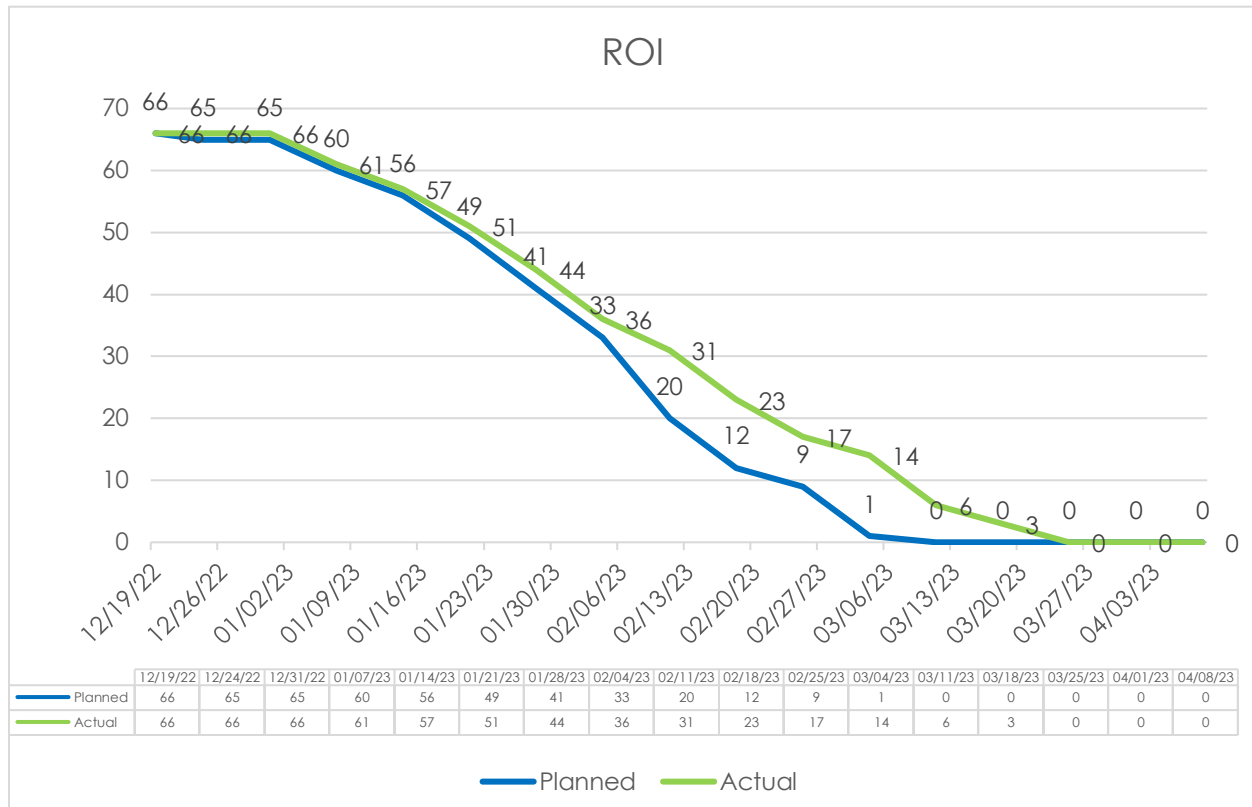


Figure 2.2-1 – Development: ROI

2.3 System Test Execution

2.3.1 Highlights of the Reporting Period – System Test Execution

- **Release 23.04.24 – CalWIN Wave 3**
 - Executed CalWIN Wave 3 Go-Live and Default Office scripts on PRD.
- **Release 23.04.25 – May Enhancements**
 - Continued validating the enhancements planned for the May Release; the first build was sent to UAT on 04/24/23.
- **Release ROI – 23.05.21**
 - Continued coordinating with CalSAWS for any partner related defects and deploying fixes for any issues found during UAT or Independent Testing.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

Below are the burndown charts used to track the progress for the Functional and Non-Functional execution.

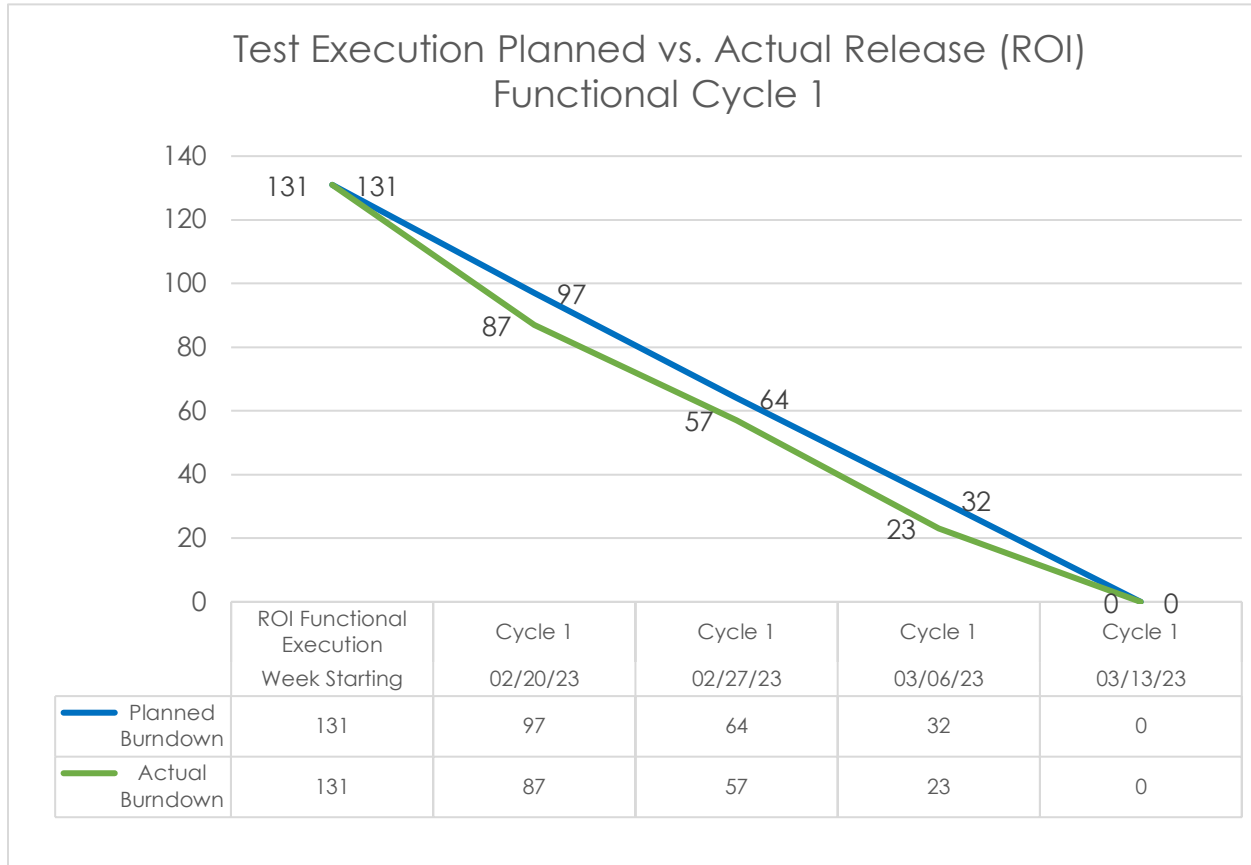


Figure 2.3-1 – ROI Functional Test Execution – Cycle 1 Burndown

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

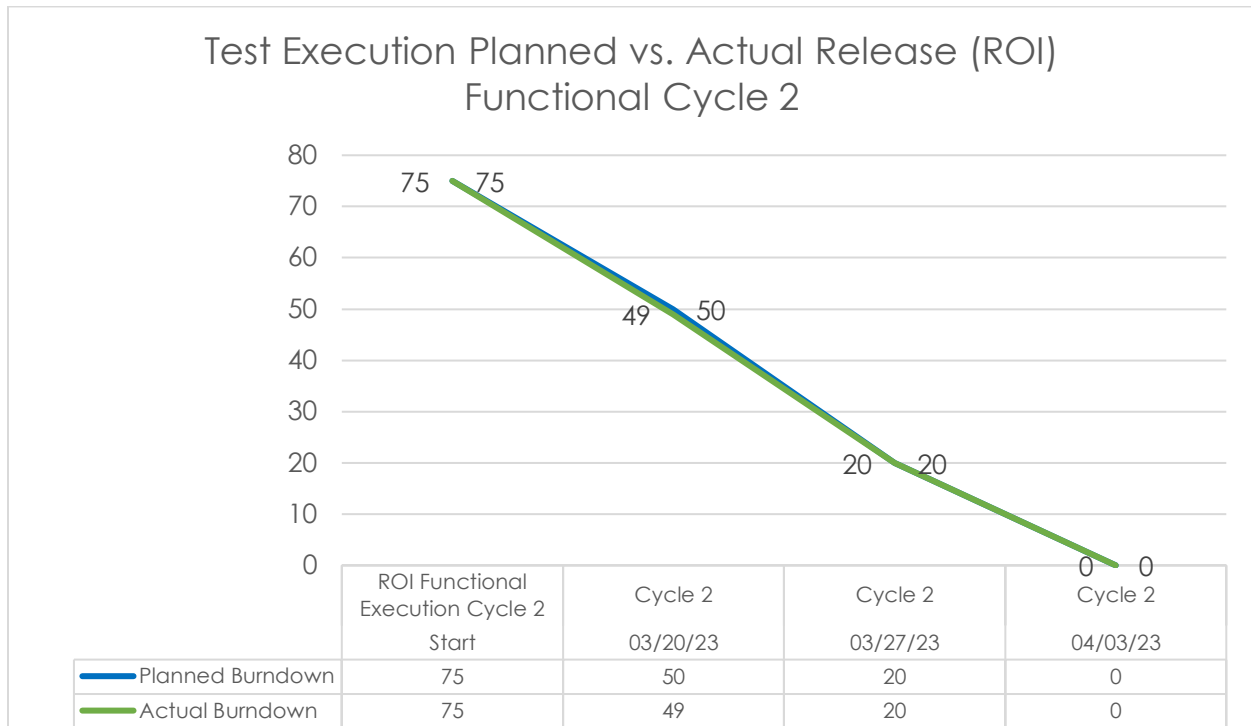


Figure 2.3-2 – ROI Functional Test Execution – Cycle 2 Burndown

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

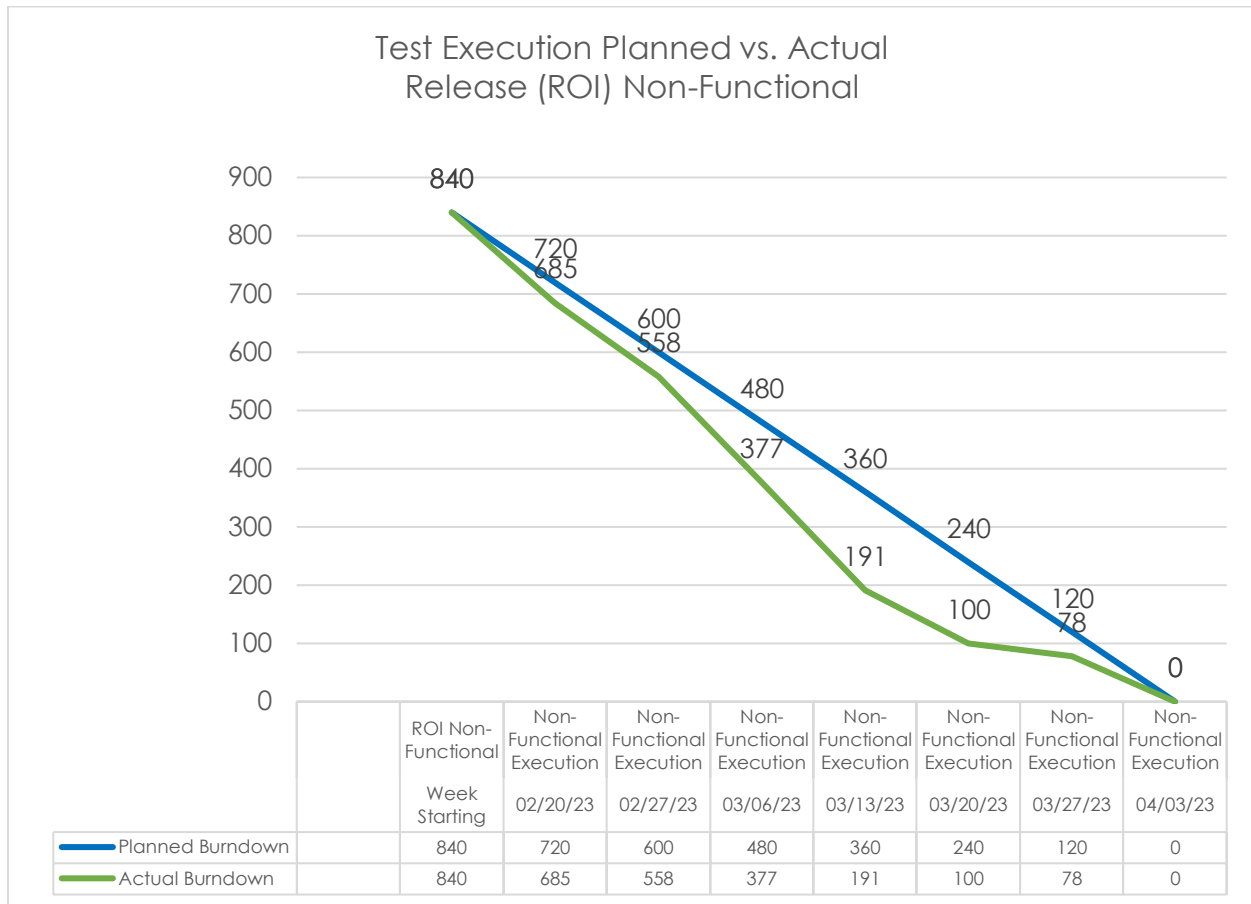


Figure 2.3-3 – ROI Non-Functional Test Execution Burndown

2.4 Activities for the Next Reporting Period – System Test Execution

- **Release ROI – 23.05.21**
 - Continue deploying fixes for ROI Execution based on the Independent Testing and UAT Testing defects (if any).
- **Release 23.05.09**
 - Deploy the priority release – 23.05.09 into PRDSTG
- **Release ROI – 23.05.25**
 - Continue validating May Release Enhancements and coordinate with the partners for any end-to-end validation.

2.5 User Acceptance Test (UAT) Planning

2.5.1 Highlights of the Reporting Period – User Acceptance Test Planning

- **UAT Test Execution**
 - None for the period.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

2.5.2 Activities for the Next Reporting Period – User Acceptance Test Planning

- **Test Support**
 - None for the period.

3.0 Performance Test

3.1 Highlights of the Reporting Period – Performance Test

- **Release ROI – 23.05.25 performance test plan**
 - The performance team completed three (3) new scenario scripts in the SIT environment and is currently working on migrating the stable code base to the performance environment to validate the scripts and prepare for test executions. The BenefitsCal Team is awaiting CalSAWS environment availability confirmation to begin the smoke and performance test execution starting 05/05/23.
- **CalWIN ISS Support and BenefitsCal May monthly release Integrated performance test plan**
 - The next/second round of Integrated performance test inclusive of Load, Endurance, and Stress tests with the BenefitsCal, CalSAWS and Hyland teams is planned to start on 05/15/23. The BenefitsCal Team will deploy the May monthly release codebase to execute the Integrated tests on the latest build.

3.2 Activities for the Next Reporting Period – Performance Test

- **Release ROI – 23.05.25 performance test plan**
 - Continuing scripting new ROI scenarios and enhancing the BenefitsCal performance scripts to incorporate and performance test ROI capabilities.

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
13	04/10/23	05/16/23	Release of Information (ROI) Enhancement	Scope: Isolated BenefitsCal performance test with three (3) new scripts and enhancements to existing Apply for Benefits scripts. Execution: Planned for 05/05/23 through 05/16/23. Dates to be finalized with the CalSAWS Team based on their environment alignment.	40%

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
13	05/15/23	06/02/23	CalWIN Statewide rollout And BenefitsCal May monthly release	<p>Scope: The BenefitsCal team has identified 32 scripts leveraging and exercising Hyland Imaging APIs for the 2nd round of Integrated testing with the CalSAWS and Hyland teams.</p> <p>Executions: Monday, 05/15/23 – Smoke Test Wednesday, 05/17/23 – Integration Performance Test Thursday, 05/18/23 – Endurance Test Friday, 05/19/23 – Stress Test Monday, 05/22/23 – Contingency Test Day 1 Thursday, 05/25/23 – Contingency Test Day 2 Tuesday, 05/30/23 – Contingency Test Day 3 Wednesday, 05/31/23 – Contingency Test Day 4 Friday, 06/02/23 – Contingency Test Day 5</p>	0%

Table 3.2-1 – Performance Test Cycles and Test Case Status

4.0 Security

4.1 User Conversion

4.1.1 Highlights of the Reporting Period – User Conversion Testing

➤ **CalWIN Conversion**

- Reviewed the exception report detailing the status of the Wave 3 Prod CBO user load and addressed feedback accordingly.

4.1.2 Activities for the Next Reporting Period – User Conversion Testing

➤ **Perform CBO User Data Validation**

- Identify Primary Points of Contact (PPOCs) for the rest of the CalWIN Counties to perform Community Based Organization (CBO) user data validation.
- Review the Exception Report generated from the Wave 3 Prod CBO user load

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

4.2 Security

4.2.1 Highlights of the Reporting Period – Security

- **SAST**
 - Executed the weekly Static Application Security Testing (SAST) of the application source code and shared the analysis of the security scan reports with the BenefitsCal Development Team for remediation on 04/28/23.

4.2.2 Activities for the Next Reporting Period – Security

- **Identified Vulnerabilities**
 - After the validation of the identified vulnerabilities, advise on the remediation activities to be performed by the BenefitsCal Development Team. Log defects in Jira for tracking purposes (Weekly recurring activity).
- **AWS SSO for BenefitsCal**
 - Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.

5.0 Communications

5.1 Highlights of the Reporting Period

- No activities planned for the reporting period.

5.2 Activities for the Next Reporting Period

- No activities planned for the next reporting period.

6.0 Appendices

6.1 Appendix A – Deliverable Summary

Deliverable Status by Submission

							Complete	Coming Soon	WAC Approval Pending
DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final Approval			
08.01	Implement, Complete Report & Final Acceptance – L.A. County	N/A	N/A	05/27/22	06/20/22	04/14/23			
09.01	Maintenance & Operations (M&O) Plan – L.A. County	N/A	N/A	N/A	06/20/22	TBD			
11.01	Mobile App Implementation Complete Report – L.A. County	N/A	N/A	05/27/22	06/20/22	04/14/23			

Table 6.1-1 – Deliverable Status for Current Reporting Period

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
	None for the reporting period.		

Table 6.1-2 – Upcoming Deliverable Deadlines

Work Product Status by Submission

Complete	Coming Soon	WAC Approval Pending
----------	-------------	----------------------

ID	Work Product Name	DWP	FWP	Final Approval
24.17	CX Report – Feb/March 2023	04/10/23	04/20/23	04/27/23
25.13	Monthly M&O Report – February 2023	03/09/23	03/21/23	03/28/23
25.14	Monthly M&O Report – March 2023	04/07/23	04/19/23	04/26/23
26.04	BOM Review and License Renewal	N/A	04/07/23	04/18/23
27.04	Certificate Review	N/A	04/07/23	04/18/23
28.12	BenefitsCal Work Plan Monthly Updates – March 2023	N/A	04/05/23	04/14/23
29.11	BenefitsCal Monthly Status Report – February 2023	N/A	03/07/23	03/16/23
29.12	BenefitsCal Monthly Status Report – March 2023	N/A	04/05/23	04/14/23

Table 6.1-3 – Upcoming Work Product Deadlines

Upcoming Work Product Deadlines

WP #	Work Product Name	Status	Next Deadline
28.13	BenefitsCal Work Plan Monthly Updates – April 2023	On-Track	FWP submission 05/05/23 FWP approval 05/15/23
29.13	BenefitsCal Monthly Status Report – April 2023	On-Track	FWP submission 05/05/23 FWP approval 05/15/23

Table 6.1-4 – Upcoming Work Product Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

6.2 Appendix B – Risks and Issues Summary

Project Risks and Issues

ID	Title	Details	Status	Impact	Probability	Date Logged
246	Perceived Gap in Functionality	<p>A perceived gap in functionality between GetCalFresh and BenefitsCal was identified. Select features identified within GetCalFresh are not present within BenefitsCal as they are not part of the project requirements, and change requests were logged to address. Impacts BenefitsCal adoption by Community Partners may be lower as they rely on features (like the referral code) to complete their work. The future migration from GCF to BenefitsCal in 2022 is at risk until features are added to BenefitsCal.</p> <p>Status Updates:</p> <p>September 2, 2022:</p> <ul style="list-style-type: none"> ▶ Had multiple meetings with CDSS to discuss the GetCalFresh Gap List with Consortium and CWDA, latest on 08/29/22. There is a bi-weekly meeting cadence. Currently there are few enhancement suggestions from CDSS on partial gaps. <p>October 3, 2022:</p> <ul style="list-style-type: none"> ▶ Continued working sessions with CDSS, CWDA, Consortium and CalSAWS. With the CDSS's analysis, there is total of 41 gaps. 32 of are logged as enhancements for prioritization and the remaining 9 will be discussed at upcoming working sessions. There is also a plan to identify/classify must have vs nice to have items. Next working session is scheduled for 10/05/22. <p>November 11, 2022</p> <ul style="list-style-type: none"> ▶ CDSS is currently reviewing the final list to confirm dispositions and next steps for prioritization. Any items that are identified as "must have" will be taken to 	Open	2	Medium	05/10/21

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

ID	Title	Details	Status	Impact	Probability	Date Logged
		collaboration model meeting. CDSS is targeting the end of the calendar year to complete the review. January 08, 2023 ► BenefitsCal team has started working on the effort estimations for the gaps list (31 gaps/52 enhancements). CWDA and Consortium will provide direction on the implementation schedule.				

Table 6.2-1 – Project Risks and Issues

6.3 CRFI/CIT/CalSAWS CR Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
None.						

Table 6.3-1 – CITs

The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period.

CRFI ID	To	Subject	Distribution Date	Status	Response Due Date	Primary BenefitsCal Contact	Backup BenefitsCal Contact
None.							

Table 6.3-2 – CRFIs


CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, May 3, 2023

Period: April 24, 2023 to April 30, 2023

6.4 Appendix C – Project Work Plan Reports

Project Timeline

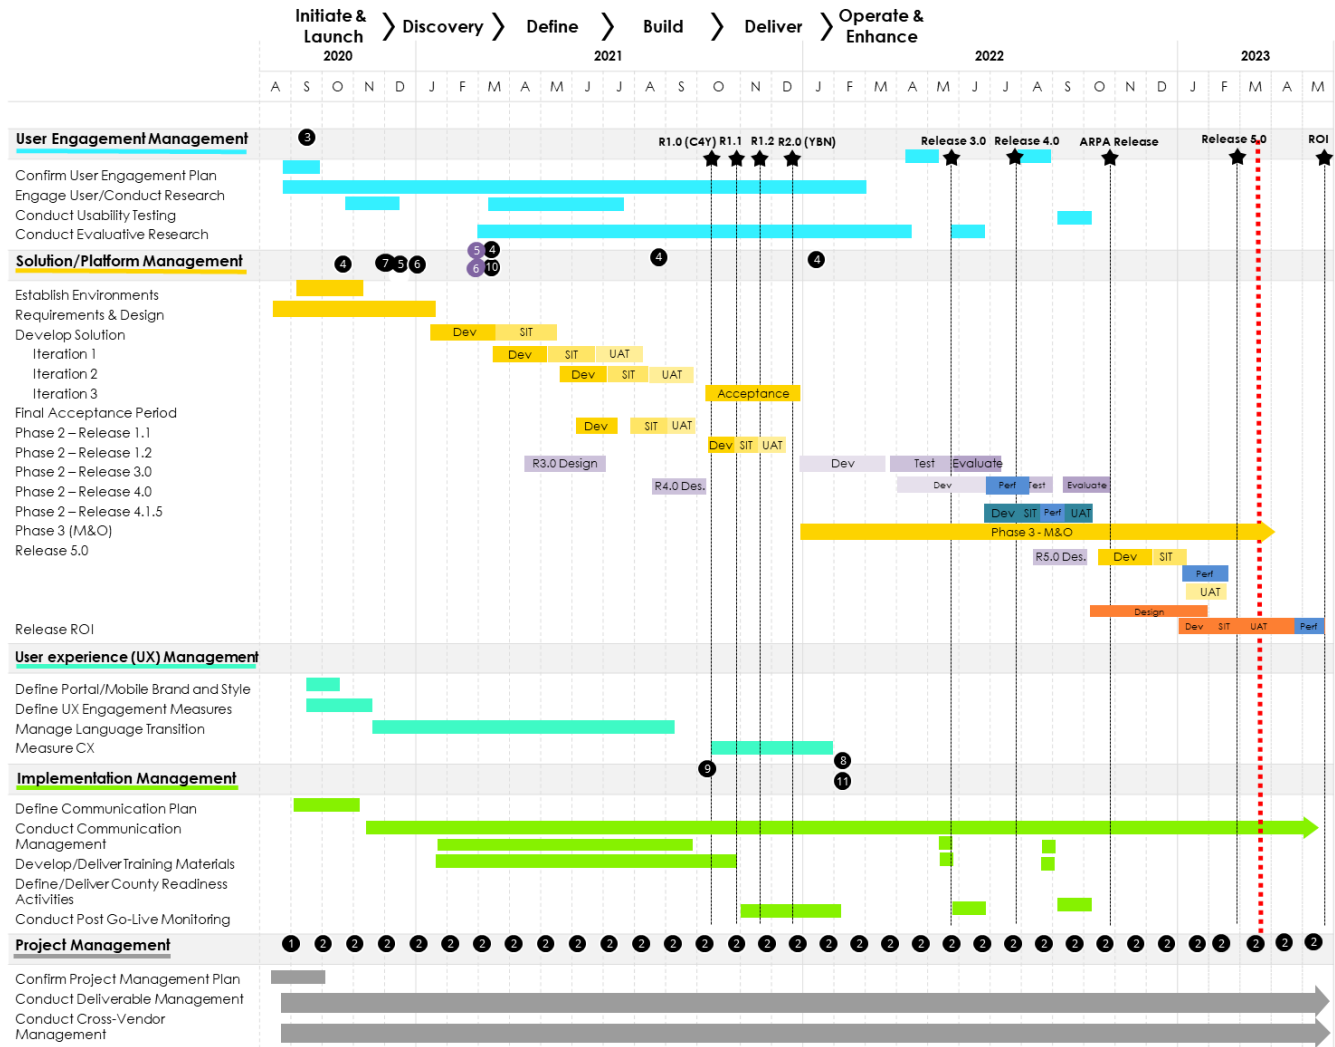

Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

ID	Description	Owner	Due Date
None			

Table 6.4-1 – Overdue Action Items
