

Wave 5 Implementation Readiness Dashboard and Packet

April 28, 2023

The **Implementation Readiness Packet & Dashboard** present a **high-level view of Project Readiness** to CalWIN Counties with information related to CalWIN Migration, BenefitsCal, and Central Print. Status will include key metrics related to the overall “health” of the Implementation effort based on measurable metrics and milestones for Wave 5. Project Milestones are identified by project team leads and CalSAWS Project leadership.

The Dashboard and Packet serve to inform Project Leadership and Counties on the progression and completion of Key Project and County Milestones. The packet will be distributed to the CalWIN Counties monthly. The information contained in the document reflects data as of **April 28, 2023**.



Readiness Packet





Application Readiness

Development / System Test

Deploy Release 23.07	07/24/2023	Project
----------------------	------------	---------

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Application Readiness: UAT

User Acceptance Test

CalSAWS UAT Plan Approved	Completed	Project
Select and Confirm CalSAWS UAT Participants for UAT	Completed	Both
UAT Users Loaded to ForgeRock/UAT Environments & Applications	Completed	Project
Complete UAT Test Script Development	Completed	Project
Complete UAT Environment setup	Completed	Project
Complete UAT Application Training	May 2 – June 21, 2022 – Group 1 June 13 – July 21, 2022– Group 2	County
Conduct UAT Execution Kick-Off	June 21 and 22, 2022 – Group 1 July 20 and 21, 2022– Group 2	Both
Complete UAT Test Execution	June 27- July 22, 2022 – Group 1 July 25 – August 19, 2022– Group 2	Both
Complete UAT Retest	August 22 – Sept 2, 2022	Both
Evaluate and confirm Exit criteria	Metric/Completion to Plan September 8, 2022	Project

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Application Readiness: Imaging

Functionality

Severity 1 & 2 Defects Resolved from UAT	UAT Complete	No Sev 1 or 2 defects reported	Project
--	--------------	--------------------------------	---------

Performance Testing

Hyland Platform Performance Test	Complete	Metric/Completion to Plan	Project
Additional Hyland Platform Performance Test	Complete	Test completed. Configuration tuned to address findings for 58+ county load.	Project
Integrated Imaging Performance Test (Informational)	In Progress	58+ county load testing scheduled to be complete on 6/7.	Project

Images Migration

County Export of Legacy Images	In Progress		County
Hyland Receive and Upload Images to Production Environment	In Progress		Project
Distribute CIT for Counties to install Webscan Kit and Virtual Printer	Completed	CIT #0110-22 distributed on April 19, 2022	Project

Imaging UAT

7/11/22-7/22/22 (retest 8/8/22-8/12/22, 9/8/2022)	Completed	61 of 61 scripts completed and passed.
---	-----------	--

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Application Readiness: Contact Center

Contact Center

Technical Connectivity	0%	
Update IVR Contact Flows for each County	3 of 3 approved	Both
Approval of County Contact Center SCRs*	0 of 3	County
Regression Test of entire Contact Center solution	0%	Project
Model Office Testing – tentative start 8/07/2023	0%	Both

*Contact Center SCRs:
CA-240168 – Alameda
CA-240169 – Sonoma
CA-240170 – Fresno

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Application Readiness: Central Print

Kickoff

Kickoff Meeting	Completed		Both
-----------------	-----------	--	------

Configuration/Validation

Configuration Meetings	In Progress	1 Completed of 3 Planned	Both
Validation Meetings	Not Started	0 Completed of 3 Planned	Both
Configuration Load	Not Started	0 Completed of 3 Planned	Project

Setup and Training

Portal Users Loaded	Not Started	0 Completed of 3 Planned	Project
Inventory Confirmed	Not Started	0 Completed of 1 Planned	Project
Postage Received	Not Started	0 Completed of 3 Planned	County
Training Materials	Completed		Project
Training Delivery	Not Started	0 Completed of 2 Planned	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

Application Readiness: BenefitsCal Conversion



Conversion Readiness

Provide extract of the CBO to the counties	Not Started	Target 05/04/2023	Project
Extract CBO User information from MyBCW for Wave 5 counties to perform mock run 1	Not Started	Target 05/01/2023	Project
Extract CBO User information from MyBCW Prod for Wave 5 counties	Not Started	Target 08/08/2023	Project

Converted Data Test

Validate CBO user load into ForgeRock – Mock Run 1	Not Started	Target 06/16/2023	Project
--	-------------	-------------------	---------

Training Delivery

Deliver training for CSC and Help Desk staff	Not Started	Target – 07/18/2023, 07/20/2023, 07/25/2023	Project
Deliver training for CBOs - Community Based Organizations	Not Started	Target – 07/27/2023	Project

Communications

Confirm Communications Plan for BenefitsCal	Not Started	Communication plan will be initially drafted by 07/07/2023.	Project
Begin Execution of BenefitsCal Communications Plan	Not Started	Execution will begin 08/02/2023.	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



BenefitsCal Implementation Readiness



System Operations

Confirm Post Implementation Support schedule and extended support	Not Started	08/07/2023 - 08/11/2023	Project
Provide Contingency Planning efforts to Consortium (Roll Back Plan)	Not Started	08/07/2023 - 08/11/2023	Project

Prod Deployment Plans

Develop Production Cutover Checklist	Not Started	Target – 08/04/2023	Project
Confirm Consortium reviewed/approved the BenefitsCal cutover and BenefitsCal rollback plans	Not Started	Target – 08/11/2023	Project
Decide to proceed with BenefitsCal Production Cutover (Go-No Go Decision)	Not Started	08/14/2023 - 08/18/2023	Project
Confirm Wave Cutover to BenefitsCal	Not Started	08/14/2023 - 08/18/2023	Project

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Conversion Readiness

Conversion Readiness – Wave 5

Conversion defects not resolved prior to Wave Go-Live (Risk 280)	The Conversion and Release Management teams maintain a schedule deploying and resolving the X defects planned during the first 10 days of county being live. All X are evaluated and documented in the W5 Go-Live Packet (where applicable) with Worker Actions.	Project
Auto Case Review Match Rate	Match Rate will come as a result of Wave 5 Mock Cutover.	Project
Complete Wave 5 Mock Cutovers	Mock Cutover – On-Schedule to begin in June 2023.	Project
Deliver Wave 5 Golden Data Set (GDS)	Wave 5 GDS#12 Remains On-Schedule for June 2023.	Project
Cutover Window (Risk 258)	The Wave 5 Cutover Plan is dependent on the Wave 5 Mock Cutover actuals (assessed) and (any) implementation decisions the project makes to achieve or minimize the impact to the 84 hours cutover window.	Project
Support Wave 5 County Data Validation - Defect Resolution	On-Schedule as planned 6/19/2023 - 6/30/2023	Project
Complete Wave 5A (County Preparation) Cutover	On-Schedule as planned 7/17/2023	Project
Complete Wave 5B (Go-Live) Cutover	On-Schedule as planned 9/4/2023	Project

Not Started	On Schedule	<14 Days Late	>=14 Days Late	Complete
-------------	-------------	---------------	----------------	----------



Integration Readiness

Interface Partner Testing: 05/17/2023 - 07/07/2023

Complete Interface Development – County
Development Phase (4/14/2023)

Behind Schedule

County

Interface Names	Alameda	Ready for IPT?	Fresno	Ready for IPT?	Sonoma	Ready for IPT?
1099 File Writer job	YES	YES	YES	YES	YES	NO
Paid Warrant Reader job	YES	YES	YES	NO	YES	NO
Foster Care Voice Response Unit (VRU) Writer	YES	NO	N/A	N/A	N/A	N/A
Foster Care Voice Response Unit (VRU) Reader	YES	NO	N/A	N/A	N/A	N/A
Outbound Collections	YES	NO	NO	N/A	NO	N/A
Inbound Collections	YES	NO	NO	N/A	NO	N/A
Warrant Print Writer	YES	YES	YES	NO	YES	NO
Warrant Print Reader	NO	N/A	NO	N/A	NO	N/A
Auditor Controller Writer	YES	YES	YES	NO	YES	NO
Positive Pay file	NO	N/A	YES	NO	NO	N/A
Direct Deposit Writer	YES	YES	YES	YES	YES	NO
Direct Deposit Reader	YES	YES	YES	YES	YES	NO
School Lunch	YES	YES	YES	YES	YES	NO

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Integration Readiness

Interface Partner Testing – 05/17/2023 - 07/07/2023

Execute Interface Testing with CalWIN County Partners	Not Started	0%	Project
Execute Interface Testing with State and Consortium Partners	Not Started	0%	Project

CONSORTIUM PARTNERS INTERFACE TESTING		
CONSORTIUM PARTNER	STATUS	TARGET COMPLETION DATE
Electronic Inter County Transfer (EICT) - CalWIN	0/3	July 7, 2023

STATE PARTNER INTERFACE TESTING		
STATE PARTNER	STATUS	TARGET COMPLETION DATE
Case Management Information and Payrolling System (CMIPS) - OSI	0/2	July 7, 2023
Electronic Benefits Transfer (EBT) - FIS	0/2	July 7, 2023
Medi-Cal Eligibility Data System (MEDS) - DHCS	0/2	July 7, 2023
Welfare Data Tracking Implementation Project (WDTIP) - OSI	0/2	July 7, 2023

CalWIN WAVE 5 COUNTIES INTERFACE TESTING		
CalWIN Wave 5 COUNTY PARTNER	STATUS	TARGET COMPLETION DATE
Alameda County	0/11	July 7, 2023
Fresno County	0/8	July 7, 2023
Sonoma County	0/7	July 7, 2023

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Technical Readiness: Networking

Networking

County Networking Connectivity

Both

CalWIN WAVE 5 COUNTIES				
NETWORKING READINESS	STATUS	ACTUAL	PLANNED	Δ
Overall Network Interconnectivity	On Schedule	93.3%	60.0%	33.3%
Critical Path	On Schedule	93.0%	68.4%	24.6%

NETWORKING READINESS	STATUS	ACTUAL	PLANNED	Δ
Alameda	On Schedule	92.7%	60.0%	32.7%
Fresno	On Schedule	80.0%	60.0%	20.0%
Sonoma	On Schedule	94.5%	60.0%	34.5%

Milestone	Status
Wave 5 County Networking Connectivity Readiness	<ul style="list-style-type: none"> Circuit Upgrade/Enhancement orders processed; Pending Carrier delivery Track ongoing delivery of secondary circuits to County sites. Completed integration with Fresno County.

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Technical Readiness: Operations

Contingency Restoration Planning

Migration Rollback Planning	In Progress	90%	Project
-----------------------------	-------------	-----	---------

Disaster Recovery Exercise

Disaster Recovery Test	In Progress	90%	Project
------------------------	-------------	-----	---------

Batch Operations

CalWIN Batch Schedules	In Progress	75%	Project
------------------------	-------------	-----	---------

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

Technical Readiness: Performance Testing

Performance Testing – Wave 3-6

CalSAWS Batch Performance (58 County)

In Progress

25%

Project

CalWIN Wave 3-6 Batch Performance Schedule and Results

Performance Cycle	Start Date	End Date	Run Time
10-day cutoff*	February 27, 2023	March 10, 2023	(Run 1) 11 hours 17 minutes (Run 2) 9 hours 36 minutes
Main Payroll	March 20, 2023	March 24, 2023	(Run 1) 9 hours 24 minutes (Run 2) 9 hours 36 minutes
Batch server upgrade	May 1, 2023	May 5, 2023	TBD
Database memory upgrade	May 8, 2023	May 12, 2023	TBD
End of Month***	May 22, 2023	May 26, 2023	TBD
10-day cutoff***	May 29, 2023	June 9, 2023	TBD
Main Payroll***	June 12, 2023	June 23, 2023	TBD
Contingency for re-execution	June 26, 2023	June 30, 2023	TBD

*Represents the highest transaction volume day

***Validation of io2 Storage option

Note: Successful completion of the 3 cycles within the batch window will indicate that all cycles can complete within the batch window

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

Technical Readiness: Performance Testing

CalSAWS 55 County Online Performance Test – Schedule

Workload Mix (WL)	Start Date	End Date	Status
#1 - CalSAWS Online	07/24/2023	08/11/2023	Not Started
#2 - CalSAWS Online + APIs	08/14/2023	08/25/2023	Not Started

CalSAWS 55 County Online Performance Test

Category	SLA	SLA Met % & Avg. Server Response Time
Screen to Screen	Peak - 98% [<=2s]	
	Prime - 99.9% [<= 10s]	
EDBC	Peak - 95% [<= 3s]	
	Prime - 99.9% [<= 20s]	
Search	Peak - 95% [<=6s]	

Online Performance Test Findings –

Exit Criteria -

- Simulate Online transaction load of CalSAWS volume at peak hours meets SLA requirements
- Performance results are successful and meet contractual SLAs – Online (Load and Endurance tests)



Technical Readiness: Security

Application Security

CalSAWS Scans/Remediation Completed	Completed	100%
-------------------------------------	-----------	------

Penetration Testing

Signed with 3 rd party to conduct Testing	Completed	100%
--	-----------	------

Penetration Testing Preparation	Completed	100%
---------------------------------	-----------	------

Penetration Testing Execution & Agreed-upon remediations (Completed for the CMS Verification in April 2022)	Completed	100%
---	-----------	------

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Training Readiness

Training Plan

Wave 5 County-Specific Training Plans	Complete		Both
Training Environment/Build Training Data	Complete		Project
Create Training Accounts in Training Environment	Complete		Project

Training Materials

Wave 5 County-specific ILT training materials finalized.	Complete		Both
Web-based Trainings updated (Accenture/Consortium)	Complete		Project

Training Delivery

Wave 5 Early Training & TTT Trainees loaded and assigned curriculum in the CalSAWS LMS	Complete	100%	Project
Wave 5 staff course assignments / registration for Early Training & TTT	Complete	100%	Project
Wave 5 Early Training & TTT Instructor-led Training Ready (Training environment connectivity, Participants Enrolled)	Not Started	0%	Project
Wave 5 Early Training & TTT Started (WBT) – start 03/13/2023	In Progress	50%	Both
Wave 5 End-User Training Started (WBT) – start 04/03/2023	In Progress	28%	Both
Wave 5 Early Training & TTT Started (ILT) – start 05/30/2023	Not Started	# Completed of # Planned	
Wave 5 End User Training (EUT) - start 07/03/2023	Not Started	# Completed of # Planned	Both

Not Started

On Schedule

<14 Days Late




>=14 Days Late

Complete



Training Readiness




WBT Progress by County

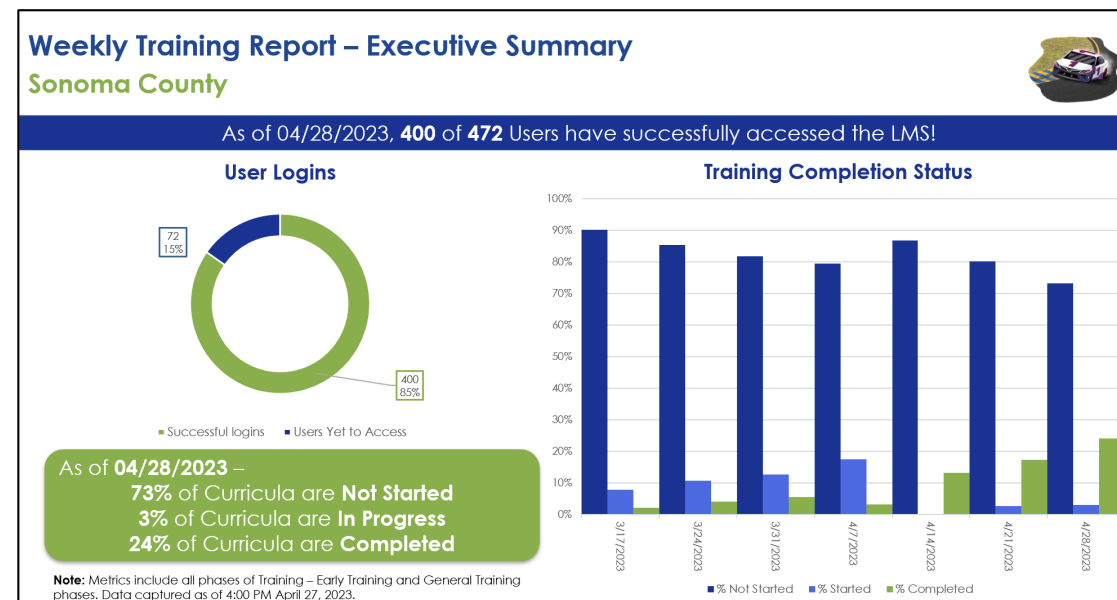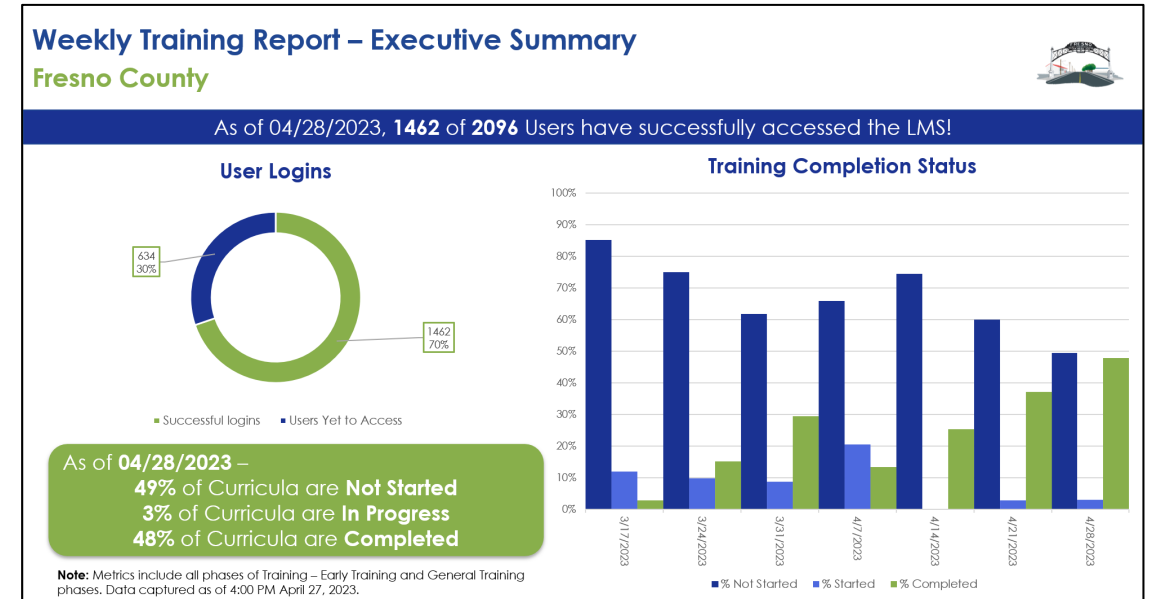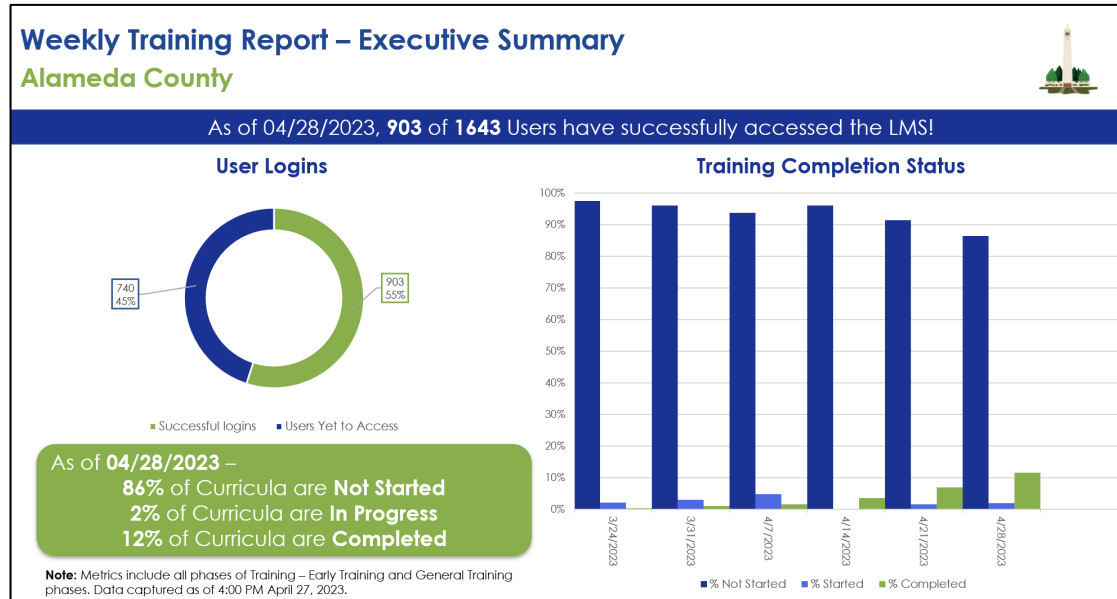



Training Readiness




Imaging WBT Progress by County

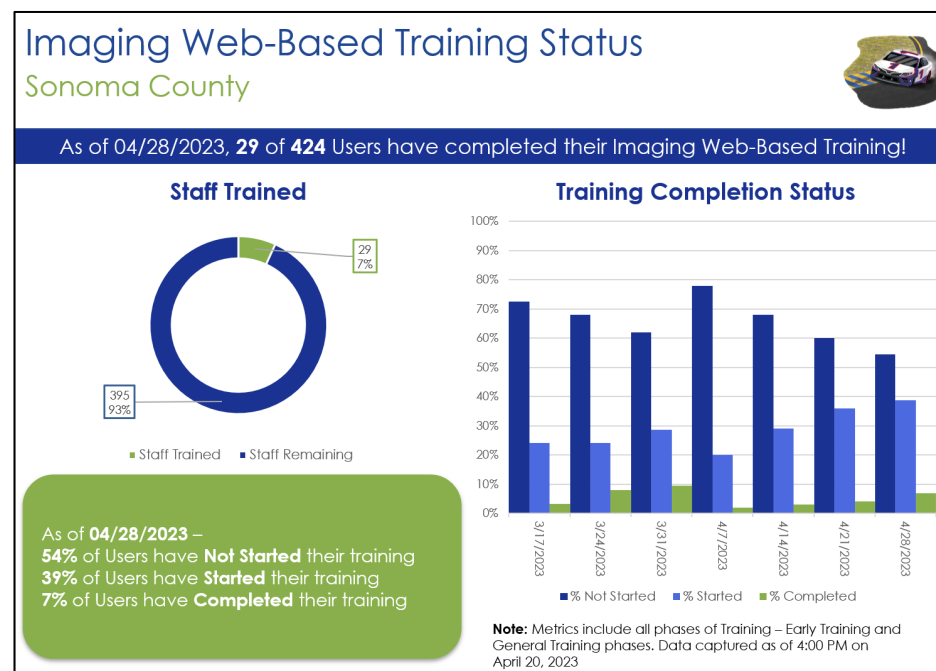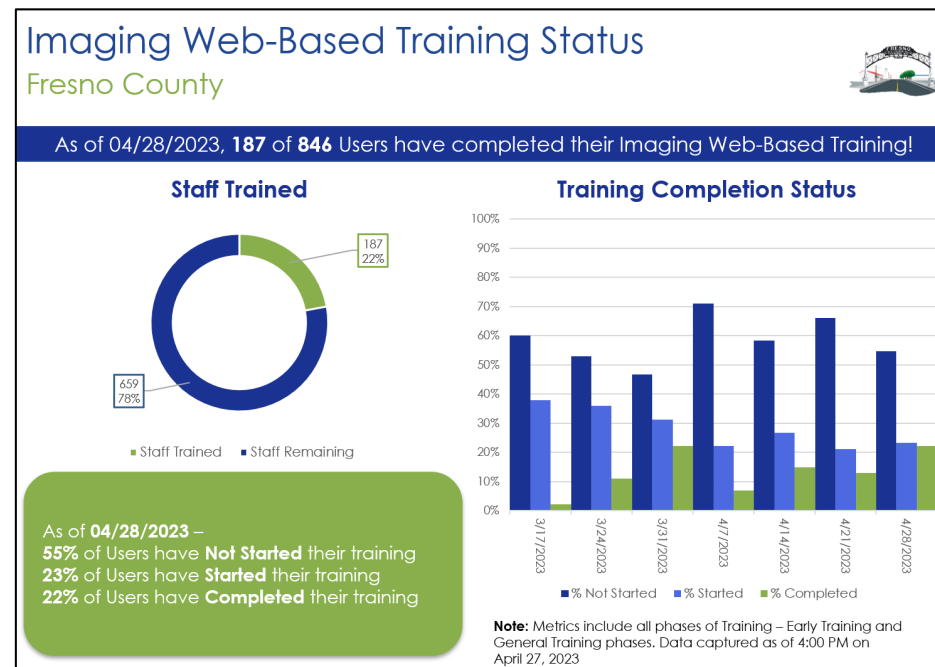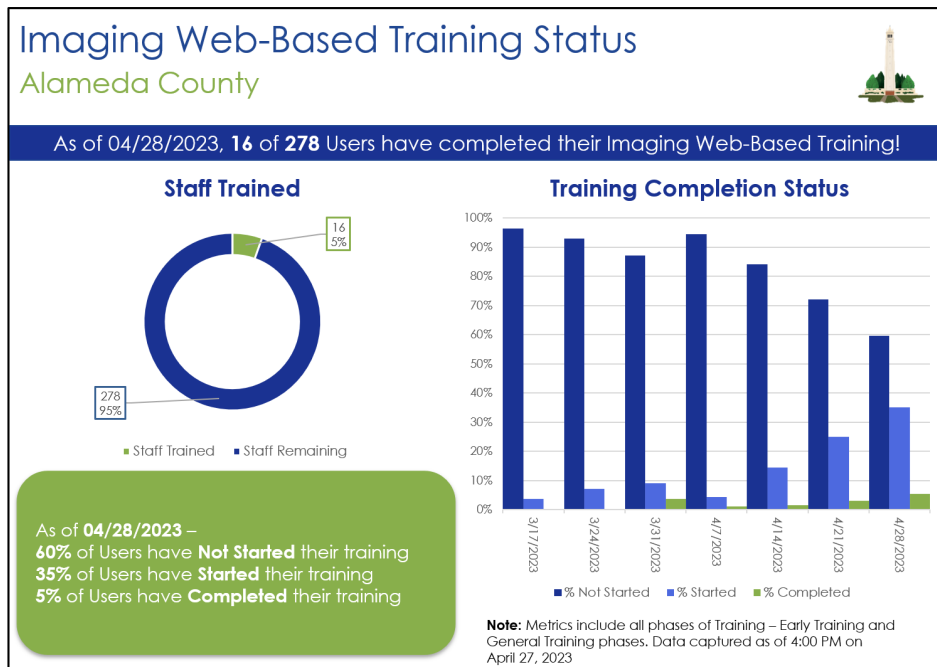



Training Readiness

Contact Center WBT Progress by County

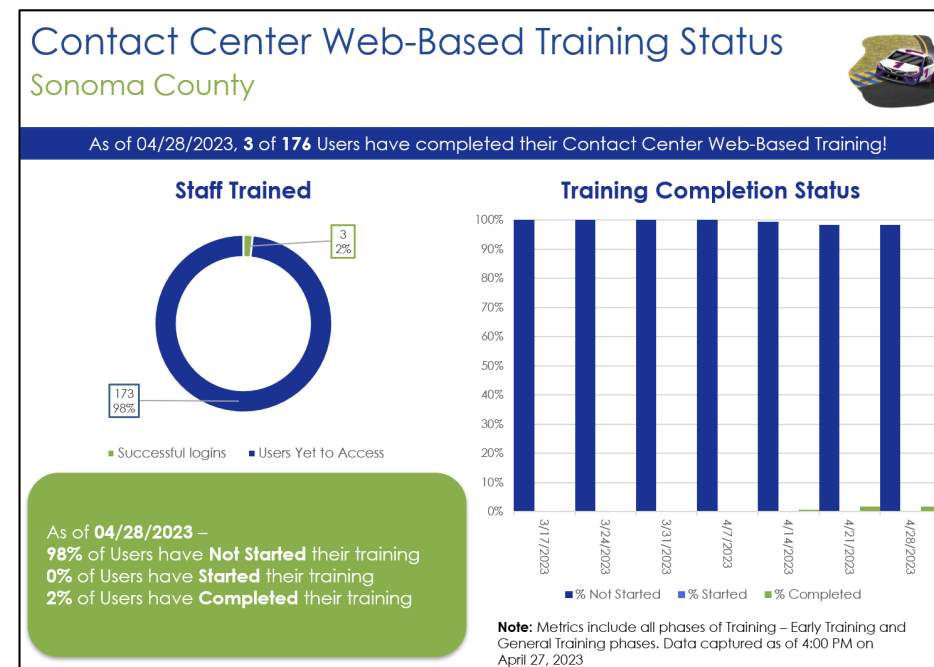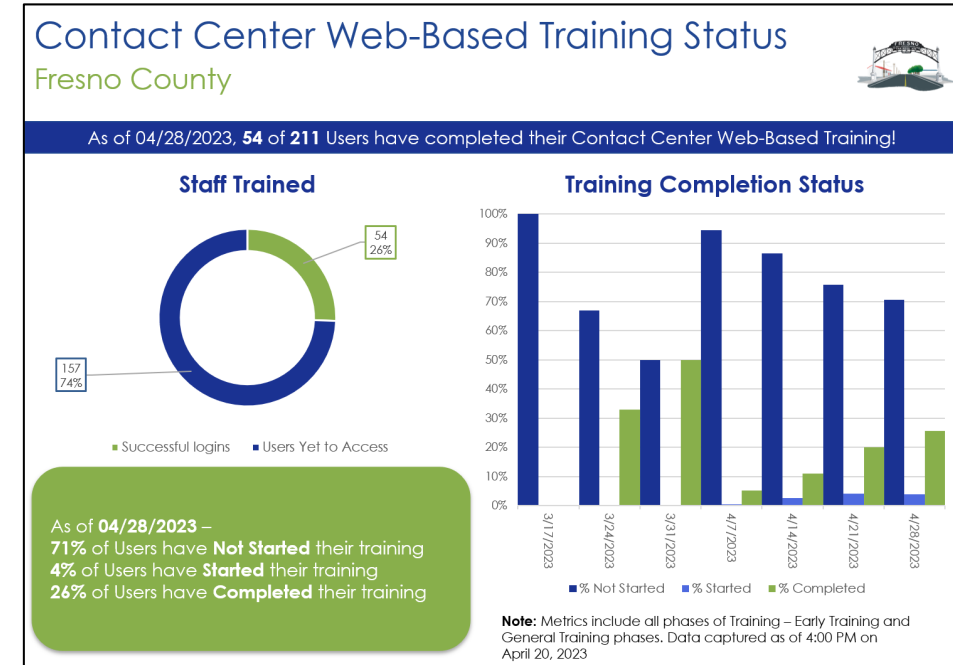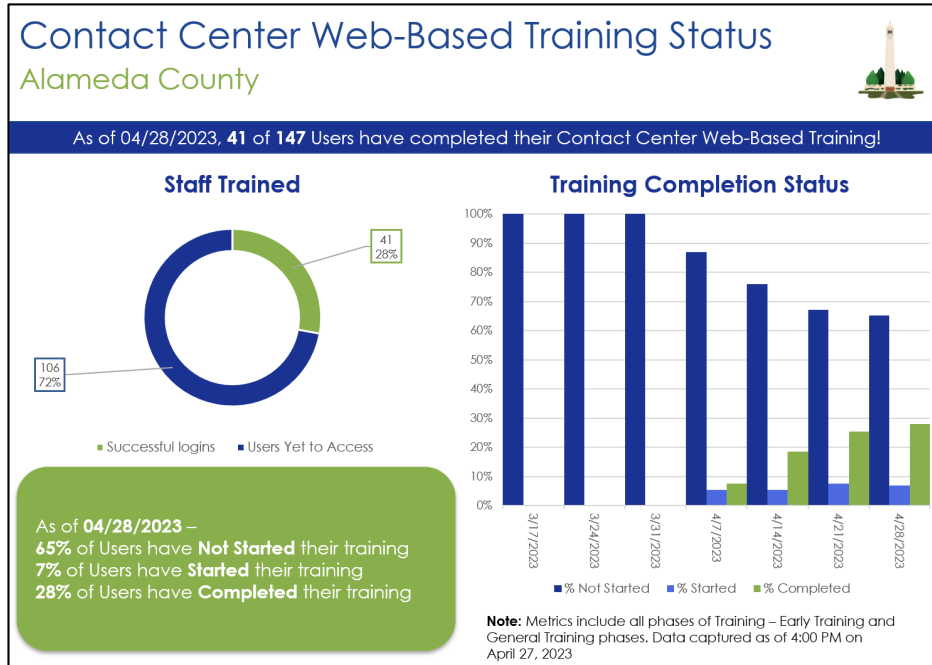

↔ Organizational Readiness: OCM

Communications & Change Discussion Guides

Wave 5 Counties DWP Signoff by 03/13/23	Complete	1 Completed of 1 Planned	Project
Wave 5 Counties FWP Signoff by 03/20/23-03/22/23	Complete	1 Completed of 1 Planned	Project
Alameda County CDG county and Consortium comments to get to FDEL signoff by 04/27	Complete	1 Completed of 1 Planned	Both
Fresno County and Consortium comments addressed to get to county FDEL signoff by 04/27	Complete	1 Completed of 1 Planned	Both
Wave 5 Counties DDEL signoff by 04/18	Complete	1 Completed of 1 Planned	County
Sonoma County and Consortium comments addressed to get to county FDEL signoff by 04/27	Complete	1 Completed of 1 Planned	Both
Prep Sessions for Supervisors, Managers, and CNCs on CDG discussion	Complete	3 Completed of 3 Planned	Both

Readiness Surveys

Wave 5 Readiness Surveys T-12 (9/26 to 10/7)	Complete	3 Completed of 3 Planned	Both
Wave 5 Readiness Surveys T-9 (1/9 to 1/23)	Complete	3 Completed of 3 Planned	Both
Wave 5 Readiness Surveys T-6 (3/20 to 4/3)	Complete	3 Completed of 3 Planned	Both
Wave 5 Readiness Surveys T-3 (6/6 to 6/16)	Not Started	0 Completed of 3 Planned	Both
Wave 5 Readiness Surveys T+6 (10/9 to 10/20)	Not Started	0 Completed of 3 Planned	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

↔ Organizational Readiness: OCM (continued)

Infographics/Newsletters

Infographics for January CalSAWS 101 and Spotlight CalSAWS Benefits (CIT 0024-23)	Complete	2 Completed of 2 Planned	Project
Infographics for February Imaging #1 and E-Applications (CIT 0064-23)	Complete	2 Completed of 2 Planned	Project
Newsletter for February (CIT 0067-23)	Complete	1 Completed of 1 Planned	Project
Infographics for March (Imaging #2 and RDB) (CIT 0124-23)	Complete	2 Completed of 2 Planned	Project
Infographics for April (Skip Issuance and WTW Assistance Unit Page)	Complete	2 Completed of 2 Planned	Project
Infographics for May	Not Started	0 Completed of 2 Planned	Project
Newsletter for May	Not Started	0 Completed of 1 Planned	Project

Change Network Champion Meetings

CNC Meeting for January	Complete	1 Completed of 1 Planned	Both
CNC Meeting for February	Complete	1 Completed of 1 Planned	Both
CNC Meeting for March	Complete	1 Completed of 1 Planned	Both
CNC Meeting for April	Complete	1 Completed of 1 Planned	Both
CNC Meeting for May	Not Started	0 Completed of 1 Planned	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

⇌ Organizational Readiness: BPR

Business Process Reengineering

BPR Plans reviewed and signed-off	Complete	3 Completed of 3 Planned	Both
To Be BPR Flows reviewed and signed-off	Complete	3 Completed of 3 Planned	Both
Close-out of pending decisions as documented in the Process Change Inventory	Complete	3 Completed of 3 Planned	Project
Automated Actions enablement decisions finalized	Complete	Initial Decisions to be finalized in advance of Process Simulation, loaded for Process Sim in the UAT Environment, validated during Process Sim and updated in advance of County Prep, ready for PROD/Go-Live.	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

↔ Organizational Readiness: Configuration

Configuration

Document Configuration Guides and Worksheets	Complete	Guide and Worksheets Documented	Project
Distribute Configuration Documentation to Wave-5 Counties	Not Started		Project
Conduct Working Sessions w/Counties to document base CalSAWS Configuration	Not Started		Both
Review, Refine and Confirm Configuration is ready for load into UAT for Process Simulation	Not Started		Both
Review Findings out of Process Simulation and Update "Must Have" Configuration items for PROD/County Prep	Not Started		Both
Update Configuration Worksheets to with Findings from Process Simulation in advance of County Prep	Not Started		Both
Load Configuration into PROD environment during County Prep	Not Started		Project
Configuration Complete	Not Started		Project

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

Organizational Readiness: Process Simulation

Process Simulation

Wave 5 Participants Confirmed	Not Started	Both
Users Loaded to ForgeRock/UAT Environments & Applications	Not Started	Project
Complete W5 Process Simulation Scenario Development	Not Started	Project
Complete data staging and JIRA prep	Not Started	Project
Complete configuration setup	Not Started	Both
Complete Process Simulation Orientation	Not Started	Project
Complete Process Simulation Execution	Not Started	Both
Evaluate and confirm Exit criteria	Not Started	Project
Process Simulation Complete	Not Started	Project

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Implementation Readiness

Planning

Wave 5 Workplans, Readiness Checklists and ongoing TOSS Meetings	In Progress	Ongoing	Both
Path to Greenlight Communicated	Complete	Socialized/completed with PSC, JPA, and OPAC (May 2022)	Project
Go Live Packet Finalized/Updated	Not Started	Will revise, if applicable, July 2023	Project
Distribute Monthly Implementation Packets	In Progress	Ongoing	Project

County Prep

County Prep Materials Finalized	Not Started	Will revise, if applicable, May 2023	Project
County Prep Kick Off	Not Started	Targeted for June 21, 2023	Both

Post-Implementation Support

Pre- and Post- Go Live Support Structure Established	Complete	County Profile drafts complete. Initial escalation model/approach planned.	Project
County Profile Review	In Progress	Confirming office profile specifics with W5 counties to prepare for gap analysis	Project

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Implementation Readiness: Help Desk

Help Desk

County Delegated Admin Training	Complete	Hosted on 2/15	Both
County Tier 1 Fulfiller Training	Complete	Hosted Week of 3/27/2023	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Implementation Readiness: System Operations

Systems Operations

CalWIN Counties Access to the Sandbox Environment	Completed	Generic user accounts provided	Both
Engage the Counties on Staff Profile/Security Administration updates	Completed	Pre-UAT exercise	Both

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete



Implementation Readiness: County Ad Hoc Reporting

Ad-Hoc Reporting Functionality

CalWIN County Education Sessions (i.e., Planned Curriculum)	<ul style="list-style-type: none">• Wave 5: CalSAWS has facilitated 100% planned Ad Hoc Support Curriculum to the Wave 5 Counties.	Both
CalWIN County Ad Hoc Reports Refactoring	<ul style="list-style-type: none">• Wave 5: Reviewed 687 reports for refactoring. Approximately 117 need to be refactored for Wave 5 Counties by go live.<ul style="list-style-type: none">• Alameda has an estimated 158 reports that need to be refactored. 117 are needed by Go Live. Alameda had reached out to Gainwell for assistance.• Fresno has an estimated 0 reports that need to be refactored and is still reviewing.• Sonoma has an estimated 9 reports that need to be refactored, and 0 are needed by go live.	County

Not Started

On Schedule

<14 Days Late

>=14 Days Late

Complete

Contact Information

THE
POWER
OF 58

WHEN SAN FRANCISCO COLLABORATES WITH NAPA.
WHEN LOS ANGELES TEAMS UP WITH SAN BERNARDINO.
WHEN WE ALL WORK TOGETHER,

THE RESULTS
ARE POWERFUL.

CalSAWS

CalWIN Migration and BenefitsCal
Implementation Contact:
Implementation@CalSAWS.org

RANCHO CORDOVA OFFICE
11290 Pyrites Way, Suite 150
Gold River, CA 95670
(916) 851-3201

ROSEVILLE OFFICE
620 Roseville Parkway
Roseville, CA 95747
(916) 846-7331

NORWALK OFFICE
12440 Imperial Highway, Suite 300
Norwalk, CA 90650
(562) 484-7914
