



CalSAWS DD&I Weekly Status Report

Reporting Period: July 17, 2023, to July 23, 2023

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

1.0	Project Management	3
1.1	Project Deliverables Summary	3
1.2	Highlights of the Reporting Period	3
1.2.1	Project Management	3
1.2.2	Communications Management	5
1.2.3	Cultural Transformation.....	7
1.2.4	Inclusion, Diversity, and Equality Advancement (IDEA)	7
1.3	CRFI/CIT Communications Information	8
1.4	Activities for the Next Reporting Period.....	9
1.4.1	Project Management	9
1.4.2	Communications Management	10
1.4.3	Cultural Transformation.....	10
1.4.4	Inclusion, Diversity & Equality Advancement (IDEA)	10
1.5	Deviations from Plan/Adjustments.....	10
2.0	Imaging	11
2.1	Highlights of the Reporting Period	11
2.2	Activities for the Next Reporting Period.....	12
2.3	Upcoming Performance Tests	12
2.4	Deviations from Plan/Adjustments.....	12
3.0	Customer Service Center (CSC)	13
3.1	Highlights of the Reporting Period	13
3.2	Activities for the Next Reporting Period.....	14
3.3	Upcoming Performance Tests	14
3.4	Deviations from Plan/Adjustments.....	14
4.0	Application Development and Test	15
4.1	Highlights of the Reporting Period	15
4.1.1	Application Development Summary.....	16
4.1.2	State and CalWIN Wave 5 County Interface Partner File Exchange Test (IPT)	17
4.1.3	State and CalWIN Wave 6 County Interface Partner File Exchange Test (IPT)	18
4.2	Activities for the Next Reporting Period.....	19
4.3	Upcoming Performance Tests	19
4.4	Deviations from Plan/Adjustments.....	19
5.0	Conversion	20

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

5.1	Highlights of the Reporting Period	20
5.1.1	CalWIN Conversion	20
5.1.2	CalWIN Conversion Defects	20
5.1.3	Gainwell Technologies	22
5.1.4	Ancillary Systems Conversion	26
5.1.5	CalWIN Migration Planning	28
5.1.6	Deliverable Management.....	29
5.2	Activities for the Next Reporting Period.....	29
5.2.1	CalWIN Conversion	29
5.2.2	CalWIN Migration Planning	29
5.2.3	Gainwell Technologies	29
5.2.4	Ancillary Systems Conversion	30
5.2.5	Deliverable Management.....	30
5.3	Deviations from Plan/Adjustments.....	30
6.0	CalWIN Functional Support	30
6.1	Highlights of the Reporting Period	30
6.2	Activities for the Next Reporting Period.....	31
6.3	Deviations from Plan/Adjustments.....	31
7.0	Technical Infrastructure	31
7.1	Highlights of the Reporting Period	31
7.2	Activities for the Next Reporting Period.....	33
7.3	Deviations from Plan/Adjustments.....	33
8.0	Appendices.....	35

1.0 Project Management

1.1 Project Deliverables Summary

Table 1.1-1 – Overall Summary of Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	TEAM	STATUS [1]	STATUS
	None for the reporting period			

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

1.2 Highlights of the Reporting Period

Table 1.2-1 – CalSAWS Project Management Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Project Management	<ul style="list-style-type: none"> None to note for the reporting period

1.2.1 Project Management

- ▶ Continued CalSAWS DD&I Facility Management activities, including:
 - Key initiatives related to facilities at the Rancho Cordova Project Office are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) below

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 1.2.1-1 – Key Facility Initiatives/Projects

ITEM #	INITIATIVES/PROJECTS	LOCATION	TARGET DATE	NOTES/STATUS
1	Return to Office (RTO)	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> • Continued reviewing and processing Return to Office (RTO) Approval Request forms submitted by CalSAWS Project staff, which are required to access the CalSAWS Rancho Cordova or Norwalk Project offices • Continued to monitor and review requests from CalSAWS Project staff who are interested in returning to the CalSAWS Rancho Cordova and Norwalk Project offices on a hybrid schedule • Continued to assess updates to Federal, State, and local policies and ordinances for the CalSAWS Project's return to office processes
2	Large Meeting Requests	Rancho Cordova and Norwalk Project Offices	Ongoing	<ul style="list-style-type: none"> • Continued planning facility capacity and equipment needs for requested on-site meetings

- ▶ Continued CalSAWS Risks and Issues Management activities, including:
 - Continued to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues.
- ▶ Continued activities to support Project staff working remotely.
 - Continued developing Project communications, as needed.
 - Conducted virtual CalSAWS All Staff Meeting held on July 19, 2023
- ▶ Participated in the Joint Powers Authority (JPA) Meeting held on July 21, 2023
- ▶ Participated in the Project Steering Committee (PSC) Meeting held on July 20, 2023
- ▶ Continued to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continued performing contract management activities:
 - Change Notice 27 (August JPA) is in development and has no DD&I items included
 - Amendment 31 (August JPA) is undergoing Client approval process and will include:
 - Endpoint Detection Response (EDR) Qualys
 - Data Growth/Cost Avoidance - Archiving Phase 1
 - Data Growth/Cost Avoidance - Archiving Microservices POC (Phase 2)
 - Data Growth/Cost Avoidance - Task Management
 - Data Growth/Cost Avoidance - Test Data Slicer/Scrubber Capability
 - Los Angeles Contact Center Milestone Payment Shift
 - Technical Architecture System Change Requests (SCRs)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

- NIST Rev 5 Uplift
- Facility - Removal of Suite 130
- Continued planning the implementation of requirements from the DHCS and CDSS Privacy and Security Agreements (PSAs) that were approved by the Joint Powers Authority (JPA) Board of Directors on April 16, 2021
- ▶ Continued performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.2.1-2 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

1.2.2 Communications Management

- ▶ CalSAWS Communications Management activities including
 - Continued to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy
 - Continued oversight and management of Power of 58 materials
- ▶ CalSAWS External Website (www.calsaws.org)
 - Continued the administration and support of the CalSAWS external website
 - See Table 1.2.2-1 for details on website support activities

Table 1.2.2-1 – Website Support Activities

TASK	DATE (S)	TASK TYPE
Updated Plugin Changes	July 12, 2023	Maintenance

Table 1.2.2-2 – CalSAWS.org Usage Statistics

CATEGORY	DURING REPORTING PERIOD	SINCE LAUNCH
Total Number of Subscribers	76	4,805
Total Number of Unique Users	4,261	2,027,176
Total Number of New Users	2,738	2,021,226
Total Number of Sessions (Individual site visits)	5,299	2,978,883
Average Number of Sessions per User	1.24	1.47
Average Number of Page Views per Session	1.48	1.36
Average Session Duration	1:24	0:58
AskCalSAWS Inquiries – Received/Resolved	28/8	1,446/1,437


Note: Due to system unavailability, the data above is reflecting week ending July 9, 2023. The Team has opened a ServiceNow ticket to investigate

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Figure 1.2.2-1 – Overall CalSAWS.org Usage Trend

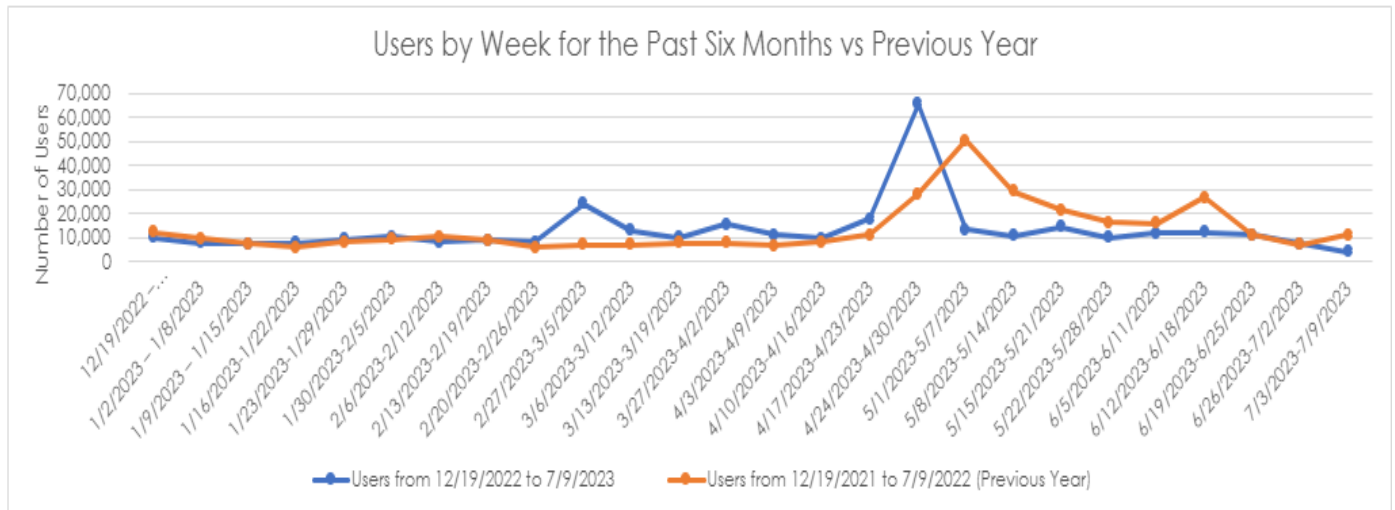

Note: Due to system unavailability, the data above is reflecting week ending July 9, 2023. The Team has opened a ServiceNow ticket to investigate

Table 1.2.2-3 – CalSAWS.org Subscription Service Statistics

WEBPAGE	PERCENT OF SUBSCRIBERS
Latest News – CalSAWS Buzz Newsletter	21%
Latest News – News	16%
Other Updates – System Updates	16%
Other Updates – Careers	15%
CalSAWS Committees – CalWORKs/CalFresh	16%

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

1.2.3 Cultural Transformation

- ▶ Culture Ambassadors Network (CAN)
 - Wellness Wednesday
 - Distributed content for July Wellness Wednesday – Importance of Community
 - Continued to prepare for upcoming activities and events
 - Summer Photo/Best Vacation
 - SAWS memorabilia
 - October – National Art Month

1.2.4 Inclusion, Diversity, and Equality Advancement (IDEA)

- ▶ Co-Create Phase
 - CalSAWS “We Are One” SharePoint Site
 - Continued to update the “We Are One” website tab
 - Pulse Survey
 - Continued incorporating Pulse Survey results into strategic plan
 - CalSAWS Table Talks
 - Pushing Table Talk to August 2023
 - Continue planning Table Talk for August 2023
 - Buddy Program
 - Continued supporting buddy pairs
 - Small Team Building
 - Continued to promote Small Team Building initiative opportunities for all CalSAWS teams
 - Employee Resource Groups (ERGs)
 - Continued to manage and support Employee Resource Groups (ERGs) council
- ▶ General
 - Began research phase to identify evidence-based psychological constructs predictive of successful DEI programs
 - Continued working with CalSAWS staff to create and present Inspiration Stations during monthly virtual CalSAWS Project All Staff Meetings
 - Continued conversations with volunteer organization to provide volunteer opportunities for CalSAWS members
 - Continued to partner with the CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
 - Continued to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the Project

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

1.3 CRFI/CIT Communications Information

- ▶ The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period ending July 23, 2023

Table 1.3-1 – CITs

CIT ID	SUBJECT	CATEGORY	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
0259-23	Wave 6 CalSAWS Infographics #9	Informational	July 17, 2023	Helen Cruz	Araceli Gallardo
0260-23	Wave 5 CalSAWS Infographics #9	Informational	July 17, 2023	Helen Cruz	Araceli Gallardo
0264-23	Wave 4 Counties T+6 Weeks Change Readiness Survey	Informational	July 20, 2023	Helen Cruz	Araceli Gallardo
0266-23	CalWIN M&O County Allocations SFY 2023-24 v1	Informational	July 21, 2023	Tracy Berhel	Girish Uppal

- ▶ The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period ending July 23, 2023

Table 1.3-2 – CRFIs

CRFI ID	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	CalSAWS CONTACT
23-090	CalWIN Migration Wave 5 – CalSAWS County On-Site & Virtual Support	June 26, 2023	Open	July 28, 2023	Jeffrey Fuller
23-091	CalWIN Migration Wave 5 –On-Site Support from Wave 6 CalWIN Counties	June 26, 2023	Closed	July 14, 2023	Jeffrey Fuller
23-092	CalWIN Migration Wave 5 – Observers From Wave 6 CalWIN Counties	June 26, 2023	Closed	July 14, 2023	Jeffrey Fuller
23-096	CalWIN Wave 6 Counties - Request to Identify/Review Portal CBO Data	July 13, 2023	Open	July 27, 2023	Marsale Eramya

- ▶ The following table outlines overdue CalSAWS Requests for Information (CRFIs) for the reporting period ending July 23, 2023

Table 1.3-3 – Overdue CRFIs

CRFI ID	Subject	Region 1	Region 2	Region 3	Region 4	Region 5	Region 6
None							

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

1.4 Activities for the Next Reporting Period

1.4.1 Project Management

- ▶ Continue CalSAWS DD&I Facility Management activities, including:
 - Continue key initiatives related to facilities at the Rancho Cordova and Norwalk Project Offices, which are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) above
- ▶ Continue CalSAWS Risks and Issues Management Group (RMG) activities, including:
 - Continue to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
 - Start preparations for Monthly Risks and Issues Management Group (RMG) meeting to be held on August 2, 2023
- ▶ Continue activities to support Project staff working remotely
 - Continue developing Project communications, as needed
- ▶ Continue to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue performing Contract Management activities for the CalSAWS DD&I Project
- ▶ Continue performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.4.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

1.4.2 Communications Management

- ▶ Continue to monitor usage and update materials as requested
 - See table 1.4.2-1 for planned website support activities
- ▶ CalSAWS Communications Management activities including:
 - Continue to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy:
 - Continue oversight and management of Power of 58 roll out

Table 1.4.2-1 – Website Support Activities

TASK	DATE(S)	TASK TYPE
None for the reporting period	N/A	N/A

1.4.3 Cultural Transformation

- ▶ Develop Wellness Wednesday monthly topics for 2023
- ▶ Develop calendar of events for the ambassador initiatives the year 2023
- ▶ Continue to provide Project management support to Cultural Ambassadors as they continue to develop the plans for the initiatives
- ▶ Continue to coordinate working sessions for each Ambassador group to further their initiatives planning and discuss their individual contributions
- ▶ Continue to develop wellness initiative content to keep the project staff engaged
- ▶ Continue to update resources and a collaboration workspace (Teams Channel) with new relevant materials to support the implementation of the prioritized initiatives
- ▶ Continue to monitor Microsoft Teams channels for any help needed from Ambassadors

1.4.4 Inclusion, Diversity & Equality Advancement (IDEA)

- ▶ Continue creating transition plan for IDEA lead scheduled paternity leave
- ▶ Continue conversations with nonprofit to provide volunteer opportunities to staff in Los Angeles
- ▶ Continue exploring Table Talk topic of Bronfenbrenner Model and how it can be applied and relevant to CalSAWS
- ▶ Continue planning Employee Resource Group (ERG) Collaboration Events
- ▶ Continue partnering with CalSAWS members to create an Inspiration Station and present during virtual CalSAWS Project All Staff Meeting
- ▶ Continue to partner with CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the Project
- ▶ Continue to promote small team building activities

1.5 Deviations from Plan/Adjustments

- ▶ None for the reporting period

2.0 Imaging











2.1 Highlights of the Reporting Period

Table 2.1-1 – CalSAWS Imaging Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Appendix E	<ul style="list-style-type: none"> • Sacramento: <ul style="list-style-type: none"> ○ CalSAWS Project team met with Sacramento County last week and were informed that Sacramento County have begun activities associated with the August 2, 2023 and September 1, 2023 commitments. ○ Sacramento County will stay on Amber status as they finalize the timing for Delta 2 on September 1, 2023. They are also testing the custom import of MyBCW images, and the results will be available on August 2nd. We will keep the risk level as Amber until the Delta 2 timing and MyBCW import process are confirmed.

- ▶ Continued to monitor Imaging migration status by County
 - For future details of status' by County, they are now available in Appendix E - CalSAWS Imaging Document Migration

Table 2.1-2 – CalSAWS Imaging County Migration Risk Status

WAVE	COUNTY	STATUS [1]
4	• San Diego County	
	• Santa Cruz County	
	• Solano County	
	• San Mateo County	
5	• Alameda County	
	• Fresno County	
	• Sonoma County	
6	• San Francisco County	
	• San Luis Obispo County	
	• Sacramento County	

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Note:

- Detailed metrics of each County by wave has been included in the Appendix E - CalSAWS Imaging Document Migration

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 2.1-3 – CalSAWS Imaging Project Milestones for Current Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 4	Conduct San Diego County Document Migration Discovery Session Check-in	July 17, 2023	Completed
WAVE 5	Conduct Alameda County Document Migration Discovery Session Check-in	July 17, 2023	Completed
	Conduct Fresno County Document Migration Discovery Session Check-in	July 19, 2023	Completed
	Conduct Sonoma County Document Migration Discovery Session Check-in	July 19, 2023	Completed
WAVE 6	Conduct Sacramento County Document Migration Discovery Session Check-in	July 19, 2023	Completed

Table 2.1-4 – CalSAWS Imaging Project Milestones for Next Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 4	Conduct San Diego County Document Migration Discovery Session Check-in	July 25, 2023	Scheduled
WAVE 5	Conduct Alameda County Document Migration Discovery Session Check-in	July 24, 2023	Scheduled
	Conduct Fresno County Document Migration Discovery Session Check-in	July 26, 2023	Scheduled
	Conduct San Luis Obispo County Document Migration Discovery Session Check-in	July 25, 2023	Scheduled

2.2 Activities for the Next Reporting Period

- ▶ Continue to manage the milestones for the Image Migrations in the tables in Appendix E

2.3 Upcoming Performance Tests

- ▶ None for the reporting period

2.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

3.0 Customer Service Center (CSC)

3.1 Highlights of the Reporting Period

Table 3.1-1 – CalSAWS Customer Service Center Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
3.1	<ul style="list-style-type: none"> Performance test of the system completed successfully

- ▶ Continued System Testing of Wave 5 Contact Centers (CA-240168, CA-240169, and CA-240170)
- ▶ Continued build of Wave 6 Contact Centers (CA-240171, CA-240172, and CA-240173)
- ▶ Continued build of Scheduled Callback (CA-229573)
- ▶ Continued System Testing of Inbound IVR additional languages SCR (CA-226837)
- ▶ Scheduled Wave 5 On-Site Model Office preparation meeting for the Contact Centers

Table 3.1-2 – Customer Service Center Enhancement Milestones

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2292, 2697, 2698, 2723, 2724 WFM/QA/QM Reporting (CA-226209)	December 3, 2021	In Production	22.01
DDID 2700 Enhanced CCP (CA-226844)	March 18, 2022	In Production	22.03 22.05.06
DDID 2727 Work-from-home Modifications (CA-227064)	March 18, 2022	In Production	22.03 22.05.06
DDID 2216, 2725 External Party Access IVR (CA-226839)	March 25, 2022	In Production	22.05
DDID 2211, 2217, 2218, 2220, 2729, 2730, 2731, 2046, 2732 Telephonic Signature (CA-226838)	April 1, 2022	In Production	22.05
DDID 2704 Post-Call Survey (CA-228023)	July 8, 2022	In Production	22.07 22.09.16
DDID 2687, 2688, 2689, 2690, 2691, 2692, 2693, 2694, 2695, 2696, 2222, 2702, 2721, 2169, 2284, 2722 Admin Page (CA-226672)	October 7, 2022	In Production	22.11 22.12.11
DDID 2718 Task for Cancelling an Appointment in Outbound IVR (CA-231234)	November 11, 2022	In Production	23.01 23.02.17
DDID 2219, 2716, 2717, 2728 Outbound IVR - (CA-226207)	November 11, 2022	In Production	23.01 23.02.17
DDID 2701, 2706 Voice Authentication Languages (CA-226843)	October 7, 2022	In Production	23.01 23.02.16

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2699, 2210, 2705, 2707, 2708, 2709, 2710, 2711, 2712, 2713, 2714, 2715, 2719, 2720, 2258 Inbound IVR (CA-226837)	January 12, 2023	System Test	23.07 23.08.24
DDID 2284 Scheduled Callback (CA-229573)	July 8, 2022	In Development	23.09 23.09.28
DDID 2268 Display the CalSAWS Contact Center IVR Caller ID for outbound calls	June 14, 2023	Design in progress	23.09 23.09.28

Table 3.1-3 – Los Angeles County Milestones

MILESTONES	DUE DATE	OWNER
1 Design completion	March 11, 2022	CalSAWS Project Team
2 Initial performance/load testing	March 18, 2022	CalSAWS Project Team
3 Training development	May 16, 2022	CalSAWS Project Team
4 Build and unit test	May 20, 2022	CalSAWS Project Team
5 Training content review	May 20, 2022	Consortium
6 Training execution	June 29, 2022	CalSAWS Project Team
7 System Test	July 15, 2022	CalSAWS Project Team
8 Conduct model office	January 9, 2023	Los Angeles County
9 Go-live	November 17, 2023	CalSAWS Project Team
10 Post go-live support	November 20, 2023	CalSAWS Project Team

3.2 Activities for the Next Reporting Period

- ▶ Continue System Testing of Wave 5 Contact Centers (CA-240168, CA-240169, and CA-240170)
- ▶ Continue build of Wave 6 Contact Centers (CA-240171, CA-240172, and CA-240173)
- ▶ Continue build of Scheduled Callback (CA-229573)
- ▶ Continue System Testing of Inbound IVR additional languages SCR (CA-226837)

3.3 Upcoming Performance Tests

- ▶ No upcoming performance tests

3.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

4.0 Application Development and Test

4.1 Highlights of the Reporting Period

Table 4.1-1 – CalSAWS Application Development and Test Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
4.1.1-2 CalSAWS System Change Request (SCR) Test Status - 23.07	<ul style="list-style-type: none">• Deployed the 23.07 baseline release to production.• Continued 23.09 test script preparation.
4.1.2 State and CalWIN Wave 5 County Interface Partner File Exchange Test (IPT)	<ul style="list-style-type: none">• Wave 5 IPT State, Consortium, and County IPT completed. 37 of 37 interfaces have successfully passed validation.
4.1.3 State and CalWIN Wave 6 County Interface Partner File Exchange Test (IPT)	<ul style="list-style-type: none">• Continued execution activities for Wave 6 IPT. 5 of 36 Consortium, State, and County interfaces have successfully passed validation.

4.1.1 Application Development Summary

Table 4.1.1-1 – CalSAWS Application Development Summary


	Status	23.06	23.07	23.09
Design	New	0	0	3
	Design in Progress	0	1	1
	Ready for Committee	0	0	1
	Committee review	0	0	0
	Pending approval	0	0	0
Build	Approved	0	5	4
	In Development	1	6	6
	Development completed	0	3	3
	In Assembly Test	0	0	0
Test	System Test	0	2	0
	Test completed	1	2	0
	In Production	20	1	0
	Grand total	22	20	18

System Change Requests (SCRs) in Production	1,041
---	-------

Note:

- This table includes Application Development System Change Requests (SCRs) with migration impact. SCRs in production represents a count of any SCR that have a project phase of migration and have been deployed to production
- Continued drafting designs and development activities. Status is provided in Table 4.1.1-1 (CalSAWS Application Development Summary)

Figure 4.1.1-1 – CalSAWS Test Summary

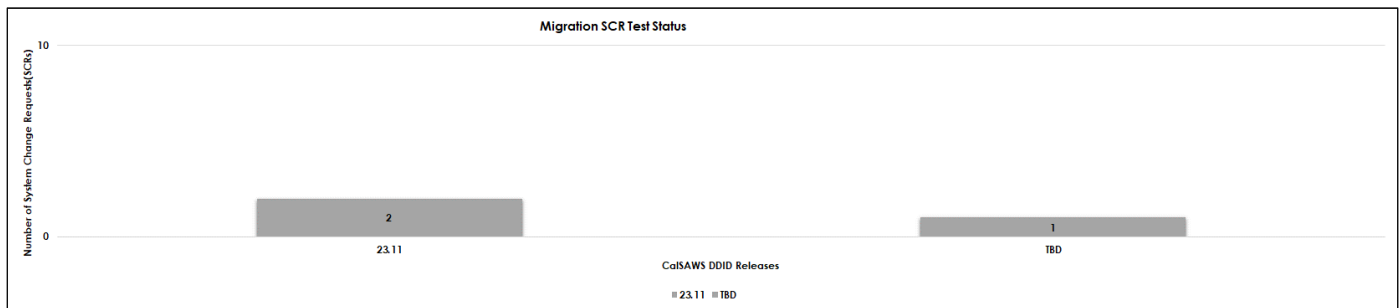


Note:

- Includes all System Change Requests (SCRs) that have a funding source of 'CalSAWS DD&I' with a Funding Source ID of 'Application Development and Test' that are not in "Rejected" or "Pending Rejection" status and are targeted for a baseline release excluding any Support or Design SCRs. In Production includes In Production statuses; Test Complete includes Test Completed status; System Test includes System Test status; Not in System Test includes all SCR statuses prior to System Test delivery.

Table 4.1.1-2 – CalSAWS System Change Request (SCR) Test Status - 23.07

Pass Rate Target as of July 19, 2023	100%
Pass Rate Actual as of July 19, 2023	100%
System Test Complete Date: July 19, 2023	

Figure 4.1.1-2 – DDID System Test Execution Status – 23.07

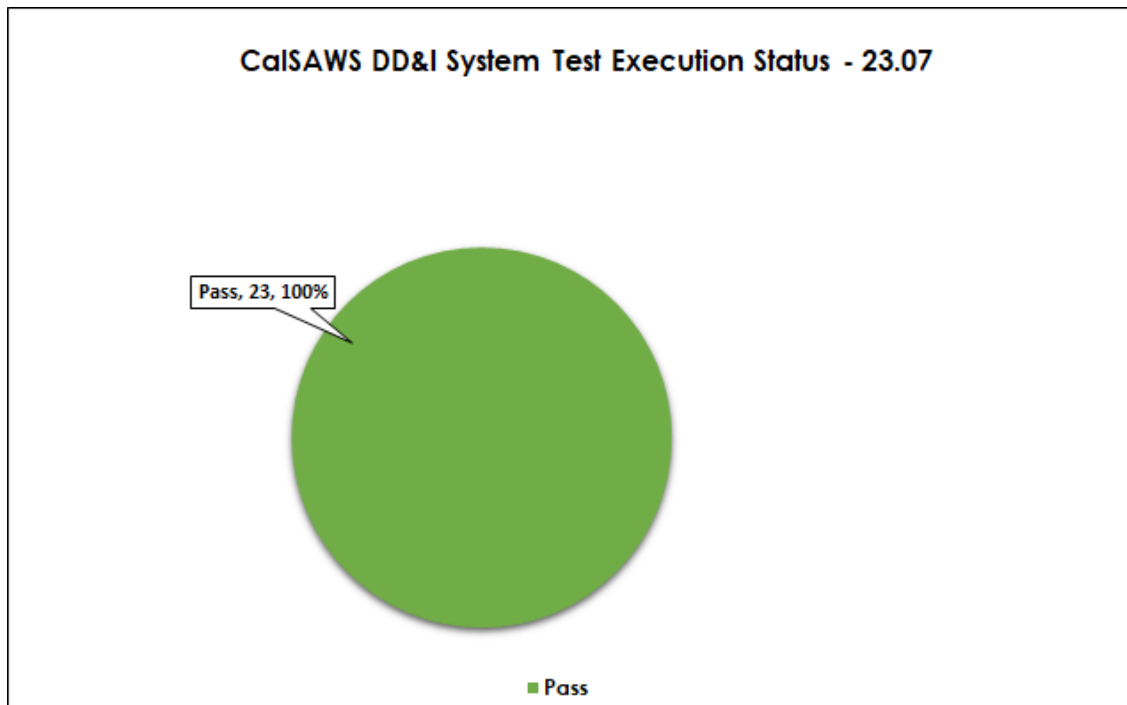

Note:

- Test Script counts are subject to change as test scripts are added or removed throughout the execution phase. Includes testing execution for all CalSAWS DD&I Test Scripts in the release

► Completed test execution for 23.07

4.1.2 State and CalWIN Wave 5 County Interface Partner File Exchange Test (IPT)

Table 4.1.2-1 – Consortium Partners

INTERFACE TESTING		
CONSORTIUM PARTNER	STATUS	TARGET COMPLETION DATE
Electronic Inter County Transfer (EICT) - CalWIN	3/3	May 31, 2023

Note:

- Completed Testing

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 4.1.2-2 – State Partners

INTERFACE TESTING		
STATE PARTNER	STATUS	TARGET COMPLETION DATE
Case Management Information and Payrolling System (CMIPS) – OSI	2/2	May 17, 2023
Electronic Benefits Transfer (EBT) - FIS	2/2	June 14, 2023
Medi-Cal Eligibility Data System (MEDS) - DHCS	2/2	June 20, 2023
Welfare Data Tracking Implementation Project (WDTIP) – OSI	2/2	May 17, 2023

Note:

- Completed Testing

Table 4.1.2-3 – CalWIN County Partners

INTERFACE TESTING		
CalWIN Wave 5 COUNTY PARTNER	STATUS	TARGET COMPLETION DATE
Alameda County	11/11	July 12, 2023
Fresno County	8/8	July 20, 2023
Sonoma County	7/7	June 14, 2023

Notes:

- Fresno County as of July 20, 2023
 - Completed testing.

4.1.3 State and CalWIN Wave 6 County Interface Partner File Exchange Test (IPT)

Table 4.1.3-1 – State Partners

INTERFACE TESTING		
STATE PARTNER	STATUS	TARGET COMPLETION DATE
Case Management Information and Payrolling System (CMIPS) – OSI	2/2	July 14, 2023
Electronic Benefits Transfer (EBT) - FIS	0/2	September 15, 2023
Medi-Cal Eligibility Data System (MEDS) - DHCS	1/2	September 15, 2023
Welfare Data Tracking Implementation Project (WDTIP) – OSI	2/2	July 19, 2023

Note:

- Testing in progress

Table 4.1.3-2 – CalWIN County Partners

INTERFACE TESTING		
CalWIN Wave 6 COUNTY PARTNER	STATUS	TARGET COMPLETION DATE
Sacramento County	0/11	September 15, 2023
San Francisco County	0/9	September 15, 2023
San Luis Obispo County	0/8	September 15, 2023

Notes:

- Testing in progress

4.1.4 Deliverable Management

Table 4.1.3-1 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

4.2 Activities for the Next Reporting Period

- ▶ Continue drafting designs for Migration Impact System Change Requests (SCRs)

4.2.1 Deliverable Management

Table 4.2.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

4.3 Upcoming Performance Tests

- ▶ Planned upcoming Performance tests for Batch, CalSAWS Core Batch, and Core Online
 - o Batch (batperf2 environment)
 - Environment refreshed with Golden Data Set (GDS) 13 (55 county data)
 - Execute performance runs to validate changes for CA-260380 - Performance: The Child Support Balancer job stages more records than required
 - o Analytics
 - Continue work on SCR CA-258929 - Upgrade EMR Clusters to EMR Serverless
 - o Core Online

Table 4.3-1 – Core Online Upcoming Performance Cycle

Performance Cycle	Start Date	End Date	Status
eCCP Performance Testing	June 26, 2023	July 28, 2023	In progress
Wave 5 Performance Testing	July 24, 2023	August 25, 2023	In progress

4.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

5.0 Conversion

5.1 Highlights of the Reporting Period

Table 5.1-1 – CalSAWS Conversion Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
5.1.1 CalWIN Conversion	<ul style="list-style-type: none"> Supported Wave 1, Wave 2, Wave 3, Wave 4, Counties post Go-Live Wave 5 DCR and ETL defects Began Wave 6 Mock pre activities (5B performance)
5.1.3 Gainwell Technologies	<ul style="list-style-type: none"> County Refactoring Overview San Diego County Refactoring Status Solano County Refactoring Status San Mateo County Refactoring Status Alameda County Refactoring Status

5.1.1 CalWIN Conversion

- Supported Wave 1, Wave 2, Wave 3, Wave 4, Counties post Go-Live
- Conversion DCR development and testing
- Wave 5 DCR and ETL defects
- Began Wave 6 Mock pre activities
- Began Wave 5B Performance execution

Table 5.1.1-1 – CalWIN Conversion Statistics Wave5B Go-live (June 2023 – Aug 2023)

Sprint	Total - Deferred Items	Sprint Duration		Wave 4B								
				Item Status								
				0%	25%	30%	50%	75%	5%	100%	100%	0%
				Not Started	Analysis & Mapping in Progress	Ready for Consortium Review	Build In Progress	Ready for AT	On Hold	Completed (Tested)*	CNR	Deferred
Overall	45	6/12/2023	7/14/2023	0	0	0	3	14	0	26	0	0
Wave 4C/5A Go-Live Sprint	2	6/16/2023	7/6/2023	0	0	0	0	0	0	2	0	0
Wave 5B pre-sprint	4	6/12/2023	6/23/2023	0	0	0	0	0	0	4	0	0
Wave 5B Sprint 1	39	6/26/2023	7/14/2023	0	0	0	3	14	0	22	0	0
Wave 5B Sprint 2 (DM changes)	49	7/24/2023	8/4/2023	11	8	0	3	2	0	25	0	0
Wave 5B Hardening	TBD	8/7/2023	8/18/2023	0	0	0	0	0	0	0	0	0

5.1.2 CalWIN Conversion Defects

- ▶ Table 5.1.2-1 – Open CalWIN Production Defects below represents Conversion Defects identified by the Counties Post Go-Live. Defects are triaged, assessed, and resolved as quickly as they via Data Change Requests (DCR)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 5.1.2-1 – Open CalWIN Production Defects to be Resolved by Conversion

Resolution by Delivery Date	P1	P2	P3	P4	Total
Between May 1 – July 31, 2023	0	60	83	13	156
Total Open Defects	0	60	83	13	156

Note: This table now includes the defects pending for Waves 1, 2, 3 and 4

- Table 5.1.2-2 – Open Converted Data Test (CDT), County Data Validation (CDV), and User Acceptance Test (UAT), Interface Partner Testing (IPT), System Test, Assembly Testing, and Post Go-Live Defects below represents Conversion Defects identified via testing effort prior to the respective Wave Go-Live. Defects prioritized for a Target Release after each wave Cutover will be assessed for inclusion into the Wave 3 Go Live Packet (GLP)

Table 5.1.2-2 – Open Defects to be Resolved by Conversion (by Status)

Open Defects by Status	P1	P2 - Normal/Medium	3 - Normal/Low	4 - Cosmetic	Grand Total
Pending Rejection	0	2	0	0	2
Reopened	0	0	0	0	0
New	0	20	15	3	38
Assigned	0	16	9	0	25
In Assembly Test	0	4	1	0	5
In Development	0	18	4	0	22
Development Complete	0	0	0	0	0
System Test	0	0	2	0	2
Test Complete	0	9	0	0	9
In Production	0	0	0	0	0
Grand Total	0	69	31	3	103

Note: This is the preliminary chart of the Wave 5 defects as of July 17, 2023

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 5.1.2-3 – Open Defects to be Resolved by Conversion (by Target Release)

Open Defects by Status	P1	P2 - Normal/Medium	3 - Normal/Low	4 - Cosmetic	Grand Total
Post Cutover 4B Day 1 – 10	0	0	0	0	0
Cutover 5A	0	8	0	0	8
Cutover 5B	0	1	0	0	1
Cutover 5B Go-live dependent (Post Cutover) DCRs	0	23	1	0	24
Cutover 5B Day 1-10 (Post Cutover)	0	8	0	0	8
Cutover 6A	0	29	0	0	29
Cutover 6B	0	0	0	0	0
Grand Total	0	0	30	3	33


Note:

- This is the preliminary chart of the Wave 5 defects as of July 17, 2023
 - These are Priority 3 defects for Wave 5 and these will be resolved by between Cutover 5B Day 1 and Cutover 6B

5.1.3 Gainwell Technologies

- ▶ CalWIN Document Migration
 - Continued delivery of Client Correspondence (CC) from CalWIN
 - Completed CC for all waves
 - Working through a small number of errored CC reported by document migration team

Figure 5.1.3-1 – Total Client Correspondence Sent

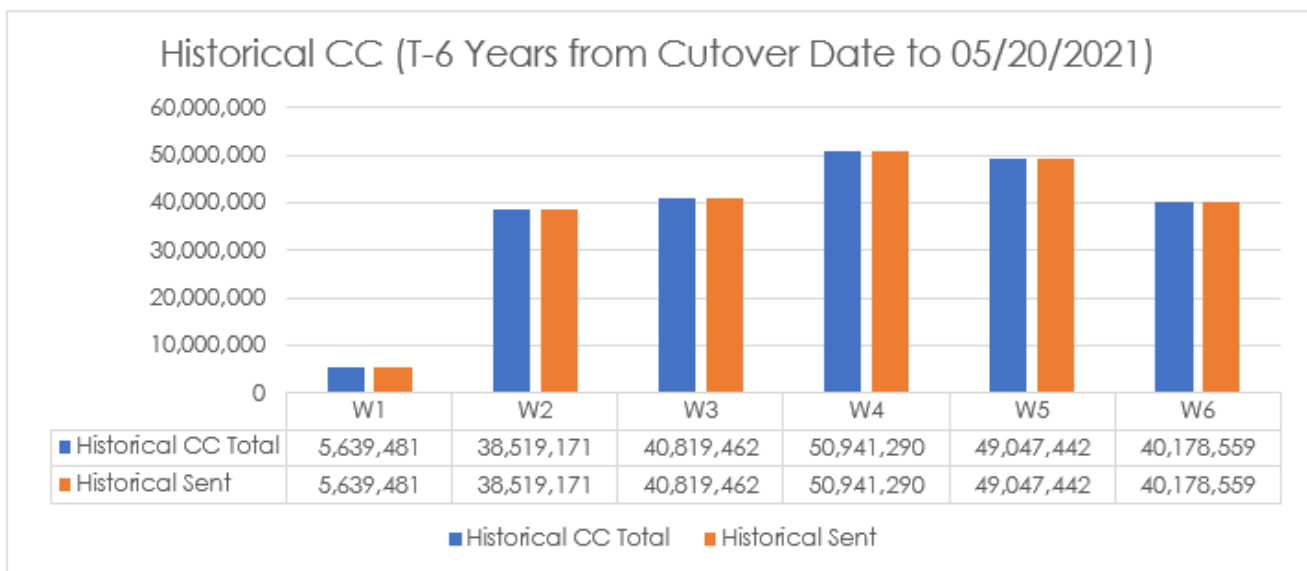

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 5.1.3-1 – CalWIN Notices Remaining Delivery

	June 1, 2023	June 15, 2023	July 1, 2023	July 15, 2023	July 30, 2023
Wave 1 Planned	15,721	0	0	0	0
Wave 1 Remaining	15,721	0	0	0	0
Wave 2 Planned	133,949	0	0	0	0
Wave 2 Remaining	133,949	0	0	0	0
Wave 3 Planned	263,641	263,641	0	0	0
Wave 3 Remaining	263,641	263,641	0	0	0
Wave 4 Planned	1,533,748	1,533,748	0	0	0
Wave 4 Remaining	1,533,748	1,533,748	0	0	0
Wave 5 Planned	1,296,052	1,296,052	1,296,052	0	0
Wave 5 Remaining	1,296,052	1,296,052	1,296,052	1,296,052	0
Wave 6 Planned	932,502	932,502	932,502	0	0
Wave 6 Remaining	932,502	932,502	932,502	932,502	0

- ▶ Sacramento County NoHo
 - Initial data delivered June 18, 2023, for County Data Validation (CDV) Inclusion
 - CDV to occur Mid-August 2023
 - Working with Conversion to include NoHo data for Mock 6
- ▶ County Collections
 - Engaged with Sacramento County for planning
 - Meeting with Alameda County for immediate assistance

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 5.1.3-2 – County Refactoring Overview

County	Migration Wave	Check-In Email Sent to County Y/N	CalSAWS Report Mapping Complete Y/N	PPM Proposal #	# of Reports to be Refactored	PPM Project #
Placer (PLA)	1	Y	Y	N/A	0	
Yolo (YOL)	1	Y	Y	N/A	46	63049
Contra Costa (CCS)	2	Y	N	63098	Day 1 – 21 Total -26	63580
Santa Clara (SCL)	2	Y	Y	63487	64	63497
Tulare (TUL)	2	Y	Y	N/A	0	
Orange (ORG)	3	Y	N	63688	Day 1 - 66	64076
Santa Barbara (SBR)	3	Y	Y	63730	Day 1 - 2 Total - 34	64224
Ventura (VEN)	3	Y	N	64186	0	64398
San Diego (SDG)	4	Y		63914	Day 1 – 43 Total - 151	64451
San Mateo (SMT)	4	Y	N	63099	Day 1- 4 Total - 74	TBD
Santa Cruz (SCZ)	4	Y	N	64077	Day 1 - 1 Total - 33	TBD
Solano (SOL)	4	Y	N	63871	Day 1- 18 Total - 62	64413
Alameda (ALA)	5	Y	N	63568	Day 1- 33 Total - 84	64651
Fresno (FRS)	5	N	N	N/A	0	N/A
Sonoma (SON)	5	N	N	64698	Day 1- 0 10	TBD
Sacramento (SAC)	6	N	N	64371	TBD	TBD
San Francisco (SFO)	6	N	N	64187	Day 1- 22 Total - 56	TBD
San Luis Obsipo (SLO)	6	N	N	64283	Day 1 – TBD Total - 33	TBD

Table 5.1.3-4 – San Diego County Refactoring Status

San Diego County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	5	0	0	0	0	0	5
Medium	16	1	0	0	0	1	14
Large	7	1	0	0	0	0	6
X-Large	11	0	0	0	0	5	6
XX-Large	4	0	0	0	0	2	2
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	43	2	0	0	0	8	33

- ▶ Solano County ad hoc report refactoring
 - Continued working with the County on development and approval of reports

Table 5.1.3-5 – Solano County Refactoring Status

Solano County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	1	0	0	0	0	0	1
Medium	4	0	0	0	0	1	3
Large	10	0	0	0	0	2	8
X-Large	3	0	0	0	0	1	2
XX-Large	0	0	0	0	0	0	0
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	18	0	0	0	0	4	14

- ▶ San Mateo County ad hoc report refactoring
Working with the County on development and approval of reports

Table 5.1.3-6 – San Mateo County Refactoring Status


San Mateo Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	0	0	0	0	0	0	0
Medium	1	0	0	0	0	0	1
Large	1	0	0	0	0	0	1
X-Large	0	0	0	0	0	0	0
XX-Large	2	0	0	0	0	2	0
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	4	0	0	0	0	2	2

- ▶ Alameda County ad hoc report refactoring
Working with the County on development and approval of reports.

Table 5.1.3-8 – Alameda County Refactoring Status

Alameda County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	2	0	0	0	0	2	0
Medium	3	0	0	1	0	2	0
Large	14	0	7	3	2	2	0
X-Large	10	0	4	2	2	2	0
XX-Large	4	0	2	1	1	0	0
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	33	0	13	7	5	8	0

Figure 5.1.3-2 – Alameda County Refactoring Status

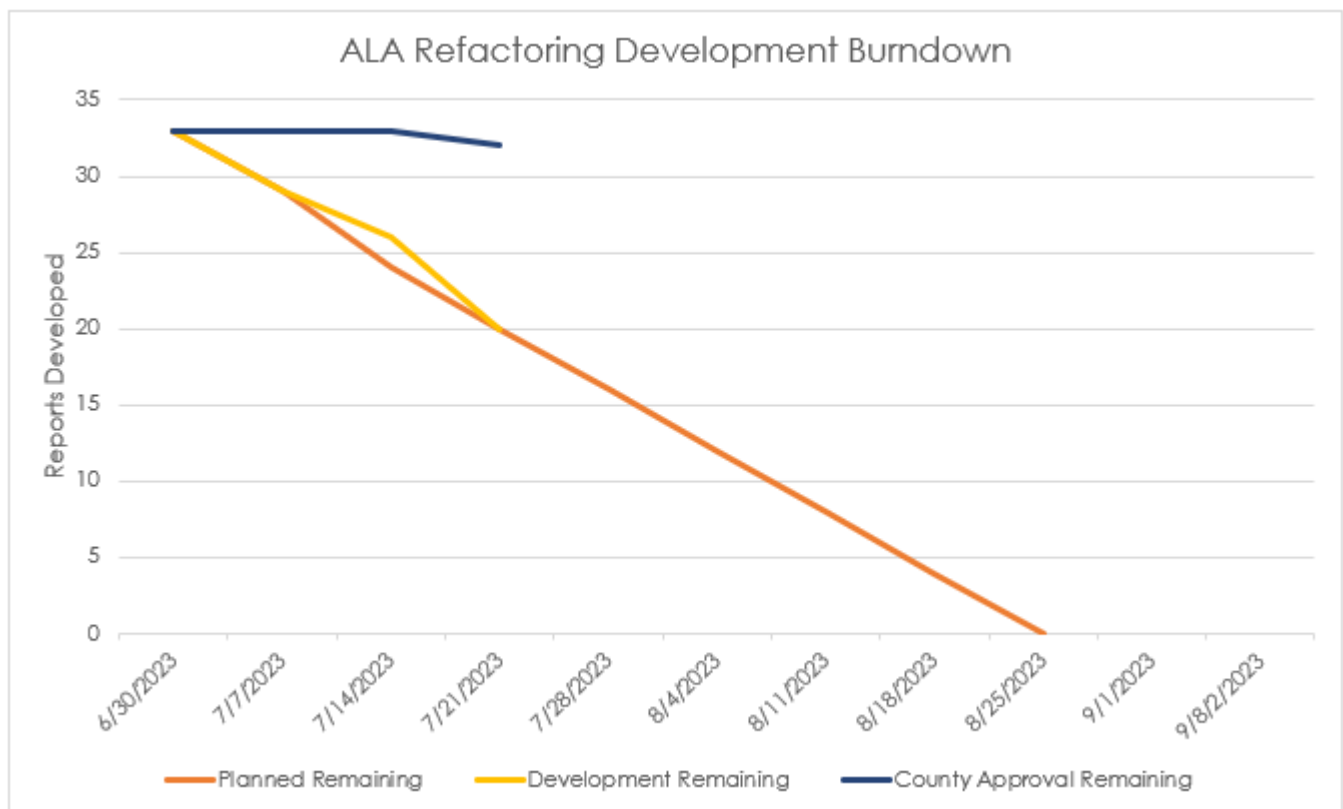

5.1.4 Ancillary Systems Conversion

- ▶ Continued to address issues found in production dataset size files. These files are necessary for CalWIN Core Conversion orchestration and integrations
- ▶ Facilitated exception reports review sessions with the Ancillary Counties to address questions and concerns

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

- ▶ Execute for Pref 5B to prepare for 5C Mock

Table 5.1.4-1 – Ancillary Systems Conversion Milestones

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
July 2020	Project Kick-Off/Discovery Sessions	Team introductions and Project overview	Completed
August 2020	File Specification Document (FSD)	CalSAWS Database (DB) (structures) as Conversion target	Completed
August 2020	Project Planning	Detailed walkthrough of the Project schedule and File Specification Document (FSD)	Completed
December 2020	Automation Framework Completed	Exception handling for Ancillary provided data is ready for the Counties	Completed
February 2021	Design/Mapping	All CalSAWS DB targets (defined in FSD) have source mappings from Ancillary	Completed
July 2021	Build	Development activities, dependent design mapping, are ready to begin (or are completed)	Completed
January 2022	System Test	System Test execution, dependent on test scripts and build completed, are ready to begin (or are completed)	Completed
June 2022	Integration Test	End-to-End Test execution, dependent on test scripts, System Test completed, and CDT completed, are ready to begin (or are completed)	Completed
August 2022	Wave 1 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
October 2022	Wave 2 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
February 2023	Wave 3 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
April 2023	Wave 4 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
June 2023	Wave 5 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed
August 2023	Wave 6 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	In progress

Table 5.1.4-2 – Ancillary Conversion Milestones

WAVE	MOCK B	MOCK C	CUTOVER B	CUTOVER C
Wave 1	August 6, 2022	N/A	October 27, 2022	N/A
	Completed	N/A	Completed	N/A
Wave 2	December 3, 2022	January 28, 2023	February 23, 2023	March 10, 2023
	Completed	Completed	Completed	Completed
Wave 3	February 4, 2023	April 1, 2023	April 20, 2023	May 22, 2023
	Completed	Completed	Completed	Completed
Wave 4	April 8, 2023	June 10, 2023	June 29, 2023	July 15, 2023
	Completed	Completed	Completed	Completed
Wave 5	June 17, 2023	July 29, 2023	August 31, 2023	September 16, 2023
	Completed	Not started	Not started	Not started
Wave 6	August 5, 2023	TBD	October 26, 2023	November 13, 2023
	Not started	Not started	Not started	Not started

Note: Ancillary Conversion only participates in B and C activities

5.1.5 CalWIN Migration Planning

- ▶ Completed the Wave 5A/4C Production Cutover
- ▶ Continued finalizing the Wave 5B Production Cutover plan and schedule
- ▶ Continued building the Wave 6A/5C Mock Cutover plan for review
- ▶ Began building the Wave 6B Mock Cutover plan for review
- ▶ Began building the Wave 6C Mock Cutover plan for review

Table 5.1.5-1 – Cutover Migration Milestones

MOCK CUTOVER			
WAVE	CUTOVER A <i>(Users and Offices)</i>	CUTOVER B <i>(Active Cases and Closed Case < 2 years)</i>	CUTOVER C <i>(Closed Cases > 2 years)</i>
Wave 2	Completed	Completed	Completed
Wave 3	Completed	Completed	Completed
Wave 4	Completed	Completed	Completed
Wave 5	Completed	Completed	July 29, 2023
Wave 6	July 29, 2023	August 5, 2023	August 14, 2023

Table 5.1.5-2 – Cutover Migration Milestones

WAVE	CUTOVER WINDOW	GO-LIVE
Wave 2C/3A	March 10, 2023 – March 13, 2023	March 13, 2023
Wave 3B	April 20, 2023 – April 24, 2023	April 24, 2023
Wave 4A	May 12, 2023 - May 15, 2023	May 15, 2023
Wave 3C	May 19, 2023 – May 22, 2023	May 22, 2023
Wave 4B	June 29, 2023 - July 3, 2023	July 3, 2023
Wave 4C/5A	July 14, 2023 - July 17, 2023	July 17, 2023
Wave 5B	August 31, 2023 - September 4, 2023	September 4, 2023
Wave 5C/6A	September 15, 2023 - September 18, 2023	September 18, 2023
Wave 6B	October 26, 2023 - October 30, 2023	October 30, 2023
Wave 6C	November 11, 2023 - November 13, 2023	November 13, 2023

5.1.6 Deliverable Management

Table 5.1.6-1 – Conversion Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
84	CalSAWS Deployment Complete Milestone/Report - CalWIN Wave 4	<ul style="list-style-type: none"> Continued developing the Draft Deliverable Submission of the DDEL is due on August 9, 2023

5.2 Activities for the Next Reporting Period

5.2.1 CalWIN Conversion

- ▶ Continue to triage, assess, and resolve CalWIN Wave 1, Wave 2, Wave 3, and Wave 4 Post Go-Live Issues
- ▶ Continue Wave 5 development
- ▶ Begin Wave 5 and 6 Mock activities

5.2.2 CalWIN Migration Planning

- ▶ Finalize the 6A/5C Mock Cutover plan
- ▶ Prepare the 6A/5C Mock Cutover Table Read
- ▶ Continue preparing the 6B Mock Cutover plan for review
- ▶ Continue preparing the 6C Mock Cutover plan for review

5.2.3 Gainwell Technologies

- ▶ CalWIN Data Migration
 - Continue planning for future CalWIN extractions
- ▶ CalWIN Data Retention Maintenance & Operations (M&O)
 - Continue planning for future data retention runs

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

5.2.4 Ancillary Systems Conversion

- ▶ Review and address tickets for Cutover 3B, 3C, 4B, 4C
- ▶ Prepare Wave 5C Mock Cutover

5.2.5 Deliverable Management

Table 5.2.5-1 – Conversion Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
84	CalSAWS Deployment Complete Milestone/Report – CalWIN Wave 4	<ul style="list-style-type: none">• Continue developing the Draft Deliverable• Submission of the DDEL is due on August 9, 2023

5.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

6.0 CalWIN Functional Support

6.1 Highlights of the Reporting Period

Table 6.1-1 – CalSAWS CalWIN Functional Support Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
	<ul style="list-style-type: none">• None to note for this reporting period

- ▶ Continued CalWIN Functional Support coordination during July 17 – 21, 2023 by:
 - Supported Implementation Support Services (ISS) Team Lead Meeting on July 18, 2023
 - Supported CalSAWS Weekly Status Meeting on July 19, 2023, to highlight key workstream reporting items
- ▶ Wave 4 Post Implementation Support during July 17 – 21, 2023 by:
 - Provided virtual and extended post implementation support
 - Supported daily Project Production and County Operations calls. Maintained Issues tracker and reported on status of open issues.
 - Provided daily business metrics
- ▶ Wave 5 Process Simulation during July 17 – 21, 2023 by:
 - Provided functional support to Wave 5 Counties during Process Sim
 - Supported batch operations in UAT2 environment
- ▶ Wave 5 County Preparation during July 17 – 21, 2023 by:
 - Provided functional support to Wave 5 Counties and supported Daily County Preparation Phase Debrief meetings
 - Provided daily and weekly metrics
- ▶ Wave 5 Implementation Support during July 17 – 21, 2023 by:

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

- o Facilitated Open Defects Strike Team meetings for Wave 5

6.2 Activities for the Next Reporting Period

- ▶ Continue CalWIN Functional Support coordination during July 24 – 28, 2023 by:
 - o Prepare for ISS Team Lead Meeting on July 25, 2023
 - o Prepare for CalSAWS Weekly Status Meeting on July 16, 2023, to highlight key workstream reporting items
- ▶ Wave 4 Post Implementation Support during July 24 – 28, 2023 by:
 - o Provide virtual and extended post implementation support
 - o Support daily Project Production and County Operations calls. Maintain Issues tracker and report out on status of open issues.
 - o Provide daily business metrics
- ▶ Wave 5 Process Simulation during July 24 – 28, 2023 by:
 - o Provide functional support to Wave 5 Counties during Process Sim
 - o Support batch operations in UAT2 environment
- ▶ Wave 5 County Preparation during July 24 – 28, 2023 by:
 - o Provide functional support to Wave 5 Counties and support Daily County Prep Phase Debrief meetings
 - o Provide daily and weekly metrics
- ▶ Wave 5 Implementation Support during July 24 – 28, 2023 by:
 - o Prepare for Open Defect Strike Team meetings for Wave 5

6.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

7.0 Technical Infrastructure

7.1 Highlights of the Reporting Period

Table 7.1-1 – CalSAWS Technical Infrastructure Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
	<ul style="list-style-type: none">• None to note for this reporting period

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

Table 7.1-2 – County Network Connectivity Readiness Status

CalWIN WAVE 1 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	Completed	100.0%	100.0%
Critical Path	Completed	100.0%	100.0%

CalWIN WAVE 2 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	Completed	100.0%	100.0%
Critical Path	Completed	100.0%	100.0%

CalWIN WAVE 3 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Overall Network Interconnectivity	Completed	100.0%	100.0%
Critical Path	Completed	100.0%	100.0%

CalWIN WAVE 4 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Project Networking Connectivity	Completed	100.0%	97.2%
County Networking Connectivity	Completed	100.0%	100.0%

CalWIN WAVE 5 COUNTIES			
NETWORKING READINESS	STATUS	ACTUAL	PLANNED
Project Networking Connectivity	Completed	100.0%	100.0%
County Networking Connectivity	Completed	100.0%	100.0%

CalWIN WAVE 6 COUNTIES				
NETWORKING READINESS	STATUS		ACTUAL	PLANNED
Project Networking Connectivity	Completed	100.0%	98.2%	
County Networking Connectivity	Completed	100.0%	100.0%	

- ▶ Wave 1
 - Completed County migration
 - Completed Operational handover of sites to CalSAWS Technical teams
- ▶ Wave 2
 - Completed County migration
 - Completed Operational handover of sites to CalSAWS Technical teams

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

- ▶ Wave 3
 - Completed County migration
 - Completed Operational handover of sites to CalSAWS Technical teams
- ▶ Wave 4
 - Completed County migration
 - Completed Operational handover of sites to CalSAWS Technical teams
- ▶ Wave 5
 - Completed preparation for County migration
 - Completed Operational handover of sites to CalSAWS Technical teams
- ▶ Wave 6
 - Completed all technical readiness activities for Wave 6 Counties
 - Ongoing San Francisco County Circuit delivery
 - Delivered and activated AT&T circuit
 - Risk 288 to be closed post activation of Comcast circuit.

7.2 Activities for the Next Reporting Period

- ▶ Provide troubleshooting support for Wave 5 to 6 Counties to connect to CalSAWS
- ▶ Continue to track secondary circuit deliveries for San Francisco County

7.3 Deviations from Plan/Adjustments

- ▶ Risk 281.4 for San Diego County for Point of Presence (POP) location change
 - New CalSAWS Requests for Information (CRFI) to be submitted outlining changes made to Evoque Data Center
 - Reconfiguration require use of temporary alternate IP Addressing space to accommodate counties Data Center move
 - Risk probability has been lowered and will remain a watchlist item
 - Both circuits delivered, pending activation
 - Risk rating revised due to County notifying CalSAWS of 1-month delays in having the Cage / Rack ready. This results in downstream tech tasks getting compressed.
 - WAN connectivity completed at San Diego Databank on May 30, 2023, for device installation
 - County integration with San Diego Databank completed on June 28, 2023.
 - County Functional and Interface Partner Testing (IPT) Regression (with Blank file) testing to commence and complete by July 31, 2023
 - County cutover to Databank planned for August 4, 2023.
 - All IPT regression testing (Connectivity) successfully completed.
- ▶ Risk 288 for San Francisco County delay in Circuit delivery
 - Ongoing carrier delays in Level 3 / Lumen Circuit delivery due to projected construction
 - Lumen circuits cancelled and replaced with Comcast (ETC – 3 months)
 - Risk 288 impact and probability rating raised due to additional delays to the circuit delivery (Projection of Sept 2023 for completion of construction)
 - As per alignment in Risk meeting, contingency plan to replace Comcast with secondary AT&T Fiber circuit initiated. Circuit order submitted.

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: July 17, 2023, to July 23, 2023

- o Residual risk remains of site lacking carrier diversity and risk of imminent impact to all users if AT&T carrier is affected.
- o Conducted a site survey on July 16, 2023 to determine feasibility of delivering AT&T circuit.
- o Circuit delivered and activated on July 25, 2023, Risk to be sunset.

8.0 Appendices

Appendix A – CalSAWS Deliverable Summary

Appendix B – CalSAWS Migration Work Plan Summary

Appendix C – CalSAWS DD&I Project Gantt Chart

Appendix D – CalSAWS Project Risks and Issues Report

Appendix E – CalSAWS Imaging Document Migration

