



CalSAWS DD&I Weekly Status Report

**Reporting Period: October 2, 2023, to October 8,
2023**

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

1.0	Project Management	3
1.1	Project Deliverables Summary	3
1.2	Highlights of the Reporting Period	3
1.2.1	Project Management	3
1.2.2	Communications Management	4
1.2.3	Cultural Transformation	5
1.2.4	Inclusion, Diversity, and Equality Advancement (IDEA)	5
1.3	CRFI/CIT Communications Information	6
1.4	Activities for the Next Reporting Period	7
1.4.1	Project Management	7
1.4.2	Communications Management	8
1.4.3	Cultural Transformation	8
1.4.4	Inclusion, Diversity & Equality Advancement (IDEA)	8
1.5	Deviations from Plan/Adjustments	9
2.0	Imaging	9
2.1	Highlights of the Reporting Period	9
2.2	Activities for the Next Reporting Period	10
2.3	Upcoming Performance Tests	10
2.4	Deviations from Plan/Adjustments	10
3.0	Customer Service Center (CSC)	10
3.1	Highlights of the Reporting Period	10
3.2	Activities for the Next Reporting Period	12
3.3	Upcoming Performance Tests	12
3.4	Deviations from Plan/Adjustments	12
4.0	Application Development and Test	13
4.1	Highlights of the Reporting Period	13
4.1.1	Application Development Summary	13
4.2	Activities for the Next Reporting Period	14
4.3	Deviations from Plan/Adjustments	14
5.0	Conversion	14
5.1	Highlights of the Reporting Period	14
5.1.1	CalWIN Conversion	14
5.1.2	CalWIN Conversion Defects	15

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

5.1.3	Gainwell Technologies	16
5.1.4	Ancillary Systems Conversion	20
5.1.5	CalWIN Migration Planning	21
5.1.6	Deliverable Management.....	21
5.2	Activities for the Next Reporting Period.....	21
5.2.1	CalWIN Conversion	21
5.2.2	CalWIN Migration Planning	22
5.2.3	Gainwell Technologies	22
5.2.4	Ancillary Systems Conversion	22
5.2.5	Deliverable Management.....	22
5.3	Deviations from Plan/Adjustments.....	22
6.0	CalWIN Functional Support	22
6.1	Highlights of the Reporting Period	22
6.2	Activities for the Next Reporting Period.....	23
6.3	Deviations from Plan/Adjustments.....	23
7.0	Appendices.....	24

1.0 Project Management

1.1 Project Deliverables Summary

Table 1.1-1 – Overall Summary of Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	TEAM	STATUS [1]	STATUS
	None for the reporting period			

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

1.2 Highlights of the Reporting Period

Table 1.2-1 – CalSAWS Project Management Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Project Management	<ul style="list-style-type: none"> None to note for the reporting period

1.2.1 Project Management

- ▶ Continued CalSAWS DD&I Facility Management activities, including:
 - Key initiatives related to facilities at the Rancho Cordova Project Office are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) below

Table 1.2.1-1 – Key Facility Initiatives/Projects

ITEM #	INITIATIVES/PROJECTS	LOCATION	TARGET DATE	NOTES/STATUS
1	Facility Closure and transition	Rancho Cordova and Norwalk Project Offices	October 31, 2023	<ul style="list-style-type: none"> Continued planning facility closure of both the ADF (Application Development Facility) and the PMO (Project Management Office) locations and transition facility to our CalSAWS Roseville office location Office location lease expirations scheduled for October 31, 2023

- ▶ Continued to support requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue CalSAWS Risks and Issues Management Group (RMG) activities, including:
 - Continue to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
 - Conducted Monthly Risks and Issues Management Group (RMG) meeting held on October 4, 2023
- ▶ Continue activities to support Project staff working remotely

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

- o Continued preparations for the Monthly CalSAWS Connect to be distributed on October 12, 2023
- o Continued developing Project communications, as needed
- ▶ Completed developing materials for the monthly CalSAWS IT Project Status Report for September 2023 and preparations for the monthly CalSAWS IT Report Meeting with OTSI (Office of Technology and Solutions Integration), CMS (Centers for Medicare and Medicaid Services), and FNS (Food and Nutrition Service) that is scheduled for October 11, 2023
- ▶ Continued performing contract management activities:
 - o Change Notice 29 (October JPA) is in development and may include:
 - Requirement reconciliation to conform with approved requirements in JIRA
 - o Continued planning the implementation of requirements from the DHCS and CDSS Privacy and Security Agreements (PSAs) that were approved by the Joint Powers Authority (JPA) Board of Directors on April 16, 2021
- ▶ Continued performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.2.1-2 – Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for the reporting period	

1.2.2 Communications Management

- ▶ CalSAWS Communications Management activities including
 - o Continued to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy
 - o Continued oversight and management of Power of 58 materials
- ▶ CalSAWS External Website (www.calsaws.org)
 - o Continued the administration and support of the CalSAWS external website
 - See Table 1.2.2-1 for details on website support activities

Table 1.2.2-1 – Website Support Activities

TASK	DATE (S)	TASK TYPE
Updated WordPress Plugins	October 5, 2023	Website Maintenance

Table 1.2.2-3 – CalSAWS.org Subscription Service Statistics

WEBPAGE	PERCENT OF SUBSCRIBERS
Latest News – CalSAWS Buzz Newsletter	20%
Latest News – News	16%
Other Updates – System Updates	16%
Other Updates – Careers	14%
CalSAWS Committees – CalWORKs/CalFresh	15%

Note: Due to the unavailability of Google Analytics, the 'CalSAWS.org Usage Statistics' table and the 'Overall

CalSAWS.org Usage Trend' graph have been removed.

1.2.3 Cultural Transformation

- ▶ Culture Ambassadors Network (CAN)
 - Wellness Wednesday
 - Distributed content for September Wellness Wednesday – “Building Resilience”
 - Planning for Movember
 - Continued to prepare for upcoming activities and events
 - Summer Photo/Best vacation
 - SAWS memorabilia
 - Annual Art Tour
 - Planning for future Wellness Wednesday topics through end of 2023
 - October - Building Your Resilience
 - November - Gratefulness
 - December – Celebrating You

1.2.4 Inclusion, Diversity, and Equality Advancement (IDEA)

- ▶ Co-Create Phase
 - CalSAWS “We Are One” SharePoint Site
 - Continued to update the “We Are One” website tab
 - Pulse Survey
 - Continued researching evidence-based psychological constructs predictive of successful DEI programs
 - Prepare for redesigning the pulse survey to measure inclusive leadership
 - CalSAWS Table Talks
 - Continued planning logistics of next Table Talk
 - Buddy Program
 - Continued supporting buddy pairs
 - Continued planning for closing of Buddy Program round 4 and the opening of round 5
 - Employee Resource Groups (ERGs)
 - Continued to manage and support Employee Resource Groups (ERGs) council
 - Planned ERG Showcase meeting to encourage recruitment amongst ERG membership
- ▶ General
 - Continued working with CalSAWS staff to create and present Inspiration Stations during monthly virtual CalSAWS Project All Staff Meetings
 - Continued conversations with volunteer organization to provide volunteer opportunities for CalSAWS members
 - Continued to partner with the CalSAWS Connect team to provide content for the CalSAWS monthly newsletter
 - Continued to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the Project

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

1.3 CRFI/CIT Communications Information

- The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period ending October 8, 2023

Table 1.3-1 – CITs

CIT ID	SUBJECT	CATEGORY	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
0344-23	Wave 6 CalWIN County Go-Live Packet	Informational	October 2, 2023	Kishan Mallur	Rachel Frey, and Duncan Gilliam
0345-23	CalSAWS Project County Reallocations SFY 2023-24 v2	Informational	October 4, 2023	Britt Carlsen	Girish Uppal
0348-23	Wave 6C Cutover Weekend Calendar Infographic – System Downtime	Informational	October 5, 2023	Anand Kulkarni	Lesley Pevny

- The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period ending October 8, 2023

Table 1.3-2 – CRFIs

CRFI ID	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	CalSAWS CONTACT
23-101	Changes to accessing APEX URL for CalSAWS Ad-Hoc	July 28, 2023	Open	August 11, 2023	Melanie Gines, and Lloyd Rankine
23-104	Access to CalWIN Read-Only Portal over CalSAWS Extranet	August 4, 2023	Open	September 30, 2023	Melanie Gines, and Lloyd Rankine
23-113	EBT Account Activity File	September 6, 2023	Open	September 26, 2023	Sheryl Eppler
23-115	CalWIN Wave 6 Counties - Identify Participants for CalWIN Go-Live: 1) County Click-Through, 2) CalHEERS and GA/GR Correspondence Smoke Testing	September 19, 2023	Closed	October 2, 2023	Cristy Sharma

- ▶ The following table outlines overdue CalSAWS Requests for Information (CRFIs) for the reporting period ending October 8, 2023

Table 1.3-3 – Overdue CRFIs

CRFI ID	Subject	Region 1	Region 2	Region 3	Region 4	Region 5	Region 6
23-101	Changes to accessing APEX URL for CalSAWS Ad-Hoc			Trinity County			
23-104	Access to CalWIN Read-Only Portal over CalSAWS Extranet	San Mateo County				Ventura County	
23-113	EBT Account Activity File	San Francisco County	El Dorado, Mono, Sierra, Sutter, and Yuba Counties	Siskiyou County	Inyo, and Mariposa Counties	San Bernadino, Santa Barbara, Riverside and Ventura Counties	

1.4 Activities for the Next Reporting Period

1.4.1 Project Management

- ▶ Continue CalSAWS DD&I Facility Management activities, including:
 - Continue key initiatives related to facilities at the Rancho Cordova and Norwalk Project Offices, which are provided in Table 1.2.1-1 (Key Facility Initiatives/Projects) above
- ▶ Continue CalSAWS Risks and Issues Management Group (RMG) activities, including:
 - Continue to work with risk and issue owners to monitor risks and update risk mitigation plans for CalSAWS DD&I Project risks and issues
- ▶ Continue activities to support Project staff working remotely
 - Continue developing Project communications, as needed
 - Complete the Monthly CalSAWS Connect to be distributed on October 12, 2023
- ▶ Participate in the monthly CalSAWS IT Report Meeting with OTSI (Office of Technology and Solutions Integration), CMS (Centers for Medicare and Medicaid Services), and FNS (Food and Nutrition Service) that is scheduled for October 11, 2023
- ▶ Begin developing materials for the Project Steering Committee (PSC) Meeting that is scheduled for October 19, 2023
- ▶ Begin developing materials for the Joint Powers Authority (JPA) Meeting that is scheduled for October 20, 2023
- ▶ Continue to support Return to Office (RTO) requests for CalSAWS Project staff to visit the CalSAWS Rancho Cordova and Norwalk Project offices, and support CalSAWS Project staff who have returned to work at the project offices (either full time or as part of the 50/50 model)
- ▶ Continue performing Contract Management activities for the CalSAWS DD&I Project
- ▶ Continue performing Deliverable Management activities for the CalSAWS DD&I Project

Deliverable Management

Table 1.4.1-1 – Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
	None for next reporting period	

1.4.2 Communications Management

- ▶ Continue to monitor usage and update materials as requested
 - See table 1.4.2-1 for planned website support activities
- ▶ CalSAWS Communications Management activities including:
 - Continue to gather key communication milestones from the Project teams
- ▶ CalSAWS Enhanced Communications Strategy:
 - Continue oversight and management of Power of 58 roll out

Table 1.4.2-1 – Website Support Activities

TASK	DATE(S)	TASK TYPE
None to note for the reporting period	N/A	N/A

1.4.3 Cultural Transformation

- ▶ Develop Wellness Wednesday monthly topics for 2023
- ▶ Develop calendar of events for the ambassador initiatives the year 2023
- ▶ Continue to provide Project management support to Cultural Ambassadors as they continue to develop the plans for the initiatives
- ▶ Continue to coordinate working sessions for each Ambassador group to further their initiatives planning and discuss their individual contributions
- ▶ Continue to develop wellness initiative content to keep the project staff engaged
- ▶ Continue to update resources and a collaboration workspace (Teams Channel) with new relevant materials to support the implementation of the prioritized initiatives
- ▶ Continue to monitor Microsoft Teams channels for any help needed from Ambassadors

1.4.4 Inclusion, Diversity & Equality Advancement (IDEA)

- ▶ Continue planning for close of buddy program round 4 and opening of round 5
- ▶ Continue to redesign pulse survey
- ▶ Explore DEI learning curriculum for 2024
- ▶ Continue creating transition plan for IDEA lead scheduled paternity leave
- ▶ Continue conversations with nonprofit to provide volunteer opportunities to staff in Los Angeles
- ▶ Continue exploring November Table Talk topic
- ▶ Continue planning Employee Resource Group (ERG) Collaboration Events
- ▶ Continue partnering with CalSAWS members to create an Inspiration Station and present during virtual CalSAWS Project All Staff Meeting
- ▶ Continue to partner with CalSAWS Connect team to provide content for the CalSAWS monthly newsletter

- ▶ Continue to engage the Employee Resource Groups (ERGs) to assist with events or ideas to represent their members across the Project

1.5 Deviations from Plan/Adjustments

- ▶ None for the reporting period

2.0 Imaging




2.1 Highlights of the Reporting Period

Table 2.1-1 – CalSAWS Imaging Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
Appendix E	<ul style="list-style-type: none"> • Sacramento County: <ul style="list-style-type: none"> ◦ Sacramento County is working with Hyland to reconcile their manifest.

- ▶ CA-253637 - DDID 2261 - Imaging CalWIN Retention Phase 2 on track in system test with no blockers.
- ▶ Continued to monitor Imaging migration status by County.
 - For future details of status' by County, they are now available in Appendix E - CalSAWS Imaging Document Migration

Table 2.1-2 – CalSAWS Imaging County Migration Risk Status

WAVE	COUNTY	STATUS [1]
6	• San Francisco County	
	• San Luis Obispo County	
	• Sacramento County	

[1] Status: **Green:** On schedule, performing as planned; **Amber:** Potential delay/monitor with no material schedule impact; **Red:** Behind schedule and requires escalation

Note:

- Detailed metrics of each County by wave has been included in the Appendix E - CalSAWS Imaging Document Migration

Table 2.1-3 – CalSAWS Imaging Project Milestones for Current Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 6	Conduct San Francisco County Document Migration Discovery Session Check-in	October 3, 2023	Completed

Table 2.1-4 – CalSAWS Imaging Project Milestones for Next Reporting Period

WAVE	MILESTONES Migration Activities	DUE DATE	STATUS
WAVE 6	Conduct San Luis Obispo County Document Migration Discovery Session Check-in	October 9, 2023	Scheduled
	Conduct Sacramento County Document Migration Discovery Session Check-in	October 11, 2023	Scheduled

2.2 Activities for the Next Reporting Period

- ▶ Continue to manage the milestones for the Image Migrations in the tables in Appendix E

2.3 Upcoming Performance Tests

- ▶ None for the reporting period

2.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

3.0 Customer Service Center (CSC)

3.1 Highlights of the Reporting Period

Table 3.1-1 – CalSAWS Customer Service Center Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
3.1	<ul style="list-style-type: none"> Continued Wave 6 Model Office

- ▶ Continued System Testing of Wave 6 Contact Centers (CA-240171, CA-240172, and CA-240173)
- ▶ Continued System Testing of Phase 3 eCCP Migration SCRs (CA-258660, CA-258662, CA-258647, and CA-258663)
- ▶ Continued build of Scheduled Callback (CA-229573)
- ▶ Continued System Testing of Inbound IVR additional languages SCR (CA-226837)

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

Table 3.1-2 – Customer Service Center Enhancement Milestones

MILESTONES	SYSTEM TEST DELIVERY DATE	STATUS	RELEASE/ MINOR RELEASE
DDID 2292, 2697, 2698, 2723, 2724 WFM/QA/QM Reporting (CA-226209)	December 3, 2021	In Production	22.01
DDID 2700 Enhanced CCP (CA-226844)	March 18, 2022	In Production	22.03 22.05.06
DDID 2727 Work-from-home Modifications (CA-227064)	March 18, 2022	In Production	22.03 22.05.06
DDID 2216, 2725 External Party Access IVR (CA-226839)	March 25, 2022	In Production	22.05
DDID 2211, 2217, 2218, 2220, 2729, 2730, 2731, 2046, 2732 Telephonic Signature (CA-226838)	April 1, 2022	In Production	22.05
DDID 2704 Post-Call Survey (CA-228023)	July 8, 2022	In Production	22.07 22.09.16
DDID 2687, 2688, 2689, 2690, 2691, 2692, 2693, 2694, 2695, 2696, 2222, 2702, 2721, 2169, 2284, 2722 Admin Page (CA-226672)	October 7, 2022	In Production	22.11 22.12.11
DDID 2718 Task for Cancelling an Appointment in Outbound IVR (CA-231234)	November 11, 2022	In Production	23.01 23.02.17
DDID 2219, 2716, 2717, 2728 Outbound IVR - (CA-226207)	November 11, 2022	In Production	23.01 23.02.17
DDID 2701, 2706 Voice Authentication Languages (CA-226843)	October 7, 2022	In Production	23.01 23.02.16
DDID 2699, 2210, 2705, 2707, 2708, 2709, 2710, 2711, 2712, 2713, 2714, 2715, 2719, 2720, 2258 Inbound IVR (CA-226837)	January 12, 2023	System Test	23.09 23.10.19
DDID 2284 Scheduled Callback (CA-229573)	July 8, 2022	In Development	23.09 23.10.31
DDID 2268 Display the CalSAWS Contact Center IVR Caller ID for outbound calls	June 14, 2023	Design In Progress	23.09 23.10.31

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

Table 3.1-3 – Los Angeles County Milestones

MILESTONES		DUE DATE	OWNER
1	Design completion	March 11, 2022	CalSAWS Project Team
2	Initial performance/load testing	March 18, 2022	CalSAWS Project Team
3	Training development	May 16, 2022	CalSAWS Project Team
4	Build and unit test	May 20, 2022	CalSAWS Project Team
5	Training content review	May 20, 2022	Consortium
6	Training execution	June 29, 2022	CalSAWS Project Team
7	System Test	July 15, 2022	CalSAWS Project Team
8	Conduct model office	January 9, 2023	Los Angeles County
9	Go-live	November 17, 2023	CalSAWS Project Team
10	Post go-live support	November 20, 2023	CalSAWS Project Team

Table 3.1-3 – Former C-IV County eCCP Migration

PHASE	COUNTIES	GO-LIVE	STATUS
1	Merced, and San Joaquin Counties	May 12, 2023	In Production
2	Butte, Marin, and Sutter Counties	August 16, 2023	In Production
3	Kern, Kings, Riverside, and Stanislaus Counties	September 28, 2023	In Production
4	Humboldt, Monterey, San Bernardino, and Yuba Counties	December 15, 2023	In Development

3.2 Activities for the Next Reporting Period

- ▶ Complete System Testing Wave 6 Contact Centers (CA-240171, CA-240172, and CA-240173)
- ▶ Complete System Testing of Phase 3 eCCP Migration SCRs (CA-258660, CA-258662, CA-258647, and CA-258663)
- ▶ Continue build of Scheduled Callback (CA-229573)
- ▶ Continue System Testing of Inbound IVR additional languages SCR (CA-226837)

3.3 Upcoming Performance Tests

- ▶ No upcoming performance tests.

3.4 Deviations from Plan/Adjustments

- ▶ None for the reporting period

4.0 Application Development and Test

4.1 Highlights of the Reporting Period

Table 4.1-1 – CalSAWS Application Development and Test Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
4.1.1 Application Development Summary	<ul style="list-style-type: none"> Continued implementation of the remaining 23.09 DD&I priority release System Change Requests (SCRs).

4.1.1 Application Development Summary

Table 4.1.1-1 – CalSAWS Application Development Summary

	Status	23.09
Design	New	1
	Design in Progress	1
	Ready for Committee	0
	Committee review	0
	Pending approval	0
Build	Approved	4
	In Development	5
	Development completed	3
	In Assembly Test	1
Test	System Test	1
	Test completed	3
	In Production	3
	Grand total	22

System Change Requests (SCRs) in Production	1,080
---	-------

Note:

- This table includes Application Development System Change Requests (SCRs) with migration impact. SCRs in production represents a count of any SCR that have a project phase of migration and have been deployed to production.

- ▶ Continued drafting designs and development activities. Status is provided in Table 4.1.1-1 (CalSAWS Application Development Summary)

4.1.2 Deliverable Management

- ▶ There are no remaining DD&I Deliverables

4.2 Activities for the Next Reporting Period

- ▶ Continue drafting designs for Migration Impact System Change Requests (SCRs)

4.2.1 Upcoming Performance Tests

- ▶ Planned upcoming Performance tests for Core Online
 - Core Online

Table 4.3-1 – Core Online Upcoming Performance Cycle

Performance Cycle	Start Date	End Date	Status
Hyland performance testing	September 15, 2023	October 25, 2023	In progress
CW6 – 58 County Performance testing	September 25, 2023	October 20, 2023	In progress

4.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

5.0 Conversion

5.1 Highlights of the Reporting Period

Table 5.1-1 – CalSAWS Conversion Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
5.1.1 CalWIN Conversion	<ul style="list-style-type: none">• Supported Wave 1, Wave 2, Wave 3, Wave 4, and Wave 5 Counties post Go-Live• Continuing Wave 6B development and fittest activities• Conversion ETL and DCR development and testing• Began 6B Fittest activities (September CalWIN Wave 6 data (with NoHo)
5.1.3 Gainwell Technologies	<ul style="list-style-type: none">• County Refactoring Overview• Alameda County Refactoring Status• Wave 6 Refactoring Update

5.1.1 CalWIN Conversion

- ▶ Supported Wave 1, Wave 2, Wave 3, Wave 4, and Wave 5 Counties post Go-Live
- ▶ Continued conversion DCR development and testing
- ▶ Continued conversion ETL development and testing for data model updates
- ▶ Began 6B Fittest activities (September CalWIN Wave 6 data (with NoHo)

Table 5.1.1-1 – CalWIN Conversion Statistics Wave 6B Go-live (August – October 2023)

Sprint	Total - Deferred Items	Wave 6B										
		Sprint Duration		Item Status								
				0%	25%	30%	50%	75%	5%	100%	100%	0%
				Not Started	Analysis & Mapping In Progress	Ready for Consortium Review	Build In Progress	Ready for AT	On Hold	Completed (Tested)*	CNR	Deferred
Overall	65	7/31/2023	9/22/2023	2	1	0	1	22	0	39	0	0
Wave 6B pre-sprint	11	7/31/2023	8/18/2023	0	0	0	0	2	0	9	0	0
Wave 6B Sprint 1	18	8/21/2023	9/8/2023	0	0	0	0	10	0	8	0	0
Wave 6B Sprint 2	36	9/11/2023	9/22/2023	2	1	0	1	10	0	22	0	0
Wave 6B Hardening	TBD	9/25/2023	10/13/2023	0	0	0	1	9	0	5	0	0

5.1.2 CalWIN Conversion Defects

- Table 5.1.2-1 – Open CalWIN Production Defects below represents Conversion Defects identified by the Counties Post Go-Live. Defects are triaged, assessed, and resolved as quickly as they via Data Change Requests (DCR)

Table 5.1.2-1 – Open CalWIN Production Defects to be Resolved by Conversion

Resolution by Delivery Date	P1	P2	P3	P4	Total
Between August 1 – September 30, 2023	0	36	39	2	77
Total Open Defects	0	36	39	2	77

Note: This table now includes the defects pending for Waves 1, 2, 3, 4 and 5.

- Table 5.1.2-2 – Open Converted Data Test (CDT), County Data Validation (CDV), and User Acceptance Test (UAT), Interface Partner Testing (IPT), System Test, Assembly Testing, and Post Go-Live Defects below represents Conversion Defects identified via testing effort prior to the respective Wave Go-Live. *Note: The below defects are Wave 6 defects and Days 1-10, post-Days 1-10 plan is being worked on.*

Table 5.1.2-2 – Open Defects to be Resolved by Conversion (by Status)

Open Defects by Status	P1	P2 - Normal/Medium	3 - Normal/Low	4 - Cosmetic	Grand Total
Pending Rejection	0	1	0	0	1
Reopened	0	0	0	0	0
New	0	9	6	0	15
Assigned	0	21	17	4	42
In Assembly Test	0	5	5	0	10
In Development	0	11	12	1	24
Development Complete	0	1	4	1	6
System Test	0	0	1	0	1
Test Complete	0	2	4	0	6
In Production	0	0	0	0	0
Grand Total	0	50	49	6	105


Table 5.1.2-3 – Open Defects to be Resolved by Conversion (by Target Release)

Open Defects by Status	P1 High	P2 - Normal/Medium	P3 - Normal/Low	P4 - Cosmetic	Grand Total
Cutover 6A	0	0	0	0	0
Cutover 6B	0	4	6	0	10
Cutover 6B Go-live dependent (Post Append) DCRs	0	7	9	0	16
Cutover 6B Post Cutover (Days 1-10)	0	20	0	0	20
Cutover 6B Post Cutover (Post Days 1-10)	0	19	34	6	59
Grand Total	0	50	49	6	105

5.1.3 Gainwell Technologies

- CalWIN Document Migration
 - Additional documents identified based on County request approximately 8,357,116 documents will be converted to PDF and transferred to CalSAWS under PPM 65023 and CA-268083. Projects continued to meet and create burndowns for this effort

Figure 5.1.3-1 – Additional Documents CA-268083 and PPM65023

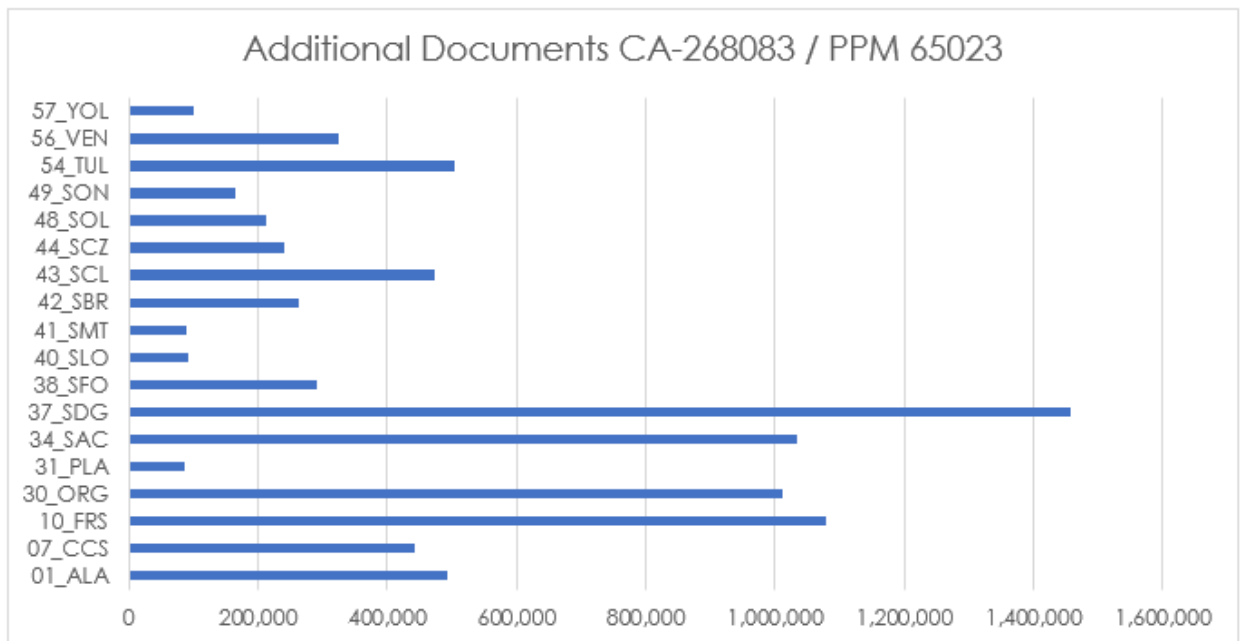

- Sacramento County NoHo
 - Delivered updated NoHo data for "Fit Test" October 1, 2023
- County Collections
 - Engaged with Sacramento County for planning

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

Table 5.1.3-1 – County Refactoring Overview

County	Migration Wave	Check-In Email Sent to County Y/N	CalSAWS Report Mapping Complete Y/N	PPM Proposal #	# of Reports to be Refactored	PPM Project #
Placer (PLA)	1	Y	Y	N/A	0	
Yolo (YOL)	1	Y	Y	N/A	46	63049
Contra Costa (CCS)	2	Y	N	63098	Day 1 – 21 Total -26	63580
Santa Clara (SCL)	2	Y	Y	63487	64	63497
Tulare (TUL)	2	Y	Y	N/A	0	
Orange (ORG)	3	Y	N	63688	Day 1 - 66	64076
Santa Barbara (SBR)	3	Y	Y	63730	Day 1 - 2 Total - 34	64224
Ventura (VEN)	3	Y	N	64186	0	64398
San Diego (SDG)	4	Y		63914	Day 1 – 43 Total - 151	64451
San Mateo (SMT)	4	Y	N	63099	Day 1 - 4 Total - 74	TBD
Santa Cruz (SCZ)	4	Y	N	64077	Day 1 - 1 Total - 33	TBD
Solano (SOL)	4	Y	N	63871	Day 1- 18 Total - 62	64413
Alameda (ALA)	5	Y	N	63568	Day 1- 33 Total - 84	64651
Fresno (FRS)	5	N	N	65059	Day 1 – 0 Total -13	N/A
Sonoma (SON)	5	N	N	64698	Day 1- 0 10	64783
Sacramento (SAC)	6	N	N	64731	Day 1 - 33 47	65003
San Francisco (SFO)	6	N	N	64187	Day 1- 12 Total - 39	64970
San Luis Obispo (SLO)	6	N	N	64283	Day 1 – 6 Total - 26	64971

Table 5.1.3-2 – Alameda County Refactoring Status

Alameda County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	2	0	0	0	0	0	2
Medium	3	0	0	0	0	2	1
Large	14	0	0	0	0	12	2
X-Large	10	0	0	0	0	9	1
XX-Large	4	0	0	0	0	4	0
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	33	0	0	0	0	27	6

Table 5.1.3-3 – San Francisco County Refactoring Status

San Francisco County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	0	0	0	0	0	0	0
Medium	0	0	0	0	0	0	0
Large	8	0	0	0	5	4	0
X-Large	4	0	0	0	2	1	0
XX-Large	0	0	0	0	0	0	0
XXX-Large	0	0	0	0	0	0	0
TBD	0	0	0	0	0	0	0
Total	12	0	0	0	7	5	0

Figure 5.1.3-2 – San Francisco (SFO) County Refactoring Status

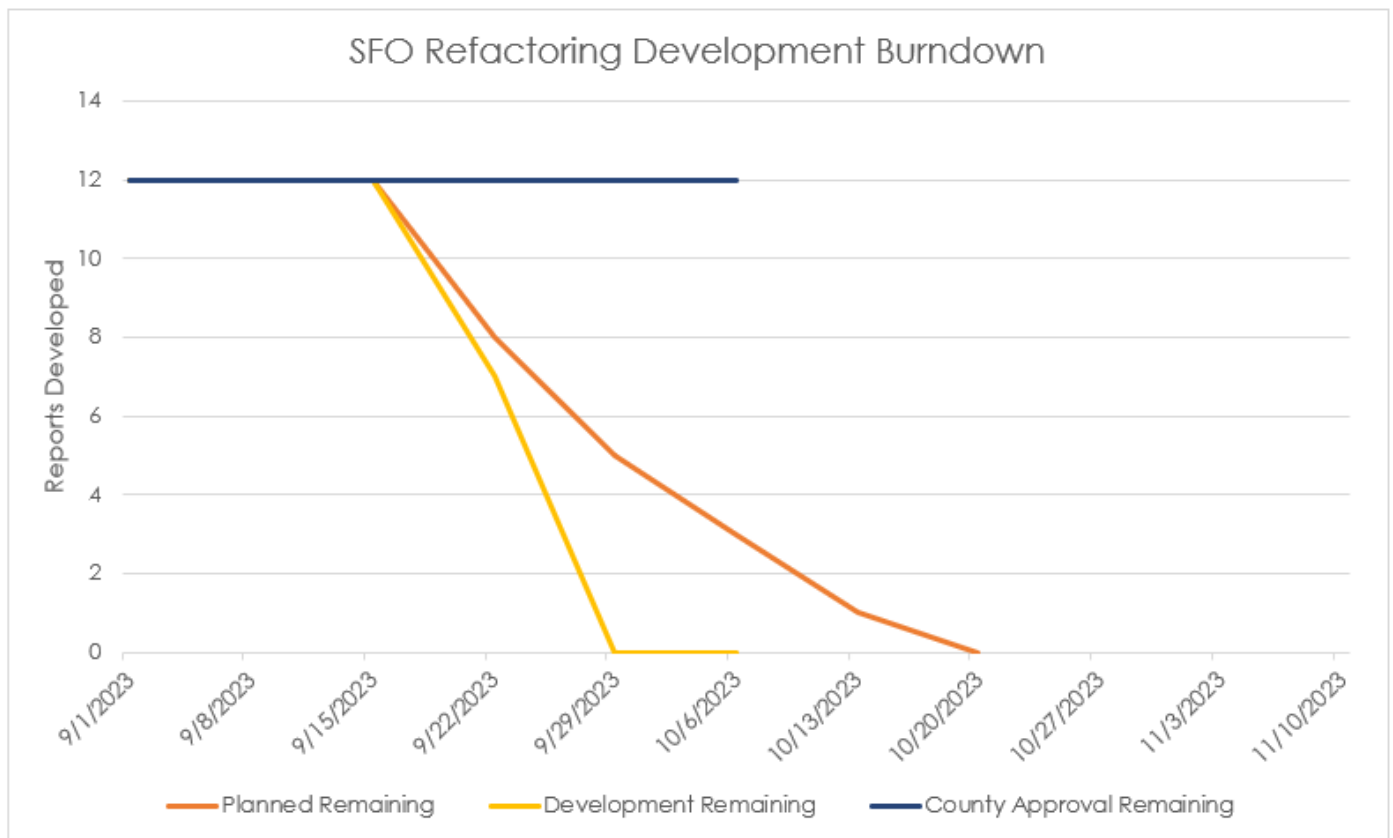


Table 5.1.3-5 – San Luis Obispo County Refactoring Status

San Luis Obispo County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	0	0	0	0	0	0	0
Medium	2	0	0	0	0	2	0

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

Large	2	0	0	0	0	2	0
X-Large	1	0	0	0	0	1	0
XX-Large	0	0	0	0	0	0	0
XXX-Large	1	0	0	1	0	0	0
TBD	0	0	0	0	0	0	0
Total	6	0	0	1	0	5	0

Figure 5.1.3-3 – San Luis Obispo (SLO) County Refactoring Status

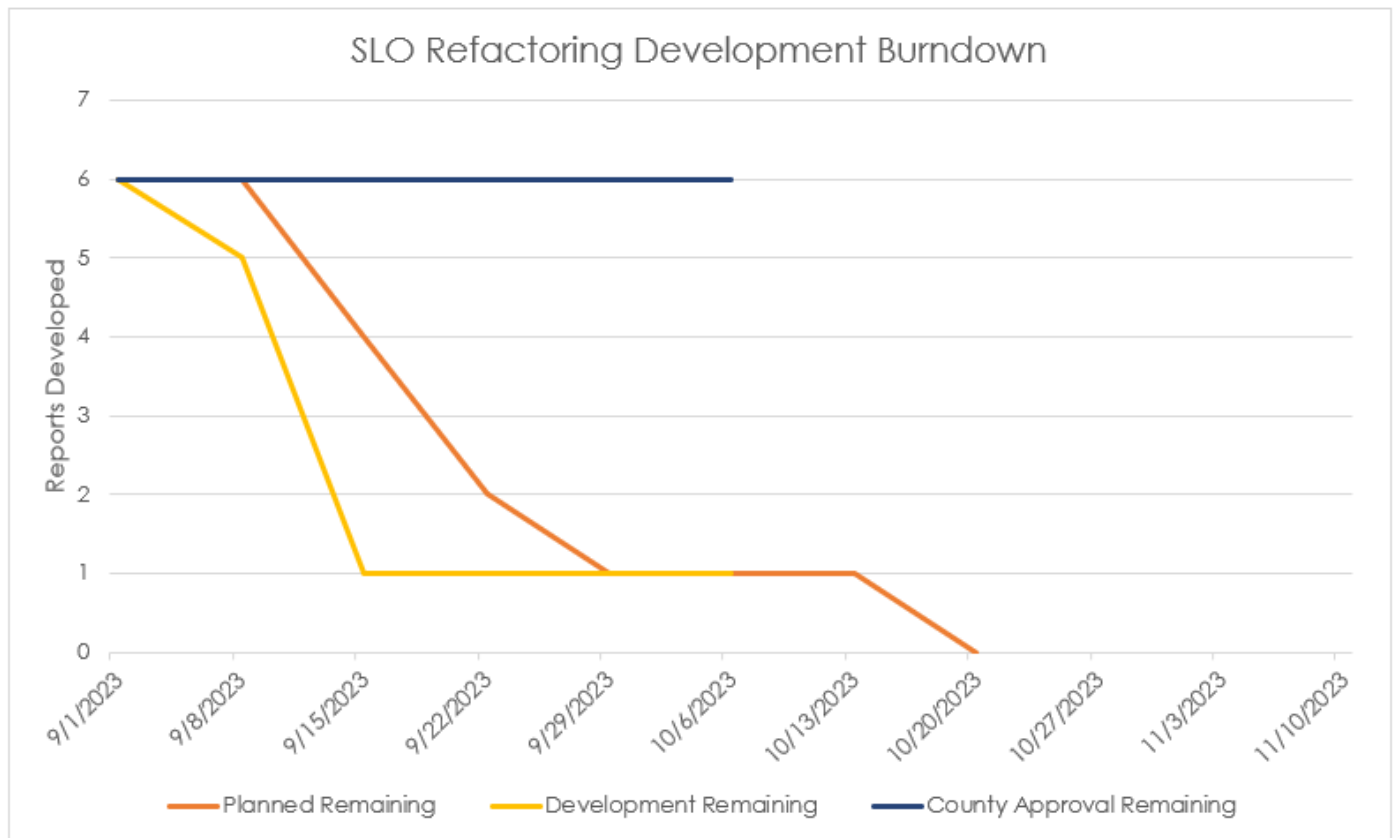


Table 5.1.3-6 – Sacramento County Refactoring Status

Sacramento County Refactoring Status							
	Number	Not Required	Not Started	Gainwell Development	Development Completed	County Validation	Completed
Small	0	0	0	0	0	0	0
Medium	5	0	0	2	0	3	0
Large	12	0	4	4	0	8	0
X-Large	12	0	0	7	0	1	0
XX-Large	2	0	0	2	0	0	0


CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

XXX-Large	2	0	0	1	0	1	0
TBD	0	0	0	0	0	0	0
Total	33	0	4	16	0	13	0

Figure 5.1.3-4 Sacramento (SAC) County Refactoring Status

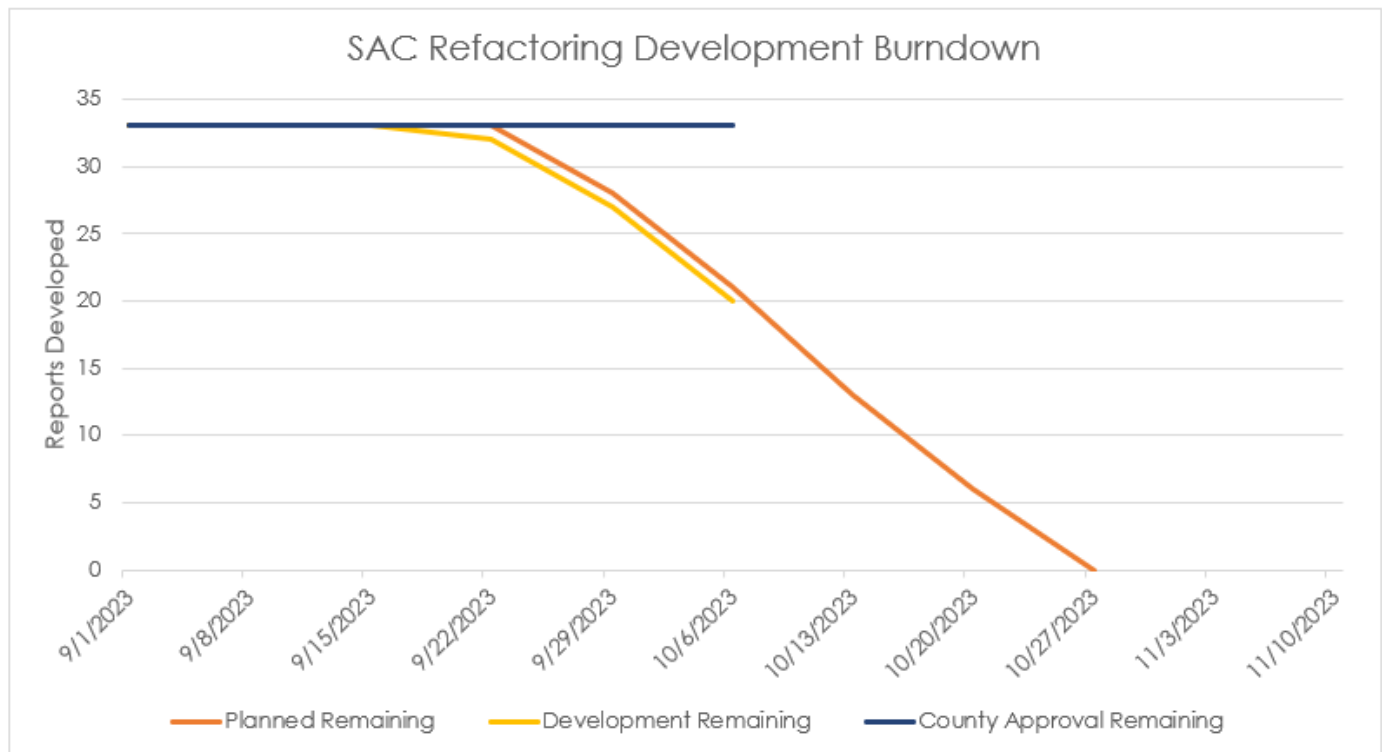

5.1.4 Ancillary Systems Conversion

- ▶ Facilitated exception reports review sessions with the Ancillary Counties to address questions and concerns
- ▶ Partnered with Wave 6 Counties to Address Data Extract issues found in County Data Validation (CDV) or Mock Cutover
- ▶ Executed Wave 6 6B fit test
- ▶ Generated Wave 6 Exception Report for September 27, 2023 Optional Data Delivery

Table 5.1.4-1 – Ancillary Systems Conversion Milestones

FINISH	MILESTONE	MILESTONE DESCRIPTION	STATUS
August 2023	Wave 6 Mock Conversion Data Validation	Validation of Data, (from Mock Conversion), are ready to begin (or are completed)	Completed

Table 5.1.4-2 – Ancillary Conversion Milestones

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

WAVE	MOCK B	MOCK C	CUTOVER B	CUTOVER C
Wave 5	June 17, 2023	July 29, 2023	August 31, 2023	September 16, 2023
	Completed	Completed	Completed	Completed
Wave 6	August 5, 2023	August 14, 2023	October 26, 2023	November 13, 2023
	Completed	Completed	Not started	Not started

Note: Ancillary Conversion only participates in B and C activities

5.1.5 CalWIN Migration Planning

- ▶ Began execution of the Wave 6B Internal Fitness Test activities
- ▶ Continued building the Wave 6B Master Cutover plan
- ▶ Continued building the Wave 6C Master Cutover plan

Table 5.1.5-1 – Cutover Migration Milestones

MOCK CUTOVER			
WAVE	CUTOVER A (Users and Offices)	CUTOVER B (Active Cases and Closed Case < 2 years)	CUTOVER C (Closed Cases > 2 years)
All Mock Cutovers have been completed			

Table 5.1.5-2 – Cutover Migration Milestones

WAVE	CUTOVER WINDOW	GO-LIVE
Wave 6B	October 26, 2023 - October 30, 2023	October 30, 2023
Wave 6C	November 11, 2023 - November 13, 2023	November 13, 2023

5.1.6 Deliverable Management

Table 5.1.6-1 – Conversion Deliverable Status for Current Reporting Period

DEL #	DELIVERABLE NAME	STATUS
87	CalSAWS Deployment Complete Milestone/Report - CalWIN Wave 5	<ul style="list-style-type: none">Continued developing the Draft Deliverable (DDEL)Submission of the DDEL is due on October 11, 2023

5.2 Activities for the Next Reporting Period

5.2.1 CalWIN Conversion

- ▶ Continue to triage, assess, and resolve CalWIN Wave 1, Wave 2, Wave 3, Wave 4, and Wave 5 Post Go-Live Issues

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

- ▶ Continue Wave 6 ETL/Data model updates
- ▶ Complete Wave 6B Fittest activities, and Begin 6C Fittest activities

5.2.2 CalWIN Migration Planning

- ▶ Complete execution of the 6B Fitness Test activities
- ▶ Continue building the Wave 6B Master Cutover Plan
- ▶ Continue building the Wave 6C Master Cutover Plan

5.2.3 Gainwell Technologies

- ▶ CalWIN Data Migration
 - Continue planning for future CalWIN extractions
- ▶ CalWIN Data Retention Maintenance & Operations (M&O)
 - Continue planning for future data retention runs

5.2.4 Ancillary Systems Conversion

- ▶ Review and address tickets for Cutover 3B, 3C, 4B, 4C, 5B, 5C
- ▶ Review Wave 6B fit test Exception Report Details

5.2.5 Deliverable Management

Table 5.2.5-1 – Conversion Deliverable Status for Next Reporting Period

DEL #	DELIVERABLE NAME	STATUS
87	CalSAWS Deployment Complete Milestone/Report – CalWIN Wave 5	<ul style="list-style-type: none">• Finalize and submit the Draft Deliverable (DDEL) to the Consortium for review and feedback on October 11, 2023• Comments for the DDEL are due on October 20, 2023
91	CalSAWS Deployment Complete Report – CalWIN Wave 1-6	<ul style="list-style-type: none">• Begin drafting the Draft Deliverable Expectation Document (DDED)• Submission of the DDED is due on November 2, 2023

5.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

6.0 CalWIN Functional Support

6.1 Highlights of the Reporting Period

Table 6.1-1 – CalSAWS CalWIN Functional Support Status Agenda Topic

STATUS REPORT SUB-SECTION	STATUS AGENDA TOPIC
---------------------------	---------------------

CalSAWS – California Statewide Automated Welfare System

CalSAWS DD&I Project Phase

Weekly Status Report Period: October 2, 2023, to October 8, 2023

- | | |
|--|--|
| | <ul style="list-style-type: none">• None to note for this reporting period |
|--|--|

- ▶ Provided CalWIN Functional Support coordination during October 2 - 6, 2023 by:
 - Supported Implementation Support Services (ISS) Team Lead Meeting on October 3, 2023
 - Supported CalSAWS Weekly Status Meeting on October 4, 2023, to highlight key workstream reporting items
- ▶ Wave 5 Post Implementation Support during October 2 - 6, 2023 by:
 - Provided virtual and extended post implementation support
 - Supported Project Production and County Operations daily calls. Maintained Issues tracker and reported on status of open issues.
 - Provided daily business metrics
- ▶ Wave 6 County Preparation during October 2 - 6, 2023 by:
 - Supported Wave 6 County Preparation Office Hours and Daily Debrief calls

6.2 Activities for the Next Reporting Period

- ▶ Continue CalWIN Functional Support coordination during October 9 - 13, 2023 by:
 - Prepare for Implementation Support Services (ISS) Team Lead Meeting on October 10, 2023
 - Prepare for CalSAWS Weekly Status Meeting on October 11, 2023, to highlight key workstream reporting items
- ▶ Wave 5 Post Implementation Support during October 9 - 13, 2023 by:
 - Provide virtual and extended post implementation support
 - Support Project Production and County Operations daily calls. Maintain Issues tracker and report on status of open issues.
 - Provide daily business metrics
- ▶ Wave 6 County Preparation and Implementation during October 9 - 13, 2023 by:
 - Support Wave 6 County Preparation Office Hours and Daily Debrief calls
 - Facilitate Open Defects Strike Meeting to review open defects for possible inclusion in the Go Live Packet update

6.3 Deviations from Plan/Adjustments

- ▶ None for the reporting period

7.0 Appendices

Appendix A – CalSAWS Deliverable Summary

Appendix B – CalSAWS Migration Work Plan Summary

Appendix C – CalSAWS DD&I Project Gantt Chart

Appendix D – CalSAWS Project Risks and Issues Report

Appendix E – CalSAWS Imaging Document Migration

