

CalSAWS BenefitsCal (Portal/Mobile) Weekly Status Report

**Reporting Period: October 1, 2023 to
October 8, 2023**

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

Table of Contents

1.0	Project Management	4
1.1	Executive Summary	4
1.2	PMO	5
1.2.1	Highlights of the Reporting Period	5
1.2.2	Activities for the Next Reporting Period	5
1.3	BenefitsCal Collaboration Model (CM)	6
1.3.1	Highlights of the Reporting Period	6
1.3.2	Activities for the Next Reporting Period	7
2.0	Application Development and Test	8
2.1	Requirements and Design	8
2.1.1	Highlights of the Reporting Period – Requirements and Design	8
2.1.2	Activities for the Next Reporting Period – Requirements and Design	8
2.1.3	Highlights of the Reporting Period – User Centered Design (UCD)	9
2.1.4	Activities for the Next Reporting Period – UCD – during the week of 09/10/23	10
2.2	Development	11
2.2.1	Highlights of the Reporting Period – Development	11
2.2.2	Activities for the Next Reporting Period – Development	11
2.3	System Test Execution	12
2.3.1	Highlights of the Reporting Period – System Test Execution	12
2.4	Activities for the Next Reporting Period – System Test Execution	12
2.5	User Acceptance Test (UAT) Planning	13
2.5.1	Highlights of the Reporting Period – User Acceptance Test Planning	13
2.5.2	Activities for the Next Reporting Period – User Acceptance Test Planning	13
3.0	Performance Test	13
3.1	Highlights of the Reporting Period – Performance Test	13

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

4.0	Security	14
4.1	User Conversion	14
4.1.1	Highlights of the Reporting Period – User Conversion Testing	14
4.1.2	Activities for the Next Reporting Period – User Conversion Testing	14
4.2	Security	14
4.2.1	Highlights of the Reporting Period – Security	14
4.2.2	Activities for the Next Reporting Period – Security	14
5.0	Communications and Training	15
5.1	Highlights of the Reporting Period	15
5.2	Activities for the Next Reporting Period	15
6.0	Appendices	15
6.1	Appendix A – Deliverable Summary	15
6.2	Appendix B – Risks and Issues Summary	17
6.3	CRFI/CIT/CalSAWS CR Communications Information	22
6.4	Appendix C – Project Work Plan Reports	23

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

1.0 Project Management

1.1 Executive Summary

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
October Enhancements	<ul style="list-style-type: none"> ➤ Nine (9) enhancements will be delivered with the October Release 23.10.19: <ul style="list-style-type: none"> ○ One (1) Collaboration Enhancement ○ One (1) Partner Support Enhancement ○ Two (2) Production Priority Enhancements ○ Two (2) Policy Enhancement ○ Three (3) Technical Enhancements
CalWIN Implementation Support Services (ISS) Support	<p>Wave 5</p> <ul style="list-style-type: none"> ➤ Maintenance & Operations (M&O) service management is in progress. ➤ Health Metrics generation is in progress. <p>Wave 6</p> <ul style="list-style-type: none"> ➤ Email-2 campaign preparation is in progress. ➤ Production cutover checklist is reviewed and approved by the Consortium. ➤ The Community Based Organization (CBO) user conversion mock-run is complete, and the exception report has been generated. No exceptions were identified. ➤ Production data extract for the CBOs is complete. County review is in progress.
User Centered Design (UCD) Activities	<p>Customer Experience (CX) Measurements Data</p> <ul style="list-style-type: none"> ➤ Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues. ➤ Continued working on the upcoming Quarterly Report due in October. <p>User Engagement</p> <ul style="list-style-type: none"> ➤ Prepped for Authorized Representative research (CSPM-67150) ➤ Recruited County Staff members, CBO assistants and BenefitsCal customers. <p>Enhancements</p> <ul style="list-style-type: none"> ➤ Planned and recruited for Authorized Representative research (CSPM-67150). ➤ Began design development on next phase of Chatbot Expansion (CSPM-66583).

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
	<p>Advocate Engagement</p> <ul style="list-style-type: none"> ➤ Finalized draft for the next UCD Monthly Meeting (Chatbot expansion and Time Clocks).
GetCalFresh (GCF) Parity List	<ul style="list-style-type: none"> ➤ Participated in sessions facilitated by the California Department of Social Services (CDSS) on 09/19/23, with participation from the County Welfare Directors Association of California (CWDA), the Consortium and BenefitsCal for parity list. ➤ BenefitsCal responses for parity list SCERFRA 23-500 for tracking IDs 9, 19, 20, 31, and 63 were provided to the CDSS on 09/22/23. ➤ Another working session is facilitated on 10/04/23 with participation from the CWDA, the Consortium, BenefitsCal, and CalSAWS. One (1) item is resolved, and eight (8) items are remaining where the CDSS and CFA are to provide confirmation to finalize.
Collaboration Model	<ul style="list-style-type: none"> ➤ Next Collaboration Model meeting is scheduled for 12/01/23. ➤ The following CM Enhancements/Research activities will be performed in the month of October: <ul style="list-style-type: none"> ○ CSPM-43163: Collaboration Model: Restrict the user to create multiple Redeterminations and Periodic reports associated with particular case number (Part 2). ○ CSPM-67150: Identify user journeys and research Authorized representative user type in BenefitsCal. ○ CSPM-67600: Update location of where YouTube Videos are located.

Table 1.1-1 – CalSAWS Executive Summary Agenda Topics

1.2 PMO

1.2.1 Highlights of the Reporting Period

- **Deliverables and Work Products submitted:**
 - FWP 26.06: BOM Review and License Renewals on 10/06/23.
 - FWP 27.06: Certificate Review on 10/06/23.
 - FWP 28.18: BenefitsCal Work Plan Monthly Updates – September 2023 on 10/06/23.
 - FWP 29.18: BenefitsCal Monthly Status Report – September 2023 on 10/06/23.

1.2.2 Activities for the Next Reporting Period

- **Deliverable and Work Product submissions for next reporting period:**
 - DWP 24.20: CX Report – Aug/Sept 2023 on 10/10/23.
 - DWP 25.20: Monthly M&O Report – September 2023 on 10/10/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

1.3 BenefitsCal Collaboration Model (CM)

1.3.1 Highlights of the Reporting Period

- Continued to prepare a roadmap for the CM model prioritized items.
- Analyzed the Quarter 2 Prioritization Results for the seven (7) enhancements prioritized in the last CM survey which closed on 07/05/23.
- Logged Research Items/SCRs (Enhancements) based on the above analysis and prioritized them for upcoming months.
- Identified Collaboration Model priorities as enhancements versus action items to perform additional research.

The table below contains the enhancements prioritized by Collaboration Model and their updates from this week:

ID	Summary	Status	Update this Week
CSPM-64323 (Action Item)	Research for CM Enhancement: Public dashboard of BenefitsCal data	In Progress	Research is in progress.
CSPM-43163 (Enhancement)	Restrict the user to create multiple Redeterminations and Periodic reports associated with a particular case number	Development In Progress	Finalized Design & continued with Development
CSPM-67119 (Enhancement)	Collaboration Model: Document Upload for Users with No Account	Design Update Needed	Awaiting CalSAWS confirmation on revised timeline for implementation of a new API endpoint to validate DOB entered by the customer with household members in CalSAWS. Received API Swagger from CalSAWS.
CSPM-67105 (Research Item)	Research for CM Enhancement: Doc Upload Type Assistance	Closed	Performed generative research synthesis and logged the enhancement CSPM-67785 as on outcome of the research. Closed the research item after reviewing the logged enhancement.
CSPM-67149 (Research Item)	Research for CM Enhancement: Application Status Tracker	Closed	Performed generative research synthesis and logged the enhancement CSPM-67761 as on outcome of the research. Closed the research item after reviewing the logged enhancement.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Summary	Status	Update this Week
CSPM-67150 (Research Item)	Research for CM Enhancement: Authorized Representative	In Progress	Started working on the script for generative research.
CSPM-67104 (Research Item)	Research for CM Enhancement: Leverage Email Communications and Interactions	Not Started	Research Item logged from CM Q2 meeting in held in June 2023.
CSPM-67600 (Research Item)	Research for CM Enhancement: Link to YouTube Videos on the dashboard and banner	Not Started	Research Item logged from CM Q2 meeting in held in June 2023.
CSPM-67189 (Enhancement)	Research for CM Enhancement: Display Primary Applicant Status on a Case	Not Started	Generative Research planned in November 2023.

Table 1.3-1 – Enhancements Updates, Prioritized by CM

1.3.2 Activities for the Next Reporting Period

- Perform design, development, and implementation analysis for enhancements and research action items identified in the Collaboration Model.

The table below contains all enhancements prioritized by CM (not yet delivered to production) and planned activities for the next week.

ID	Summary	Activity for Next Week	Target Delivery Date
CSPM-64323 (Action Item)	Research for CM Enhancement: Public dashboard of BenefitsCal data	Continue Research	October 2023
CSPM-43163 (Enhancement)	Restrict the user to create multiple Redeterminations and Periodic reports associated with a particular case number	Continue Development	October 2023
CSPM-67119 (Enhancement)	Collaboration Model: Document Upload for Users with No Account	Coordinate with CalSAWS to finalize the revised timeline	November 2023 (TBD)
CSPM-67105 (Research Item)	Research for CM Enhancement: Doc Upload Type Assistance	Prioritize the associated SCR/enhancement.	September 2023
CSPM-67149 (Research Item)	Research for CM Enhancement: Application Status Tracker	Prioritize the associated SCR/enhancement.	September 2023
CSPM-67150 (Research Item)	Research for CM Enhancement: Authorized Representative	Continue with script finalization and user recruitment for generative research	October 2023
CSPM-67104 (Research Item)	Research for CM Enhancement: Leverage Email Communications and Interactions	Create Research plan	November 2023
CSPM-67600 (Research Item)	Research for CM Enhancement: Link to YouTube Videos on the dashboard and banner	N/A	October 2023

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Summary	Activity for Next Week	Target Delivery Date
CSPM-67189 (Enhancement)	Research for CM Enhancement: Display Primary Applicant Status on a Case	N/A	November 2023

Table 1.3-2 – Planned Activities for Next Reporting Period for Enhancements, Prioritized by CM

2.0 Application Development and Test

2.1 Requirements and Design

2.1.1 Highlights of the Reporting Period – Requirements and Design

➤ Designs and Design Meetings

- Continued working with development and testing teams for the October 2023.
- Started design work for the November 2023 enhancements.
- Continued working with the development and testing teams for Release 23.11.19 CalWORKs Time Clocks.
- Continued working with development and testing teams for SSA Application on BenefitsCal enhancement CSPM-65292.
- Attended ROI Work Group Meeting Hosted by Consortium on 10/02/23.
- Cohosted the GCF Parity Planning Meeting with CalSAWS on 10/02/23.
- Cohosted Termination Reasons Meeting with CalSAWS on 10/02/23.
- Attended SSP Committee presenting BenefitsCal features on 10/03/23.
- Attended App Dev Meeting Hosted by Consortium 10/03/23.
- Co-host SCERFRA Touchpoint with CalSAWS to discuss weekly SCERFRA updates on 10/4/23.
- Hosted GCF Parity Prep Call on 10/04/23.
- Hosted CWDA Weekly Discussion meeting on 10/04/23.
- Attend GCF Parity List Discussion Meeting hosted by CDSS CF on 10/4/23.
- Hosted ABAWD Phase 1 Kickoff Discussion on 10/05/23.
- Attended App Transfer Design Updates Meeting Hosted by CalSAWS on 10/05/23.

2.1.2 Activities for the Next Reporting Period – Requirements and Design

➤ Designs and Design Meetings

- Continue working with development and testing teams for the October 2023.
- Start design work for the November 2023 enhancements.
- Continue working with the development and testing teams for Release 23.11.19 CalWORKs Time Clocks.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

- Continue working with development and testing teams for SSA Application on BenefitsCal enhancement CSPM-65292.
- Host GCF Parity Release Planning Meeting on 10/09/23.
- Attend App Dev Meeting Hosted by the Consortium on 10/10/23.
- Attend Coronavirus Food Assistance Program (CFAP) Expansion Meeting hosted by the CDSS on 10/10/23.
- Attend Termination Reasons Discussion hosted by CalSAWS on 10/10/23.
- Attend SCERFRA Discussion with CalSAWS on 10/11/23.
- Host BenefitsCal Enhancement Pipeline Discussion on 10/13/23.

2.1.3 Highlights of the Reporting Period – User Centered Design (UCD)

➤ Customer Experience (CX) Measurements Data

- Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
- Collaborated with the M&O team to prepare for the upcoming Quarterly Report due in October.
- Pulled monthly data metrics for the month of September.
- Updated the reporting template based on guidelines for better visualization of data and content.
- Resumed the creation of a detailed bi-monthly data analysis sheet with process documentation and hard coded formulas for chart generation.

➤ User Engagement

- Finalized interview protocols for upcoming research activities for Authorized Representative. Research activities to involve County Staff members, CBO assistors and BenefitsCal customers.
- Sent out over 50 emails to customers from the list of Medallia volunteers.
- Recruited County Staff and CBO assistors for upcoming focus groups.
- Planned and scheduled Integrated Eligibility SME interview for Authorized rep research activity.

➤ Enhancements

- Planned and scheduled for Authorized Representative.
- Began design development on Chatbot Expansion (CSPM-66583).

➤ Advocate Engagement

- Responded to stakeholder comments on Anonymous Document Upload.
- Finished draft for the next UCD Monthly Meeting (Chatbot expansion and Time Clocks).

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

2.1.4 Activities for the Next Reporting Period – UCD – during the week of 09/10/23.

➤ **CX Measurements Data**

- Monitor the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
- Collaborate with the M&O team to prepare for the upcoming Quarterly Report due in October.
- Update the reporting template based on guidelines for better visualization of data and content.
- Resume the creation of a detailed bi-monthly data analysis sheet with process documentation and hard coded formulas for chart generation.

➤ **User Engagement**

- Facilitate two (2) County Staff focus groups for Authorized Representative.
- Facilitate one (1) CBO focus group for Authorized Representative.
- Facilitate five (5) to seven (7) Customer interviews for Authorized Representative.
- Facilitate one (1) subject matter expert (SME) interview for Authorized Representative.

➤ **Enhancements**

- Finalize designs for the Chatbot Expansion enhancement (CSPM-66583).
- Continue Generative Research on Authorized Representative.

➤ **Advocate Engagement**

- Finalize the presentation materials for the next UCD Monthly Meeting (Chatbot expansion and Time Clocks).

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

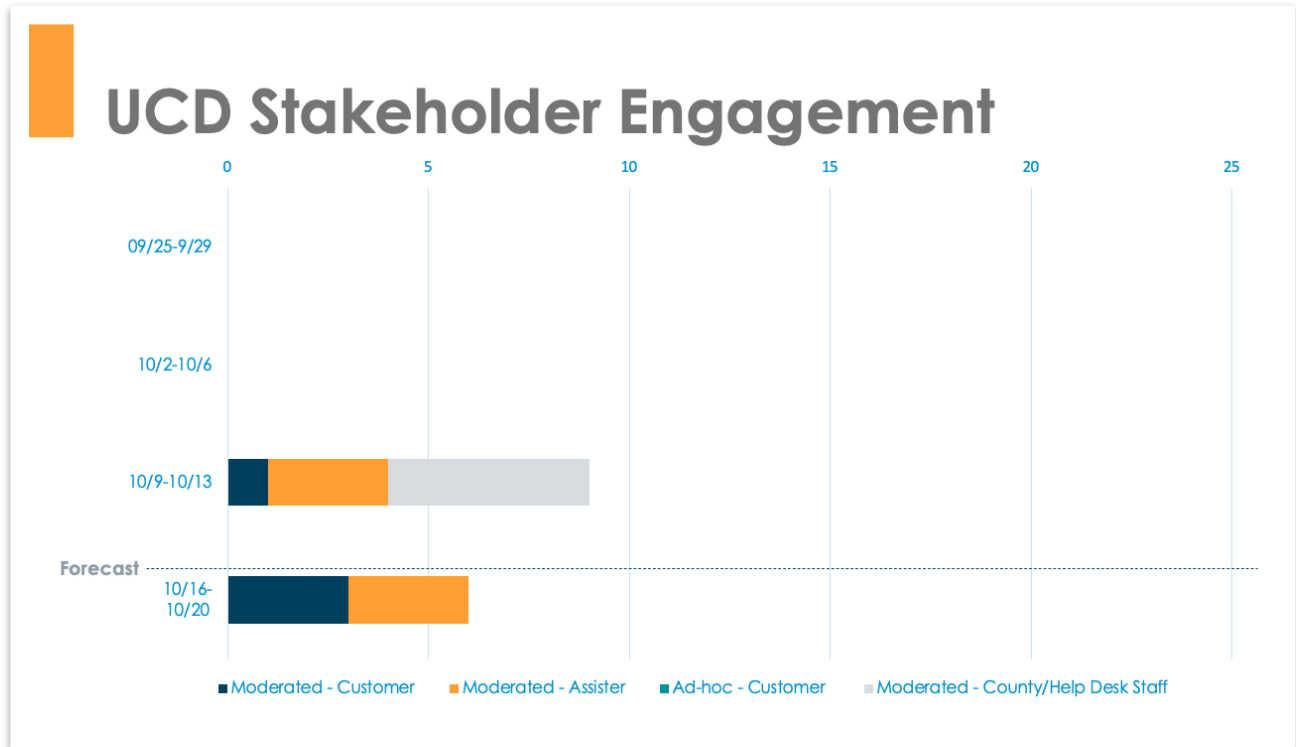


Figure 2.1-1 – UCD Stakeholder Engagement

2.2 Development

2.2.1 Highlights of the Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 10/06/23	Actual for Week Ending 10/06/23	Total Planned for the Release	Comments
23.10.19	3	3	9	
23.10.30	1	1	1	CalWIN Wave 6 release planned for 10/30/23.

Table 2.2-1 – Enhancement Actuals for Reporting Period

2.2.2 Activities for the Next Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 10/13/23	Total Planned for the Release	Total Completed for the Release	Comments
23.10.19	5	9	4	

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

Release	Planned for Week Ending 10/13/23	Total Planned for the Release	Total Completed for the Release	Comments
23.10.30	1	1	1	CalWIN Wave 6 release planned for 10/30/23.

Table 2.2-2 – Planned Enhancement Work

Unscheduled Release Updates

➤ Chatbot

- For the 25 issues that we have reported earlier related to Currency Slot and Custom Slot for Chinese, Japanese, and Korean languages, the Amazon Web Services (AWS) team is updating the Language model at their end and the provided an ETA for those fixes was June 2023 – awaiting response from AWS team. After the confirmation from AWS, the BenefitsCal Team will decide on next steps.
- The Amazon Web Services (AWS) team stated they have rolled out the fix for the mute detection issue in the Spanish, Korean, and Japanese languages, but during validation, we found the issue was still reproduceable in the Spanish and Korean languages. The AWS team is yet to provide an ETA for the resolution and fix. This is being tracked by CSPM-56537 – awaiting response from the AWS team. After confirmation from AWS, the BenefitsCal Team will define the next steps.
- Support for additional languages Korean, Japanese and Chinese is still not released by AWS. The next update is expected by January 2024.
- New intents of Chatbot tracked through CSPM-65313 were deployed to production as part of Release 23.09.28. These were unrelated to CSPM-56537.

➤ Time Clock

- Go-Live for the Time Clock enhancements to be finalized in the coming weeks.

2.3 System Test Execution

2.3.1 Highlights of the Reporting Period – System Test Execution

➤ Release 23.10.19 – October Monthly Release

- The first build into UAT was deployed on 10/02/23. Co-ordinated with the partners for E2E tickets. Continued validating all other tagged tickets to October.

2.4 Activities for the Next Reporting Period – System Test Execution

➤ Release 23.10.19 – October Monthly Release

- Validate tickets deployed to SIT for this release. Coordinate with the partners for any E2E tickets.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

2.5 User Acceptance Test (UAT) Planning

2.5.1 Highlights of the Reporting Period – User Acceptance Test Planning

- **UAT Test Execution**
 - None for the period.

2.5.2 Activities for the Next Reporting Period – User Acceptance Test Planning

- **Test Support**
 - None for the period.

3.0 Performance Test

3.1 Highlights of the Reporting Period – Performance Test

- **Release 23.10.19– October Monthly Release**
 - The BenefitsCal team started the rescripting activities for the October release enhancements. One (1) enhancement related to the Node.js runtime update requires CalSAWS environment for end-to-end performance testing and BenefitsCal team reached out to partners with release details to share the environment availability. Based on the latest code migration, planned next week, the team will plan and execute two (2) rounds of isolated performance tests. The team planned a 1st test with the Mock services and second test is planned with the CalSAWS environment.

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
13	08/21/23	09/20/23	Release 23.09.24 – September Baseline Release	Scope: Four (4) BenefitsCal enhancements for September release requires updates to existing six (6) Document upload scripts and develop a new Redet TNB4 script. Executions: BenefitsCal isolated performance tests leveraging Partners Perf infra. Tuesday, 09/12/23 Wednesday, 09/20/23	100%
13	09/25/23	10/13/23	Release 23.10.19 – October Monthly Release	Scope: Three (3) BenefitsCal enhancements for October release requires 1 new inbound API script development and potentially minor updates to existing scripts. Executions: BenefitsCal isolated performance tests plan: Wednesday, 10/11/23 Friday, 10/13/23	40%

Table 3.1-1 – Performance Test Cycles and Test Case Status

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

4.0 Security

4.1 User Conversion

4.1.1 Highlights of the Reporting Period – User Conversion Testing

➤ **CalWIN Conversion**

- Received the Wave 6 CBO User extract from the Gainwell team. This extract will be used to create the Wave 6 CBO User listing for the Wave 6 Counties to validate prior to the load.

4.1.2 Activities for the Next Reporting Period – User Conversion Testing

➤ **Perform CBO User Data Validation**

- Hand off the Wave 6 CBO user listing to the Wave 6 Counties to validate.

4.2 Security

4.2.1 Highlights of the Reporting Period – Security

➤ **SAST**

- Executed the weekly Static Application Security Testing (SAST) of the application source code and shared the analysis of the security scan reports with the BenefitsCal Development Team for remediation on 10/06/23.

4.2.2 Activities for the Next Reporting Period – Security

➤ **Identified Vulnerabilities**

- After the validation of the identified vulnerabilities, advise on the remediation activities to be performed by the BenefitsCal Development Team. Log defects in Jira for tracking purposes (weekly recurring activity).

➤ **AWS SSO for BenefitsCal**

- Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

5.0 Communications and Training

5.1 Highlights of the Reporting Period

- No activities for the reporting period.

5.2 Activities for the Next Reporting Period

- Send email 2 to the Wave 6 customers on 10/12/23.
- Send SMS 1 communications to the Wave 6 customers on 10/13/23.
- No training activities planned for the next reporting period.

6.0 Appendices

6.1 Appendix A – Deliverable Summary

Deliverable Status by Submission

							Complete	Coming Soon	WAC Approval Pending
DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final Approval			
None for the reporting period.									

Table 6.1-1 – Deliverable Status for Current Reporting Period

Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
None for the reporting period.			

Table 6.1-2 – Upcoming Deliverable Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

Work Product Status by Submission

		Complete	Coming Soon	WAC Approval Pending
ID	Work Product Name	DWP	FWP	Final Approval
24.18	CX Report – April/May 2023	06/09/23	06/21/23	06/28/23
24.19	CX Report – June/July 2023	08/11/23	08/24/23	08/30/23
24.20	CX Report – August/September 2023	10/09/23	10/19/23	10/26/23
25.20	Monthly M&O Report – September 2023	10/09/23	10/19/23	10/26/23
26.07	BOM Review and License Renewals	N/A	10/05/23	10/18/23
27.07	Certificate Review	N/A	10/05/23	10/18/23
28.18	BenefitsCal Work Plan Monthly Updates – September 2023	N/A	10/06/23	10/16/23
29.17	BenefitsCal Monthly Status Report – August 2023	N/A	09/08/23	09/19/23
29.18	BenefitsCal Monthly Status Report – September 2023	N/A	10/06/23	10/16/23

Table 6.1-3 – Upcoming Work Product Deadlines

Upcoming Work Product Deadlines

WP #	Work Product Name	Status	Next Deadline
26.06	BOM Review and License Renewals	On Track	FWP submitted 10/06/23 FWP approval 10/17/23
26.06	Certificate Review	On Track	FWP submitted 10/06/23 FWP approval 10/17/23
28.18	BenefitsCal Work Plan Monthly Updates – September 2023	On Track	FWP submitted 10/06/23 FWP approval 10/17/23
29.18	BenefitsCal Monthly Status Report – September 2023	On Track	FWP submitted 10/06/23 FWP approval 10/17/23

Table 6.1-4 – Upcoming Work Product Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

6.2 Appendix B – Risks and Issues Summary

Project Risks and Issues

ID	Title	Details	Status	Risk Level	Severity	Date Logged
246	Perceived Gap in Functionality	<p>A perceived gap in functionality between GetCalFresh and BenefitsCal was identified. Select features identified within GetCalFresh are not present within BenefitsCal as they are not part of the project requirements, and change requests were logged to address. Impacts BenefitsCal adoption by Community Partners may be lower as they rely on features (like the referral code) to complete their work. The future migration from GCF to BenefitsCal in 2022 is at risk until features are added to BenefitsCal.</p> <p>Status Updates:</p> <p>September 2, 2022:</p> <ul style="list-style-type: none"> Had multiple meetings with CDSS to discuss the GetCalFresh Gap List with Consortium and CWDA, latest on 08/29/22. There is a bi-weekly meeting cadence. Currently there are few enhancement suggestions from CDSS on partial gaps. Teams are going to continue having working sessions to decide any of these must have or nice to have <p>September 30, 2022:</p> <ul style="list-style-type: none"> Continued working sessions with CDSS, CWDA, Consortium and CalSAWS. With the CDSS's analysis, there is total of 41 gaps. 32 are logged as enhancements for prioritization and the remaining 9 will be discussed at upcoming working sessions. There is also a plan to identify/classify must have vs nice to have items. Next working session is scheduled for 10/05/22. <p>January 6, 2023:</p> <ul style="list-style-type: none"> BenefitsCal team has started working on the effort estimations for the gaps list (31 gaps/52 enhancements). Targeting to complete the estimations by 01/16 and propose prioritization. CDSS, CWDA and Consortium will 	Open	Low	Medium	05/10/21

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>provide direction on the implementation schedule.</p> <p>January 11, 2023:</p> <ul style="list-style-type: none"> • Prioritization is requested by end of month so it can be incorporated into the roadmap <p>February 2, 2023:</p> <ul style="list-style-type: none"> • Provided responses to CDSS SCERFRA with estimates for GCF parity list items. CDSS to confirm the SCERFRA approval and prioritization to establish a roadmap for implementation. <p>February 3, 2023:</p> <ul style="list-style-type: none"> • Attended meeting with CDSS, CalSAWS, and CWDA for the GCF Parity List on 02/02/23. Provided responses to CDSS SCERFRA with estimates for GCF parity list items. <p>March 3, 2023:</p> <ul style="list-style-type: none"> • RMG: Attended meeting with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/01/23. CDSS to confirm the SCERFRA approval and prioritization to establish a roadmap for implementation <p>April 7, 2023</p> <ul style="list-style-type: none"> • Attended meetings with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/22/23 and 04/05/23. CDSS shared decommissioning timeline got GCF components/CDSS will map the components planned for decommissioning to parity list items to confirm the SCERFRA approval, funding source and prioritization to establish a roadmap for implementation <p>April 28, 2023:</p> <ul style="list-style-type: none"> • Attended meetings with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/22/23 and 04/19/23. CDSS is currently mapping the components planned for decommissioning to parity list items and will confirm the SCERFRA approval for SCERFRA 23-512, CDSS is also confirming the funding source to establish a 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>roadmap for implementation. Next meeting is scheduled on 05/03/23</p> <p>June 2, 2023:</p> <ul style="list-style-type: none"> Participated in the bi-weekly meetings on 05/03/23 and 05/17/23. Worked with the California Welfare Directors Association (CWDA) and the Consortium and provided line-item level analysis for a Legislative request on 05/19/23. Next bi-weekly meeting is scheduled for 06/07/23. The California Department of Social Services (CDSS) continued mapping the components planned for decommissioning to the parity list items. <p>June 9, 2023:</p> <ul style="list-style-type: none"> BenefitsCal and CalSAWS teams connected with ODI on Friday 06/09/23. Next steps identified for ODI to provide the raw data from GCF to begin the analysis. <p>June 30, 2023:</p> <ul style="list-style-type: none"> Bi-weekly meeting conducted with CDSS, CWDA, Consortium and CalSAWS on 06/21/23. CDSS to provide final list of excel extract of items based on legislative response. Also, teams continued to work with ODI team on the analysis and data needs/questions. <p>July 28, 2023:</p> <ul style="list-style-type: none"> A working session is scheduled for 08/02/23 to talk about SCERFRA 23-500, SCERFRA 23-512 (SSA flow) and CF 303 – Benefit Replacement with CDSS, CWDA, Consortium and CalSAWS. <p>September 1, 2023:</p> <ul style="list-style-type: none"> Multiple working sessions have been facilitated by CDSS with participation by CWDA, Consortium, BenefitsCal, and CalSAWS. Since August 02, 2023, Out of 26 items, 4 items have been closed, 4 items are in-plan. 9 items are awaiting confirmation/response by CDSS and another 9 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>are scheduled to be discussed with CDSS during the next working session on September 06, 2023. In plan items include the SSA Application flow in BenefitsCal, design activities for SCERFRA 23-512 (SSA flow) is on track to be completed by 09/08/23.</p> <p>September 8, 2023:</p> <ul style="list-style-type: none"> Working session facilitated by CDSS with participation by CWDA, Consortium, BenefitsCal and CalSAWS on 09/06/23. CDSS is going to provide offline response for the remaining items. Next working session is schedule on 10/04/23. Also working with ODI on recommender widget analysis. Next meeting is on 09/12/23. 				
290	Recently released ROI policy lacks clarity which may create privacy and liability exposure for counties and customers	<p>Recently issued Release of Information (ROI) policy is not detailed enough, nor is it consistent between the two state Departments (CDSS and DHCS). The policy as written may create customer information privacy/security, safeguard and county operations concerns, and liabilities. As the policy was released after the completion of ROI design, development, and testing of the functionality in BenefitsCal and CalSAWS, counties have not had sufficient time to assess the ROI functionality with the high-level policy and to be able to determine impacts to their county operations and the associated alignment with the existing BenefitsCal/CalSAWS design. The policy as written does not give clear direction on County responsibilities associated with the establishment of CBO agreements, provisions of those agreements and monitoring of CBO compliance with the agreements. Counties also have not had sufficient time to be able to determine if their current CBO agreement language is adequate and includes provisions and protections to further protect customer information when being accessed by CBOs via BenefitsCal. BenefitsCal/CalSAWS initial design and implementation has been postponed until final/revised policy is issued by both</p>	Open	Medium	High	05/19/23

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>CDSS and DHCS and there is operational clarity agreed to by all parties.</p> <p>June 16, 2023:</p> <ul style="list-style-type: none"> Responded to SIRFRA 1270/1271 regarding Expanding the Release of Information Feature with set of questions to DHCS from BenefitsCal, CalSAWS, and CWDA on 06/12/23. <p>June 30, 2023:</p> <ul style="list-style-type: none"> Risk was reduced to probability of 30% which brings it to an overall medium level. State partners to confirm the topics and agenda items for the workgroup discussions. Topic was also covered during the June JPA Board meeting on 6/29/23. <p>July 28, 2023:</p> <ul style="list-style-type: none"> Workgroup member names are being collected including representatives from CDSS, DHCS, OSI, CWDA, Counties, Advocates and CalSAWS. Draft topics are also being reviewed, Preliminary categories including, Policy Guidance Considerations/ Questions, Processes, System Functionality/Automation. Meeting Schedule and cadence is in progress. <p>September 1, 2023:</p> <ul style="list-style-type: none"> Kickoff meeting conducted during the week of 8/14. Primary objective was the member introductions and review of the agenda topics, gathering topics for upcoming meetings in the areas of Policy, Processes and Automation. Next meeting is scheduled on 9/11 as a working session. <p>September 22, 2023:</p> <ul style="list-style-type: none"> ROI Workgroup met on Sept 11 and Sept 18, 2023. Group discussed policy questions and clarifications. Next meeting scheduled for Oct 2, 2023, to discuss draft applicant/recipient roles/responsibilities (e.g., 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		Authorized Representatives, Power of Attorney, CBOs, etc.)				

Table 6.2-1 – Project Risks and Issues

6.3 CRFI/CIT/CalSAWS CR Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
None for the reporting period						

Table 6.3-1 – CITs

The following table outlines CalSAWS Requests for Information (CRFIs) sent for the reporting period.

CRFI ID	To	Subject	Distribution Date	Status	Response Due Date	Primary BenefitsCal Contact	Backup BenefitsCal Contact
None for the reporting period							

Table 6.3-2 – CRFIs


CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

6.4 Appendix C – Project Work Plan Reports


Project Timeline

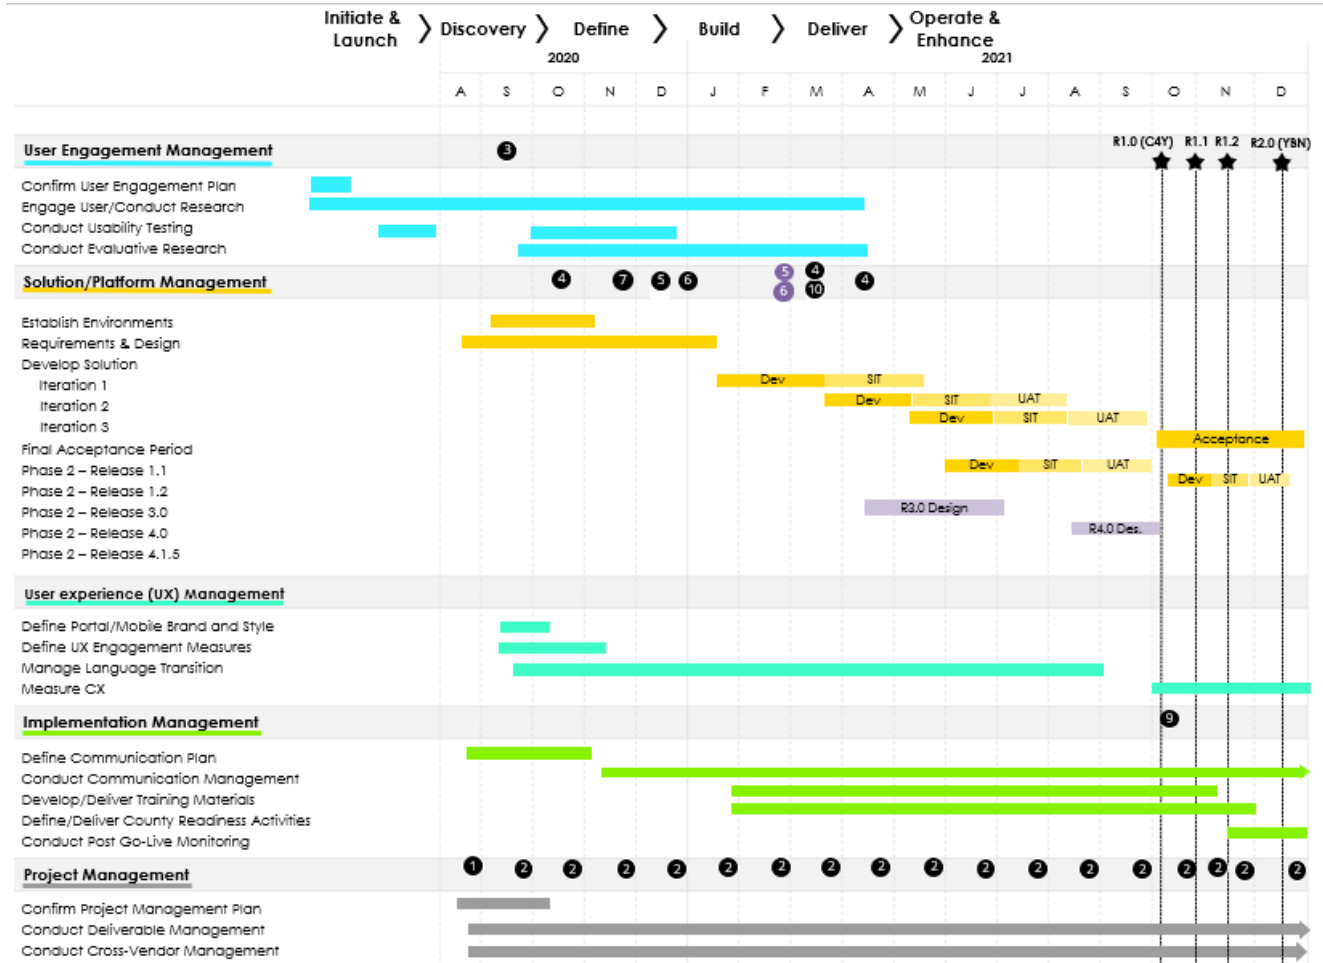

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, October 11, 2023

Period: October 1, 2023 to October 8, 2023

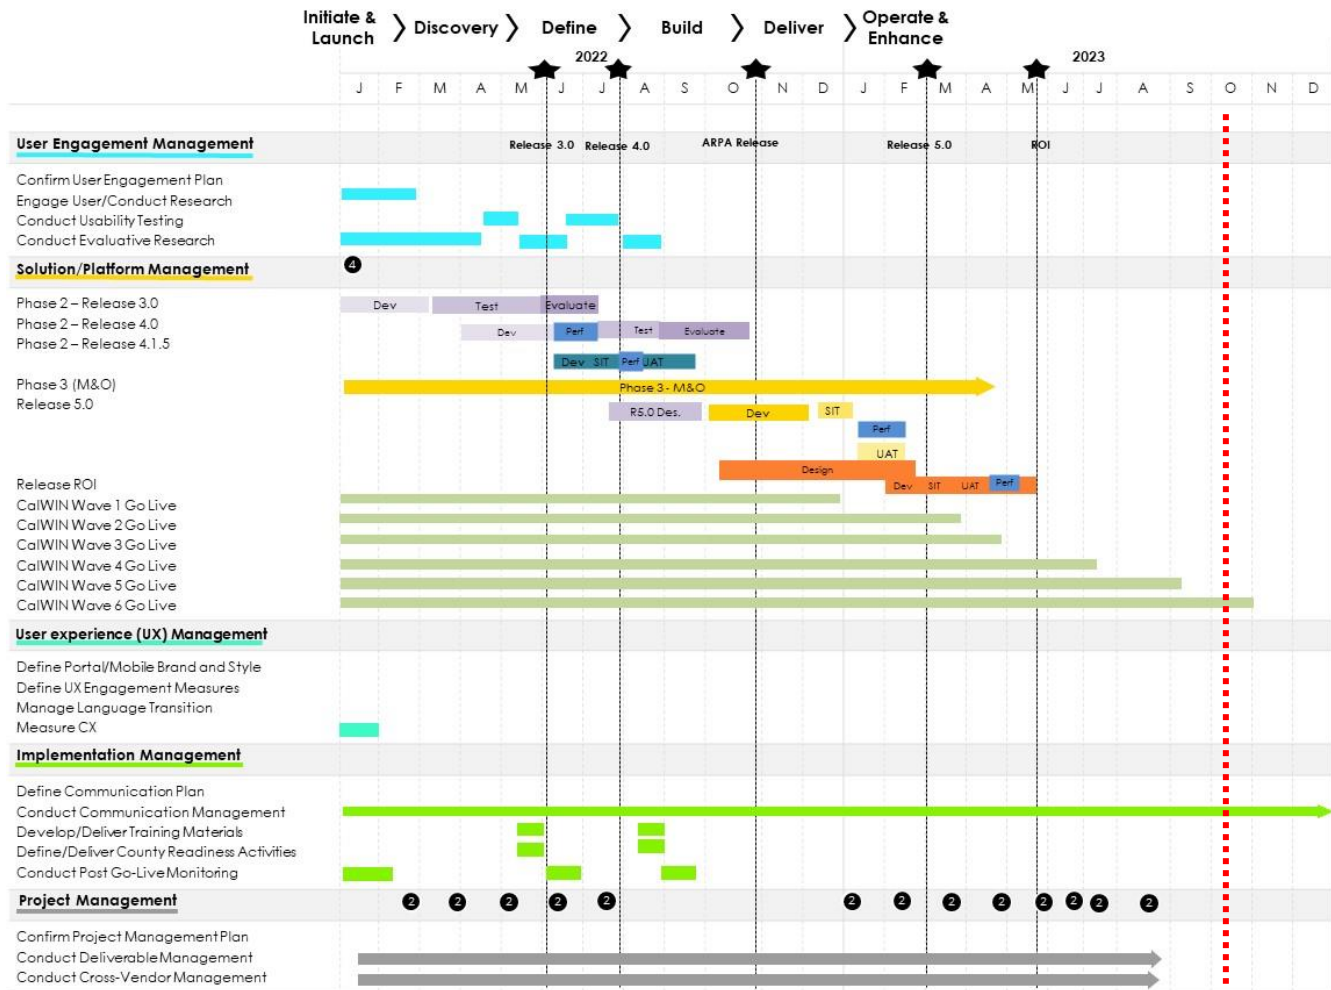

Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

ID	Description	Owner	Due Date
None			

Table 6.4-1 – Overdue Action Items
