

CalSAWS BenefitsCal (Portal/Mobile) Weekly Status Report

**Reporting Period: November 27, 2023 to
December 3, 2023**

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

Table of Contents

1.0	Project Management	4
1.1	Executive Summary	4
1.2	PMO	5
1.2.1	Highlights of the Reporting Period	5
1.2.2	Activities for the Next Reporting Period	5
1.3	BenefitsCal Collaboration Model (CM)	6
1.3.1	Highlights of the Reporting Period	6
1.3.2	Activities for the Next Reporting Period	7
2.0	Application Development and Test	7
2.1	Requirements and Design	7
2.1.1	Highlights of the Reporting Period – Requirements and Design	7
2.1.2	Activities for the Next Reporting Period – Requirements and Design	8
2.1.3	Highlights of the Reporting Period – User Centered Design (UCD)	9
2.1.4	Activities for the Next Reporting Period – UCD	9
2.2	Development	10
2.2.1	Highlights of the Reporting Period – Development	10
2.2.2	Activities for the Next Reporting Period – Development	11
2.3	System Test Execution	11
2.3.1	Highlights of the Reporting Period – System Test Execution	11
2.4	Activities for the Next Reporting Period – System Test Execution	12
2.5	User Acceptance Test (UAT) Planning	12
2.5.1	Highlights of the Reporting Period – User Acceptance Test Planning	12
2.5.2	Activities for the Next Reporting Period – User Acceptance Test Planning	12
3.0	Performance Test	12
3.1	Highlights of the Reporting Period – Performance Test	12

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

4.0	Security	13
4.1	User Conversion	13
4.1.1	Highlights of the Reporting Period – User Conversion Testing	13
4.1.2	Activities for the Next Reporting Period – User Conversion Testing	13
4.2	Security	13
4.2.1	Highlights of the Reporting Period – Security	13
4.2.2	Activities for the Next Reporting Period – Security	14
5.0	Communications and Training	14
5.1	Highlights of the Reporting Period	14
5.2	Activities for the Next Reporting Period	14
6.0	Appendices	14
6.1	Appendix A – Deliverable Summary	14
6.2	Appendix B – Risks and Issues Summary	16
6.3	CRFI/CIT/CalSAWS CR Communications Information	23
6.4	Appendix C – Project Work Plan Reports	24

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

1.0 Project Management

1.1 Executive Summary

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
November Enhancements	<ul style="list-style-type: none"> ➤ Five (5) enhancements were delivered to Production with the November Release 23.11.30: <ul style="list-style-type: none"> ○ One (1) Collaboration Enhancement ○ One (1) Partner Support Enhancement ○ Two (2) Production Priority Enhancements ○ One (1) Technical Enhancements
CalWIN Implementation Support Services (ISS) Support	<p>Wave 6</p> <ul style="list-style-type: none"> ➤ Maintenance & Operations (M&O) service management is in progress. ➤ Health Metrics generation is in progress.
User Centered Design (UCD) Activities	<p>Customer Experience (CX) Measurements Data</p> <ul style="list-style-type: none"> ➤ Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues. ➤ Analyzed always-on survey results for November. <p>User Engagement</p> <ul style="list-style-type: none"> ➤ Sent recruitment emails to customers for Usability testing sessions for EBT 2259 and CF 303 <p>Enhancements</p> <ul style="list-style-type: none"> ➤ Finalized Time Clock design edits based on the usability testing feedback. ➤ Continued synthesis for <i>Email notification</i> generative research. ➤ Conducted secondary research for <i>Display Primary Applicant</i>. ➤ Synthesized SME interview for <i>Authorized Representative</i>. ➤ Finalized design updates for CSPM-66846 and CSPM-67993 based on advocate feedback. ➤ Finalized designs for the EBT2259/CF303 enhancement. ➤ Collaborated with Consortium on 'Termination Reasons' <p>Advocate Engagement</p> <ul style="list-style-type: none"> ➤ Conducted UCD Monthly Meeting (November) on 11/29/23

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

STATUS REPORT SUBSECTION	STATUS AGENDA TOPIC
GetCalFresh (GCF) Parity List	<ul style="list-style-type: none">➤ Next working session is scheduled on 12/06/23.➤ BenefitsCal and CalSAWS teams provided the revised version of the estimates for the SCERFRA 23-500 the 5 parity items (#'s 22, 38, 44, 52, 55) on 11/17/23.➤ 4 items are pending clarification from CDSS & CFA before proceeding forward
Collaboration Model (CM)	<ul style="list-style-type: none">➤ Collaboration Model Quarterly meeting happened on 12/01/23.➤ The following CM Enhancements/Research activities were delivered/performed in the month of November 2023:<ul style="list-style-type: none">○ CSPM-67119: Collaboration Model – Document Upload for Users with No Account○ CSPM-67189: Research for CM Enhancement: Display Primary Applicant Status on a Case○ CSPM-67104: Research for CM Enhancement: Research E-mail Notifications to be sent from BenefitsCal

Table 1.1-1 – CalSAWS Executive Summary Agenda Topics

1.2 PMO

1.2.1 Highlights of the Reporting Period

➤ **Deliverables and Work Products submitted:**

- None for the reporting period.

1.2.2 Activities for the Next Reporting Period

➤ **Deliverable and Work Product submissions for next reporting period:**

- FWP 28.20: BenefitsCal Work Plan Monthly Updates – November 2023 on 12/07/23.
- FWP 29.20: BenefitsCal Monthly Status Report – November 2023 on 12/07/23.
- DWP 24.21: CX Report – October/November 2023 on 12/07/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

1.3 BenefitsCal Collaboration Model (CM)

1.3.1 Highlights of the Reporting Period

- Delivered a roadmap for the CM model prioritized items in preparation of the December 1, 2023, Quarter 4 CM meeting.
- Completed analysis of the Quarter 3 Prioritization Results for the ten (10) enhancements prioritized in the last CM survey and logged them in Jira.

The table below contains the enhancements prioritized by Collaboration Model and their updates from this week:

ID	Summary	Status	Update this Week
CSPM-67119 (Enhancement)	Collaboration Model: Document Upload for Users with No Account	Closed	Deployed to Production
CSPM-67104 (Research Item)	Research for CM Enhancement: Leverage Email Communications and Interactions	Closed	Research Completed; Enhancement CSPM-68370 logged.
CSPM-67189 (Research Item)	Research for CM Enhancement: Display Primary Applicant Status on a Case	Closed	Research Completed; Enhancement CSPM-68377 logged.
CSPM-67785	Collaboration Model: Update Document Type/ Upload feature	Prioritization Needed	Enhancement created as an outcome of the research CSPM-67105
CSPM-67761	Collaboration Model: Update Application and RE/SAR 7 Status Tracker	Prioritization Needed	Enhancement created as an outcome of the research CSPM-67149
CSPM-68266	Collaboration Model: Link to YouTube Videos on the dashboard and banner	Prioritization Needed	Enhancement created as an outcome of the research CSPM-67600
CSPM-68377 (Enhancement)	Collaboration Model: Display primary applicant	Prioritization Needed	Enhancement created as an outcome of the research CSPM-67189
CSPM-68370 (Enhancement)	Collaboration Model: Leverage email communication and interactions	Prioritization Needed	Enhancement created as an outcome of the research CSPM-67104
CSPM-64323 (Action Item)	Research for CM Enhancement: Public dashboard of BenefitsCal data	Not Started	Research not started

Table 1.3-1 – Enhancements Updates, Prioritized by CM

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

1.3.2 Activities for the Next Reporting Period

- Perform design, development, and implementation analysis for enhancements and research action items identified in the Collaboration Model.

The table below contains all enhancements prioritized by CM (not yet delivered to production) and planned activities for the next week.

ID	Summary	Activity for Next Week	Target Delivery Date
CSPM-67785 (Enhancement)	Collaboration Model: Update Document Type/ Upload feature	Prioritize for Future Release	TBD
CSPM-67761 (Enhancement)	Collaboration Model: Update Application and RE/SAR7 Status Tracker	Prioritize for Future Release	TBD
CSPM-68266 (Enhancement)	Collaboration Model: Link to YouTube Videos on the dashboard and banner	Prioritize for Future Release	TBD
CSPM-64323 (Action Item)	Research for CM Enhancement: Public dashboard of BenefitsCal data	Prioritize for Future Release	TBD
CSPM-68377 (Enhancement)	Collaboration Model: Display primary applicant	Prioritize for Future Release	TBD
CSPM-68370 (Enhancement)	Collaboration Model: Leverage email communication and interactions	Prioritize for Future Release	TBD

Table 1.3-2 – Planned Activities for Next Reporting Period for Enhancements, Prioritized by CM

2.0 Application Development and Test

2.1 Requirements and Design

2.1.1 Highlights of the Reporting Period – Requirements and Design

- **Designs and Design Meetings**
 - Continued design work for the December 2023 enhancements.
 - Began design work for the January 2024 enhancements.
 - Continued working with the development and testing teams for the November 2023 enhancements.
 - Began working with the development and testing teams for the December 2023 enhancements.
 - Continued working with the development and testing teams for CalWORKs Time Clocks enhancement.
 - Continued working with the development and testing teams for the SSA Application on BenefitsCal enhancement CSPM-65292.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

- Hosted the BenefitsCal County Welfare Directors Association of California (CWDA) Check-In on 11/27/23.
- Hosted Prep for November UCD Monthly Meeting on 11/27/23.
- Hosted DDI and M&O Bi-Weekly Call on 11/28/23.
- Attended App Dev Meeting on 11/28/23.
- Hosted EBT 2259 and CF 303 Discussion with CalSAWS on 11/28/23.
- Attended CFAP Expansion Meeting on 11/28/23.
- Cohosted SCERFRA Weekly Touchpoint on 11/29/23.
- Hosted the November UCD Monthly Meeting with State Partners and Advocates on 11/29/23.
- Hosted the BenefitsCal PM Stand-Up Meeting with the Consortium on 11/29/23.
- Hosted DDI and M&O Bi-Weekly Call on 11/30/23.
- Cohosted EBT 2259 and CF 303 Working Design Sessions on 11/30/23.
- Cohosted Collaboration Model Meeting on 12/01/23.
- Cohosted the SSP Committee Review Meeting with CalSAWS on 12/01/23.

2.1.2 Activities for the Next Reporting Period – Requirements and Design

➤ Designs and Design Meetings

- Continue design work for the December 2023 enhancements.
- Continue design work for the January 2024 enhancements.
- Continue working with the development and testing teams for the November 2023 enhancements.
- Continue working with the development and testing teams for the December 2023 enhancements.
- Begin working with the development and testing teams for the January 2024 enhancements.
- Continue working with the development and testing teams for CalWORKs Time Clocks enhancement.
- Continue working with the development and testing teams for the SSA Application on BenefitsCal enhancement CSPM-65292.
- Host the BenefitsCal County Welfare Directors Association of California (CWDA) Check-In on 12/04/23.
- Attend ROI Workgroup Meeting on 12/04/23.
- Cohost BenefitsCal Analytics Consultation on 12/04/23.
- Host DDI and M&O Bi-Weekly Call on 12/05/23.
- Attend App Dev Meeting on 12/05/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

- Attend SSP Committee Meeting on 12/05/23.
- Cohost SCERFRA Weekly Touchpoint on 12/6/23.
- Host the BenefitsCal PM Stand-Up Meeting with the Consortium on 12/6/23.
- Attend GCF Parity List Meeting on 12/6/23.
- Host DDI and M&O Bi-Weekly Call on 12/7/23.
- Host BenefitsCal Enhancement Pipeline Discussion on 12/8/23.

2.1.3 Highlights of the Reporting Period – User Centered Design (UCD)

➤ Customer Experience (CX) Measurements Data

- Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
- Resumed the creation of a detailed bimonthly data analysis sheet with process documentation and hard coded formulas for chart generation.
- Analyzed always-on survey results for November.

➤ User Engagement

- Sent recruitment emails to customers for Usability testing sessions for EBT 2259 and CF 303.

➤ Enhancements

- Finalized synthesis for *Email notification* generative research.
- Finalized synthesis for *Display Primary Applicant*.
- Conducted SME interview for *Authorized Representative*.
- Finalized design for EBT 2259 and CF 303.
- Finalized draft of January Enhancements (CSPM-67784, CSPM-67657, CSPM-67656 and CSPM-67746).

➤ Advocate Engagement

- Conducted UCD Monthly Meeting (November).
- Responded to advocate comments on December Enhancement (CSPM-66846 and CSPM-67993)

2.1.4 Activities for the Next Reporting Period – UCD

➤ CX Measurements Data

- Monitor the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
- Update the reporting template based on guidelines for better visualization of data and content.
- Resume the creation of a detailed bimonthly data analysis sheet with process documentation and hard coded formulas for chart generation.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

- **User Engagement.**
 - Conduct customer feedback sessions for EBT2259/CF303.
- **Enhancements**
 - Conduct EBT2259/CF303 customer feedback sessions.
 - Provide BenefitsCal language recommendations for “Termination Reasons.”
- **Advocate Engagement**
 - Respond to advocate comments on December Enhancement (CSPM-66846 and CSPM-67993).

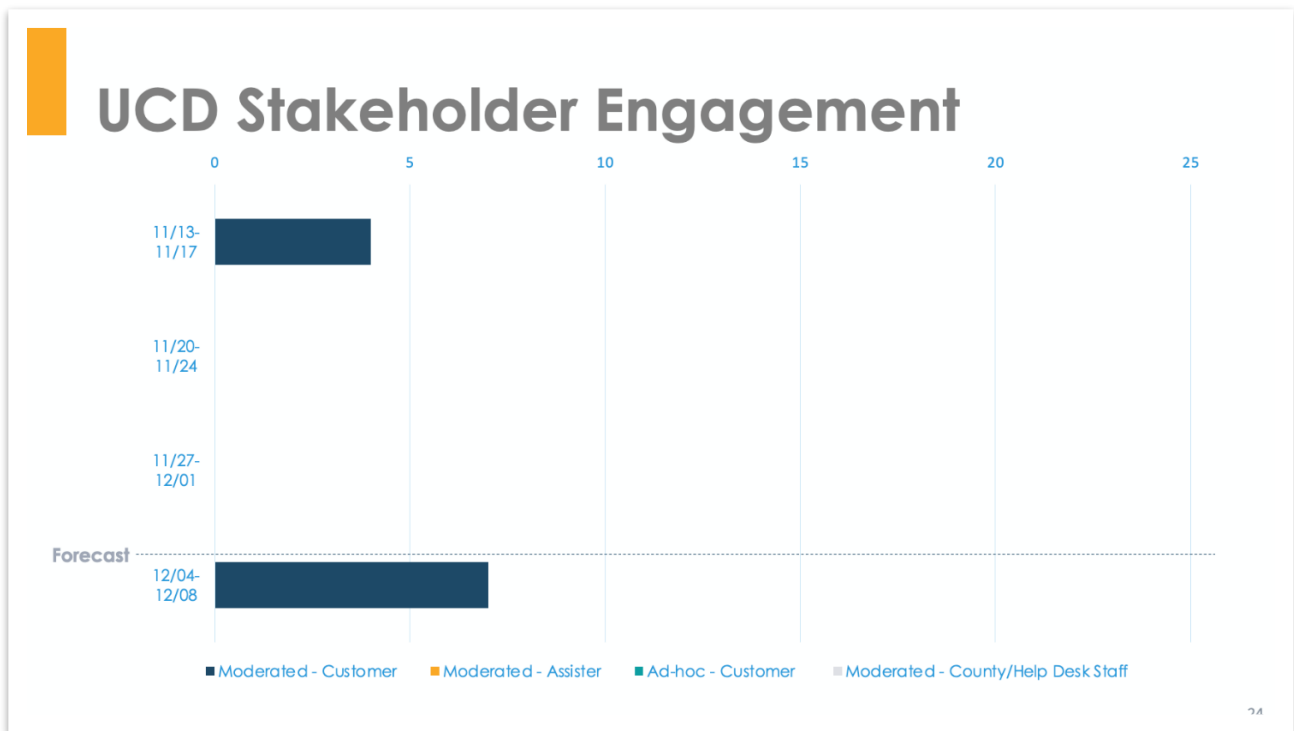


Figure 2.1-1 – UCD Stakeholder Engagement

2.2 Development

2.2.1 Highlights of the Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 12/01/23	Actual for Week Ending 12/01/23	Total Planned for the Release	Comments
23.11.30	2	2	6	Release 23.11.30 was deployed to production on 11/30/23.
23.12.19	3	3	4	

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

Release	Planned for Week Ending 12/01/23	Actual for Week Ending 12/01/23	Total Planned for the Release	Comments
24.01.25 (GCF-Parity)	1	1	3	GCF Parity items are planned for Release 24.01.25 along with regular monthly release for the month of January.

Table 2.2-1 – Enhancement Actuals for Reporting Period

2.2.2 Activities for the Next Reporting Period – Development

Enhancements (M&E)

Release	Planned for Week Ending 12/08/23	Total Planned for the Release	Total Completed for the Release	Comments
23.11.30	0	6	6	Release 23.11.30 was deployed to production on 11/30/23
23.12.19	1	4	3	Development for Release 23.12.19 has been started
24.01.25	3	3		GCF Parity items are planned for Release 24.01.25 along with regular monthly release for the month of January.

Table 2.2-2 – Planned Enhancement Work

Unscheduled Release Updates

➤ Chatbot

- The Amazon Web Services (AWS) team reported that the solution for the mute detection issues along with custom slot, currency slot issues in Chinese, Korean, and Japanese has been deployed. For these languages, testing is in progress. Once testing is complete and issues are identified, we will collaborate with the Amazon team to resolve them.
- Support for additional languages Korean, Japanese and Chinese is still not released by AWS. The next update is expected by January 2024.

➤ Time Clock

- The Time Clock release is planned for 03/25/24.

2.3 System Test Execution

2.3.1 Highlights of the Reporting Period – System Test Execution

➤ Release 23.11.30 – November Monthly Release

- Deployed the November Release into PRD on 11/30/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

➤ **Release 23.12.19 – December Monthly Release**

- Deployed the first build into SIT on 11/28/23.
- Planned first UAT build for 12/04/23.

➤ **Release 24.01.25 – January Monthly Release**

- Deployed the first build into SIT on 11/28/23, specifically to validate the GCF items planned for January.

2.4 Activities for the Next Reporting Period – System Test Execution

➤ **Release 23.12.07 – Priority Release**

- Deploy the EBT 2259 Spanish Form in Production on 12/07/23.

➤ **Release 23.12.19 – December Monthly Release**

- Continue validating the tickets and co-ordinate with the partners for any E2E validation.

➤ **Release 24.01.25 – January Monthly Release**

- Continue validating the GCF items planned for January.

2.5 User Acceptance Test (UAT) Planning

2.5.1 Highlights of the Reporting Period – User Acceptance Test Planning

➤ **UAT Test Execution**

- None for the period.

2.5.2 Activities for the Next Reporting Period – User Acceptance Test Planning

➤ **Test Support**

- None for the period.

3.0 Performance Test

3.1 Highlights of the Reporting Period – Performance Test

➤ **Release 23.11.30– November Monthly Release**

- The BenefitsCal team has identified the performance testing scope of the December monthly release. AWS Vulnerabilities and Logger Optimization enhancements are in scope and no new script development is anticipated, however, updates to existing scripts are planned on the latest stable build codebase. The BenefitsCal team has planned the isolated performance tests with the Mock services.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

Cycle	Start Date	End Date	Scope	Test Cases Status	Execution Status
13	10/23/23	11/24/23	Release 23.11.30 – November Monthly Release	Scope: Three (3) BenefitsCal enhancements are in scope for November monthly release. Document upload for users with no account requires existing document upload scripts updates and potentially new script development. Executions: Monday, 11/20/23 (Round 1 & 2)	100%
13	11/27/23	12/12/23	Release 23.12.19– December Monthly Release	Scope: AWS Vulnerabilities and Logger Optimization enhancements are in scope for December monthly release. No new script development is anticipated, however, updates to existing scripts is planned on the latest stable build. Executions: BenefitsCal isolated performance tests with Mock services plan: Monday, 12/11/23 Tuesday, 12/12/23	20%

Table 3.1-1 – Performance Test Cycles and Test Case Status

4.0 Security

4.1 User Conversion

4.1.1 Highlights of the Reporting Period – User Conversion Testing

- **CalWIN Conversion**
 - No updates for this reporting period.

4.1.2 Activities for the Next Reporting Period – User Conversion Testing

- **Perform CBO User Data Validation**
 - No updates for this reporting period.

4.2 Security

4.2.1 Highlights of the Reporting Period – Security

- **SAST**
 - Executed the weekly Static Application Security Testing (SAST) of the application source code and shared the analysis of the security scan reports with the BenefitsCal Development Team for remediation on 12/01/23.

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

4.2.2 Activities for the Next Reporting Period – Security

➤ **Identified Vulnerabilities**

- After the validation of the identified vulnerabilities, advise on the remediation activities to be performed by the BenefitsCal Development Team. Log defects in Jira for tracking purposes (weekly recurring activity).

➤ **AWS SSO for BenefitsCal**

- Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.

5.0 Communications and Training

5.1 Highlights of the Reporting Period

- No customer communication campaign was launched for the reporting period.
- Ad hoc training was conducted for the San Francisco County and CBO staff on 11/26/23.

5.2 Activities for the Next Reporting Period

- No activities for the reporting period.

6.0 Appendices

6.1 Appendix A – Deliverable Summary

Deliverable Status by Submission

		Complete	Coming Soon	WAC Approval Pending		
DEL ID	Deliverable Name	DDED	FDED	DDEL	FDEL	Final Approval
None for the reporting period.						

Table 6.1-1 – Deliverable Status for Current Reporting Period

Upcoming Deliverable Deadlines

DEL #	Deliverable Name	Status	Next Deadline
None for the reporting period.			

Table 6.1-2 – Upcoming Deliverable Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

Work Product Status by Submission

		Complete	Coming Soon	WAC Approval Pending
ID	Work Product Name	DWP	FWP	Final Approval
24.20	CX Report – August/September 2023	10/13/23	10/25/23	11/01/23
24.21	CX Report – October/November 2023	12/07/23	12/19/23	12/26/23
25.21	Monthly M&O Report – October 2023	11/08/23	11/21/23	11/30/23
25.22	Monthly M&O Report – November 2023	12/11/23	12/21/23	12/29/23
28.19	BenefitsCal Work Plan Monthly Updates – October 2023	N/A	11/07/23	11/17/23
28.20	BenefitsCal Work Plan Monthly Updates – November 2023	N/A	12/07/23	12/18/23
28.19	BenefitsCal Monthly Status Report – October 2023	N/A	11/07/23	11/17/23
28.20	BenefitsCal Monthly Status Report – November 2023	N/A	12/07/23	12/18/23

Table 6.1-3 – Upcoming Work Product Deadlines

Upcoming Work Product Deadlines

WP #	Work Product Name	Status	Next Deadline
24.21	CX Report – October/November 2023	On Track	DWP submission 12/07/23 FWP submission 12/19/23 FWP approval 12/26/23
25.22	Monthly M&O Report – November 2023	On Track	DWP submission 12/11/23 FWP submission 12/21/23 FWP approval 12/29/23
28.20	BenefitsCal Work Plan Monthly Updates – November 2023	On Track	FWP submission 12/07/23 FWP approval 12/18/23
28.20	BenefitsCal Monthly Status Report – November 2023	On Track	FWP submission 12/07/23 FWP approval 12/18/23

Table 6.1-4 – Upcoming Work Product Deadlines

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

6.2 Appendix B – Risks and Issues Summary

Project Risks and Issues

ID	Title	Details	Status	Risk Level	Severity	Date Logged
246	Perceived Gap in Functionality	<p>A perceived gap in functionality between GetCalFresh and BenefitsCal was identified. Select features identified within GetCalFresh are not present within BenefitsCal as they are not part of the project requirements, and change requests were logged to address. Impacts BenefitsCal adoption by Community Partners may be lower as they rely on features (like the referral code) to complete their work. The future migration from GCF to BenefitsCal in 2022 is at risk until features are added to BenefitsCal.</p> <p>Status Updates:</p> <p>September 2, 2022:</p> <ul style="list-style-type: none"> Had multiple meetings with CDSS to discuss the GetCalFresh Gap List with Consortium and CWDA, latest on 08/29/22. There is a bi-weekly meeting cadence. Currently there are few enhancement suggestions from CDSS on partial gaps. Teams are going to continue having working sessions to decide any of these must have or nice to have. <p>September 30, 2022:</p> <ul style="list-style-type: none"> Continued working sessions with CDSS, CWDA, Consortium and CalSAWS. With the CDSS's analysis, there is total of 41 gaps. 32 are logged as enhancements for prioritization and the remaining 9 will be discussed at upcoming working sessions. There is also a plan to identify/classify must have vs nice to have items. Next working session is scheduled for 10/05/22. <p>January 6, 2023:</p> <ul style="list-style-type: none"> BenefitsCal team has started working on the effort estimations for the gaps list (31 gaps/52 enhancements). Targeting to complete the estimations by 01/16 and propose prioritization. CDSS, CWDA and Consortium will 	Open	Low	Medium	05/10/21

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>provide direction on the implementation schedule.</p> <p>January 11, 2023:</p> <ul style="list-style-type: none"> • Prioritization is requested by end of month so it can be incorporated into the roadmap. <p>February 2, 2023:</p> <ul style="list-style-type: none"> • Provided responses to CDSS SCERFRA with estimates for GCF parity list items. CDSS to confirm the SCERFRA approval and prioritization to establish a roadmap for implementation. <p>February 3, 2023:</p> <ul style="list-style-type: none"> • Attended meeting with CDSS, CalSAWS, and CWDA for the GCF Parity List on 02/02/23. Provided responses to CDSS SCERFRA with estimates for GCF parity list items. <p>March 3, 2023:</p> <ul style="list-style-type: none"> • RMG: Attended meeting with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/01/23. CDSS to confirm the SCERFRA approval and prioritization to establish a roadmap for implementation. <p>April 7, 2023</p> <ul style="list-style-type: none"> • Attended meetings with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/22/23 and 04/05/23. CDSS shared decommissioning timeline got GCF components/CDSS will map the components planned for decommissioning to parity list items to confirm the SCERFRA approval, funding source and prioritization to establish a roadmap for implementation. <p>April 28, 2023:</p> <ul style="list-style-type: none"> • Attended meetings with CDSS, CalSAWS, and CWDA for the GCF Parity List on 03/22/23 and 04/19/23. CDSS is currently mapping the components planned for decommissioning to parity list items and will confirm the SCERFRA approval for SCERFRA 23-512, CDSS is also confirming the funding source to establish a 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>roadmap for implementation. Next meeting is scheduled on 05/03/23.</p> <p>June 2, 2023:</p> <ul style="list-style-type: none"> Participated in the bi-weekly meetings on 05/03/23 and 05/17/23. Worked with the California Welfare Directors Association (CWDA) and the Consortium and provided line-item level analysis for a Legislative request on 05/19/23. Next bi-weekly meeting is scheduled for 06/07/23. The California Department of Social Services (CDSS) continued mapping the components planned for decommissioning to the parity list items. <p>June 9, 2023:</p> <ul style="list-style-type: none"> BenefitsCal and CalSAWS teams connected with ODI on Friday 06/09/23. Next steps identified for ODI to provide the raw data from GCF to begin the analysis. <p>June 30, 2023:</p> <ul style="list-style-type: none"> Bi-weekly meeting conducted with CDSS, CWDA, Consortium and CalSAWS on 06/21/23. CDSS to provide final list of excel extract of items based on legislative response. Also, teams continued to work with ODI team on the analysis and data needs/questions. <p>July 28, 2023:</p> <ul style="list-style-type: none"> A working session is scheduled for 08/02/23 to talk about SCERFRA 23-500, SCERFRA 23-512 (SSA flow) and CF 303 – Benefit Replacement with CDSS, CWDA, Consortium and CalSAWS. <p>September 1, 2023:</p> <ul style="list-style-type: none"> Multiple working sessions have been facilitated by CDSS with participation by CWDA, Consortium, BenefitsCal, and CalSAWS. Since August 02, 2023, Out of 26 items, 4 items have been closed, 4 items are in-plan. 9 items are awaiting confirmation/response by CDSS and another 9 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>are scheduled to be discussed with CDSS during the next working session on September 06, 2023. In plan items include the SSA Application flow in BenefitsCal, design activities for SCERFRA 23-512 (SSA flow) is on track to be completed by 09/08/23.</p> <p>September 8, 2023:</p> <ul style="list-style-type: none"> Working session facilitated by CDSS with participation by CWDA, Consortium, BenefitsCal and CalSAWS on 09/06/23. CDSS is going to provide offline response for the remaining items. Next working session is schedule on 10/04/23. Also working with ODI on recommender widget analysis. Next meeting is on 09/12/23. <p>September 29, 2023:</p> <ul style="list-style-type: none"> Continue to participate in working sessions facilitated by CDSS with participation from CWDA, Consortium, BenefitsCal and CalSAWS. Project has provided revised estimate for 5 parity items on 9/22 via SCERFRA 23-500 that includes SSA Flow, CF-303 and three other changes. Next meeting with CDSS is scheduled for 10/4/2023 where 9 remaining items will be discussed. <p>October 6, 2023:</p> <ul style="list-style-type: none"> Participated in sessions facilitated by CDSS on 09/19/23, with participation from CWDA, Consortium and BenefitsCal for parity list. BenefitsCal responses for parity list SCERFRA 23-500 for tracking IDs 9, 19, 20, 31, 63 are provided to CDSS on 09/22. Another working session is facilitated on 10/04/23 with participation from CWDA, Consortium, BenefitsCal and CalSAWS. 1 item is resolved, and 8 items are remaining where CDSS and CFA to provide confirmation to finalize. <p>November 3, 2023:</p> <ul style="list-style-type: none"> Participated in sessions facilitated by CDSS on 11/01/23, with 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>participation from CWDA, Consortium and BenefitsCal for parity list. Three items are closed, and four items have had clarification provided to BenefitsCal team to start estimation. Three items are remaining where CDSS and CFA to provide confirmation to finalize. One on BenefitsCal team to clarify by end of week starting 11/06/23.</p> <p>November 10, 2023:</p> <ul style="list-style-type: none"> • Work order # 14 is submitted on 10/23/23 including the following items: <ul style="list-style-type: none"> ○ GCF Parity#20: CalFresh Application "Joint Processing" by Social Security Administration and County Welfare Departments in BenefitsCal – Development and Implementation ○ GCF Parity#31: CF303 ○ GCF Parity#9: Vaccination ○ GCF Parity#19: Self Employment Help Text ○ GCF Parity#63 Language Specific URLs 				

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
290	Recently released ROI policy lacks clarity which may create privacy and liability exposure for counties and customers	<p>Recently issued Release of Information (ROI) policy is not detailed enough, nor is it consistent between the two state Departments (CDSS and DHCS). The policy as written may create customer information privacy/security, safeguard and county operations concerns, and liabilities. As the policy was released after the completion of ROI design, development, and testing of the functionality in BenefitsCal and CalSAWS, counties have not had sufficient time to assess the ROI functionality with the high-level policy and to be able to determine impacts to their county operations and the associated alignment with the existing BenefitsCal/CalSAWS design. The policy as written does not give clear direction on County responsibilities associated with the establishment of CBO agreements, provisions of those agreements and monitoring of CBO compliance with the agreements. Counties also have not had sufficient time to be able to determine if their current CBO agreement language is adequate and includes provisions and protections to further protect customer information when being accessed by CBOs via BenefitsCal. BenefitsCal/CalSAWS initial design and implementation has been postponed until final/revised policy is issued by both CDSS and DHCS and there is operational clarity agreed to by all parties.</p> <p>June 16, 2023:</p> <ul style="list-style-type: none"> Responded to SIRFRA 1270/1271 regarding Expanding the Release of Information Feature with set of questions to DHCS from BenefitsCal, CalSAWS, and CWDA on 06/12/23. <p>June 30, 2023:</p> <ul style="list-style-type: none"> Risk was reduced to probability of 30% which brings it to an overall medium level. State partners to confirm the topics and agenda items for the workgroup discussions. Topic was also covered during the June JPA Board meeting on 6/29/23. 	Open	Medium	High	05/19/23

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

ID	Title	Details	Status	Risk Level	Severity	Date Logged
		<p>July 28, 2023:</p> <ul style="list-style-type: none"> Workgroup member names are being collected including representatives from CDSS, DHCS, OSI, CWDA, Counties, Advocates and CalSAWS. Draft topics are also being reviewed, Preliminary categories including, Policy Guidance Considerations/ Questions, Processes, System Functionality/Automation. Meeting Schedule and cadence is in progress. <p>September 1, 2023:</p> <ul style="list-style-type: none"> Kickoff meeting conducted during the week of 8/14. Primary objective was the member introductions and review of the agenda topics, gathering topics for upcoming meetings in the areas of Policy, Processes and Automation. Next meeting is scheduled on 9/11 as a working session. <p>September 22, 2023:</p> <ul style="list-style-type: none"> ROI Workgroup met on Sept 11 and Sept 18, 2023. Group discussed policy questions and clarifications. Next meeting scheduled for Oct 2, 2023, to discuss draft applicant/recipient roles/responsibilities (e.g., Authorized Representatives, Power of Attorney, CBOs, etc.) <p>November 3, 2023:</p> <ul style="list-style-type: none"> Applicant/recipient roles/responsibilities matrix (e.g., Authorized Representatives, Power of Attorney, CBOs, etc.) is currently jointly being developed. It will address Medi-Cal, CalFresh and CalWORKs programs. Next workgroup meeting is scheduled on 11/13/23. 				

Table 6.2-1 – Project Risks and Issues

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

6.3 CRFI/CIT/CalSAWS CR Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

CIT ID	To	Subject	Category	Distribution Date	Primary CalSAWS Contact	Backup CalSAWS Contact
0395-23	Notify.All; usbenefitscaldevops@deloitte.com; operator@calheers.ca.gov; HoweG@CalSAWS.org; QuijadaP@CalSAWS.org; TombakianM@CalSAWS.org; Tech.ProductionOperations@CalSAWS.org	Scheduled Downtime Notification – 12/17/23	CalSAWS M&E	11/29/23	Anand Kulkarni	Pete Quijada

Table 6.3-1 – CITs

The following table outlines CalSAWS Requests for Information (CRFIs) distributed or with a response due date within the reporting period.

CRFI ID	To	Subject	Distribution Date	Status	Response Due Date	Primary BenefitsCal Contact	Backup BenefitsCal Contact
None.							

Table 6.3-2 – CRFIs


CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

6.4 Appendix C – Project Work Plan Reports


Project Timeline

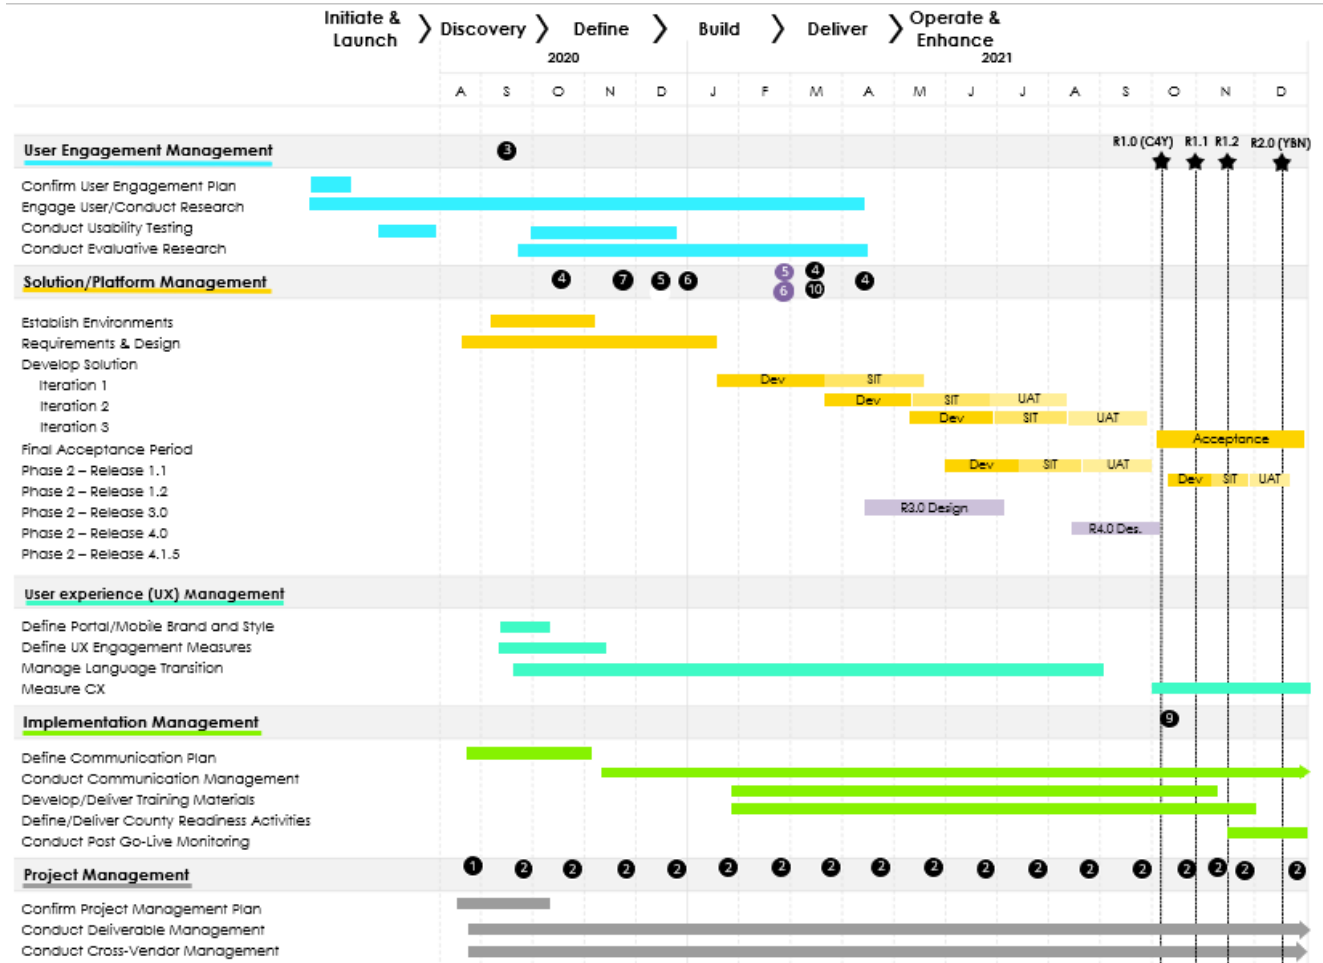

CalSAWS – BenefitsCal (Portal/Mobile) Weekly Status Report

Weekly Status Report, December 6, 2023

Period: November 27, 2023 to December 3, 2023

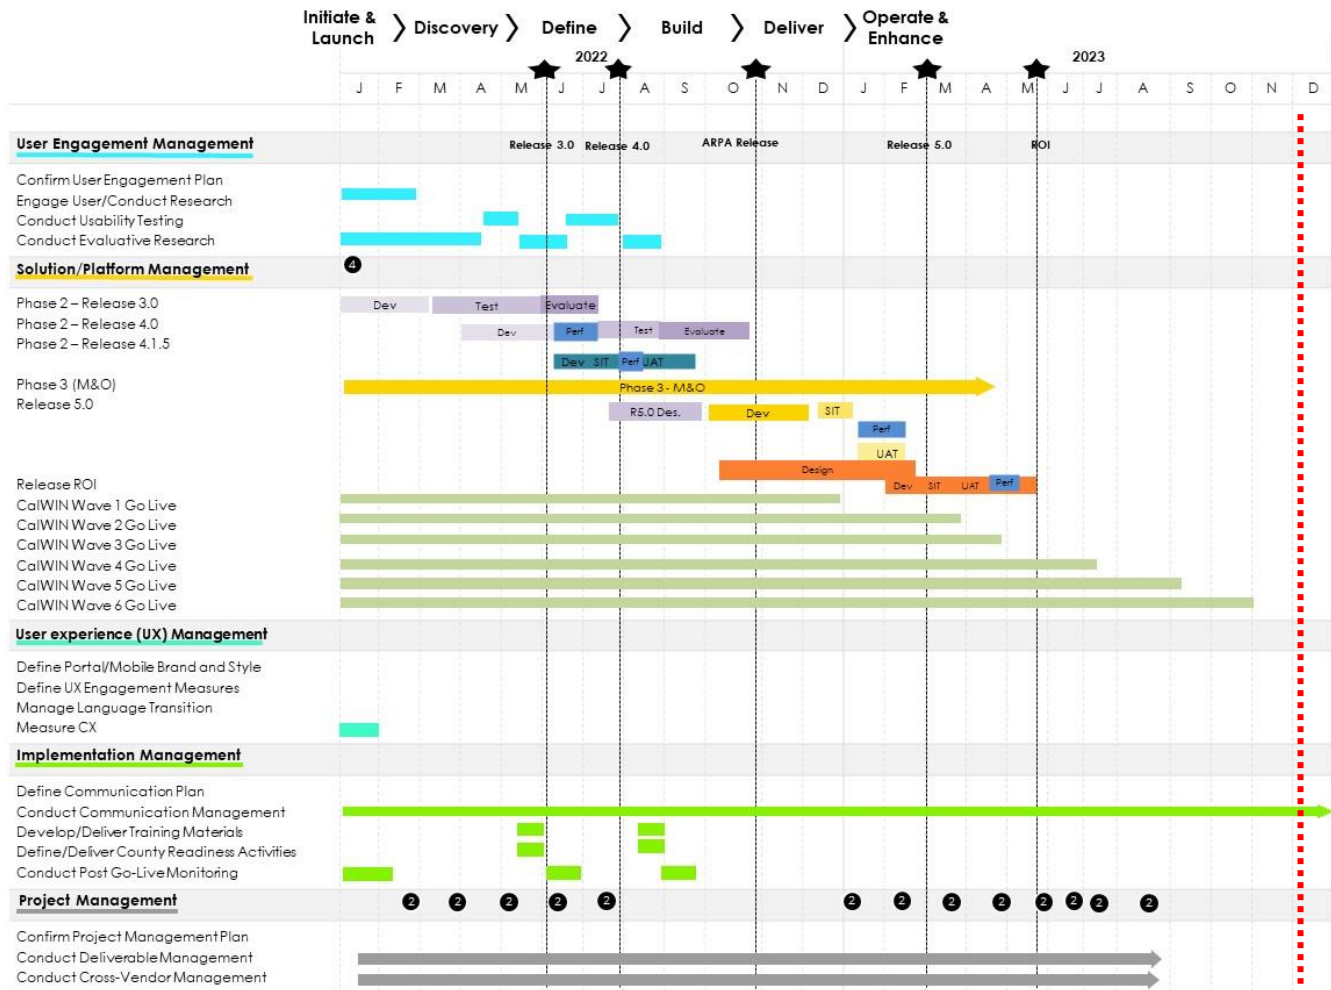

Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

ID	Description	Owner	Due Date
None.			

Table 6.4-1 – Overdue Action Items
