

CalSAWS Central Print Bi- Weekly Status Report

Reporting Period: March 24, 2024, to April 7, 2024

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

Table of Contents

1.0 CalSAWS Central Print Project2

 1.1 Highlights of the Reporting Period2

 1.2 Project Deliverable Summary3

 1.3 CRFI/CIT Communications Information4

 1.4 Activities for the Next Reporting Period.....5

 1.5 Deviations from Plan/Adjustments5

 1.6 Postage Status5

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

1.0 CalSAWS Central Print Project


1.1 Highlights of the Reporting Period

Table 1.1-1 – CalSAWS Central Print Status Agenda Topics

| STATUS REPORT SUB-SECTION | STATUS AGENDA TOPIC |
|---------------------------|---|
| 1.1 | <ul style="list-style-type: none">Continued processing of print for all 58 CalSAWS counties.Continued Return Mail processing for 5 counties. |

Requirements Verification

► No updates.

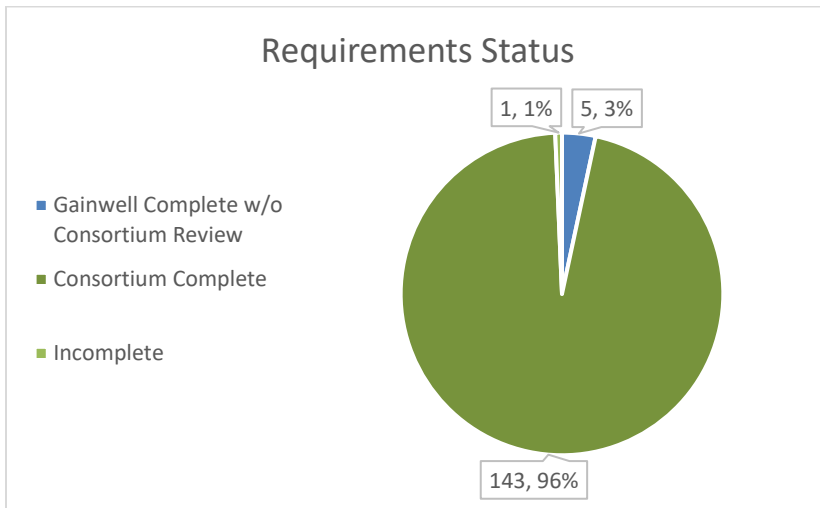

Maintenance and Operations


- Continued ongoing operations for all 58 counties.
- Completed processing of CW/CF RE packets for LA County.
- Completed processing of CW/CF RE packets for 57 counties.
- Continued Return Mail processing activities for Lake, Placer, San Diego, San Luis Obispo,

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

and Solano.

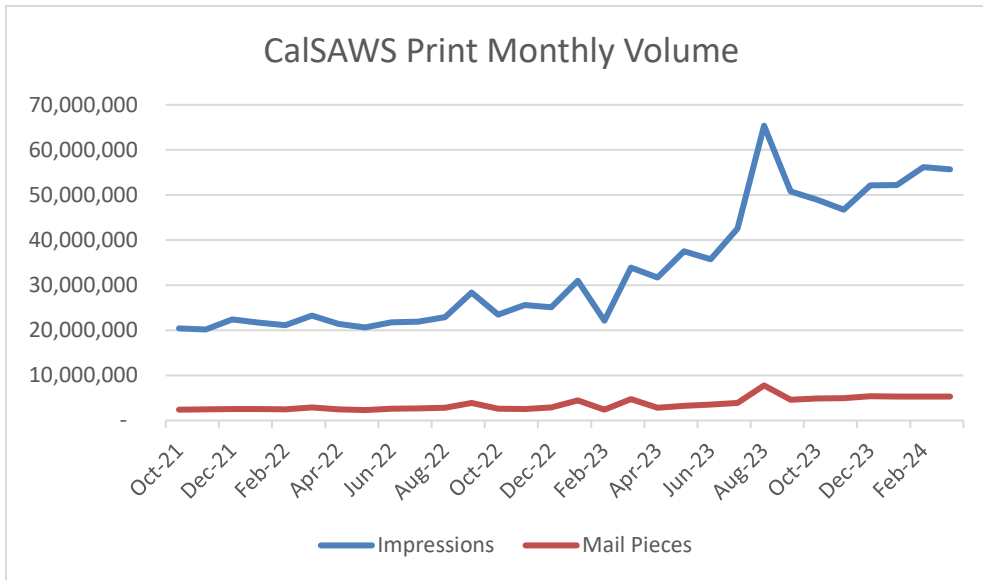

Comprehensive Testing

► No Update

Project Action Items – Overdue

► This table lists overdue action items, including the owner and due date.

| ID | Description | Owner | Due Date |
|------|--------------------------|-------|----------|
| None | No overdue actions items | | |

Table 1.1-8 – Overdue Action Items

1.2 Project Deliverable Summary

Deliverable Activity is summarized within the tables below. Note that only the initial submission of the Monthly Status Report is listed in the table below. Each remaining Monthly Status Report will be submitted as an FDEL only per the date in the approved FDED and is not included in the list below.

Deliverable Status

| DEL # | DELIVERABLE NAME | STATUS | Next Deadline |
|-------|---------------------------------------|-----------|-----------------------|
| 01.35 | Monthly Status Report – February 2024 | Completed | Del 01.36 due 4/5/24. |

Table 1.2-2 – Upcoming Deliverable Deadlines

CalSAWS – Central Print Project


Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

Project Risks and Issues

| ID | Title | Details | Status | Impact | Severity | Date Logged |
|-----|-------|---------|--------|--------|----------|-------------|
| N/A | | | | | | |

The following chart shows the number of risks currently open and previously closed, if applicable.

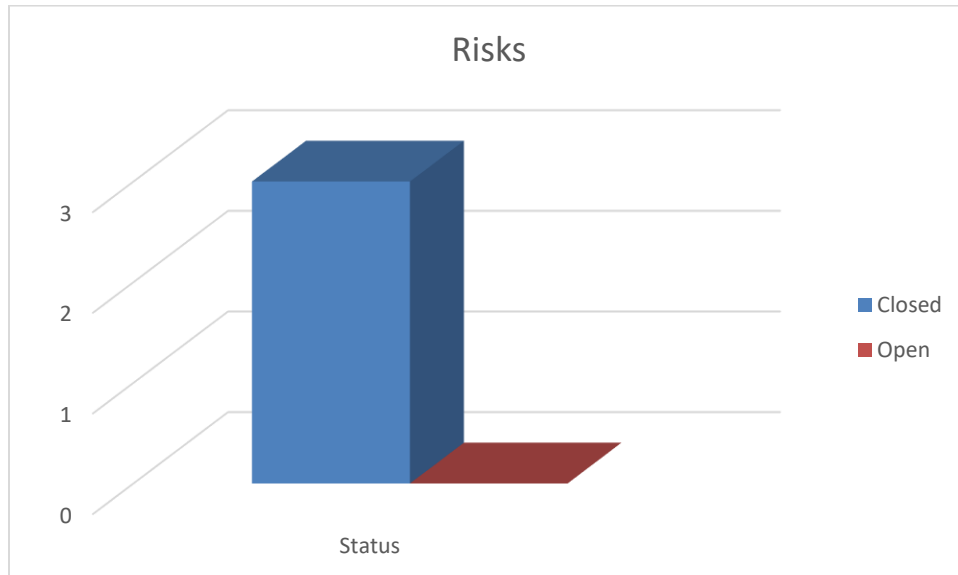

The following chart shows the number of issues currently open and previously closed, if applicable.

► Not applicable – No open or closed issues as of this status reporting period.

1.3 CRFI/CIT Communications Information

The following table outlines CalSAWS Information Transmittals (CITs) sent for the reporting period.

There were no CalSAWS Information Transmittals (CITs) submitted during the reporting period.

| CIT ID | To | Subject | Category | Distribution Date |
|--------|----|---------|----------|-------------------|
| N/A | | | | |

Table 1.4-1 – CITs

There were no CalSAWS Requests for Information (CRFIs) submitted during the reporting period.

| CRFI ID | To | Subject | Distribution Date | Status | Response Due Date |
|---------|----|---------|-------------------|--------|-------------------|
| N/A | | | | | |

Table 1.4-2 – CRFIs

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

1.4 Activities for the Next Reporting Period

Requirements Verification

- ▶ No Update

Maintenance and Operations

- ▶ Continue ongoing operations for all 58 counties.
- ▶ Complete processing of SAR7/QR7 correspondences.
- ▶ Begin processing of CW/CF RE packets for LA County.
- ▶ Begin Return Mail processing activities for Napa County.
- ▶ Continue Return Mail processing activities for Lake, Placer, San Diego, San Luis Obispo, and Solano.

1.5 Deviations from Plan/Adjustments





- ▶ No deviations.











1.6 Postage Status

- ▶ Postage Status at the end of prior month.

This section includes a summary of the postage fund status for each County.

Legend

| | |
|---|--|
|  | County has over two months of estimated funds on account. |
|  | County has between one and two months of estimated funds on account. |
|  | County has one month or less of estimated funds on account. |
|  | Not applicable (County has not started postage funding yet per plan or is not in scope). |

| Status | County | Status | County |
|---|--------------|---|-----------|
|  | Alameda |  | Alpine |
|  | Amador |  | Butte |
|  | Calaveras |  | Colusa |
|  | Contra Costa |  | Del Norte |
|  | El Dorado |  | Fresno |

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

| Status | County | Status | County |
|--------|-------------|--------|-----------------|
| | Glenn | | Humboldt |
| | Imperial | | Inyo |
| | Kern | | Kings |
| | Lake | | Lassen |
| | Los Angeles | | Madera |
| | Marin | | Mariposa |
| | Mendocino | | Merced |
| | Modoc | | Mono |
| | Monterey | | Napa |
| | Nevada | | Orange |
| | Placer | | Plumas |
| | Riverside | | Sacramento |
| | San Benito | | San Bernardino |
| | San Diego | | San Francisco |
| | San Joaquin | | San Luis Obispo |
| | San Mateo | | Santa Barbara |
| | Santa Clara | | Santa Cruz |
| | Shasta | | Sierra |
| | Siskiyou | | Solano |
| | Sonoma | | Stanislaus |
| | Sutter | | Tehama |
| | Trinity | | Tulare |
| | Tuolumne | | Ventura |
| | Yolo | | Yuba |

CalSAWS – Central Print Project

Weekly Status Report, April 8, 2024

Period: March 25, 2024, to April 7, 2024

Note: Counties in Red and Yellow have been contacted to request additional funds.
