

CalSAWS

California Statewide Automated Welfare System



Biweekly Status Report

BenefitsCal Maintenance and Operations (M&O)

Reporting Period: February 23, 2026 – March 8, 2026

Table of Contents

1 EXECUTIVE SUMMARY	4
1.1 Highlights of the Reporting Period	4
1.1.1 Deliverable Summary	5
1.2 BenefitsCal Project Status Dashboard	5
1.3 Highlights of the Reporting Period	5
1.4 Deliverable Management	6
1.5 CRFI/CIT Communications	6
1.6 Risks and Issues	7
1.6.1 Project Risks	7
1.6.2 Project Issues	7
1.7 Project Work Plan Reports	8
1.8 Project Action Items – Overdue	10
1.9 SIRFRA/SCERFRA/SIRFRA/SARRA Information	11
1.10 Deviation from Plan/Adjustments	12
1.11 Transition-Out	12
2 BENEFITSCAL COLLABORATION MODEL (CM)	12
3 MAINTENANCE AND OPERATIONS	13
3.1 Service Management	13
3.1.1 Overview	13
3.1.2 BenefitsCal Help Desk Metrics	14
3.2 Technology Operations	23
3.3 BenefitsCal Maintenance and Operations	23
3.4 Production Defect Backlog	24
3.4.1 Release Schedule Production Defect Fix	25
3.5 Production Operations	25
3.6 Deviation from Plan/Adjustments	25
4 APPLICATION DEVELOPMENT AND TEST	26
4.1 Priority Release Summary	26
4.2 Requirements and Design	26
4.3 User Centered Design (UCD)	27
4.4 Development	29
4.5 User Acceptance Test (UAT) Planning	29
4.6 Release Management	30
4.7 System Test Execution	30

4.7.1	Automated Regression Test (ART) Coverage	30
5	PERFORMANCE TEST.....	31
5.1	Performance Test	31
5.2	Training Materials Update	31
5.3	Deviations from Plan/Adjustments	31
5.4	Security	32

TABLE OF TABLES

Table 1:	Biweekly Status Agenda Topics	4
Table 2:	Deliverable Summary	5
Table 3:	Status Dashboard	5
Table 4:	CITs	6
Table 5:	CRFIs	7
Table 6:	Overdue CRFIs	7
Table 7:	Project Risks	7
Table 8:	Project Issues	8
Table 9:	Overdue Action Items	10
Table 10:	Summary of SCIRFRA/SCERFRA/SIRFRA/SARRA Requests.....	11
Table 11:	Enhancements Updates, Prioritized by CM	12
Table 12:	BenefitsCal Outages	23
Table 13:	BenefitsCal Upcoming Maintenance	23
Table 14:	Production Defect Fix – Release Schedule.....	25
Table 15:	BenefitsCal Upcoming Releases.....	26
Table 16:	Enhancement Actuals for Reporting Period	29
Table 17:	Planned Enhancement Work	29
Table 18:	Automated Regression Scripts Executed in BenefitsCal.....	30
Table 19:	Performance Test Cycles and Test Case Status	31

TABLE OF FIGURES

Figure 1:	Transition-Out Status Summary	12
Figure 2:	BenefitsCal ServiceNow Incidents Created	14
Figure 3:	BenefitsCal ServiceNow Incidents Resolved	15
Figure 4:	BenefitsCal ServiceNow Incidents Closed.....	16
Figure 5:	BenefitsCal ServiceNow Incidents Triaged	17
Figure 6:	BenefitsCal ServiceNow Problems Created	18
Figure 7:	BenefitsCal ServiceNow Problems Resolved	19
Figure 8:	BenefitsCal ServiceNow Incidents by State and Age	20
Figure 9:	BenefitsCal ServiceNow Incidents by Resolution Code	21
Figure 10:	BenefitsCal ServiceNow Incidents Created by Category.....	22
Figure 11:	Production Defects Backlog Monthly Trend.....	24

Figure 12: UCD Stakeholder Engagement.....28

Bi-Weekly Status – BenefitsCal M&O

1 EXECUTIVE SUMMARY

1.1 Highlights of the Reporting Period

Table 1: Biweekly Status Agenda Topics

STATUS REPORT SECTION	STATUS AGENDA TOPIC
1.3	<ul style="list-style-type: none"> ▪ Monthly Release 26.02.26 was successfully deployed to BenefitsCal Production on 02/26/26.
February Enhancements (February Monthly Release 26.02.26)	<ul style="list-style-type: none"> ▪ Eight (8) enhancements were successfully deployed to BenefitsCal Production on 02/26/26: <ul style="list-style-type: none"> • Four (4) Production Priority Enhancements: <ul style="list-style-type: none"> • CSPM-82297: Update the Password Complexity Validation Message During Account Creation to Help Visually-Impaired Users • CSPM-82296: Refresh the Health Rep Inquiry and Documents for Verifications Pages in BenefitsCal • CSPM-82245: Update the BenefitsCal Admin Module to Include Chatbot Income Limits • CSPM-81926: Update L.A. County CF ES pop-up screen to accommodate new hours of operation for the Call Center ▪ Two (2) Partner Support Enhancements: <ul style="list-style-type: none"> • CSPM-83075: Test Only: FIS Regression Testing Support for February 2026 Release ▪ Two (2) Technical Enhancements: <ul style="list-style-type: none"> • CSPM-82822: Technical: Storage of GetCalFresh (GCF) Referral Code • CSPM-82294: Technical: Auto-Refresh the BenefitsCal System for Users when Production Deployments Occur
User Centered Design (UCD) Activities	<ul style="list-style-type: none"> ▪ Customer Experience (CX) Measurements Data <ul style="list-style-type: none"> • Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues. • Started February Always on survey data. ▪ User Engagement <ul style="list-style-type: none"> • Conducted CBO assister session for Help Center. • Finalized synthesis for combined stakeholder Help Center findings (county worker sessions, combined advocate and state partner session, and CBO assister session). • Continued synthesis for Truv customer sessions. ▪ Enhancements

STATUS REPORT SECTION	STATUS AGENDA TOPIC
	<ul style="list-style-type: none"> Continue analysis on CSPM-80929: H.R.1 – Big Beautiful Bill – Semi-Annual Redeterminations for MAGI New Adult Group. Started ideation and consolidation of requirements from workgroup for CSPM-81960: Truv Phase 1 & 2. Started realigning approach for CSPM-66458: CM Browser Back Button. Finalized updates to designs for Digitize NA-1273.
Transition-Out	<ul style="list-style-type: none"> Advocate Engagement <ul style="list-style-type: none"> Conducted Truv Workgroup session 2. Started drafting February UCD comment log responses. Started drafting March UCD monthly deck. Conducted internal review of March UCD monthly deck. Access Requests & Shared Documents <ul style="list-style-type: none"> Completed 41 of 73 document requests. Document requests in progress. Application Access Request – Jira, Bitbucket completed. Provided KT Support (Total 89) <ul style="list-style-type: none"> KT Committed – 69 Sessions KT Scheduled – 50 Sessions KT Completed – 19 sessions

1.1.1 Deliverable Summary

Table 2: Deliverable Summary

DEL #	DELIVERABLE NAME	STATUS	NEXT DEADLINE
	None for the Reporting period		

1.2 BenefitsCal Project Status Dashboard

Table 3: Status Dashboard

TOPIC	STATUS	HIGHLIGHTS
Availability	On Time	The BenefitsCal System did not experience any unplanned outages.
Defects	On Time	There are thirty-one (31) active Production defects.
Incidents	On Time	There are six (6) open Tier 3 incidents.

1.3 Highlights of the Reporting Period

- Priority Release**
 - None for the reporting period.
- Emergency Release**
 - None for the reporting period.

- **Monthly Release**
 - The BenefitsCal Team successfully deployed Monthly Release 25.02.26 to BenefitsCal Production.
- **Planned Outages**
 - Thursday,02/26/26 8:00 pm to 9:30 pm PST
 - ♦ BenefitsCal Monthly Release 26.02.29

1.4 Deliverable Management

- **Deliverables and Work Products submitted:**
 - FWP 25.49: Monthly M&O Report – February 2026 on 03/06/26.
 - FWP 28.46: BenefitsCal Work Plan Monthly Updates – February 2026 on 03/06/26.
 - FWP 24.34: CX Bimonthly Report (Dec/Jan 2026) on 03/06/26.
- **Deliverable and Work Product submissions for the next reporting period:**
 - None for the Reporting period.

1.5 CRFI/CIT Communications

The following table outlines the CalSAWS Information Transmittals (CITs) for the reporting period.

Table 4: CITs

CIT ID	To	SUBJECT	DISTRIBUTION DATE	PRIMARY CALSAWS CONTACT	BACKUP CALSAWS CONTACT
0030-26	Notify.All; USBenefitsCalDevOps@Deloitte.com; Operator@CalHEERs.ca.gov; HoweG@CalSAWS.org; QuijadaP@CalSAWS.org; VenugopalanP@calsaws.org; Bill.Kelly@fisglobal.com; CalSAWS.All; Notify.SCATL.Outage; Consortium.RegionalManagers.All; Consortium.SectionDirectors; Communications.Infra@CalSAWS.org	Scheduled Downtime Notification – 3/15/2026	02/24/26	Communications.Infra@CalSAWS.org	Pete Quijada
0032-26	Notify.All; USBenefitsCalDevOps@Deloitte.com; Operator@CalHEERs.ca.gov; HoweG@CalSAWS.org;	Scheduled Downtime Notification – 3/22/2026	03/02/26	Communications.Infra@CalSAWS.org	Pete Quijada

CIT ID	To	SUBJECT	DISTRIBUTION DATE	PRIMARY CALSAWS CONTACT	BACKUP CALSAWS CONTACT
	QuijadaP@CalSAWS.org; VenugopalanP@calsaws.org; Bill.Kelly@fisglobal.com; CalSAWS.All; Notify.SCATL.Outage; Consortium.RegionalManagers.All; Consortium.SectionDirectors; Communications.Infra@CalSAWS.org				

The following tables outline the CalSAWS Requests for Information (CRFIs) for the reporting period.

Table 5: CRFIs

CRFI ID	To	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	PRIMARY CALSAWS CONTACT	BACKUP CALSAWS CONTACT
None.							

Table 6: Overdue CRFIs

CRFI ID	To	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	PRIMARY CALSAWS CONTACT	BACKUP CALSAWS CONTACT
None.							

1.6 Risks and Issues

1.6.1 Project Risks

This section includes a summary of the updates to open risks to the BenefitsCal Project as of the last calendar day of the reporting period. For more details and the history of each risk, please refer to the CalSAWS Consortium risk log here: [CalSAWS SharePoint > Risk Log](#)

Table 7: Project Risks

ID	TITLE	UPDATES FOR THE REPORTING PERIOD	STATUS	RISK LEVEL	DATE LOGGED
326	Lack of timely policy guidance may impact Medi-Cal HR1 delivery schedule	<ul style="list-style-type: none"> None for the reporting period 	Open	Medium	12/15/26

1.6.2 Project Issues


This section includes a summary of the updates to open issues for the BenefitsCal Project as of the last calendar day of the reporting period. For more details and the history of each issue, please refer to the CalSAWS Consortium issue log here: [CalSAWS SharePoint > Issues Log](#)


Table 8: Project Issues


ID	TITLE	UPDATES FOR THE REPORTING PERIOD	STATUS	PRIORITY	DATE LOGGED
None.					

1.7 Project Work Plan Reports

Project Timeline

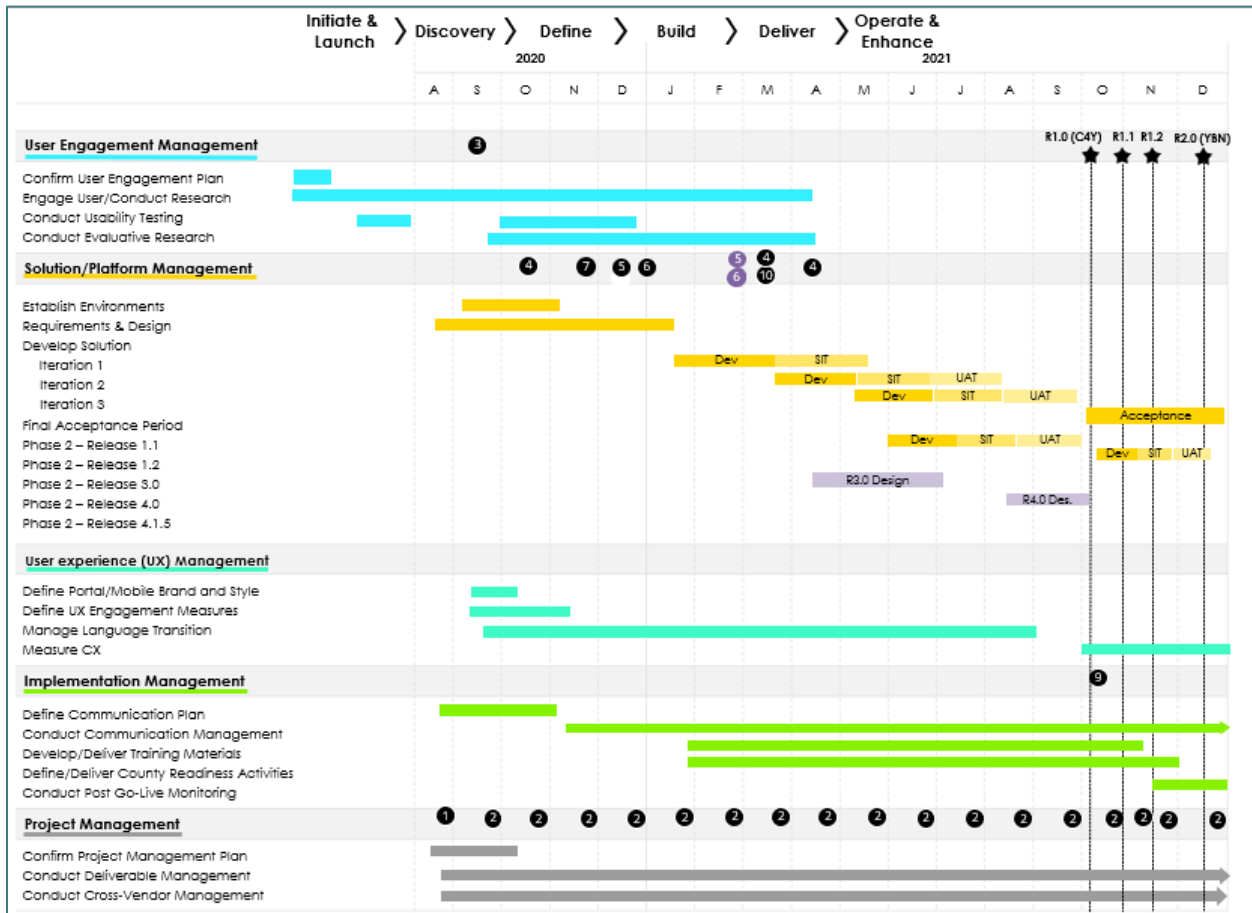

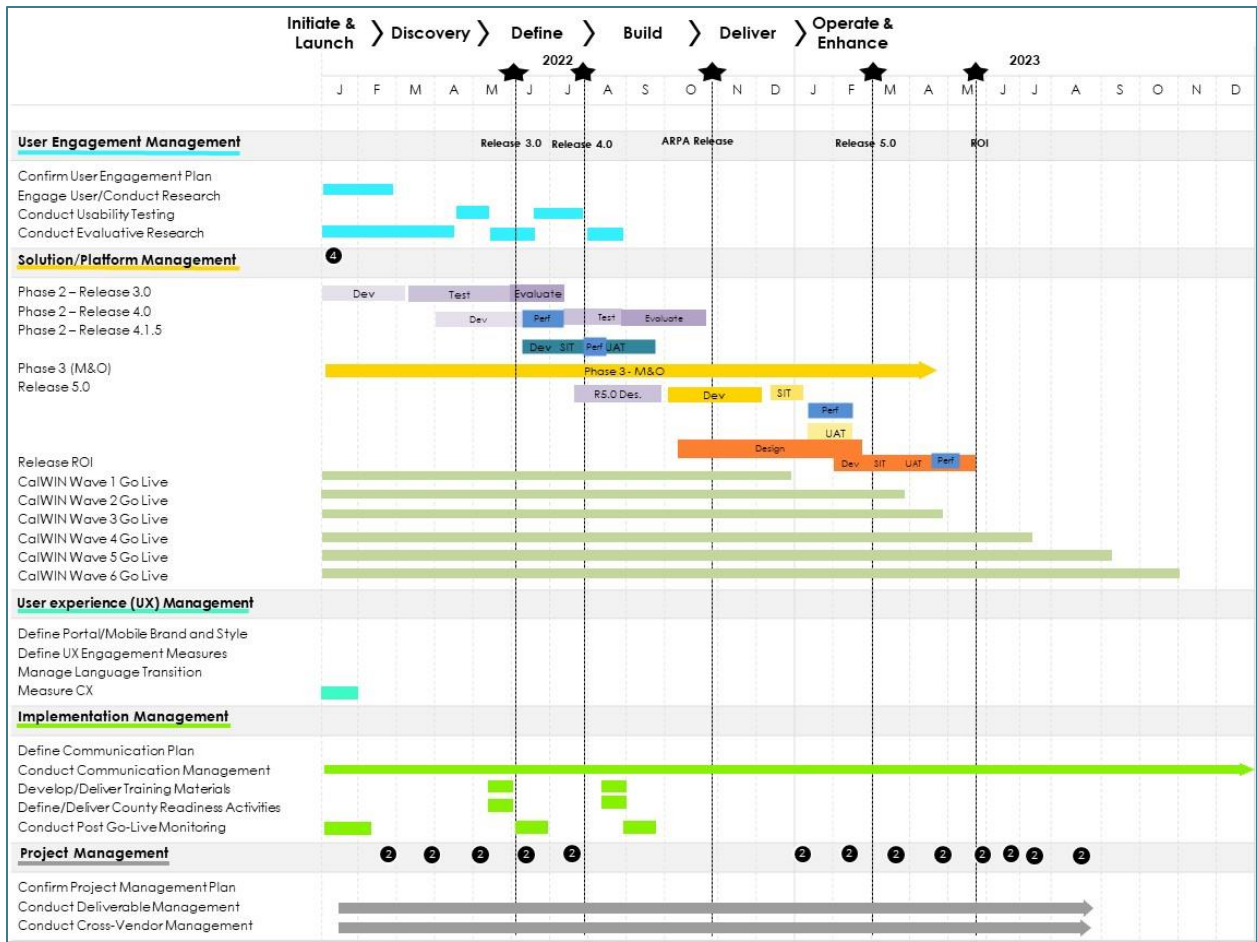

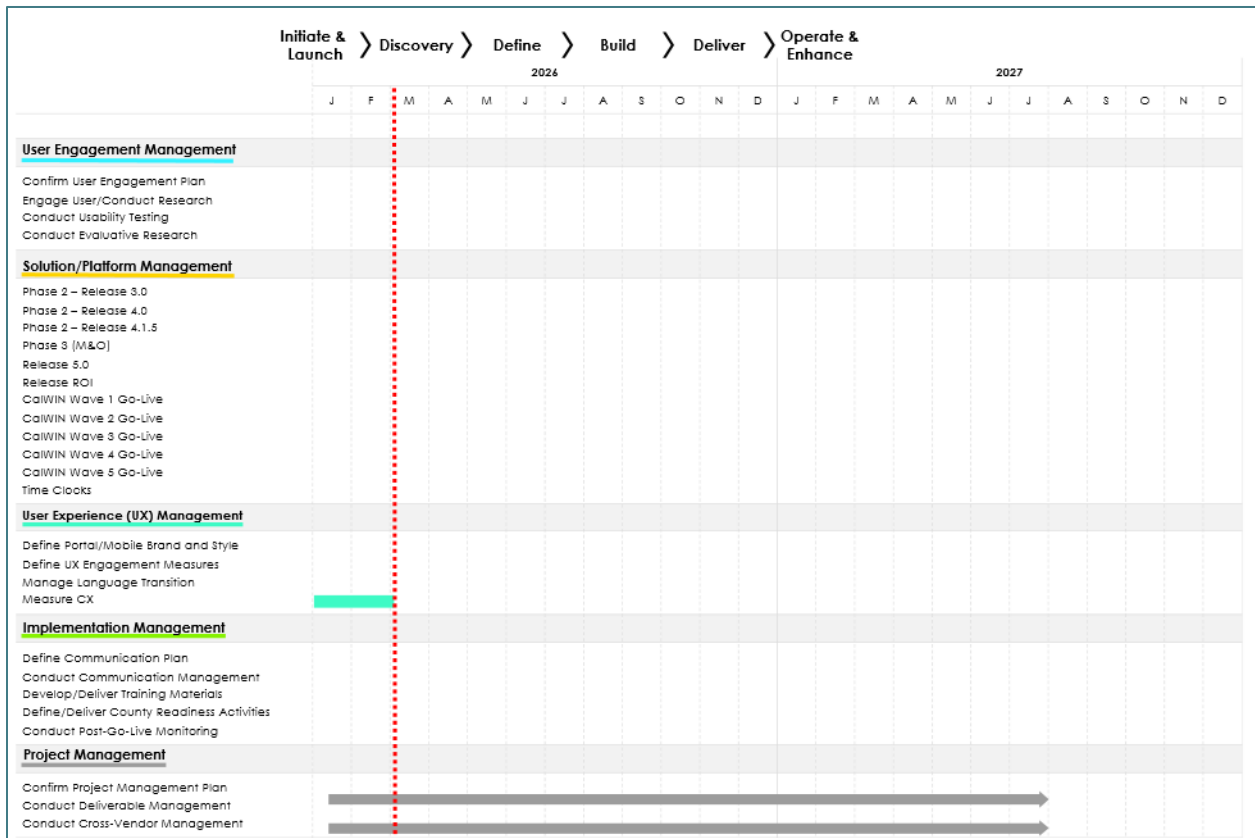

1.8 Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

Table 9: Overdue Action Items

ID	DESCRIPTION	OWNER	DUE DATE
None.			

1.9 SIRFRA/SCERFRA/SIRFRA/SARRA Information

The table below outlines the summary of SAWS Communication Information Requests for Research and Analysis (SCIRFRA), SAWS Cost Estimation Requests for Research and Analysis (SCERFRA), SAWS Information Request for Research and Analysis (SIRFRA), SAWS Advocates Request for Research and Analysis (SARRA), and Consortium Request for Policy (CRPC) activities for the reporting period.

Table 10: Summary of SCIRFRA/SCERFRA/SIRFRA/SARRA Requests

STATUS	TOTAL
Rejected/Duplicate	0
New/Assigned	10
Completed	13
Reopened	0
In Review	0
Withdrawn	0
TOTAL	23

Completed

- CSPM-75534: ROM for efforts associated with BenefitsCal adoption
- CSPM81507: SCERFRA 25-525 – BenefitsCal Income Verification Service
- CSPM-83113: SCERFRA 26-902 – Remove CalWORKs 100 Hour Rule Deprivation (AB 1755)
- CSPM-83140: CERFRA 26-904 – AB 1829 – Community Colleges: CalWORKs Recipients Education Program: Services
- CSPM-83112: SCERFRA 26-901 – AB 1049 – California Food Assistance Program: Sponsor Deeming Rules
- CSPM-83168: SIRFRA 1462 – Medi-Cal work or community engagement – AB2161
- CSPM-83154: SCERFRA 26-503 – New CalWORKs Stage One Child Care Post-Cash Aid Informing Notice
- CSPM-83221: SIRFRA 1463 – Deemed SSI Individuals
- CSPM-83227: SIRFRA 1465 – Medical: Eligibility Redetermination (AB 2201)
- CSPM-83268: SIRFRA 1470 – Eliminate Medi-Cal Expansion Freeze for Undocumented Individuals Ages 19 and Older (SB 1422)
- CSPM-83114: SCERFRA 26-903 - CalWORKs: Unrelated Adult Male (SB 1030)
- CSPM-83225: SIRFRA 1468 Cost Analysis – Collect and Report of Demographic Data for Jewish Identity (SB 1387)
- CSPM-83229: SIRFRA 1467 – Medi-Cal Strengthening Verification Protect the Promise Act (AB 2077)

New/Assigned

- CSPM-83226: SIRFRA 1464 - Data Collection: Sexual Orientation, Gender Identity, and Intersex Status: Disclosure (SB 1114)
- CSPM-83228: SIRFRA 1466 Unemployment insurance: Employment and Earning Data Reporting Requirements (SB 1054)
- CSPM-83239: SCERFRA 26-906 - AB 2765 – CalFresh and CalWORKs: Childhood Hunger and Foster Youth

- CSPM-83269: SCERFRA 26-905 - CalWORKs Family Reunification (AB 2510)
- CSPM-83275: SCERFRA 26-907 - CalFresh Contingency Fund (AB 2072)
- CSPM-83276: SIRFRA 1469 - Eliminating Food and Clothing from Income-In-Kind
- CSPM-83292: SIRFRA 1471 - Medi-Cal: Dashboard and Outreach (SB 1202)
- CSPM-83305: SCERFRA 26-908 - Collection and Reporting of Demographic Data: Jewish Identity (SB 1387)
- CSPM-83306: SCERFRA 26-911 - California Antihunger Response and Employment Training Act of 2026 (AB 2299)
- CSPM-83307: SCERFRA 26-912 - CalFresh: Veteran Eligibility (SB 1201)

1.10 Deviation from Plan/Adjustments

- None for the reporting period.

1.11 Transition-Out

The figure below provides a summary of the transition-out progress with the incoming contractor, highlighting transition sessions, access and document requests, and risks and issues.



Figure 1: Transition-Out Status Summary

2 BENEFITSCAL COLLABORATION MODEL (CM)

▪ Activities from the Reporting Period

Prioritization in progress for items prioritized in Q4 2023, Q1 2024, and Q2 2024. (They have already been logged in to Jira.)

The table below contains the current enhancements prioritized by CM in any quarter and their updates.

Table 11: Enhancements Updates, Prioritized by CM

ISSUE TYPE	ID	SUMMARY	STATUS	UPDATE THIS WEEK
Enhancements	CSPM-68370	Collaboration Model: Leverage email communication and interactions	Prioritization Needed	Tentatively Prioritized for June 2026

- **Activities for the Next Reporting Period**
 - Prioritize Collaboration Model Items for future releases.
 - Perform design, development, and implementation analysis for enhancements and research action items identified in the Collaboration Model.

3 MAINTENANCE AND OPERATIONS

- **Operational Support**
 - Provided operational support for manual reprocessing of a transaction between CalSAWS **and** BenefitsCal.
- **CFA Meeting**
 - None for the reporting period.
- **Daily Partner Coordination Meetings**
 - Conducted daily partner coordination meetings with CalSAWS covering design, development, testing, and release management for defects and enhancements impacting both systems along with production observations.
- **M&O Phases**
 - Completed the initial acceptance period and moved into Maintenance and Operations.

3.1 Service Management

3.1.1 Overview

- **Incidents Created**
 - Five (5) incidents were created in the biweekly reporting period for the BenefitsCal Tier 3 Team.
- **Incidents Resolved**
 - The BenefitsCal Tier 3 Team resolved three (3) incidents in the biweekly reporting period.
- **Incidents Closed**
 - The BenefitsCal Tier 3 Team closed one (1) incident in the biweekly reporting period.
- **Incidents Triaged**
 - The BenefitsCal Tier 3 Team has triaged four hundred and fifty-seven (457) incidents in the biweekly reporting period.
- **Problems Created**
 - The BenefitsCal Tier 3 Team created one (1) problem ticket in the biweekly reporting period.
- **Problems Resolved**
 - The BenefitsCal Tier 3 Team resolved zero (0) problem tickets in the biweekly reporting period.

3.1.2 BenefitsCal Help Desk Metrics

The charts below represent incidents created, resolved, and triaged within the reporting period. If a week is not shown within a particular chart, it is because there were no incidents to report for that week.

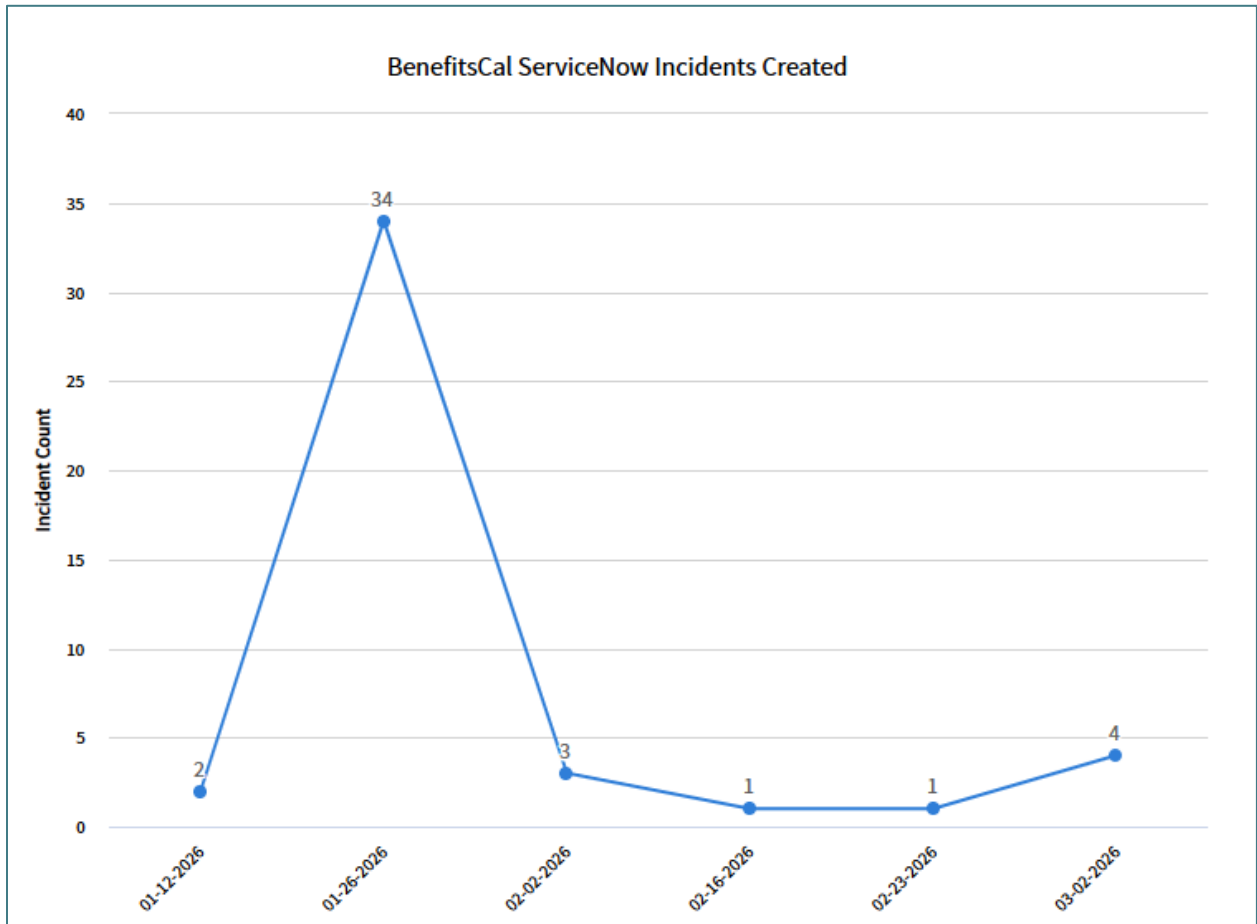


Figure 2: BenefitsCal ServiceNow Incidents Created

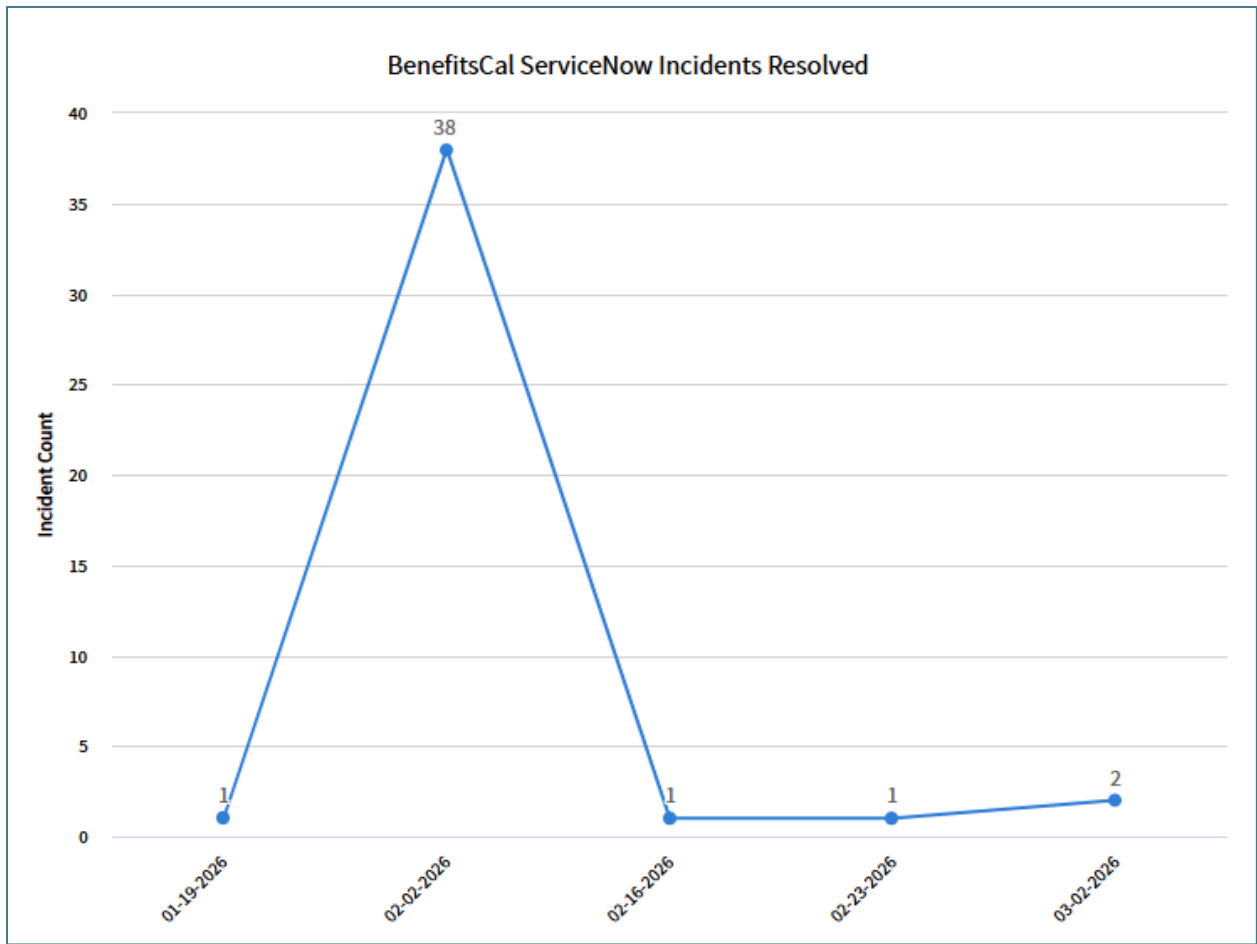


Figure 3: BenefitsCal ServiceNow Incidents Resolved




Figure 4: BenefitsCal ServiceNow Incidents Closed

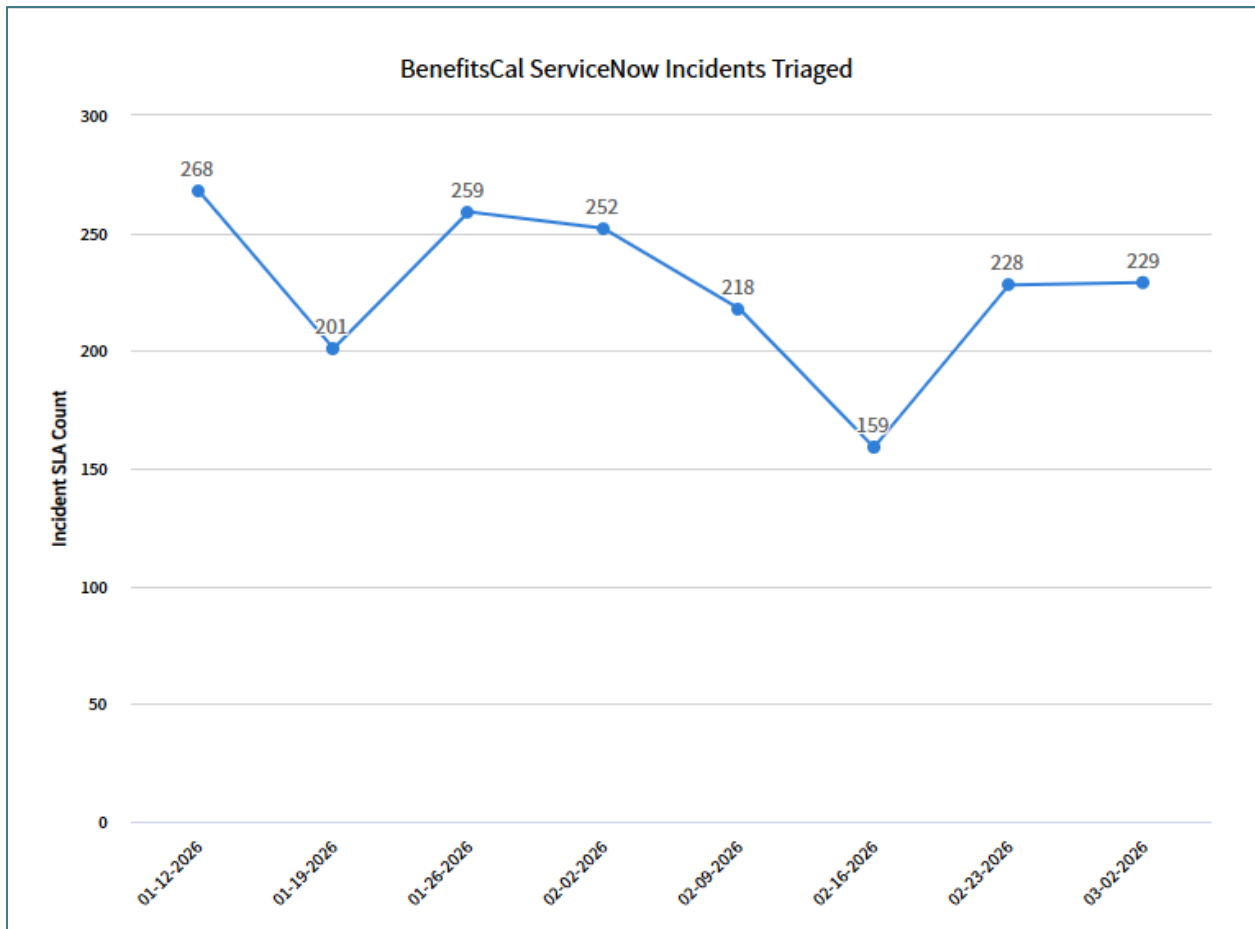


Figure 5: BenefitsCal ServiceNow Incidents Triaged

Note: The graphs above represent the ServiceNow incidents associated to all 58 Counties. Incidents represent the first level of ticketing that enters the ServiceNow system. The dates on the x-axis represent the start of week. The metrics does not include "Tier 3 App Support – BenefitsCal Questions (DLT)."

The charts below represent problems created, resolved, and triaged within the reporting period. If a week is not shown within a particular chart, it is because there were no problems to report for that week.

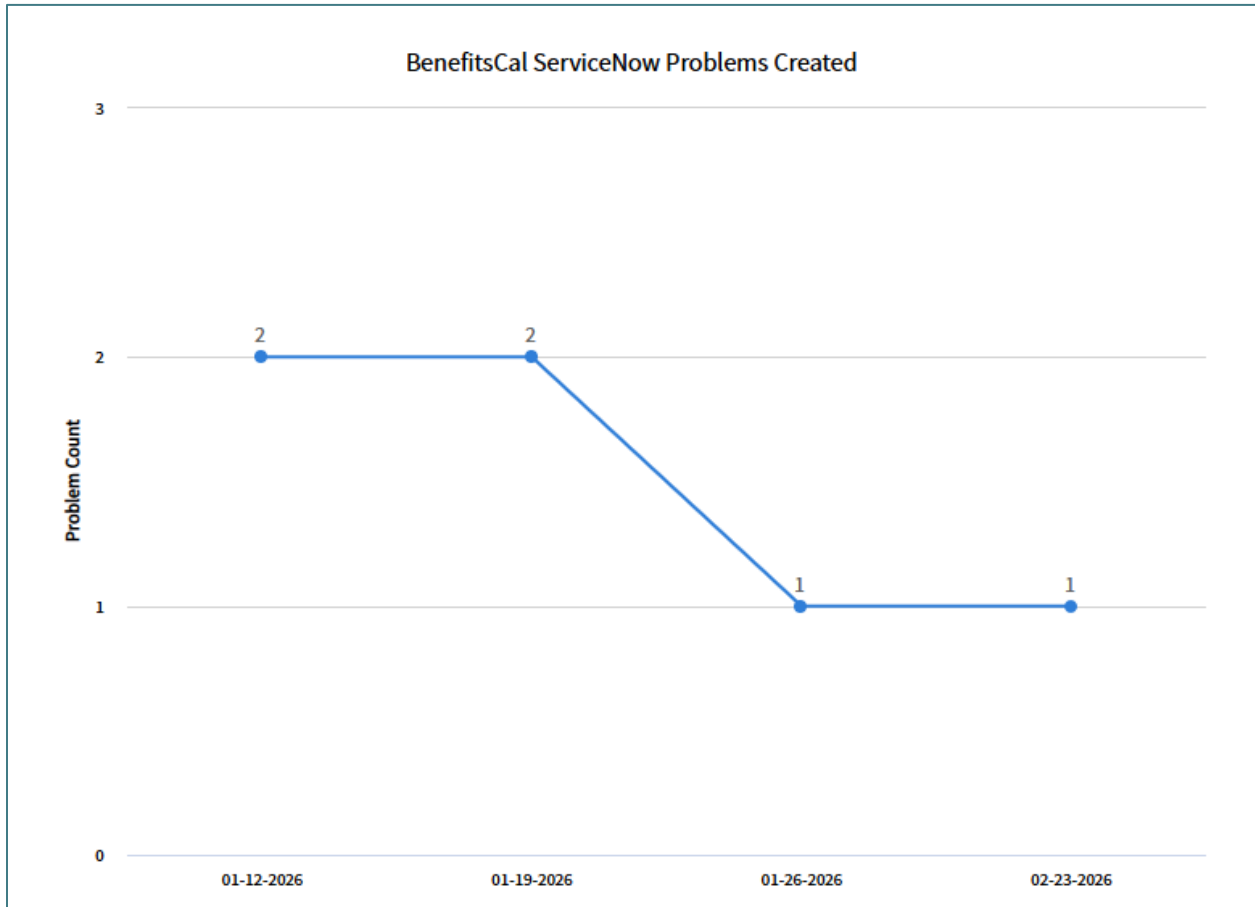


Figure 6: BenefitsCal ServiceNow Problems Created

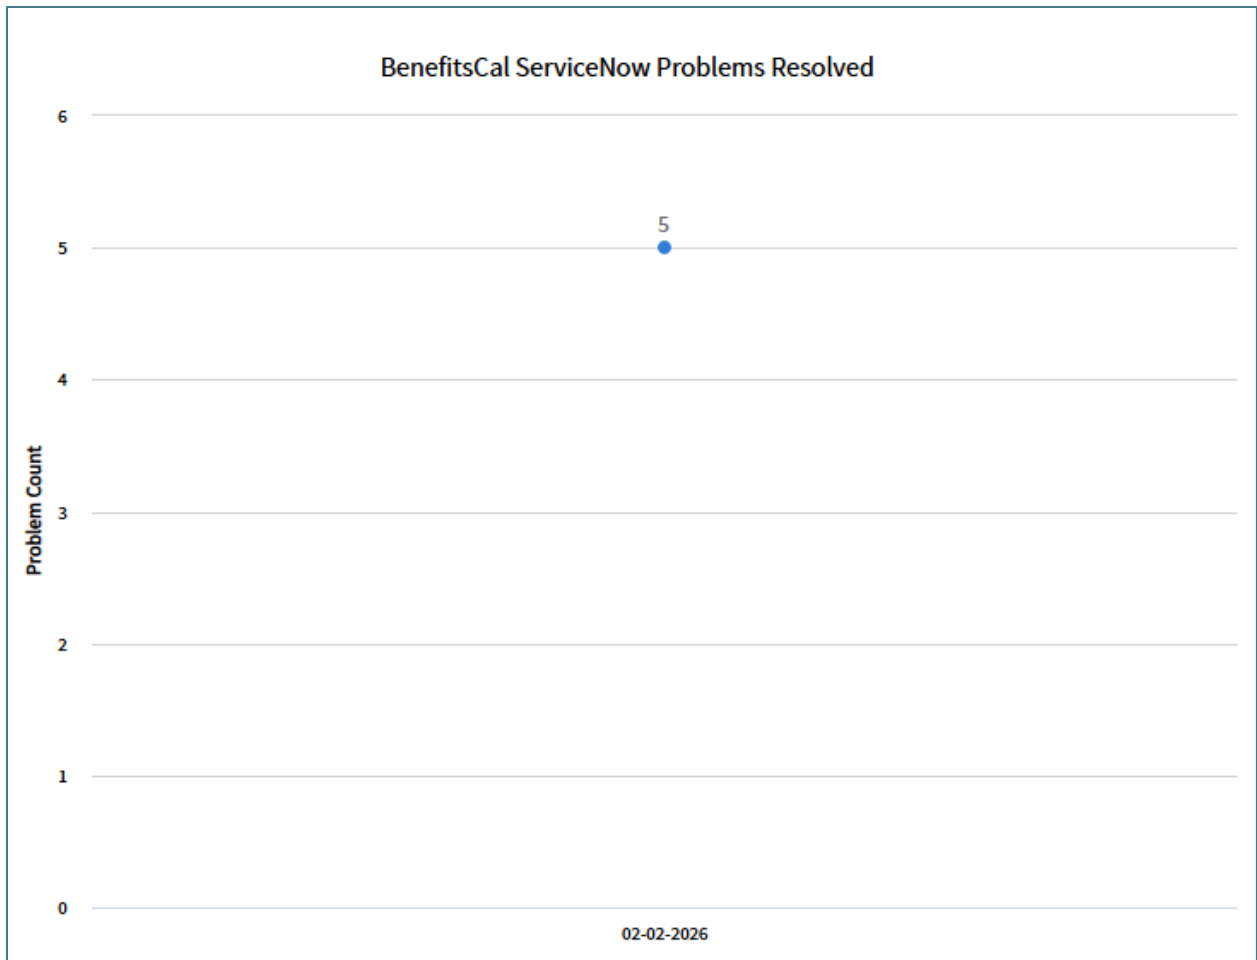


Figure 7: BenefitsCal ServiceNow Problems Resolved

Note: The graphs above represent the ServiceNow problems associated to 58 Counties. Problems represent issues that can have a many to one relationship with incidents and the last step in escalation. The dates on the x-axis represent the start of a week.

BenefitsCal ServiceNow Incidents by State and Age


State	Aging Category	1-5 Days	11-15 Days	16-30 Days	30-60 Days	60-180 Days	>180 Days	Count
	New		4	0	0	0	0	0
On Hold		0	1	0	1	0	0	2
Resolved		0	0	1	1	0	0	2
Closed		0	81	559	193	158	4	995
Count		4	82	560	195	158	4	1,003

Aging "State" definitions:

NEW	Incident triage not started.
IN PROGRESS	Incident triage in progress.
ON HOLD	Incident triage paused – awaiting information/problem.
RESOLVED	Incident triage completed providing steps for resolution.
CLOSED	Incident triage completed after a defect fix or change request implementation.

Figure 8: BenefitsCal ServiceNow Incidents by State and Age

BenefitsCal ServiceNow Incidents by Resolution Code

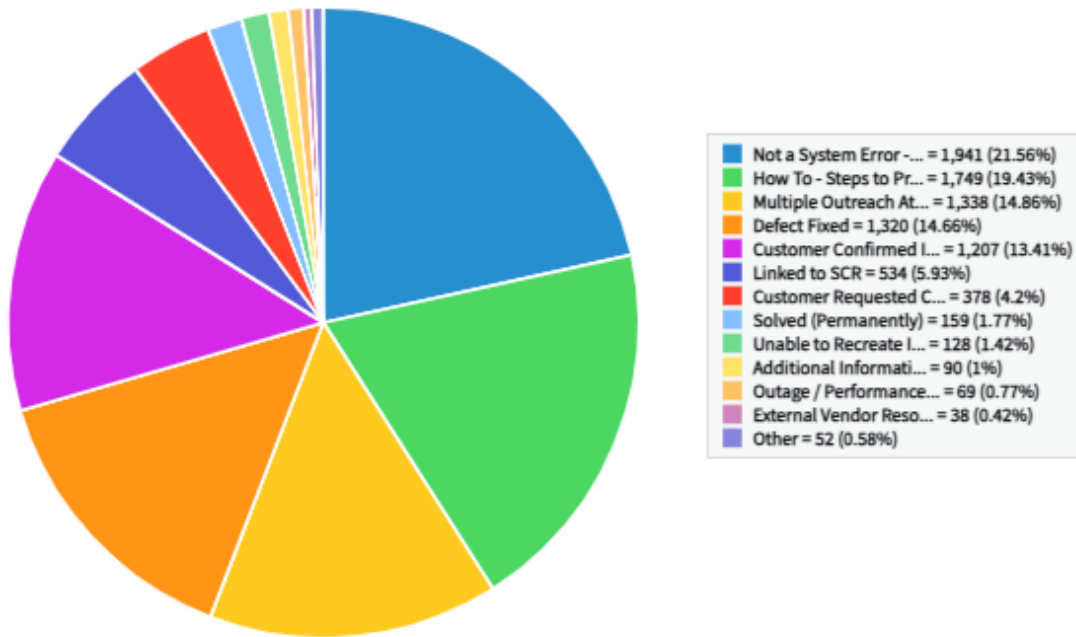

Resolution code	Incident SLA Count	Percentage of Incident SLAs
Not a System Error - With Explanation	1,941	21.56%
How To - Steps to Proceed Provided	1,749	19.43%
Multiple Outreach Attempts - No Response	1,338	14.86%
Defect Fixed	1,320	14.66%
Customer Confirmed Issue is Resolved	1,207	13.41%
Linked to SCR	534	5.93%
Customer Requested Closure	378	4.2%
Solved (Permanently)	159	1.77%
Unable to Recreate Issue	128	1.42%
Additional Information Needed	90	1%
Outage / Performance Degradation	69	0.77%
External Vendor Resolved	38	0.42%
Other	52	0.58%
Total	9,003	100%

Figure 9: BenefitsCal ServiceNow Incidents by Resolution Code

Note: The pie chart above represents Incidents resolved since BenefitsCal Go-Live on 09/27/21.




Figure 10: BenefitsCal ServiceNow Incidents Created by Category

Note: The pie chart above represents Incidents by category created since BenefitsCal Go-Live on 09/27/21. The “Other” category will cover incidents related to BenefitsCal module such as Dashboard, Help Center, Homepage, Report a Change, Application Summary.

3.2 Technology Operations

The BenefitsCal technology operations team provides Amazon Web Services (AWS) serverless infrastructure and BenefitsCal application support. Upgrades and changes to the infrastructure and application are performed following the Consortium change control process. AWS serverless infrastructure support activities include upgrades to AWS components such as the Web Application Firewall (WAF), CloudFront, Application Programming Interface (API) Gateway, Lambdas, Simple Queue Service (SQS), CloudWatch, X-Ray and Aurora Postgres, Postgres Relational Database Service (RDS), and RDS Proxy. Application maintenance and support include release and configuration management across the non-production and production environments.

3.3 BenefitsCal Maintenance and Operations

Table 12: BenefitsCal Outages

SCHEDULED DATE	OUTAGE TIMEFRAME	ACTIVITY DESCRIPTION
02/26/26	8:00 pm – 9:30 pm PST	BenefitsCal Production Deployment – 26.02.26

Table 13: BenefitsCal Upcoming Maintenance

SCHEDULED DATE	OUTAGE TIMEFRAME	APPLICATION MODE
03/26/26	8:00 pm – 9:30 pm PST	BenefitsCal Production Deployment – 26.03.26

3.4 Production Defect Backlog

The Production defect backlog bar chart depicts the balance of open (unresolved Production defects assigned to present months production release – Red and closed defects – Green), month-over-month. Defects are closed upon system test validation and release of deployment to Production.

Recently Created Chart: BC_PRD_Defects_All_v1

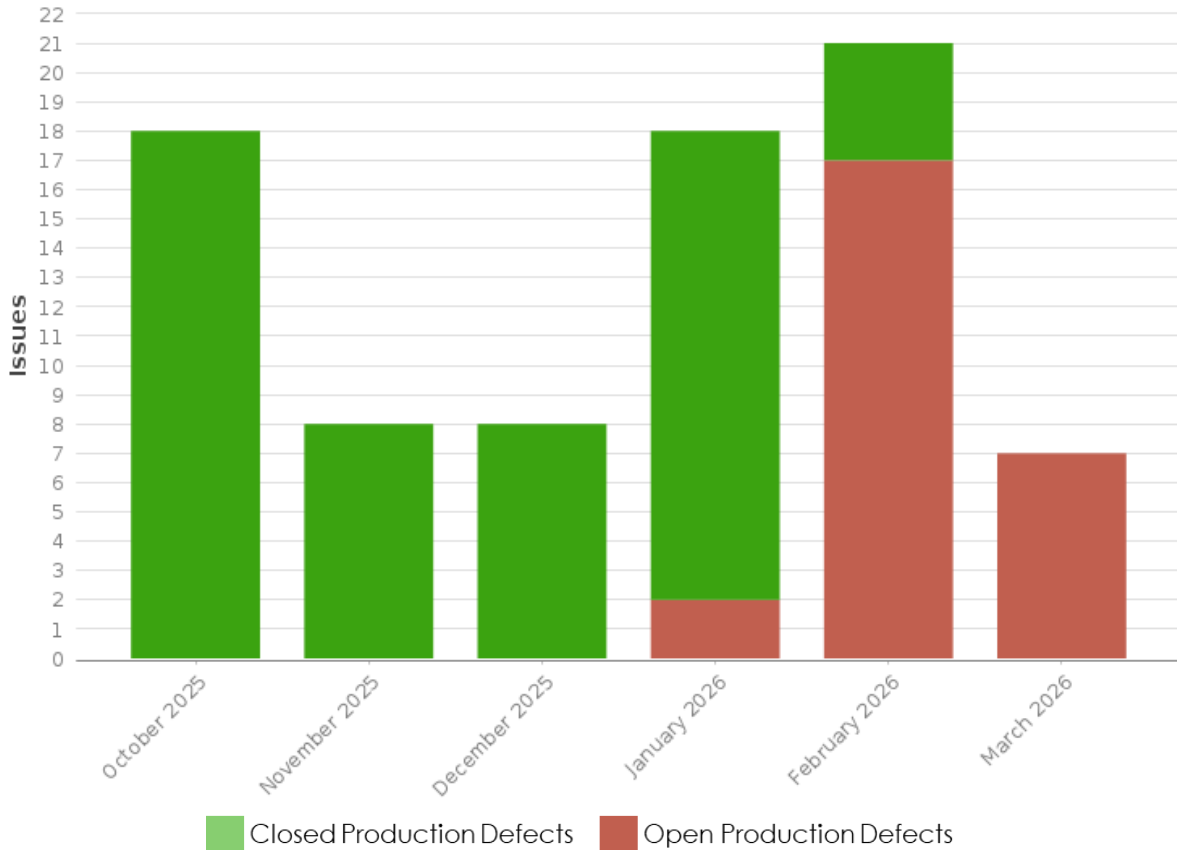


Figure 11: Production Defects Backlog Monthly Trend

3.4.1 Release Schedule Production Defect Fix

Table 14: Production Defect Fix – Release Schedule

SEVERITY	RELEASE 26.03.26	RELEASE 26.04.30	RELEASE TBD	TOTAL
1-HIGH	0	0	0	0
New	0	0	0	0
In Progress	0	0	0	0
Closed	0	0	0	0
2-NORMAL/MEDIUM	0	0	0	0
New	0	0	0	0
In Progress	0	0	0	0
Closed	0	0	0	0
3-NORMAL/LOW	19	11	1	31
New	0	0	0	0
In Progress	19	11	1	31
Closed	0	0	0	0
4-COSMETIC	0	0	0	0
New	0	0	0	0
In Progress	0	0	0	0
Closed	0	0	0	0
TOTAL	19	11	1	31

3.5 Production Operations

- **Root Cause Analysis (RCA)**
 - None for the reporting period.

3.6 Deviation from Plan/Adjustments

- None for the reporting period.

4 APPLICATION DEVELOPMENT AND TEST

4.1 Priority Release Summary

This section outlines the scope of defect fixes included in each ad-hoc priority release deployed in this reporting period.

- **BenefitsCal Monthly Release**
 - Six (6) enhancements and seventeen (17) defects were deployed with BenefitsCal Monthly Release 26.02.26 for User Error Handling, Exception Handling, and Application Summary
- **BenefitsCal Priority Release**
 - None for the reporting period.
- **BenefitsCal Emergency Release**
 - None for the reporting period.

Table 15: BenefitsCal Upcoming Releases

RELEASE	RELEASE DATE	SUMMARY
26.03.26 – Monthly	03/26/26	Four (4) enhancements and nineteen (19) production defects are planned for User Error Handling, Exception Handling, and Application Summary.

4.2 Requirements and Design

- **Activities for the Reporting Period – Requirements and Design**
 - **Designs and Design Meetings**
 - ♦ Finalized design work for the March 2026 enhancements.
 - ♦ Began design work for the April 2026 enhancements.
 - ♦ Attended the Project Milestone meetings with the Consortium and CalSAWS on 02/23/26 and 03/02/26.
 - ♦ Attended CA-266966 Design Review – BenefitsCal on 02/23/26.
 - ♦ Hosted Discuss CA-297870 Modified LA Form Names on 02/23/26.
 - ♦ Attended REST API enhancement direction / timeline on 02/24/26.
 - ♦ Hosted CalSAWS, Hyland, and BenefitsCal Connect: CA-297870 Modified LA Form Names on 02/24/26.
 - ♦ Hosted the DDI and M&O Biweekly meetings on 02/24/26, 02/26/26, 03/03/26, and 03/05/26.
 - ♦ Attended the Internal ABAWD Changes discussions on 02/24/26, 02/27/26, 03/03/26, and 03/06/26.
 - ♦ Hosted Medi-Cal Workgroup Internal Prep Call on 02/24/26.
 - ♦ Hosted ABAWD Review Workgroup - Session 3 Closeout/Next Steps on 02/25/26.
 - ♦ Hosted the BenefitsCal PM Standup Meetings with the Consortium on 02/25/26 and 03/04/26.
 - ♦ Attended Truv Workgroup Milestone 2 on 02/26/26.
 - ♦ Attended Truv and CalSAWS on 02/26/26 and 03/05/26.
 - ♦ Attended Medi-Cal Advocate Workgroup State Partner Review on 02/26/26.

- ♦ Attended 26.03 Project Integrated Readiness Areas - T-3 Integrated Readiness Status on 03/02/26.
 - ♦ Hosted UCD and CX Check-in on 03/03/26.
 - ♦ Attended the DHCS CalSAWS Touchpoint Meeting on 03/04/26.
 - ♦ Hosted Medi-Cal Workgroup Kick-off-Milestone 1 on 03/05/26.
 - ♦ Hosted the BenefitsCal Pipeline Call – New Series on 03/05/26.
- **Activities for the Next Reporting Period – Requirements and Design**
 - **Designs and Design Meetings**
 - ♦ Continue design work for the April 2026 enhancements.
 - ♦ Attend the Project Milestone meetings with the Consortium and CalSAWS on 03/09/26 and 03/16/26.
 - ♦ Host the DDI and M&O Biweekly meetings on 03/10/26, 03/12/26, 03/17/26, and 03/19/26.
 - ♦ Attend the Internal ABAWD Changes discussions on 03/10/26, 03/13/26, 03/17/26, and 03/20/26.
 - ♦ Attended KT - Session 3-3 - SCR – GSD on 03/10/26.
 - ♦ Host the BenefitsCal PM Standup Meetings with the Consortium on 03/11/26 and 03/18/26.
 - ♦ Attend Truv & CalSAWS on 03/12/26 and 03/19/26.
 - ♦ Attend 26.03 Pre-Green Light Review on 03/16/26.
 - ♦ Attend CalSAWS Virtual Greenlight Release 26.03 on 03/18/26.
 - ♦ Attend DHCS CalSAWS Touchpoint Meeting on 03/18/26.
 - ♦ Host CalFresh Processing/Error Rate Improvement: Session 4 on 03/19/26.
 - ♦ Host BenefitsCal Pipeline Call – New Series on 03/19/26.

4.3 User Centered Design (UCD)

- **Activities for the Reporting Period – UCD**
 - **Customer Experience (CX) Measurements Data**
 - ♦ Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
 - ♦ Started February Always on survey data.
 - **User Engagement**
 - ♦ Conducted CBO assister session for Help Center.
 - ♦ Finalized synthesis for combined stakeholder Help Center findings (county worker sessions, combined advocate and state partner session, and CBO assister session).
 - ♦ Continued synthesis for Truv customer sessions.
 - **Enhancements**
 - ♦ Continue analysis on CSPM-80929: *H.R. 1 – Big Beautiful Bill – Semi-Annual Redeterminations for MAGI New Adult Group*.
 - ♦ Started ideation and consolidation of requirements from workgroup for CSPM-81960: *Truv Phase 1 & 2*.
 - ♦ Started realigning approach for CSPM-66458: *CM Browser Back Button*.
 - ♦ Finalized updates to designs for *Digitize NA-1273*.

- **Advocate Engagement**
 - ◆ Conducted Truv Workgroup session 2.
 - ◆ Started drafting February UCD comment log responses.
 - ◆ Started drafting March UCD monthly deck.
 - ◆ Conducted internal review of March UCD monthly deck.
- **Activities for the Next Reporting Period – UCD**
 - **CX Measurements Data**
 - ◆ Monitor the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
 - ◆ Continue analyzing February Always on survey data.
 - **Enhancements**
 - Continue analysis on *CSPM-80929: H.R. 1 – Big Beautiful Bill – Semi-Annual Redeterminations for MAGI New Adult Group*.
 - Start initial design conversation including ideation and conceptualization for *CSPM-81960: Truv Phase 1 & 2*.
 - **User Engagement**
 - ◆ Finalize synthesis for Truv customer sessions.
 - **Advocate Engagement**
 - ◆ Share out February UCD monthly comment log responses.
 - ◆ Conduct reviews of March UCD monthly deck.

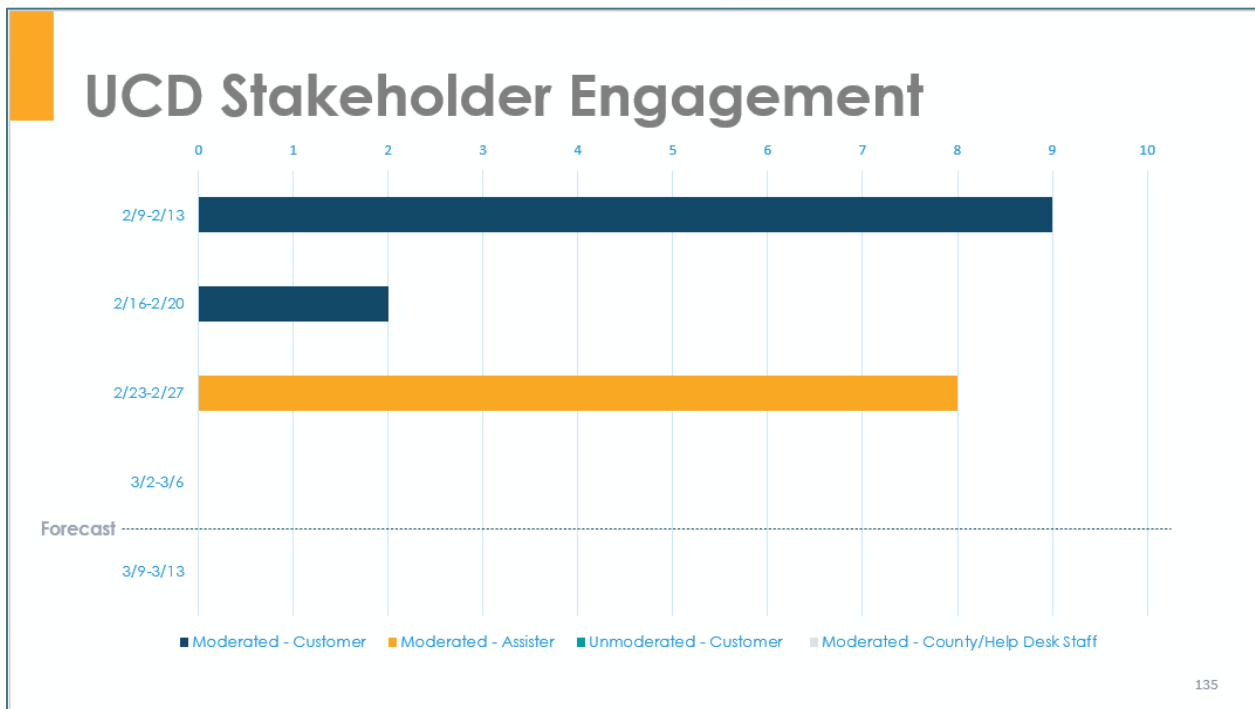


Figure 12: UCD Stakeholder Engagement

4.4 Development

- **Activities the Reporting Period – Development**
 - Enhancements (M&E)

Table 16: Enhancement Actuals for Reporting Period

RELEASE	PLANNED FOR WEEK ENDING 03/06/26	ACTUAL FOR WEEK ENDING 03/06/26	TOTAL PLANNED FOR THE RELEASE	COMMENTS
Release 26.03.26	0	0	4	Release 26.03.26 is planned for deployment on 03/26/26.

- **Activities for the Next Reporting Period – Development**
 - Enhancements (M&E)

Table 17: Planned Enhancement Work

RELEASE	PLANNED FOR WEEK ENDING 03/20/26	TOTAL PLANNED FOR THE RELEASE	TOTAL COMPLETED FOR THE RELEASE	COMMENTS
Release 26.03.26	2	4	0	Release 26.03.26 is planned for deployment on 03/26/26.
Release 26.04.30	0	1	0	Release 26.04.30 is planned for deployment on 04/30/26.

- **Unscheduled Release Updates**
 - **Chatbot**
 - ♦ Reported the issues for Chinese, Japanese, and Korean languages to AWS, and have received confirmation that these issues have been resolved.
 - ♦ Engaging with native speakers to conduct thorough testing of the bot. Following their validation, we will collaborate with the AWS team to address any further issues that may arise.

4.5 User Acceptance Test (UAT) Planning

- **Activities for the Reporting Period – User Acceptance Test Planning**
 - **UAT Test Execution**
 - ♦ Defects and Enhancements for Release 26.02.26 were validated.
 - ♦ Defects and Enhancements for Release 26.03.26 were validated.
 - **Test Support**
 - ♦ Provided clarification and support to the QA/Consortium/Independent Test Team for defects and enhancements tagged to Release 26.02.26.
 - ♦ Provided clarification and support to the QA/Consortium/Independent Test Team for defects and enhancements tagged to Release 26.03.26.
- **Activities for the Next Reporting Period – User Acceptance Test Planning**
 - **UAT Test Execution**
 - ♦ Defects for Release 26.03.26 will be validated.

- **Test Support**
 - ♦ Clarification and Support will be provided to the QA/Consortium/Independent Test Teams for defects tagged to Release 26.03.26.

4.6 Release Management

- **Activities for the Reporting Period – Release Management**
 - **Release 26.02.26– February Monthly Release**
 - ♦ Deployed the February Monthly Release – 26.02.26 in Production on 02/26/26.

4.7 System Test Execution

- **Activities for the Reporting Period – System Test Execution**
 - **Release 26.02.26– February Monthly Release**
 - ♦ Validated tickets tagged to the February Monthly Release – 26.02.26.
 - **Release 26.03.26– March Monthly Release**
 - ♦ Validated tickets tagged to the March Monthly Release – 26.03.26.

4.7.1 Automated Regression Test (ART) Coverage

The following are the automated regression scripts executed for regression in BenefitsCal for Release 26.02.26.

Table 18: Automated Regression Scripts Executed in BenefitsCal

RELEASE	# OF SCENARIOS EXECUTED	# OF SCENARIOS PASSED	# OF SCENARIOS FAILED	OVERALL PASS %	PASS OF EXECUTED	COVERAGE
26.02.26	57	57	0	100	100	CalFresh (CF), CalWORKs, Medi-Cal (MC), General Assistance or General Relief (GA/GR), and Disaster CalFresh programs with the Apply for Benefits, Report Change, Renewal, and Recertification for the MC, CF, GA/GR, and SAR 7 flows, IRT (Income Reporting Threshold), TWM along with Appointments, Administrative, Time Clock, ROI and SSA not enabled, E-Signature, Global Search, static validations, EBT2259 and CF303 are covered by automated regression. We will also validate the following flows with data in every field – AFB with all programs, CF37, DCF, MC 210, Redet CWF, MC 216, MC 217, CF Only AFB, GA/GR, Redet CW, CW

RELEASE	# OF SCENARIOS EXECUTED	# OF SCENARIOS PASSED	# OF SCENARIOS FAILED	OVERALL PASS %	PASS OF EXECUTED	COVERAGE
						Only AFB, MC Only AFB, RAC, SAR 7, Bulk Doc Upload

Note: Automated regression tests are run for each planned release. Automated regression tests are excluded for emergency releases as the window for execution is short. The regression suite is revisited after each major release and periodically updated once new application functionality has been released. The update could be adding a new script to the repository or modifying an existing script to cover new functionality since the new functionality replaces the old functionality. New functionality will be called out in the coverage column.

5 PERFORMANCE TEST

5.1 Performance Test

Release 26.03.26 – March Monthly Release

- The BenefitsCal March performance testing scope includes two (2) enhancements and nine (9) defects: CSPM-81068: *Technical: Update Case Link Logic to not de-link existing account until verified*, CSPM-82293: *Update the Apply for Benefits flow to accurately capture pregnancy information*, CSPM-83003, CSPM-83094, CSPM-83095, CSPM-83098, CSPM-83101, CSPM-83102, CSPM-83103, CSPM-83104, and CSPM-83118 respectively. The performance testing team will update the impacted scripts on the latest codebase to reflect the enhancements and defect changes, ensure all other scripts work as expected, and plan the performance tests as per the schedule below.

Table 19: Performance Test Cycles and Test Case Status

CYCLE	START DATE	END DATE	SCOPE	TEST CASES STATUS	EXECUTION STATUS
15	03/02/26	03/24/26	Release 26.03.26 March Monthly	Scope: Two (2) enhancements and nine (9) defects in scope. Executions: BenefitsCal isolated Load tests with mock services. <ul style="list-style-type: none"> Friday, March 20 Monday, March 23 	30%

5.2 Training Materials Update

- None for the reporting period.

5.3 Deviations from Plan/Adjustments

- None for the reporting period.

5.4 Security

▪ Activities for the Reporting Period – Security

- [REDACTED]
- ♦ [REDACTED]

• DAST

- ♦ Executed the biweekly Dynamic Application Security Testing (DAST) manual penetration testing test cases and shared the analysis of the security scan reports with the BenefitsCal Development Team on 03/06/26.

- [REDACTED]
- ♦ [REDACTED]

▪ Activities for the Next Reporting Period – Security

- [REDACTED]
- ♦ [REDACTED]

• AWS SSO (Single Sign-On) for BenefitsCal

- ♦ Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.
