



Transition Update

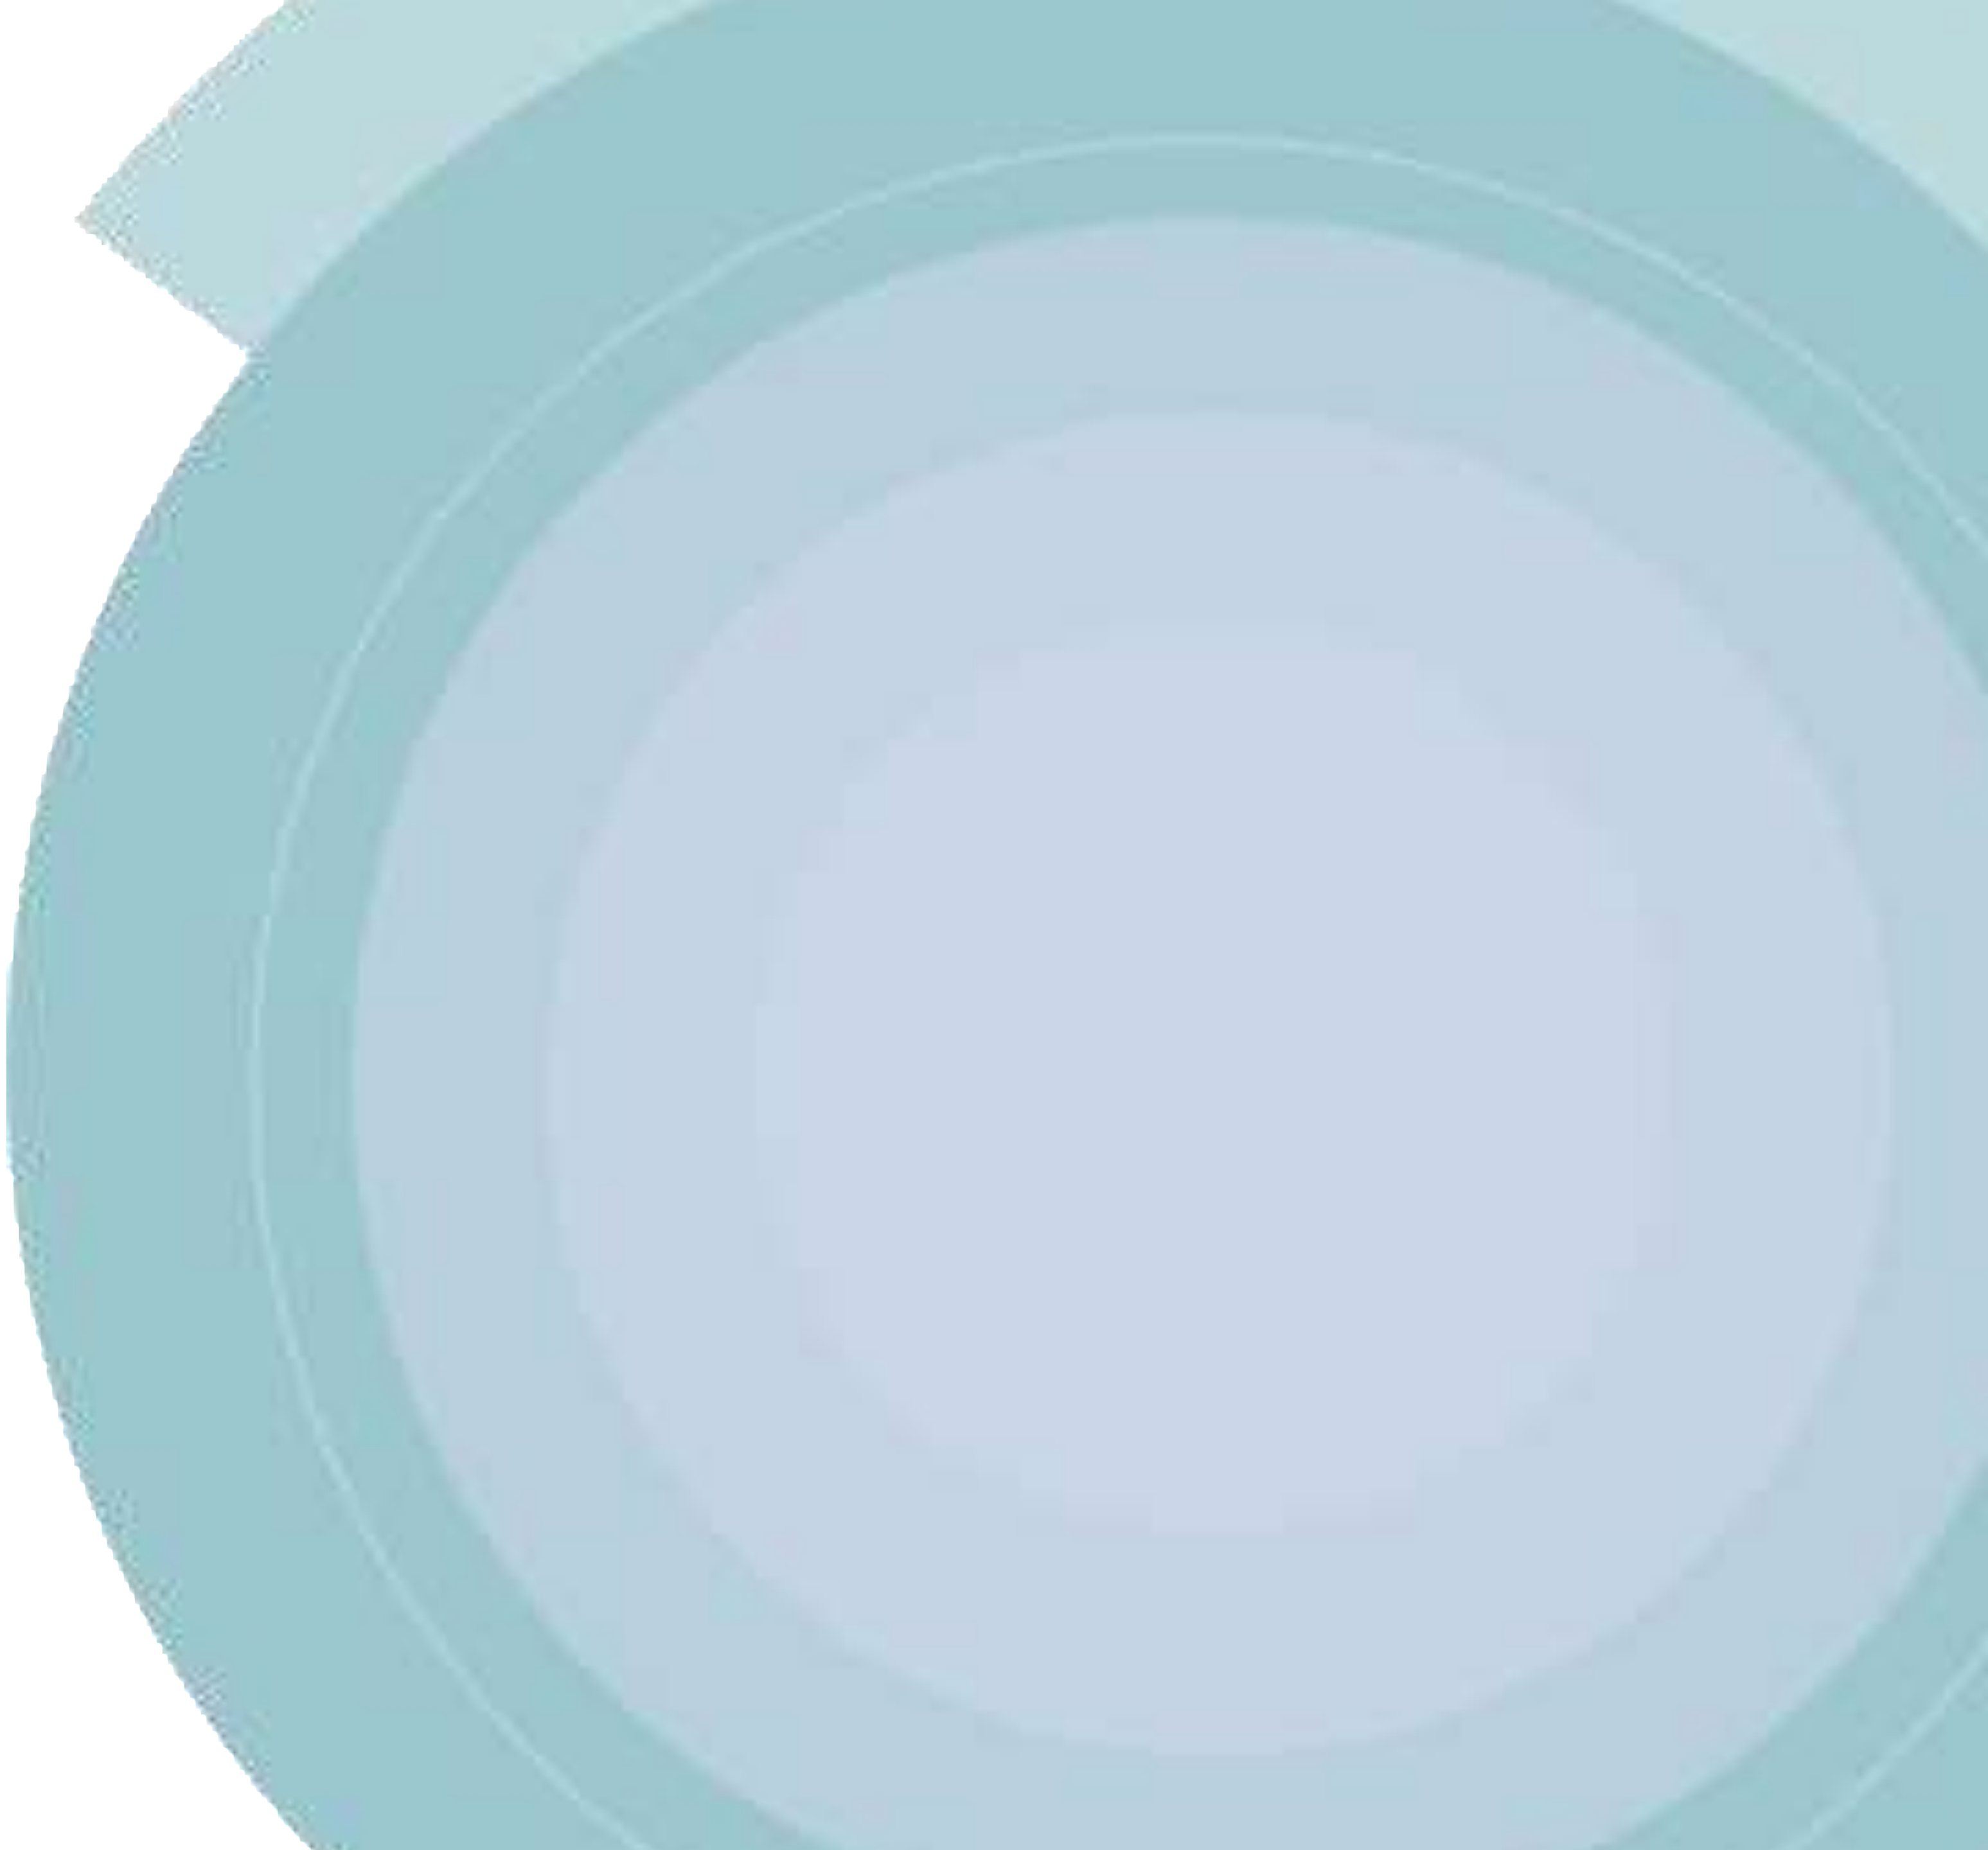

BenefitsCal Transition

Timeline

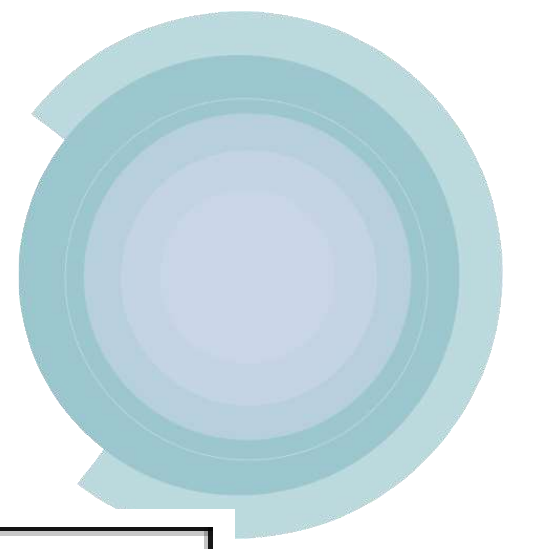

	FEB	MAR	APR	MAY	JUN	JUL	AUG
Group 1							
02-Project Management		KT					
05-Support Services	KT	JS	RJS	Cutover			
Readiness Review			Cutover Group 1				
Group 2							
07-Prod Ops		KT		JS		RJS	
08-Tech Recovery		KT	JS				Cutover
09-Security	KT				RJS		
Readiness Review		JS				Cutover Group 2	
Group 3							
01-Transition-In	TIMP and TIWS						
Training & KT	KT, JS and RJS across all workstreams						
Service & Function Migration	KT, JS and RJS across all workstreams						
Test and Validation					Validation		
03-SCR	KT			JS			Cutover
				Design / Test RJS	Build / Test RJS	Test / Deplmt RJS 26.6	
Readiness Review						Cutover Group 3	



BenefitsCal Transition

Highlights

- KT Sessions: 100% Complete (87 total)
- JS Sessions: 76% Complete

- RJS Sessions: commenced on 5/4/2026
 - SCR design
 - SCR test
 - Tier 3 support
 - Security

Risk #327 Limited Availability of Deloitte Staff May Impact the BenefitsCal Transition Schedule.

1. Reduced from a High risk to a Medium Risk.

Issue #335: Schedule Delay in BenefitsCal SCR Job Shadow Workstream. Mitigations are in place and will monitor through 5/30/2026. Issue created from risk #327

Risk #329: Delay in Providing Accenture Team Timely Access May Impact BenefitsCal Transition Activities.

1. Medium Risk.
2. Procurement and provisioning activities in process. Prioritizing based on RJS schedule
