

CalSAWS

California Statewide Automated Welfare System



Biweekly Status Report

BenefitsCal Maintenance and Operations (M&O)

Reporting Period: July 13, 2026 – July 26, 2026

Table of Contents

1	EXECUTIVE SUMMARY	3
1.1	Highlights of the Reporting Period	3
1.1.1	Deliverable Summary	4
1.2	BenefitsCal Project Status Dashboard	4
1.3	Highlights of the Reporting Period	4
1.4	Deliverable Management	5
1.5	CRFI/CIT Communications	5
1.6	Risks and Issues	6
1.6.1	Project Risks	6
1.6.2	Project Issues	7
1.7	Project Work Plan Reports	7
1.8	Project Action Items – Overdue	9
1.9	SIRFRA/SCERFRA/SIRFRA/SARRA Information	9
1.10	Deviation from Plan/Adjustments	9
1.11	Transition-Out	10
2	BENEFITS CAL COLLABORATION MODEL (CM)	10
3	MAINTENANCE AND OPERATIONS	10
3.1	Service Management	11
3.1.1	Overview	11
3.1.2	BenefitsCal Help Desk Metrics	12
3.2	Technology Operations	19
3.3	BenefitsCal Maintenance and Operations	19
3.4	Production Defect Backlog	20
3.4.1	Release Schedule Production Defect Fix	21
3.5	Production Operations	22
3.6	Deviation from Plan/Adjustments	22
4	APPLICATION DEVELOPMENT AND TEST	22
4.1	Priority Release Summary	22
4.2	Requirements and Design	23
4.3	User Centered Design (UCD)	23
4.4	Development	24
4.5	User Acceptance Test (UAT) Planning	25
4.6	Release Management	25
4.7	System Test Execution	25

4.7.1 Automated Regression Test (ART) Coverage	26
5 PERFORMANCE TEST.....	27
5.1 Performance Test	27
5.2 Training Materials Update	27
5.3 Deviations from Plan/Adjustments	27
5.4 Security	27

TABLE OF TABLES

Table 1: Biweekly Status Agenda Topics	3
Table 2: Deliverable Summary	4
Table 3: Status Dashboard	4
Table 4: CITs.....	5
Table 5: CRFIs	5
Table 6: Overdue CRFIs	6
Table 7: Project Risks	6
Table 8: Project Issues	7
Table 9: Overdue Action Items	9
Table 10: Enhancements Updates, Prioritized by CM	10
Table 11: BenefitsCal Outages	19
Table 12: BenefitsCal Upcoming Maintenance	19
Table 13: Production Defect Fix – Release Schedule.....	21
Table 14: BenefitsCal Upcoming Releases.....	22
Table 15: Enhancement Actuals for Reporting Period	24
Table 16: Planned Enhancement Work	25
Table 17: Automated Regression Scripts Executed in BenefitsCal.....	26
Table 18: Performance Test Cycles and Test Case Status	27

TABLE OF FIGURES

Figure 1: Transition-Out Status Summary	10
Figure 2: BenefitsCal ServiceNow Incidents Created	12
Figure 3: BenefitsCal ServiceNow Incidents Resolved	13
Figure 4: BenefitsCal ServiceNow Incidents Closed.....	13
Figure 5: BenefitsCal ServiceNow Incidents Triaged.....	14
Figure 6: BenefitsCal ServiceNow Problems Created	15
Figure 7: BenefitsCal ServiceNow Problems Resolved	16
Figure 9: BenefitsCal ServiceNow Incidents by Resolution Code	17
Figure 10: BenefitsCal ServiceNow Incidents Created by Category.....	18
Figure 11: Production Defects Backlog Monthly Trend.....	20
Figure 12: BenefitsCal Production Defect Fix Status.....	21
Figure 13: UCD Stakeholder Engagement.....	24

Bi-Weekly Status – BenefitsCal M&O

1 EXECUTIVE SUMMARY

1.1 Highlights of the Reporting Period

Table 1: Biweekly Status Agenda Topics

STATUS REPORT SECTION	STATUS AGENDA TOPIC
1.3	26.07.21 Emergency release was deployed as planned. 26.07.19 July Priority release was deployed as planned.
July Enhancements (July Priority Release 26.07.19, July Monthly Release 26.07.30)	- Three (3) enhancements were deployed to Production on 07/19/26: - One (1) Partner Support Enhancements: - CSPM-83427: Update list of Appointment Categories to include Telephone GA/GR RE Interview Appointments - Two (2) Policy Enhancements: - CSPM-81960: TRUV Integration – Phase 1 - CSPM-80230: NA 1273 Opt-in for e-Notifications via BenefitsCal - One (1) defect was deployed to Production on 07/21/26 as emergency release. - Six (6) enhancements are targeted for deployment to Production on 06/25/26: - Three (3) Policy Enhancements: - CSPM-84702: Create a YouTube video for the Truv functionality in BenefitsCal - CSPM-82185: Update the 'How To submit a Medi-Cal Renewal' YouTube Video - CSPM-80929: HR1 – Semi-Annual Redeterminations for MAGI New Adult Group - Three (3) Production Priority Enhancement: - CSPM-83506: Update BenefitsCal Help Center Messaging for Non-Citizen / Immigration Content (Public Charge & CFAP Guidance) - CSPM-81865: Update Application/Case Dropdown Selection for users in BenefitsCal - CSPM-80062: Update Document Upload YouTube Video
User Centered Design (UCD) Activities	- Customer Experience (CX) Measurements Data - Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues. - User Engagement - No updates for the reporting period. - Enhancements - No updates for the reporting period.

STATUS REPORT SECTION	STATUS AGENDA TOPIC
	- Advocate Engagement - Sent out responses to comment log for offline UCD deck.
Transition-Out	- Access requests - Admin access provisioning in progress - Provided knowledge transfer (KT), job shadow (JS), and Reverse Job Shadow (RJS) support: 87 KT – 100% completed. 142 JS – 100% completed. 29 RJS sessions logged (96% completed) - Action Items, Defects, and Incident stats 267 of 264 Action Items completed 21 active defects 11 active incidents

1.1.1 Deliverable Summary

Table 2: Deliverable Summary

DEL #	DELIVERABLE NAME	STATUS	NEXT DEADLINE
	None for the Reporting Period		

1.2 BenefitsCal Project Status Dashboard

Table 3: Status Dashboard

TOPIC	STATUS	HIGHLIGHTS
Availability	On Time	The BenefitsCal System did not experience any unplanned outages.
Defects	On Time	There are twenty (20) active Production defects.
Incidents	On Time	There are three (5) open Tier 3 incidents.

1.3 Highlights of the Reporting Period

- Priority Release**
 - The BenefitsCal Team successfully deployed Priority Release 26.07.19 to BenefitsCal Production.
- Emergency Release**
 - The BenefitsCal Team successfully deployed Emergency Release 26.07.21 to BenefitsCal Production.
- Monthly Release**
 - None for the reporting period.
- Planned Outages**
 - Tuesday, 07/21/26 8:00 pm to 9:30 pm PST
 - BenefitsCal Monthly Release 26.07.21

- Sunday, 07/19/26 7:00 am to 8:30 am PST
 - BenefitsCal Monthly Release 26.07.19

1.4 Deliverable Management

- **Deliverables and Work Products submitted:**
 - DWP 24.36: CX Bimonthly Report (April 2026 – June 2026) on 07/14/26.
 - FWP 24.36: CX Bimonthly Report (April 2026 – June 2026) on 07/24/26.
- **Deliverable and Work Product submissions for the next reporting period**
 - None for the Reporting Period.

1.5 CRFI/CIT Communications

The following table outlines the CalSAWS Information Transmittals (CITs) for the reporting period.

Table 4: CITs

CIT ID	To	SUBJECT	DISTRIBUTION DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
0120-26	Notify.All; USBenefitsCalDevOps@De loitte.com; Operator@CalHEERs.ca.g ov; HoweG@CalSAWS.org; QuijadaP@CalSAWS.org; VenugopalanP@calsaws. org; Bill.Kelly@fisglobal.com; CalSAWS.All; Notify.SCATL.Outage Consortium.RegionalMan agers.All; Consortium.SectionDirect ors; Communications.Infra@C alSAWS.org	Scheduled Downtime Notification – 7/26/2026	06/29/26	Communications. Infrastructure	Pete Quijada

The following tables outline the CalSAWS Requests for Information (CRFIs) for the reporting period.

Table 5: CRFIs

CRFI ID	To	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	PRIMARY CalSAWS CONTACT	BACKUP CalSAWS CONTACT
None.							

Table 6: Overdue CRFIs

CRFI ID	To	SUBJECT	DISTRIBUTION DATE	STATUS	RESPONSE DUE DATE	PRIMARY CALSAWS CONTACT	BACKUP CALSAWS CONTACT
None.							

1.6 Risks and Issues

1.6.1 Project Risks

This section includes a summary of the updates to open risks to the BenefitsCal Project as of the last calendar day of the reporting period. For more details and the history of each risk, please refer to the CalSAWS Consortium risk log here: [CalSAWS SharePoint > Risk Log](#)

Table 7: Project Risks

ID	TITLE	UPDATES FOR THE REPORTING PERIOD	STATUS	RISK LEVEL	DATE LOGGED
326	Lack of timely policy guidance may impact Medi-Cal HR1 delivery schedule	No updates for the reporting period.	Open	Medium	12/15/25
327	Limited Availability of Deloitte Staff May Impact the BenefitsCal Transition Schedule	July 20, 2026: 7/20/2026: There were 2 additional RJS sessions added reporting week of 7/19. Expected the RJS to be completed by 7/24 and extended the risk trigger date to 7/31.	Open	Low	02/04/26
328	Lack of Availability of Deloitte Offshore Resources May Impact Transition of Development KT/JS Activities	July 20, 2026: RJS is expected to complete by 7/24/2026. Risk trigger date moved to July 31, 2026.	Open	Low	02/04/26
329	Delay in Providing Accenture Team Timely Access May Impact BenefitsCal Transition Activities	None for the reporting period.	Open	Medium	02/04/26
330	Current BenefitsCal System Performance May Not Meet the New SLA Performance Standards Set In The New Contract	None for the reporting period.	Open	Low	02/04/26

1.6.2 Project Issues


This section includes a summary of the updates to open issues for the BenefitsCal Project as of the last calendar day of the reporting period. For more details and the history of each issue, please refer to the CalSAWS Consortium issue log here: [CalSAWS SharePoint > Issues Log](#)


Table 8: Project Issues


ID	TITLE	UPDATES FOR THE REPORTING PERIOD	STATUS	PRIORITY	DATE LOGGED
None.					

1.7 Project Work Plan Reports

Project Timeline

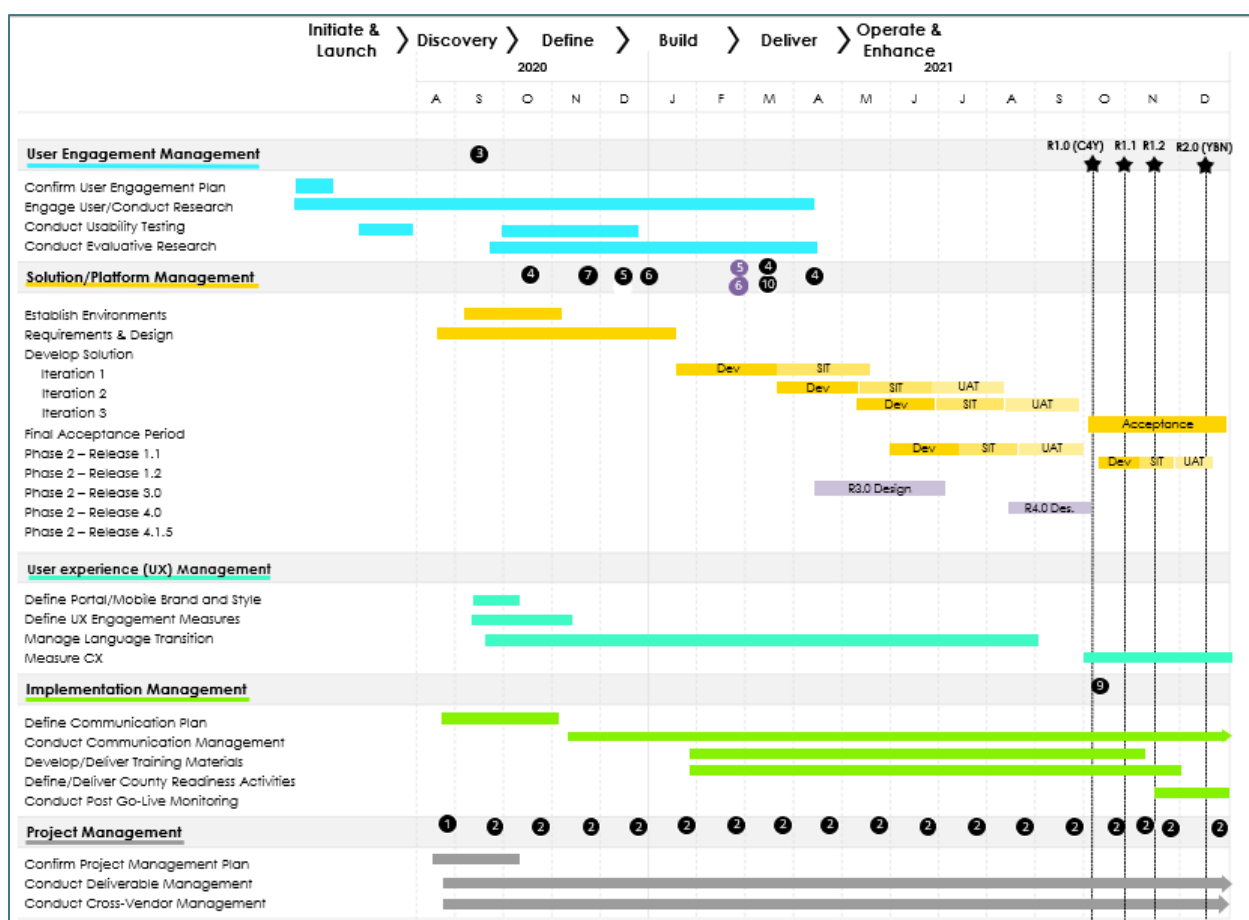

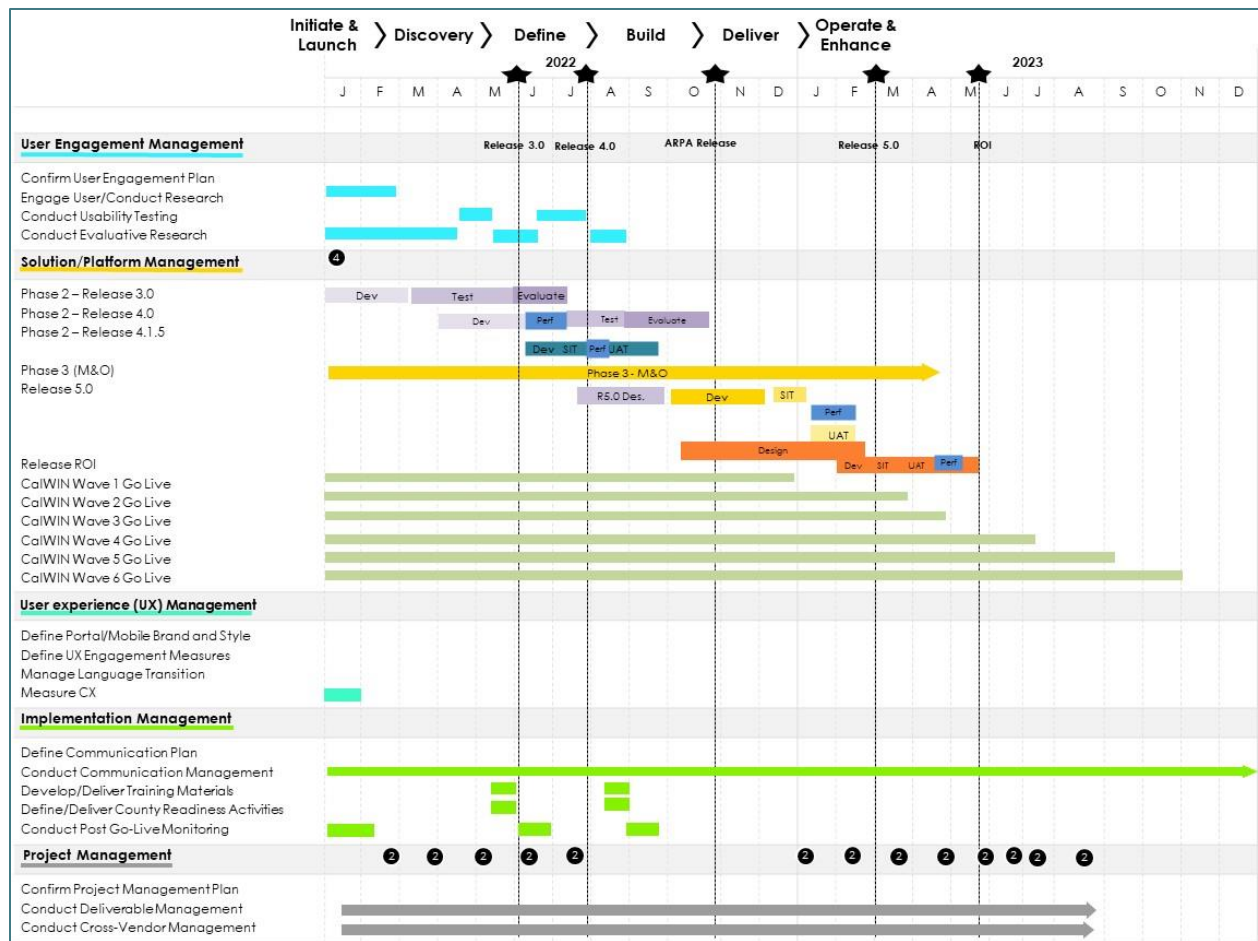

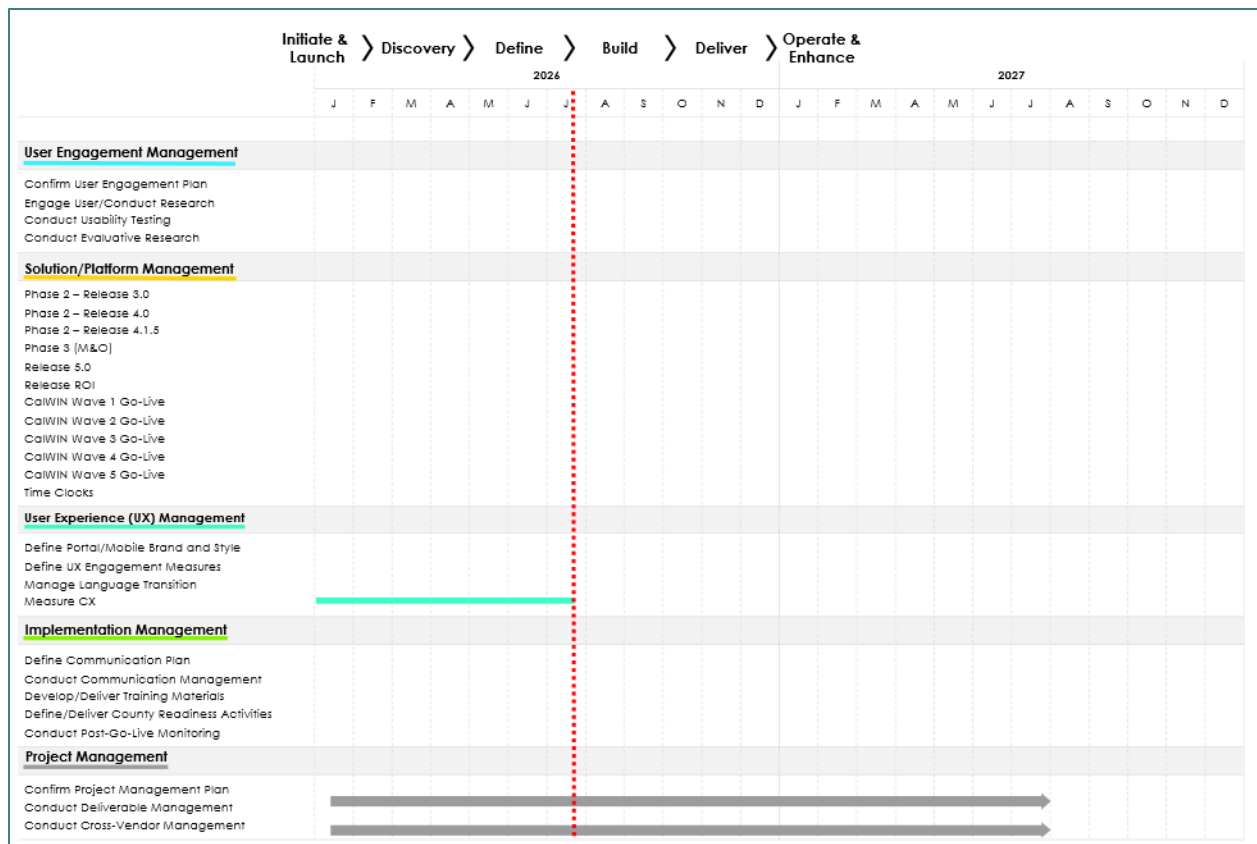

1.8 Project Action Items – Overdue

This table lists overdue action items, including the owner and due date.

Table 9: Overdue Action Items

ID	DESCRIPTION	OWNER	DUE DATE
	None for the reporting period		

1.9 SIRFRA/SCERFRA/SIRFRA/SARRA Information

The SIRFRA, SCERFRA, SIRFRA, and SARRA management and reporting for BenefitsCal has been transitioned to the Accenture BenefitsCal team as of May 1, 2026.

1.10 Deviation from Plan/Adjustments

- None for the reporting period.

1.11 Transition-Out

The figure below provides a summary of the transition-out progress with the incoming contractor, highlighting transition sessions, access and document requests, and risks and issues.

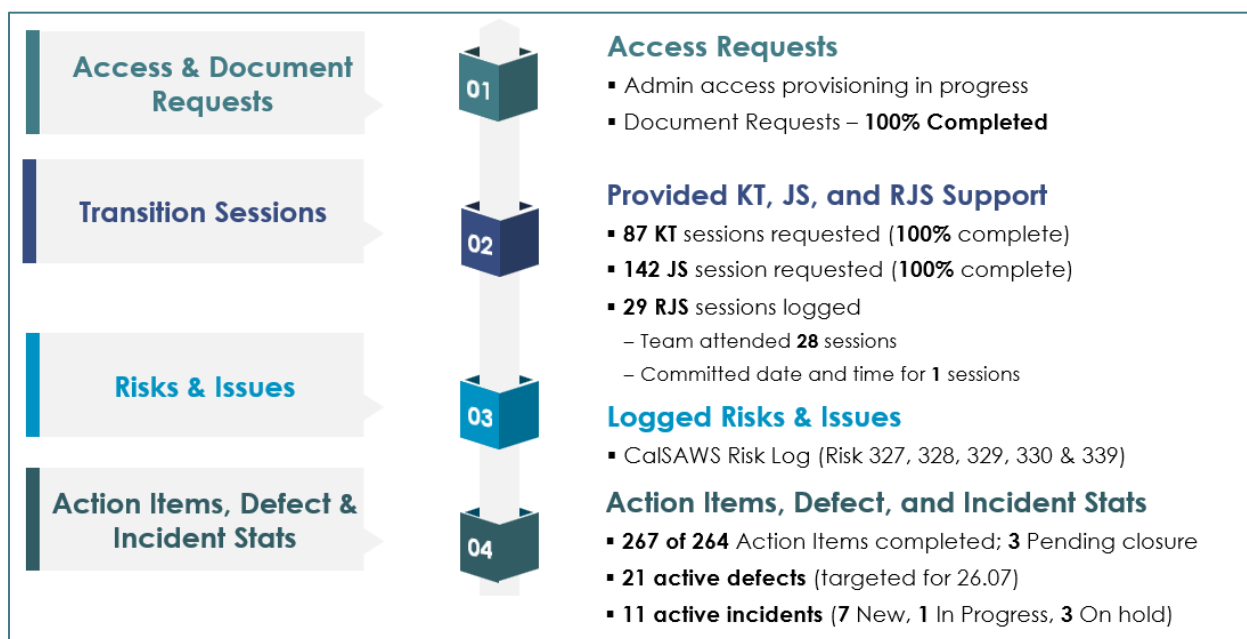


Figure 1: Transition-Out Status Summary

2 BENEFITSCAL COLLABORATION MODEL (CM)

Activities from the Reporting Period

Prioritization in progress for items prioritized in Q4 2023, Q1 2024, and Q2 2024. (They have already been logged in to Jira.)

The table below contains the current enhancements prioritized by CM in any quarter and their updates.

Table 10: Enhancements Updates, Prioritized by CM

ISSUE TYPE	ID	SUMMARY	STATUS	UPDATE THIS WEEK
None for the reporting period				

Activities for the Next Reporting Period

- Prioritize Collaboration Model Items for future releases.
- Perform design, development, and implementation analysis for enhancements and research action items identified in the Collaboration Model.

3 MAINTENANCE AND OPERATIONS

Operational Support

- Provided operational support for manual reprocessing of a transaction between CalSAWS and BenefitsCal.

CFA Meeting

- None for the reporting period.
- **Daily Partner Coordination Meetings**
 - Conducted daily partner coordination meetings with CalSAWS covering design, development, testing, and release management for defects and enhancements impacting both systems along with production observations.
- **M&O Phases**
 - Completed the initial acceptance period and moved into Maintenance and Operations.

3.1 Service Management

3.1.1 Overview

- **Incidents Created**
 - Five (5) incident was created in the biweekly reporting period for the BenefitsCal Tier 3 Team.
- **Incidents Resolved**
 - The BenefitsCal Tier 3 Team resolved two (2) incident in the biweekly reporting period.
- **Incidents Closed**
 - The BenefitsCal Tier 3 Team closed zero (0) incidents in the biweekly reporting period.
- **Incidents Triaged**
 - The BenefitsCal Tier 3 Team has triaged five hundred fifty (550) incidents in the biweekly reporting period.
- **Problems Created**
 - The BenefitsCal Tier 3 Team created two (2) problem tickets in the biweekly reporting period.
- **Problems Resolved**
 - The BenefitsCal Tier 3 Team resolved one (1) problem tickets in the biweekly reporting period.

3.1.2 BenefitsCal Help Desk Metrics

The charts below represent incidents created, resolved, and triaged within the reporting period. If a week is not shown within a particular chart, it is because there were no incidents to report for that week.

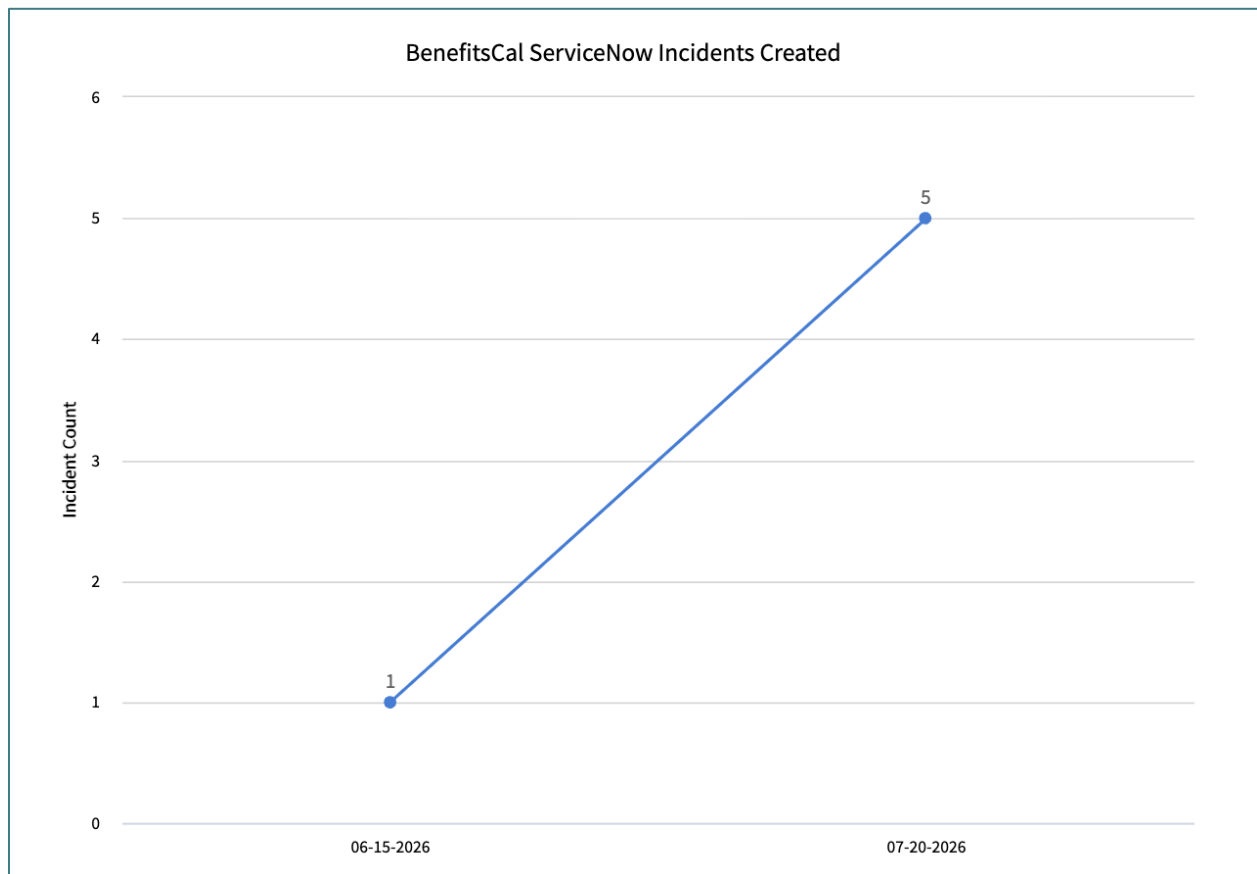


Figure 2: BenefitsCal ServiceNow Incidents Created

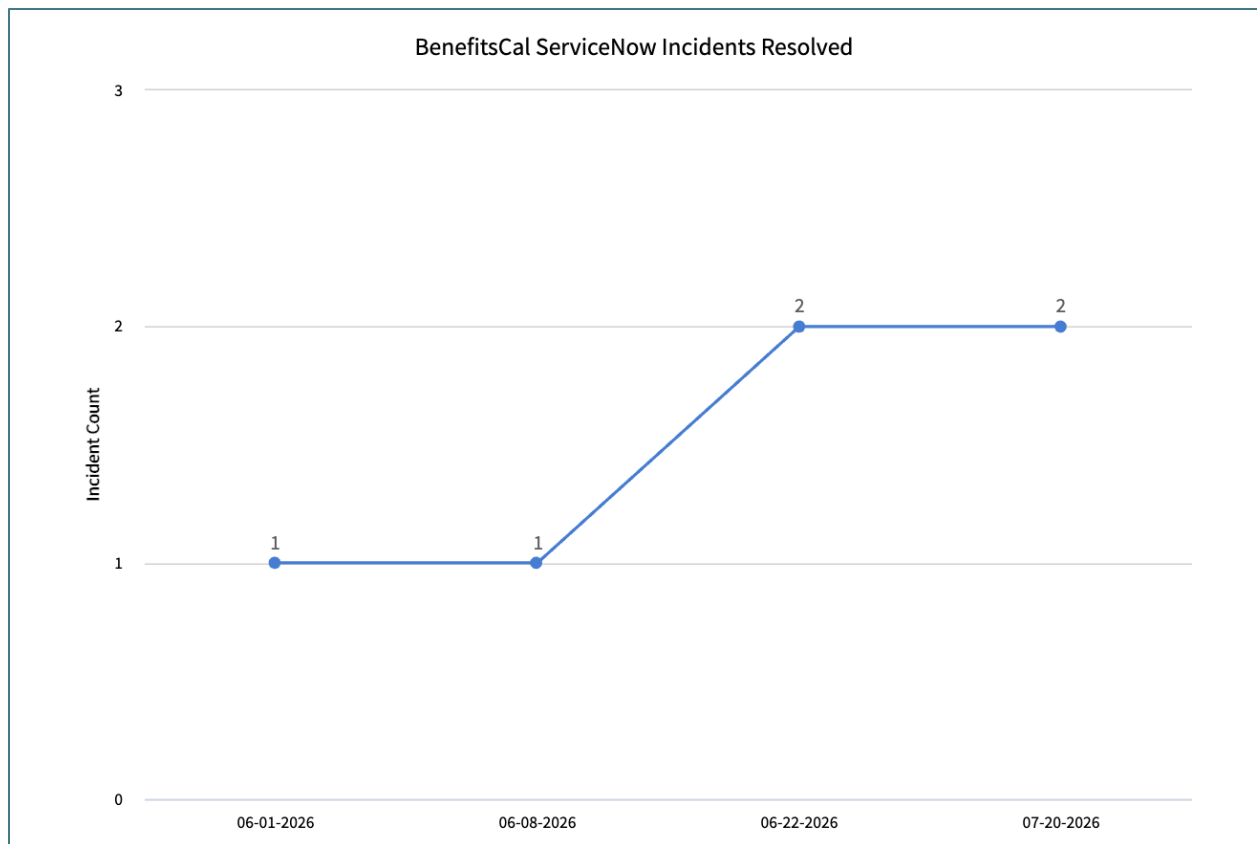


Figure 3: BenefitsCal ServiceNow Incidents Resolved

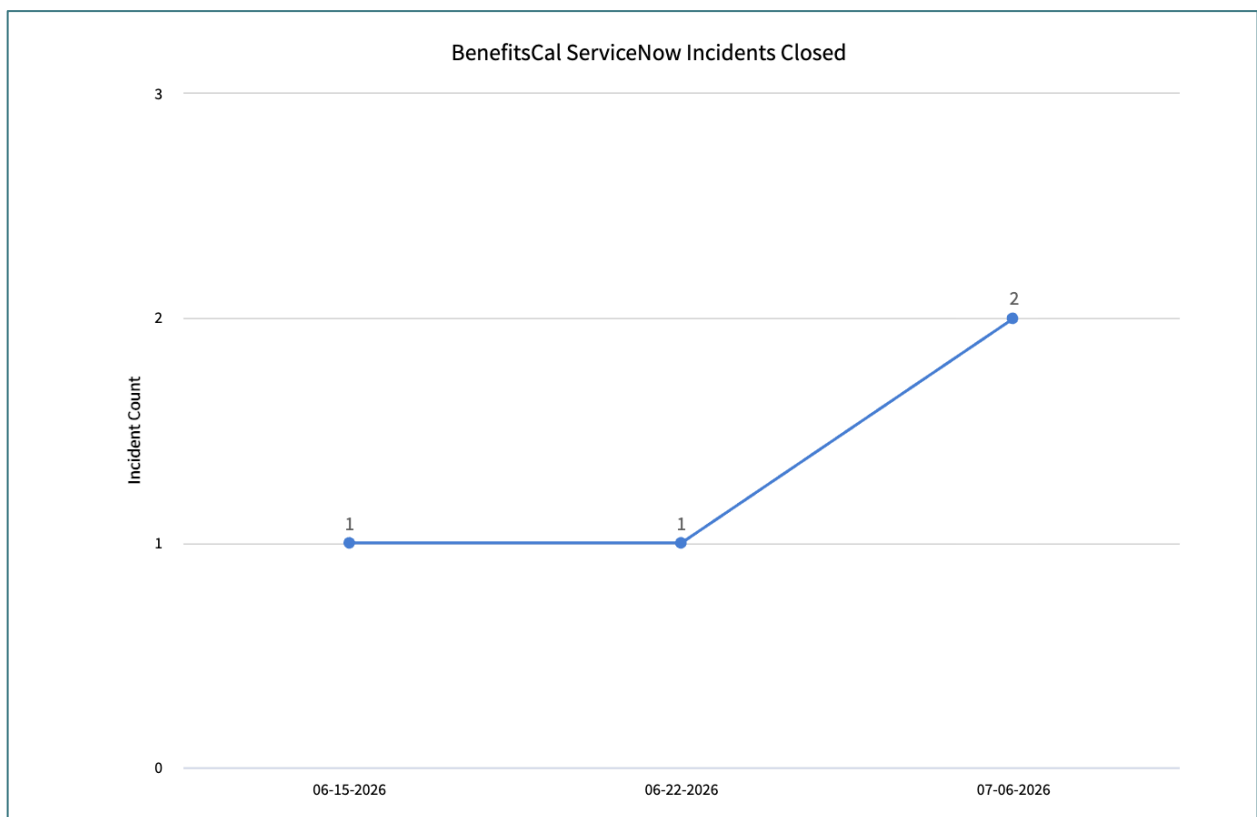


Figure 4: BenefitsCal ServiceNow Incidents Closed

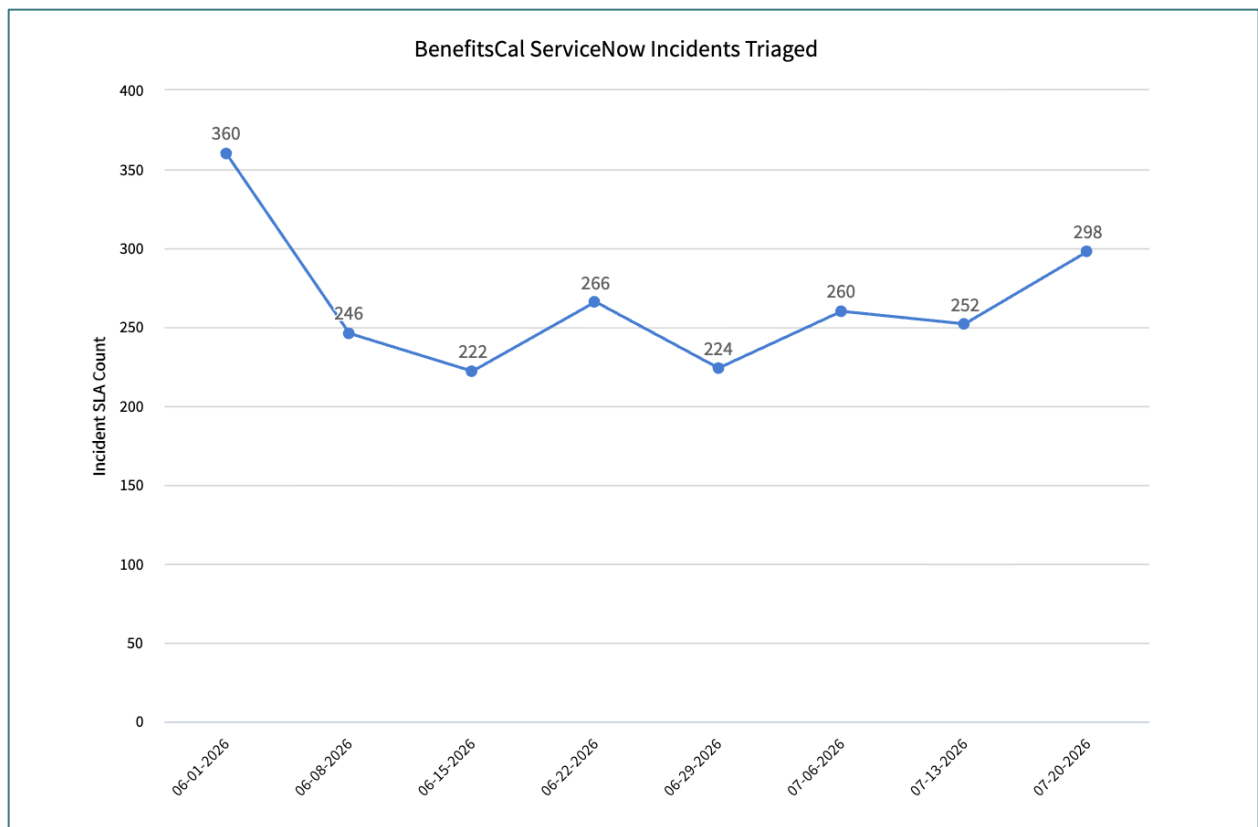


Figure 5: BenefitsCal ServiceNow Incidents Triaged

Note: The graphs above represent the ServiceNow incidents associated to all 58 Counties. Incidents represent the first level of ticketing that enters the ServiceNow system. The dates on the x-axis represent the start of week. The metrics does not include "Tier 3 App Support – BenefitsCal Questions (DLT)."

The charts below represent problems created, resolved, and triaged within the reporting period. If a week is not shown within a particular chart, it is because there were no problems to report for that week.

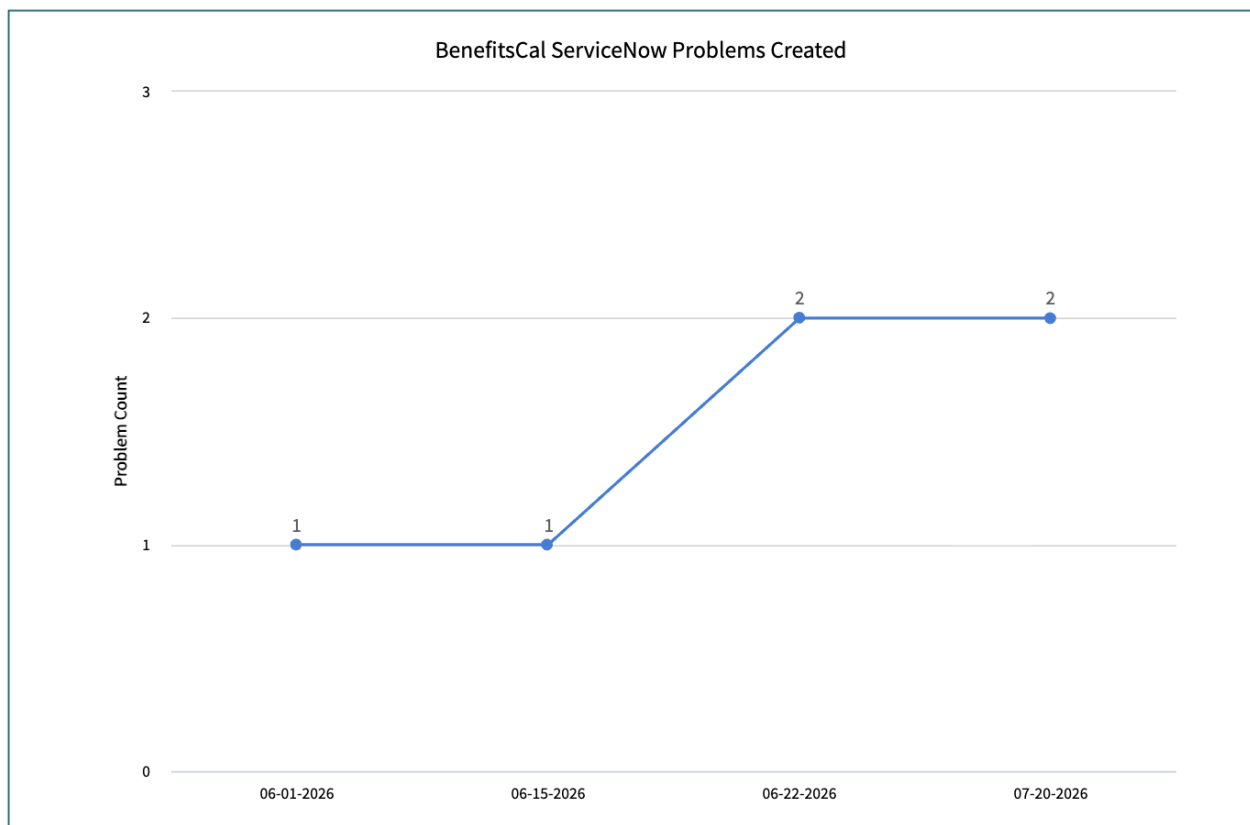


Figure 6: BenefitsCal ServiceNow Problems Created

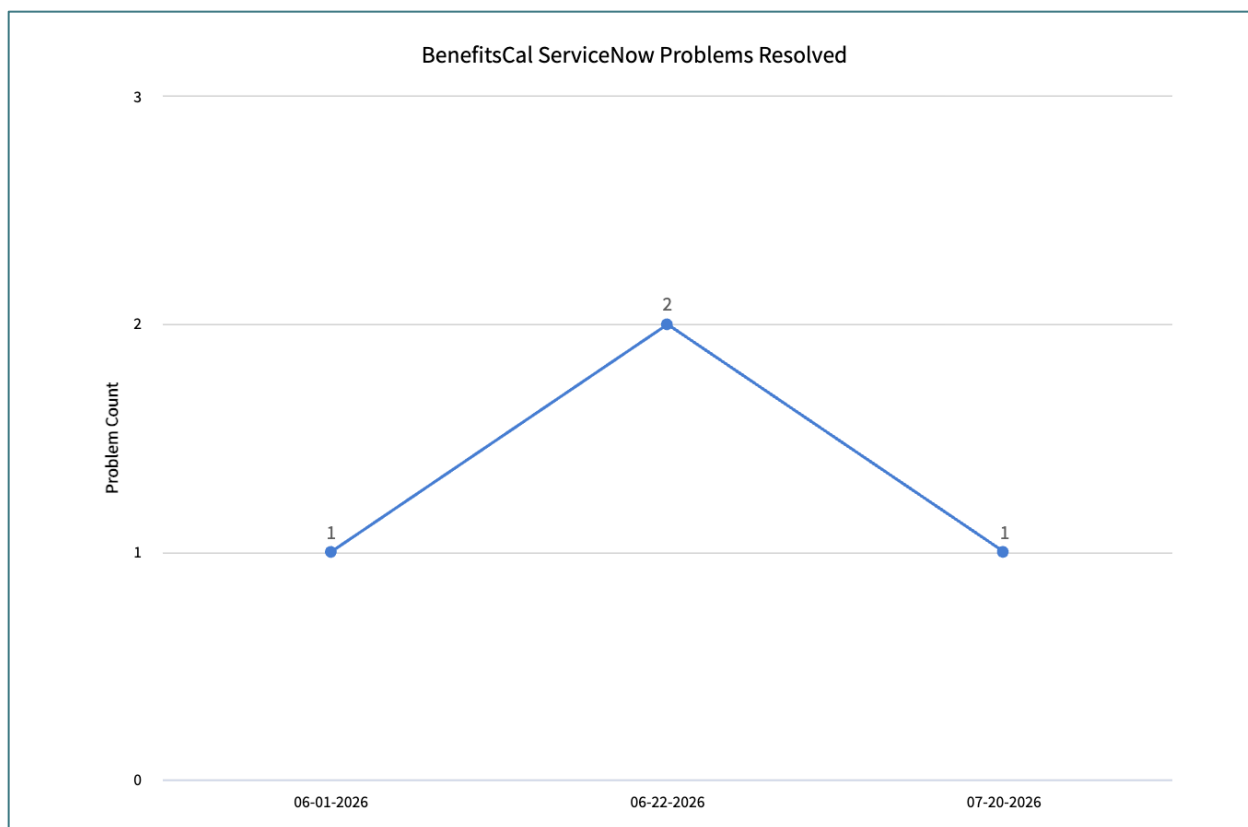


Figure 7: BenefitsCal ServiceNow Problems Resolved

Note: The graphs above represent the ServiceNow problems associated to 58 Counties. Problems represent issues that can have a many to one relationship with incidents and the last step in escalation. The dates on the x-axis represent the start of a week.

BenefitsCal ServiceNow Incidents by State and Age

State	Aging Category	(empty)	1-5 Days	6-10 Days	11-15 Days	16-30 Days	30-60 Days	60-180 Days	>180 Days	Count
New		2	0	0	0	0	0	0	0	2
In Progress		0	1	0	0	0	0	0	0	1
On Hold		0	0	0	0	0	0	2	0	2
Resolved		0	0	2	0	0	0	0	0	2
Closed		0	0	0	81	560	196	162	4	1,003
Count		2	1	2	81	560	196	164	4	1,010

Aging "State" definitions:

NEW	Incident triage not started.
IN PROGRESS	Incident triage in progress.
ON HOLD	Incident triage paused – awaiting information/problem.
RESOLVED	Incident triage completed providing steps for resolution.
CLOSED	Incident triage completed after a defect fix or change request implementation.

Figure 8: BenefitsCal ServiceNow Incidents by State and Age

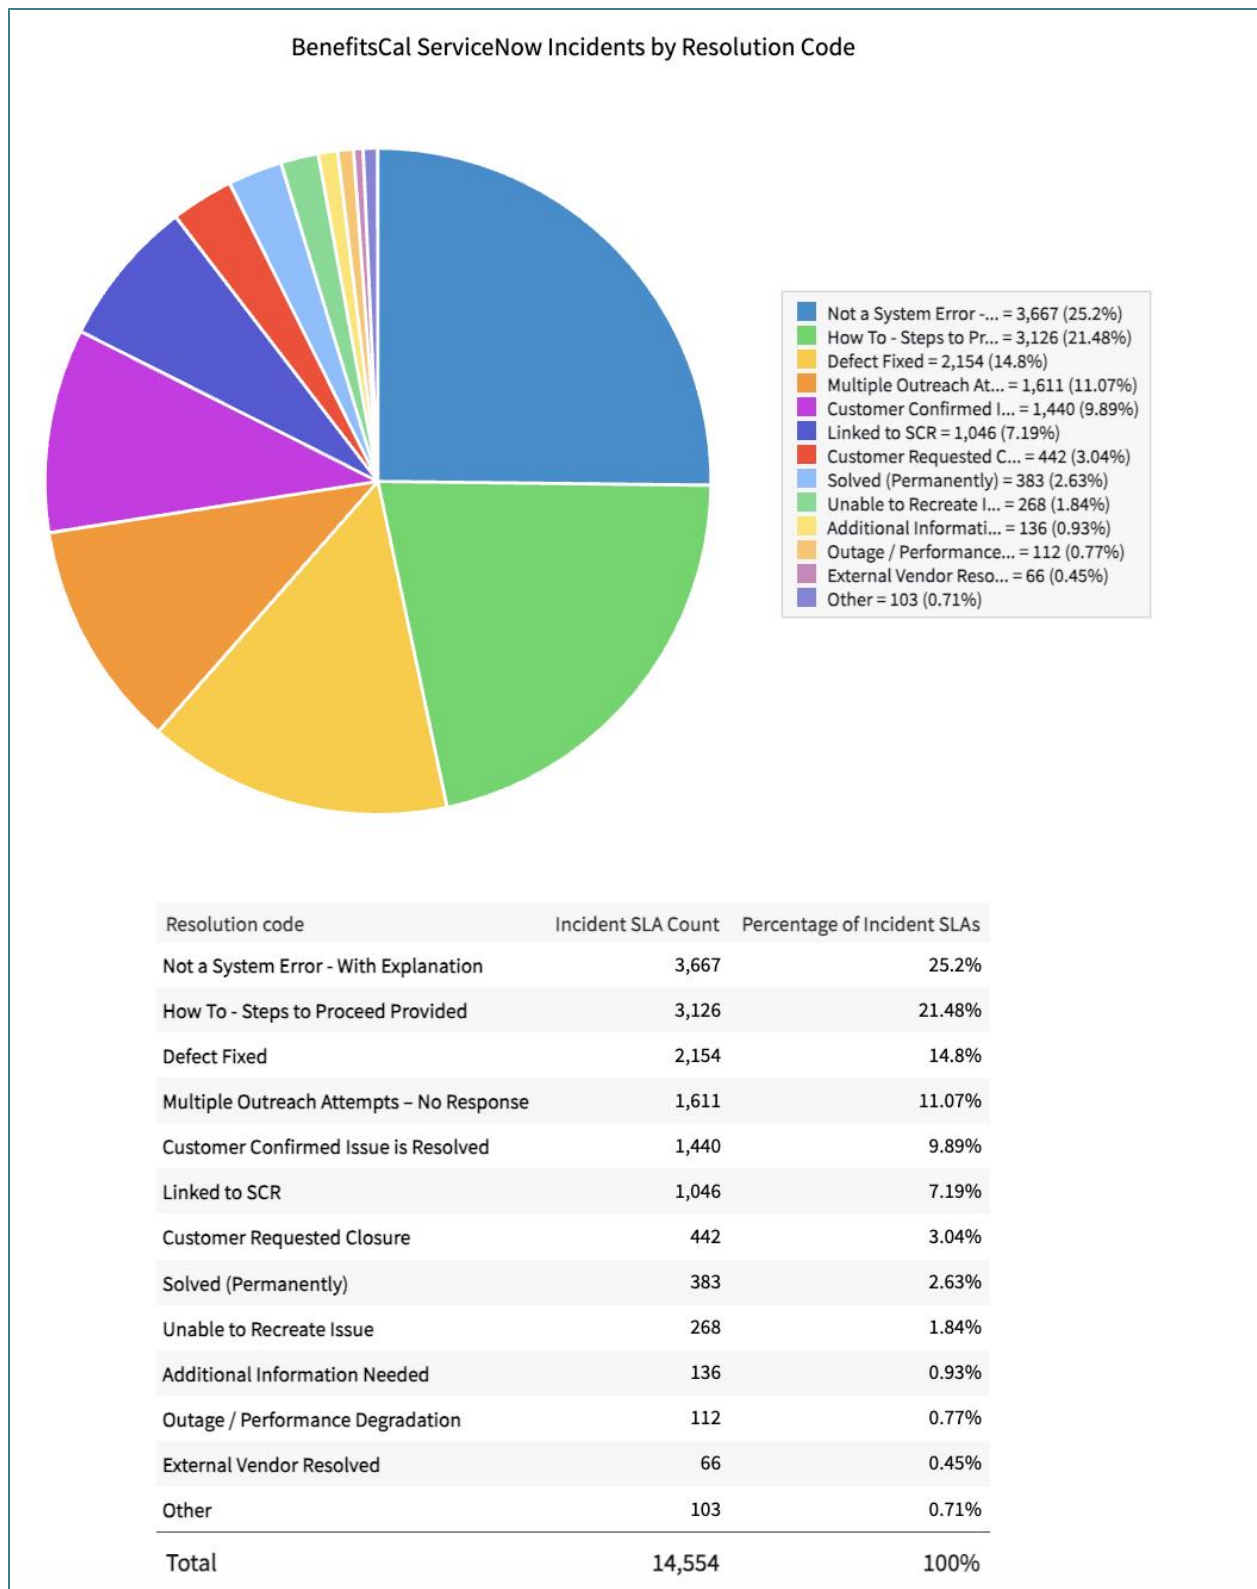


Figure 8: BenefitsCal ServiceNow Incidents by Resolution Code

Note: The pie chart above represents Incidents resolved since BenefitsCal Go-Live on 09/27/21.

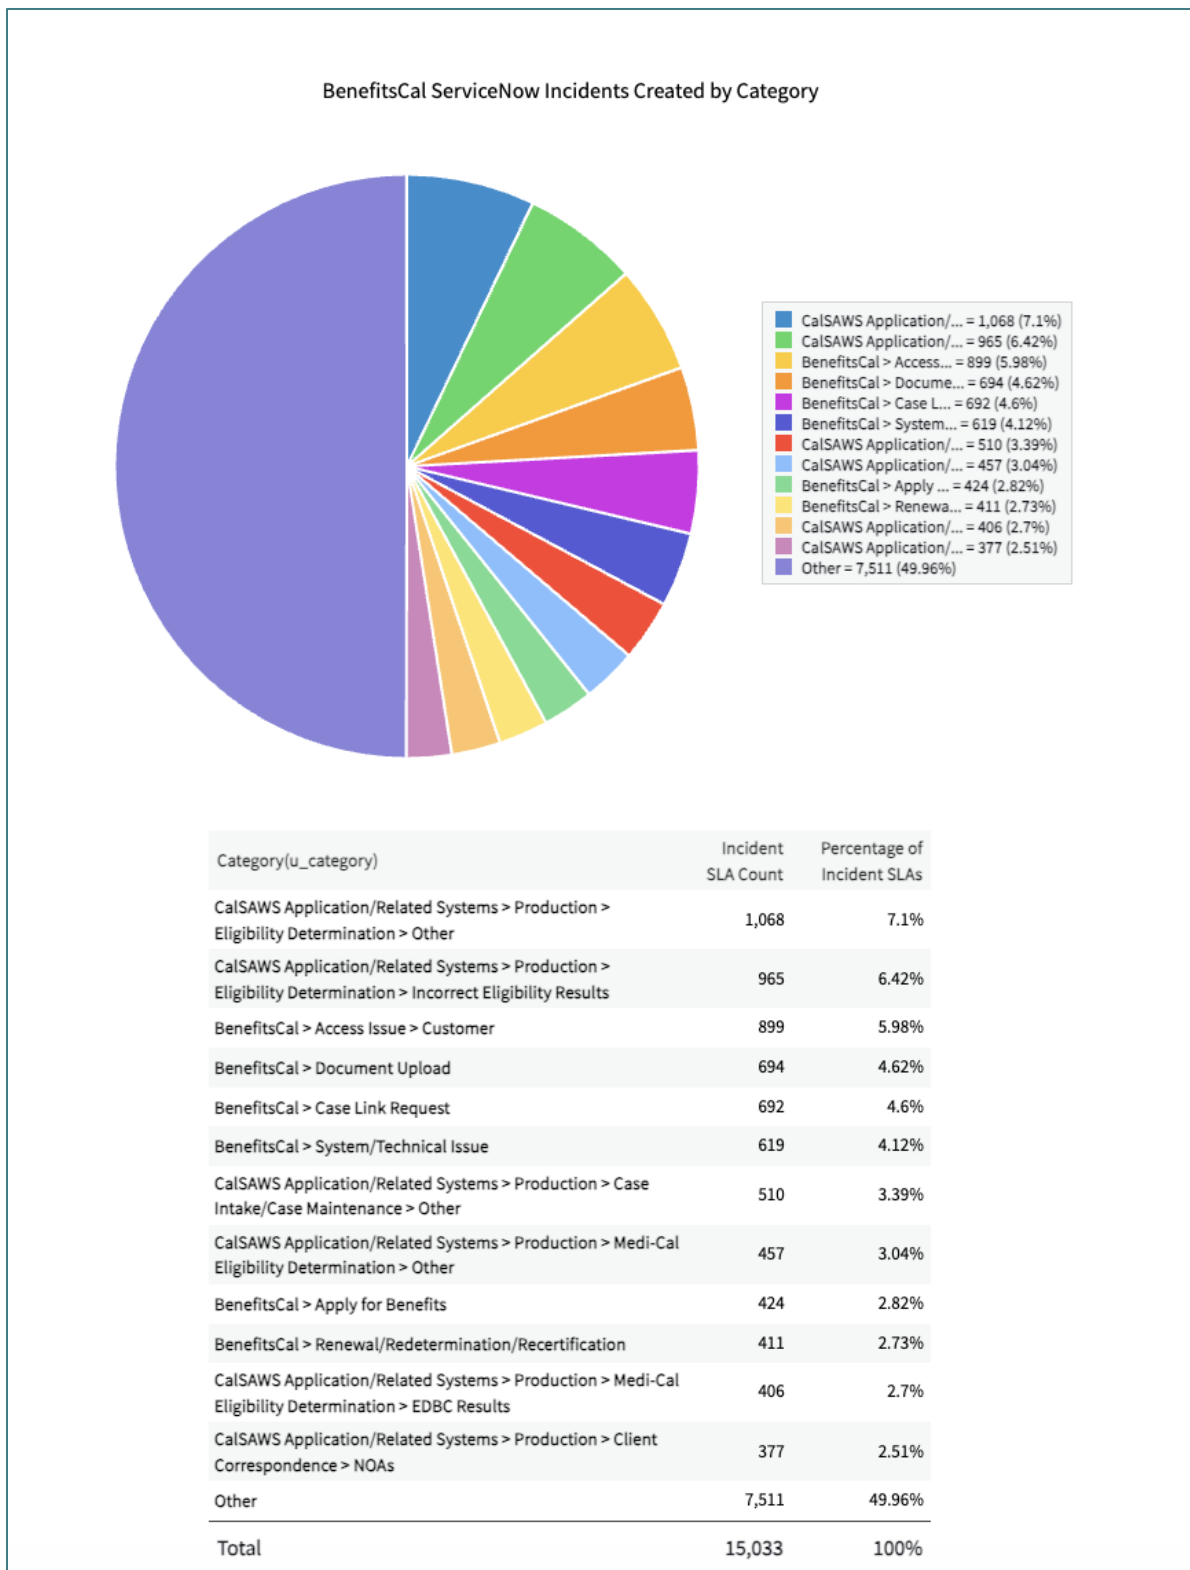


Figure 9: BenefitsCal ServiceNow Incidents Created by Category

Note: The pie chart above represents Incidents by category created since BenefitsCal Go-Live on 09/27/21. The “Other” category will cover incidents related to BenefitsCal module such as Dashboard, Help Center, Homepage, Report a Change, Application Summary.

3.2 Technology Operations

The BenefitsCal technology operations team provides Amazon Web Services (AWS) serverless infrastructure and BenefitsCal application support. Upgrades and changes to the infrastructure and application are performed following the Consortium change control process. AWS serverless infrastructure support activities include upgrades to AWS components such as the Web Application Firewall (WAF), CloudFront, Application Programming Interface (API) Gateway, Lambdas, Simple Queue Service (SQS), CloudWatch, X-Ray and Aurora Postgres, Postgres Relational Database Service (RDS), and RDS Proxy. Application maintenance and support include release and configuration management across the non-production and production environments.

3.3 BenefitsCal Maintenance and Operations

Table 11: BenefitsCal Outages

SCHEDULED DATE	OUTAGE TIMEFRAME	ACTIVITY DESCRIPTION
07/19/26	6:00 am – 1:00 pm PST	CalSAWS Application Maintenance (Offline mode)
07/19/26	7:00 am – 8:30 am PST	BenefitsCal Priority Release- 26.07.19
07/21/26	8:00 pm – 9:30 pm PST	BenefitsCal Emergency Release – 26.07.21
07/24/26	10:00 pm – 1:00 am PST	Hyland maintenance (Holding Document queues)
07/26/26	2:00 pm – 6:30 pm PST	CalSAWS Application Maintenance (Offline mode)

Table 12: BenefitsCal Upcoming Maintenance

SCHEDULED DATE	OUTAGE TIMEFRAME	APPLICATION MODE
07/30/26	8:00 pm – 9:30 pm PST	BenefitsCal Production Deployment– 26.07.30

3.4 Production Defect Backlog

The Production defect backlog bar chart depicts the balance of open (unresolved Production defects assigned to present months production release – Red and closed defects – Green), month-over-month. Defects are closed upon system test validation and release of deployment to Production.



Figure 10: Production Defects Backlog Monthly Trend

3.4.1 Release Schedule Production Defect Fix

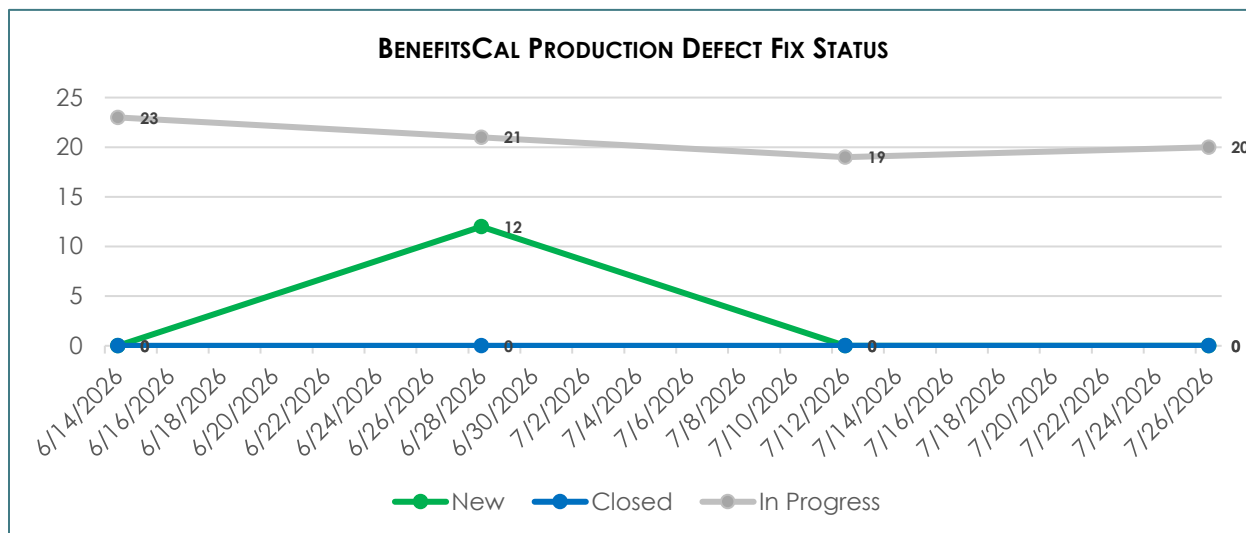


Figure 11: BenefitsCal Production Defect Fix Status

Table 13: Production Defect Fix – Release Schedule

Count of Defects	Release	
Severity	Release 26.07.30	Total
1-HIGH	1	1
New	0	0
In Progress	1	1
Closed	0	0
2-NORMAL/MEDIUM	0	0
New	0	0
In Progress	0	0
Closed	0	0
3-NORMAL/LOW	19	19
New	0	0
In Progress	19	19
Closed	0	0
4-COSMETIC	0	0
New	0	0
In Progress	0	0
Closed	0	0
TOTAL	20	20

Note: Automated regression tests are run for each planned release. Automated regression tests are excluded for emergency releases as the window for execution is short. The regression suite is revisited after each major release and periodically updated once new application functionality has been released. The update could be adding a new script to the repository or modifying an existing script to cover new functionality since the new functionality replaces the old functionality. New functionality will be called out in the coverage column.

3.5 Production Operations

- **Root Cause Analysis (RCA)**
 - None for the reporting period.

3.6 Deviation from Plan/Adjustments

- None for the reporting period.

4 APPLICATION DEVELOPMENT AND TEST

4.1 Priority Release Summary

This section outlines the scope of defect fixes included in each ad-hoc priority release deployed during this reporting period.

- **BenefitsCal Monthly Release**
 - None for the reporting period.
- **BenefitsCal Priority Release**
 - Three (3) enhancements are planned with Benefits Monthly Release 26.07.19 for User Error Handling, Exception Handling, and Application Summary.
- **BenefitsCal Emergency Release**
 - One (1) defect is deployed with Benefits Emergency Release 26.07.21 for User Error Handling, Exception Handling, and Application Summary.

Table 14: BenefitsCal Upcoming Releases

RELEASE	RELEASE DATE	SUMMARY
26.06.19-Priority	07/19/26	▪ Three (3) enhancements are planned with Benefits Monthly Release 26.07.19 for User Error Handling, Exception Handling, and Application Summary.
26.07.30 – Monthly	07/30/26	▪ Three (3) enhancements and twenty (20) production defects are planned with Benefits Monthly Release 26.07.30 for User Error Handling, Exception Handling, and Application Summary.

4.2 Requirements and Design

- **Activities for the Reporting Period – Requirements and Design**
 - **Designs and Design Meetings**
 - ♦ Attended the *Work Requirements/Six-Month Redetermination County Workgroup* debrief on 07/13/26 and 07/20/26.
 - ♦ Attended 26.07 Project Integrated Readiness Areas - T-1 Integrated Readiness Status on 07/13/26.
 - ♦ Attended URGENT: 26.07 SCR CA-297470 Outstanding Items on 07/13/26.
 - ♦ Attend 26.07 Pre Green Light Meeting on 07/13/26.
 - ♦ Hosted the DDI and M&O biweekly meetings on 07/14/26, 07/16/26, 07/21/26, and 07/23/26.
 - ♦ Hosted BenefitsCal Truv Demo for "Not my income" on 07/14/26.
 - ♦ Hosted CSPM-80929/CA-299479 (Semi-Annual RE) Discussion: E2E Testing Delays on 07/14/26.
 - ♦ Attended the BenefitsCal: July 2026 UCD Monthly Meeting on 07/15/26.
 - ♦ Attended the CalSAWS Virtual Greenlight Release 26.07 on 07/15/26.
 - ♦ Attended the Truv and CalSAWS meetings on 07/16/26 and 07/23/26.
 - ♦ Attended the SCR CA-298517 – *Truv Phase 2 – Internal Sync with CalSAWS* on 07/16/26.
- **Activities for the Next Reporting Period – Requirements and Design**
 - **Designs and Design Meetings**
 - ♦ Attend the *Work Requirements/Six-Month Redetermination County Workgroup* debrief on 07/27/26 and 08/03/26.
 - ♦ Host the DDI and M&O biweekly meetings on 07/28/26, 07/30/26, 08/04/26, and 08/06/26.
 - ♦ Attend the CalSAWS Truv Phase 2 discussion on 07/29/26 and 08/05/26.
 - ♦ Attend the Truv and CalSAWS meetings on 07/30/26 and 08/06/26.
 - ♦ Attend the SCR CA-298517 – *Truv Phase 2 – Internal Sync with CalSAWS* on 07/30/26 and 08/06/26.
 - ♦ Attend BenefitsCal - Truv Phase 1 Webinar - CBO/Assistors on 08/05/26.

4.3 User Centered Design (UCD)

- **Activities for the Reporting Period – UCD**
 - **Customer Experience (CX) Measurements Data**
 - ♦ Monitored the CX Measurements data from Medallia, Amplitude, and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
 - **User Engagement**
 - ♦ No update for the reporting period.
 - **Enhancements**
 - ♦ No updates for the reporting period.
 - **Advocate Engagement**
 - ♦ Sent out responses to comment log for offline UCD deck.

- **Activities for the Next Reporting Period – UCD**
 - **CX Measurements Data**
 - ♦ Monitor the CX Measurements data from Amplitude and BenefitsCal on a day-to-day basis to identify and address potential usability issues.
 - **Enhancements**
 - ♦ No updates for the reporting period.
 - **User Engagement**
 - ♦ No update for the reporting period.
 - **Advocate Engagement**
 - ♦ No update for the reporting period.

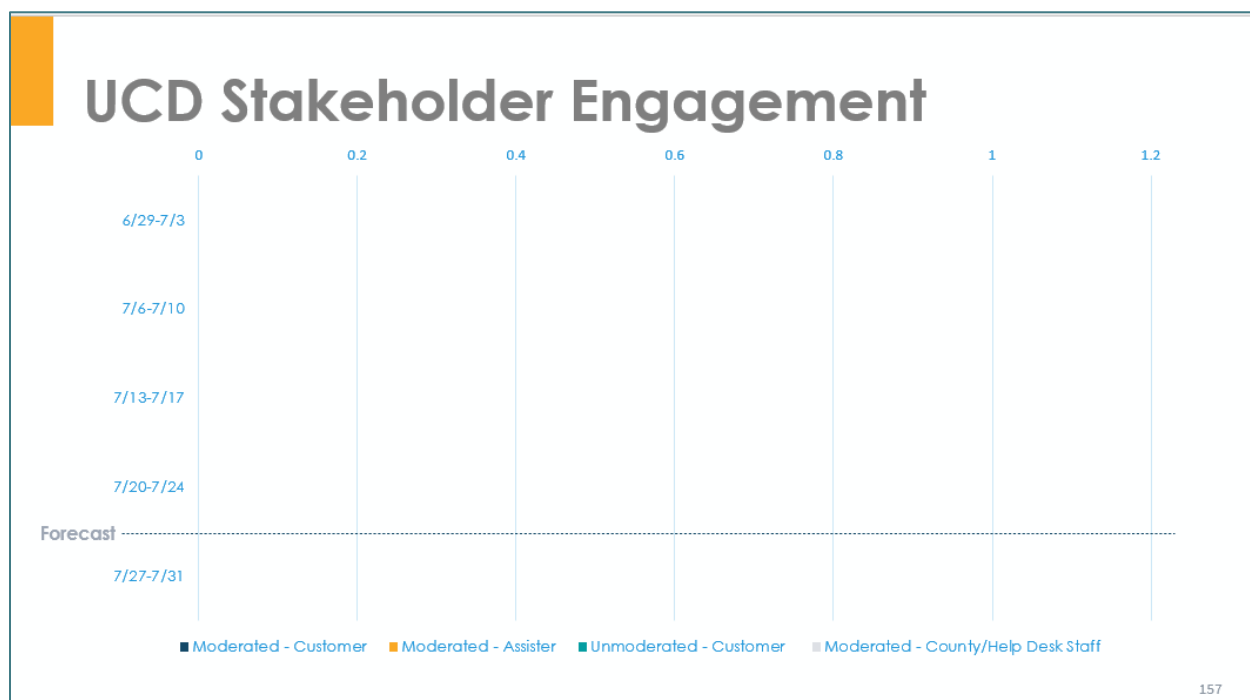


Figure 12: UCD Stakeholder Engagement

4.4 Development

- **Activities the Reporting Period – Development**
 - Enhancements (M&E)

Table 15: Enhancement Actuals for Reporting Period

RELEASE	PLANNED FOR WEEK ENDING 07/26/26	ACTUAL FOR WEEK ENDING 07/26/26	TOTAL PLANNED FOR THE RELEASE	COMMENTS
Release 26.07.30	4	4	5	Release 26.07.30 is planned for deployment on 07/30/26.

- **Activities for the Next Reporting Period – Development**

- Enhancements (M&E)

Table 16: Planned Enhancement Work

RELEASE	PLANNED FOR WEEK ENDING	TOTAL PLANNED FOR THE RELEASE	TOTAL COMPLETED FOR THE RELEASE	COMMENTS
None				

- **Unscheduled Release Updates**

- **Chatbot**
 - ♦ Reported the issues for Chinese, Japanese, and Korean languages to AWS, and have received confirmation that these issues have been resolved.
 - ♦ Engaging with native speakers to conduct thorough testing of the bot. Following their validation, we will collaborate with the AWS team to address any further issues that may arise.

4.5 User Acceptance Test (UAT) Planning

- **Activities for the Reporting Period – User Acceptance Test Planning**

- **UAT Test Execution**
 - ♦ Tickets tagged to Release 26.07.19 were validated.
 - ♦ Tickets tagged to Release 26.07.30 were validated.
- **Test Support**
 - ♦ Provided clarification and support to the QA/Consortium/Independent Test Team for defects and enhancements tagged to Release 26.07.19 and Release 26.07.30.

- **Activities for the Next Reporting Period – User Acceptance Test Planning**

- **UAT Test Execution**
 - ♦ Defects for Release 26.07.30 will be validated.
- **Test Support**
 - ♦ Clarification and Support will be provided to the QA/Consortium/Independent Test Teams for defects tagged to Release 26.07.30.

4.6 Release Management

- **Activities for the Reporting Period – Release Management**

- **Release 26.07.19 – July Priority Release**
 - ♦ Deployed the July Priority Release – 26.07.19 into Production.

4.7 System Test Execution

- **Activities for the Reporting Period – System Test Execution**

- **Release 26.07.19 – July Priority Release**
 - ♦ Validated tickets tagged to the July Priority Release – 26.07.19.
- **Release 26.07.30 – July Monthly Release**

- ♦ Validated tickets tagged to the July Monthly Release – 26.07.30.

4.7.1 Automated Regression Test (ART) Coverage

The following are the automated regression scripts executed for regression in BenefitsCal for Release 26.06.21.

Table 17: Automated Regression Scripts Executed in BenefitsCal

RELEASE	# OF SCENARIOS EXECUTED	# OF SCENARIOS PASSED	# OF SCENARIOS FAILED	OVERALL PASS %	PASS OF EXECUTED	COVERAGE
26.07.19	26	26	0	100	100	Regression cover all the important functionalities, like AFB with all programs , Continue Application for AFB , DisasterCalFresh, Report A Change, CBO M Login, Creating CBO Referral, Archiving Campaign, Dashboard - checking EBT balance, CF37 with ABAWD, MC210, Periodic Reports:SAR7, Support Request, Interview Nudge - Email /Text, IRT, Messages/Actions, AFB with ABAWD, TNB4, ROI Validations that it should not be visible, Global Search, Anonymous Document Upload, SSA, Find an Office, Help Module changes, FAT scripts for all flows . Also validated EBT functionality across 4 browsers and 4 devices.
26.07.30	73	73	0	100	100	Regression covers all the flows (AFB, RAC, MC210/216/217, TNB4, DCF, SAR7, CF37, Redet CW) and all the major functionalities for Help Module, Admin Module along with different flows and combinations covering document upload, TRUV, all user types and account management functionality, continue functionality etc.

5 PERFORMANCE TEST

5.1 Performance Test

- **Release 26.07.19 and 26.07.30 – July Priority and Monthly Release**
 - BenefitsCal July priority release performance testing scope includes three (3) enhancements: CSPM-80230: NA 1273 Opt-in for e-Notifications via BenefitsCal, CSPM-81960: TRUV Integration – Phase 1, and CSPM-83427: Update list of Appointment Categories to include Telephone GA/GR RE Interview Appointments, respectively. The performance testing team will update the impacted scripts on the latest codebase to reflect the enhancements and defect changes, ensure all other scripts work as expected, and plan the performance tests as per below schedule.

Table 18: Performance Test Cycles and Test Case Status

CYCLE	START DATE	END DATE	SCOPE	TEST CASES STATUS	EXECUTION STATUS
15	06/22/26	07/30/26	Release 26.07.19 Priority and 26.07.30 July Monthly	Scope: Three (3) enhancements in scope. Executions for Priority release: BenefitsCal isolated Load tests via mock services: ▪ Monday, July 13 (Completed) ▪ Tuesday, July 14 (Completed) Executions for Monthly release: BenefitsCal isolated Load tests via mock services: ▪ Monday, July 27 (Completed) ▪ Tuesday, July 28	90%

5.2 Training Materials Update

- None for the reporting period.

5.3 Deviations from Plan/Adjustments

- None for the reporting period.

5.4 Security

- **Activities for the Reporting Period – Security**

- [REDACTED]
- ♦ [REDACTED]

- **DAST**

- ♦ Executed the biweekly Dynamic Application Security Testing (DAST) manual penetration testing test cases and shared the analysis of the security scan reports with the BenefitsCal Development Team on 07/24/26.

- **Scan**

- ♦ [REDACTED]

- **Activities for the Next Reporting Period – Security**

- **Identified Vulnerabilities**

- ♦ [REDACTED]

- **AWS SSO (Single Sign-On) for BenefitsCal**

- ♦ Collaborate with the Consortium Security Team to update Amazon Web Services Single Sign-On (AWS SSO) users specific to BenefitsCal and facilitate onboarding and offboarding of AWS SSO for BenefitsCal users, as needed.
